

**SUBMITTAL TO THE BOARD OF SUPERVISORS
COUNTY OF RIVERSIDE, STATE OF CALIFORNIA**

426A



FROM: TLMA – Transportation Dept.

SUBMITTAL DATE:
December 8, 2003

SUBJECT: Notice of Completion – Construction of Sewer and Water Improvements, Silverhawk II Tract 29593-4, CFD 88-4, Murrieta Area

RECOMMENDED MOTION: That the Board execute and file the attached "Notice of Completion"

BACKGROUND: By Minute Order 3.23 of April 22, 2003, the Board entered into an agreement with Surina Construction Company, Inc. for the construction of sewer and water improvements within Silverhawk II, Tract 29593-4, in the Murrieta area of Riverside County. The authorized amount of the contract was \$332,685.95. The total amended contract amount (including Change Orders and quantity adjustments) is \$315,452.46, which is 5.2% less than the originally authorized amount.

This work was completed in conformance with the plans and specifications on September 15, 2003. The work was inspected by the Construction Engineering Section of the Transportation Department. Work Order 74-1004.

Continued on Page 2...

Departmental Concurrence

HS:js
Attachments: Notice of Completion

George A. Johnson
George A. Johnson
Director of Transportation

FINANCIAL DATA	Current F.Y. Total Cost:	\$ 315,452.46	In Current Year Budget:	Yes
	Current F.Y. Net County Cost:	\$ 0.00	Budget Adjustment:	No
	Annual Net County Cost:	\$ 0.00	For Fiscal Year:	2003/2004
SOURCE OF FUNDS: CFD 88-4				Positions To Be Deleted Per A-30 <input type="checkbox"/>
				Requires 4/5 Vote <input type="checkbox"/>

C.E.O. RECOMMENDATION: APPROVE

County Executive Office Signature

Jennifer S. Siefert

- Dep't Recomm.: Consent Policy
- Per Exec. Ofc.: Consent Policy

Prev. Agn. Ref.: 4/22/03 (3.23)

District: 3

Agenda Number:

3.26

The Honorable Board of Supervisors
RE: Notice of Completion

Page 2 of 2

Budget

Original Contract Amount			\$332,685.95
Tot. Chg Orders Authorized -	2	-3.0%	(\$9,823.25)
Est. Pending Change Orders		0.0%	\$0.00
Amended Contract Amount			\$322,862.70
* Quantity Adjustments		-2.2%	(\$7,344.54)
+ CCO FA Adjustments		0.0%	<u>(\$65.70)</u>
Total Amended Contract Amount		94.8%	\$315,452.46

Expenditures

Total Progress Payments -	4		\$315,452.46
Estimated Pending Payments			\$0.00
Total Expenditures			<u>\$315,452.46</u>

(Over)\Under Contract Amount \$0.00

+ Change Orders using the Force Account method of payment issued prior to the work being completed generally do not use the total authorized amount.

* CAL-Trans Standard Specifications 4-1.03B. Increases or decreases in the quantity of a contract item of work will be determined by comparing the total pay quantity of such item of work with the Engineer's Estimate therefor. If the total pay quantity of any item of work required under the contract varies from the Engineers Estimate therefor by 25 percent or less, payment will be made for the quantity of work of said item performed at contract unit price, therefor, unless eligible for adjustment pursuant to Section 4-1.03C, "Changes in Character of Work."

<p>When recorded, return to:</p> <p>After Recording, deliver to: Clerk of Board of Supervisors</p>
<p>Notice of Completion</p>
<p>(Civil Code § 3093 - Public Works)</p>

(For Recorder's use)

To be recorded with County Recorder
within 10 days after completion.
No recording fee.

Notice is hereby given by the undersigned owner, a public entity of the State of California, that a public work of improvement has been completed, as follows:

Project title or description of work: Sewer and Water Improvements Silverhawk II, Tract 29593-4

Date of Completion: _____ Date of this notice

Nature of owner: _____ County

Interest or estate of owner: _____ Public Roadway

Address of owner: _____ 4080 Lemon Street, 8th Floor, Riverside, CA 92501

Name of contractor: _____ Surina Construction Company, Inc.

Street or legal description of site: _____ McGowans Pass to 200' westerly of Vista Rock Drive, Lilac Lane, Wisteria Lane, East Green Drive, and Vista Rock Drive, in the Temecula area

Dated: _____

Owner: _____ County of Riverside
(Name of Public Entity)

By: _____
Chairman, Board of Supervisors


STATE OF CALIFORNIA)

ss

COUNTY OF RIVERSIDE)

I am the Chairman of the governing board of the County of Riverside, the public entity which executed the foregoing notice and on whose behalf I make this verification; I have read this notice, know its contents, and the same is true. I certify under penalty of perjury that the foregoing is true and correct.

Executed at Riverside, California on _____ (Date)

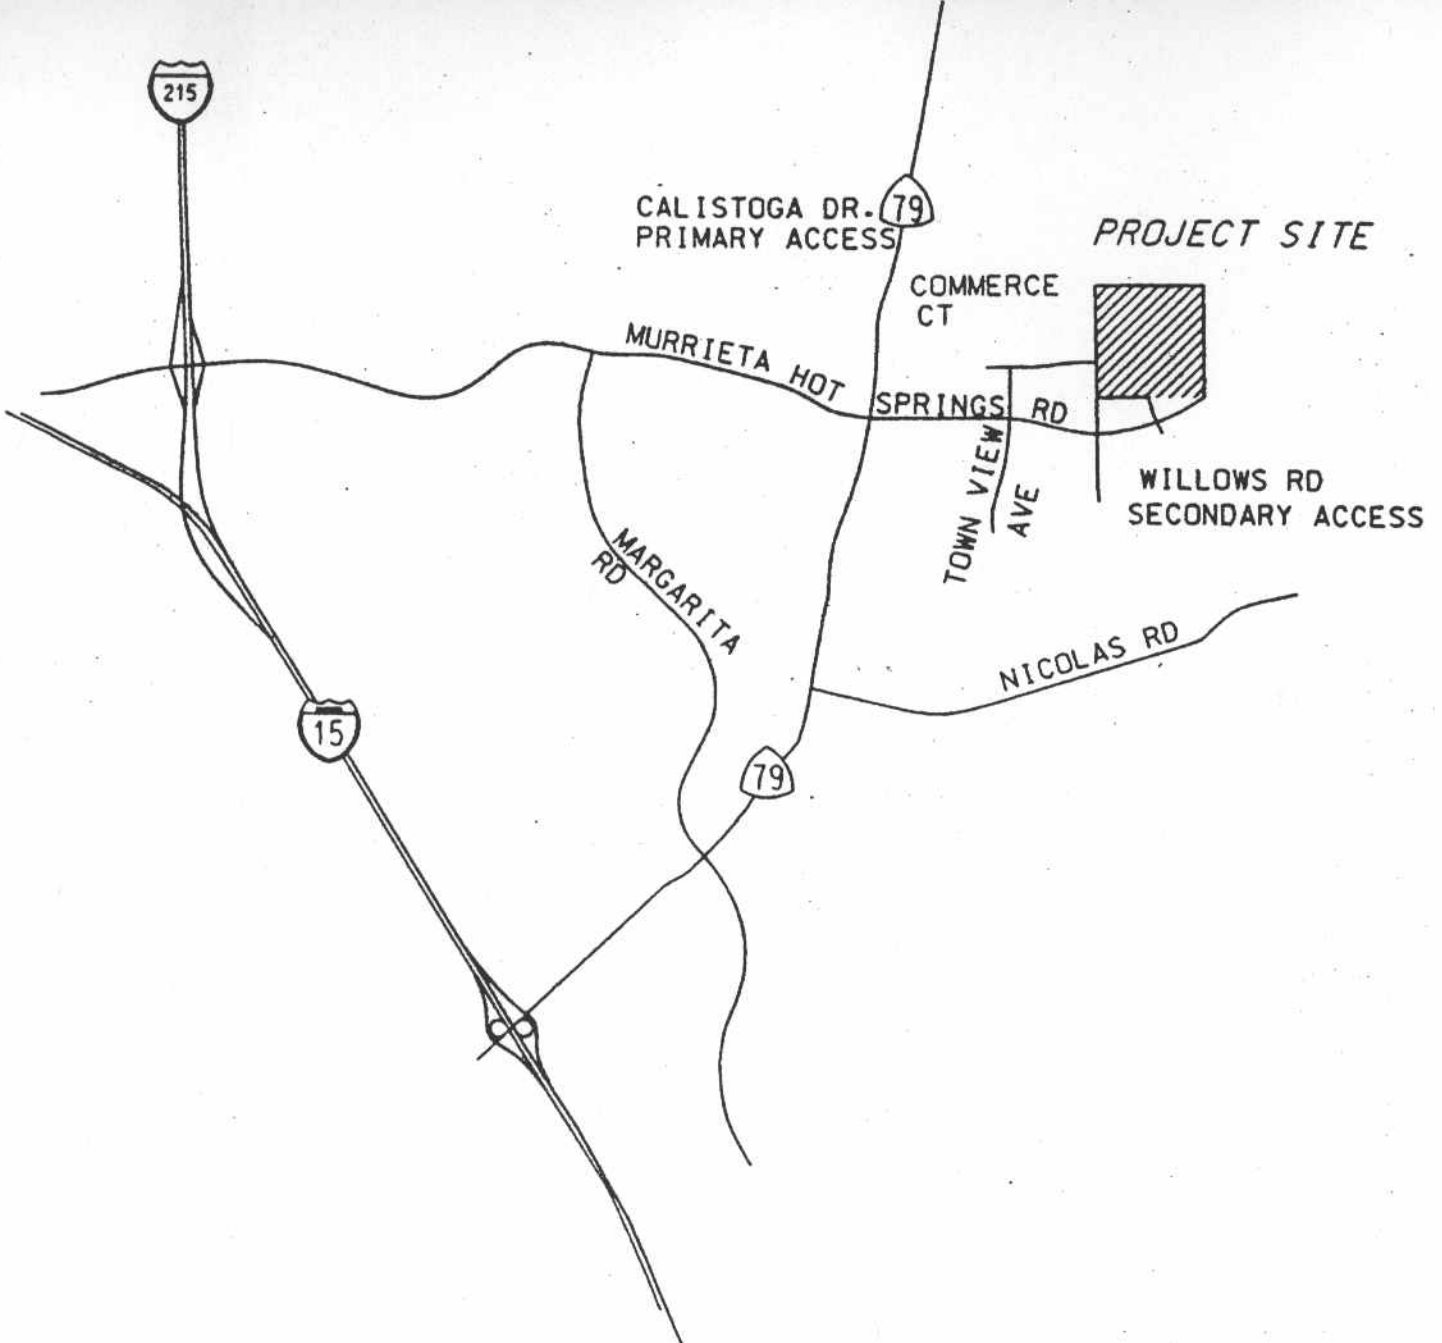

VICINITY MAP

N.T.S.

THOMAS BROS MAP BOOK: PAGE 929-B6
