

**SUBMITTAL TO THE BOARD OF SUPERVISORS
COUNTY OF RIVERSIDE, STATE OF CALIFORNIA**

530 A



FROM: TLMA – Transportation Dept.

SUBMITTAL DATE:
December 15, 2003

SUBJECT: Notice of Completion – Construction of traffic signal and roadway improvements, State Route 79 (North) at Hunter Road / Borel Road, French Valley Area

RECOMMENDED MOTION: That the Board execute and file the attached "Notice of Completion"

BACKGROUND: By Minute Order 3.30 of April 29, 2003, the Board entered into an agreement with Holland-Lowe Construction, Inc. for the construction of traffic signal, road widening and associated improvements at the intersection of State Route 79 (North) and Hunter Road / Borel Road in the French Valley area of Riverside County. The authorized amount of the contract was \$383,738.92. The total amended contract amount (including Change Orders and quantity adjustments) is \$341,673.64, which is 10.96% less than the originally authorized amount. Caltrans furnished the signal modules and traffic controller assembly at no cost to the County, and eliminated and revised some construction items in the field also resulting in a substantial cost savings to the County of Riverside.

This work was completed in conformance with the plans and specifications on September 3, 2003. The work was inspected by the Construction Engineering Section of the Transportation Department. Work Order B2-0442.

Continued on Page 2...

Departmental Concurrence

HS:js
Attachments: Notice of Completion

George A. Johnson
Director of Transportation

FINANCIAL DATA	Current F.Y. Total Cost:	\$ 341,673.64	In Current Year Budget:	Yes
	Current F.Y. Net County Cost:	\$ 0.00	Budget Adjustment:	No
	Annual Net County Cost:	\$ 0.00	For Fiscal Year:	2003/2004
SOURCE OF FUNDS: Signal Mitigation Program, Caltrans				Positions To Be Deleted Per A-30 <input type="checkbox"/>
				Requires 4/5 Vote <input type="checkbox"/>

C.E.O. RECOMMENDATION:
APPROVE

County Executive Office Signature

- Dep't Recomm.: Consent Policy
- Per Exec. Ofc.: Consent Policy

Prev. Agn. Ref.:

District: 3rd

Agenda Number:

3.24

The Honorable Board of Supervisors
 RE: Notice of Completion

Page 2 of 2

Budget

Original Contract Amount			\$383,738.92
Tot. Chg Orders Authorized -	1	-3.34%	(\$12,818.56)
Est. Pending Change Orders		0.00%	\$0.00
Amended Contract Amount			\$370,920.36
* Quantity Adjustments		-7.54%	(\$28,952.26)
+ CCO FA Adjustments		-0.08%	<u>(\$294.46)</u>
Total Amended Contract Amount		89.04%	\$341,673.64

Expenditures

Total Progress Payments -	5		\$341,673.64
Estimated Pending Payments			\$0.00
Total Expenditures			<u>\$341,673.64</u>

(Over)\Under Contract Amount \$0.00

+ Change Orders using the Force Account method of payment issued prior to the work being completed generally do not use the total authorized amount.

* CAL-Trans Standard Specifications 4-1.03B. Increases or decreases in the quantity of a contract item of work will be determined by comparing the total pay quantity of such item of work with the Engineer's Estimate therefor. If the total pay quantity of any item of work required under the contract varies from the Engineers Estimate therefor by 25 percent or less, payment will be made for the quantity of work of said item performed at contract unit price, therefor, unless eligible for adjustment pursuant to Section 4-1.03C, "Changes in Character of Work."

<p>When recorded, return to:</p> <p>After Recording, deliver to: Clerk of Board of Supervisors</p>
<p>Notice of Completion</p>
<p>(Civil Code § 3093 - Public Works)</p>

(For Recorder's use)

To be recorded with County Recorder within 10 days after completion.
 No recording fee.

Notice is hereby given by the undersigned owner, a public entity of the State of California, that a public work of improvement has been completed, as follows:

Project title or description of work: Traffic Signal and Road Improvements, State Route 79 and Hunter Road

Date of Completion: _____ Date of this notice

Nature of owner: County

Interest or estate of owner: Public Roadway

Address of owner: 4080 Lemon Street, 8th Floor, Riverside, CA 92501

Name of contractor: Holland-Lowe Construction, Inc.

Street or legal description of site: Intersection of State Route 79 and Hunter Road / Borel Road, French Valley area

Dated: _____

Owner: _____
 County of Riverside
 (Name of Public Entity)

By: _____
 Chairman, Board of Supervisors



STATE OF CALIFORNIA)

ss

COUNTY OF RIVERSIDE)

I am the Chairman of the governing board of the County of Riverside, the public entity which executed the foregoing notice and on whose behalf I make this verification; I have read this notice, know its contents, and the same is true. I certify under penalty of perjury that the foregoing is true and correct.

Executed at Riverside, California on _____ (Date)

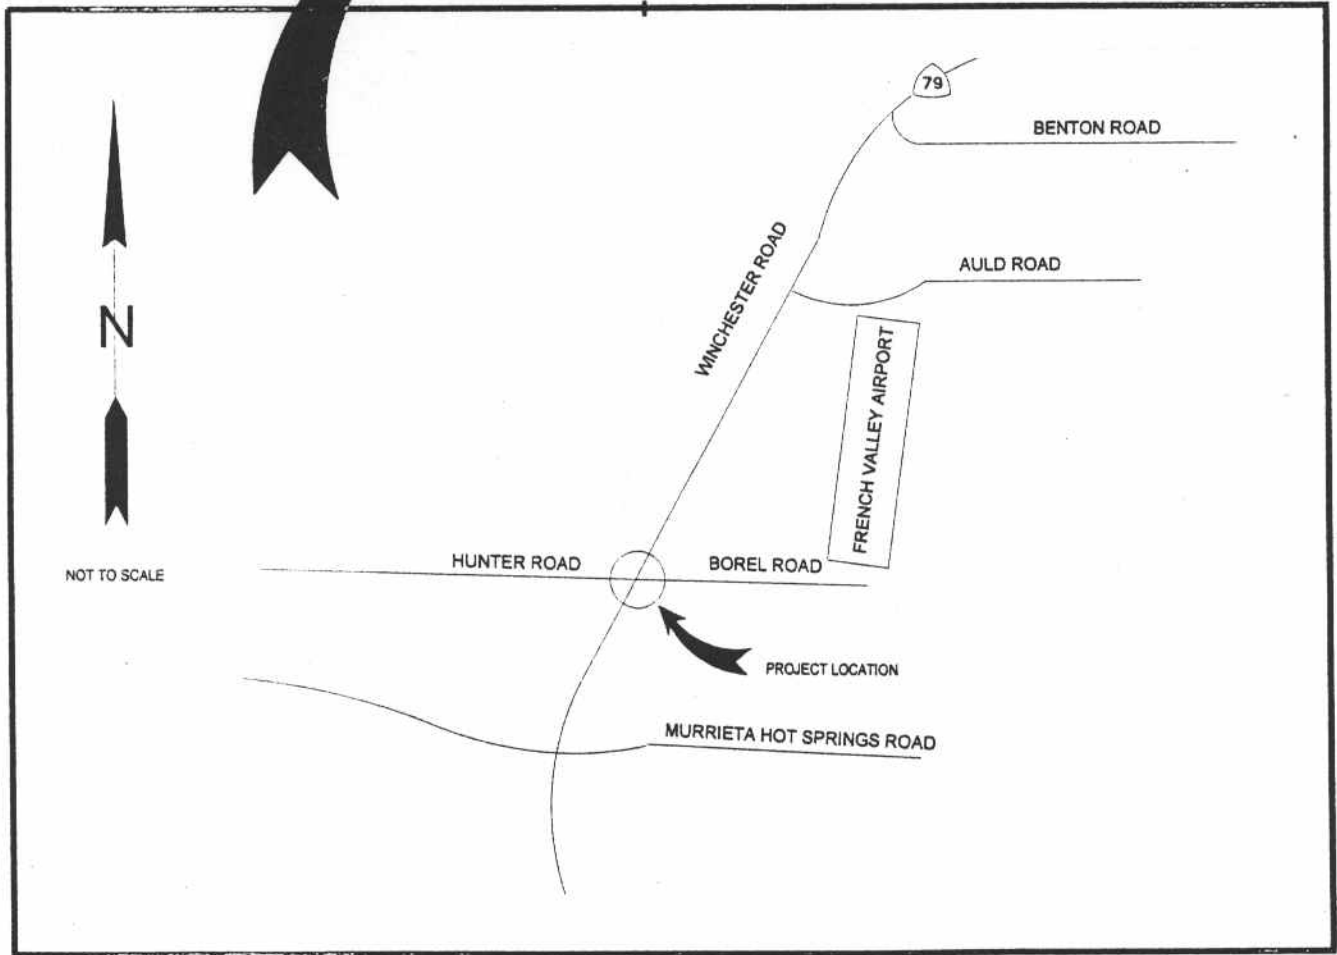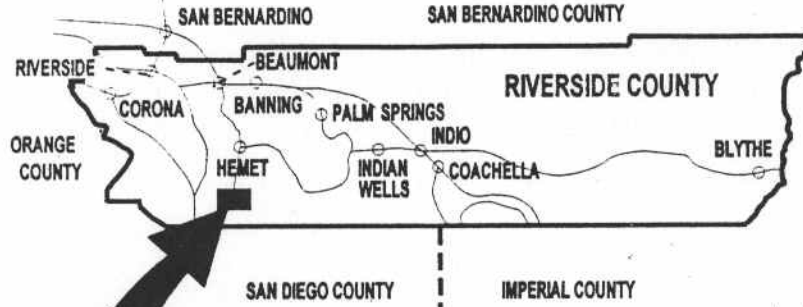

VICINITY MAP
