

**SUBMITTAL TO THE BOARD OF SUPERVISORS
COUNTY OF RIVERSIDE, STATE OF CALIFORNIA**

932A



FROM: TLMA – Transportation Dept.

SUBMITTAL DATE:
January 24, 2005

SUBJECT: Notice of Completion – Reconstruction of Simpson Road, Briggs Road to Winchester Road, Winchester Area

RECOMMENDED MOTION: That the Board execute and file the attached "Notice of Completion"

BACKGROUND: By Minute Order 3.19 of February 11, 2003, the Board entered into an agreement with R. J. Noble Company for the reconstruction of Simpson Road and associated improvements, between Briggs Road and Winchester Road in the Winchester area of Riverside County. The authorized amount of the contract was \$1,049,454.00. The total amended contract amount (including Change Orders, liquidated damages and quantity adjustments) is \$1,062,527.04, which is 1.2% more than the originally authorized amount.

This work was completed in conformance with the plans and specifications on May 6, 2004. The work was inspected by the Construction Engineering Section of the Transportation Department. Work Order A7-0347.

Continued on Page 2...

Departmental Concurrence

HS:js
Attachments: Notice of Completion

George A. Johnson
Director of Transportation

FINANCIAL DATA	Current F.Y. Total Cost:	\$ 1,062,527.04	In Current Year Budget:	Yes
	Current F.Y. Net County Cost:	\$ 0.00	Budget Adjustment:	No
	Annual Net County Cost:	\$ 0.00	For Fiscal Year:	2004/2005

SOURCE OF FUNDS: STP-Formula, Measure A/Western	Positions To Be Deleted Per A-30	<input type="checkbox"/>
	Requires 4/5 Vote	<input type="checkbox"/>

C.E.O. RECOMMENDATION: **APPROVE**

County Executive Office Signature

- Dep't Recomm.: Policy
- Per Exec. Ofc.: Policy
- Consent
- Consent

COUNTY OF RIVERSIDE
OFFICE EXECUTIVE

Budget

Original Contract Amount			\$1,049,454.00
Tot. Chg Orders Authorized -	1	-0.2%	(\$2,100.00)
Est. Pending Change Orders		0.0%	\$0.00
Amended Contract Amount			\$1,047,354.00
* Quantity Adjustments		4.2%	\$44,173.04
Less Liquidated Damages		-2.8%	<u>(\$29,000.00)</u>
Total Amended Contract Amount		101.2%	\$1,062,527.04

Expenditures

Total Progress Payments -	7		\$1,062,527.04
Estimated Pending Payments			\$0.00
Total Expenditures			<u>\$1,062,527.04</u>

(Over)\Under Contract Amount \$0.00

+ Change Orders using the Force Account method of payment issued prior to the work being completed generally do not use the total authorized amount.

* CAL-Trans Standard Specifications 4-1.03B. Increases or decreases in the quantity of a contract item of work will be determined by comparing the total pay quantity of such item of work with the Engineer's Estimate therefor. If the total pay quantity of any item of work required under the contract varies from the Engineers Estimate therefor by 25 percent or less, payment will be made for the quantity of work of said item performed at contract unit price, therefor, unless eligible for adjustment pursuant to Section 4-1.03C, "Changes in Character of Work."

<p>When recorded, return to:</p> <p>After Recording, deliver to: Clerk of Board of Supervisors</p>
<p>Notice of Completion</p>
<p>(Civil Code § 3093 - Public Works)</p>

(For Recorder's use)

To be recorded with County Recorder
 within 10 days after completion.
 No recording fee.

Notice is hereby given by the undersigned owner, a public entity of the State of California, that a public work of improvement has been completed, as follows:

Project title or description of work: Simpson Road Reconstruction

Date of Completion: Date of this notice

Nature of owner: County

Interest or estate of owner: Public Roadway

Address of owner: 4080 Lemon Street, 8th Floor, Riverside, CA 92501

Name of contractor: R. J. Noble Company

Street or legal description of site: Simpson Road from Briggs Road to Winchester Road,
 Winchester area

Dated: _____

Owner: County of Riverside
 (Name of Public Entity)

By: _____
 Chairman, Board of Supervisors


STATE OF CALIFORNIA)

ss

COUNTY OF RIVERSIDE)

I am the Chairman of the governing board of the County of Riverside, the public entity which executed the foregoing notice and on whose behalf I make this verification; I have read this notice, know its contents, and the same is true. I certify under penalty of perjury that the foregoing is true and correct.

Executed at Riverside, California on _____ (Date)

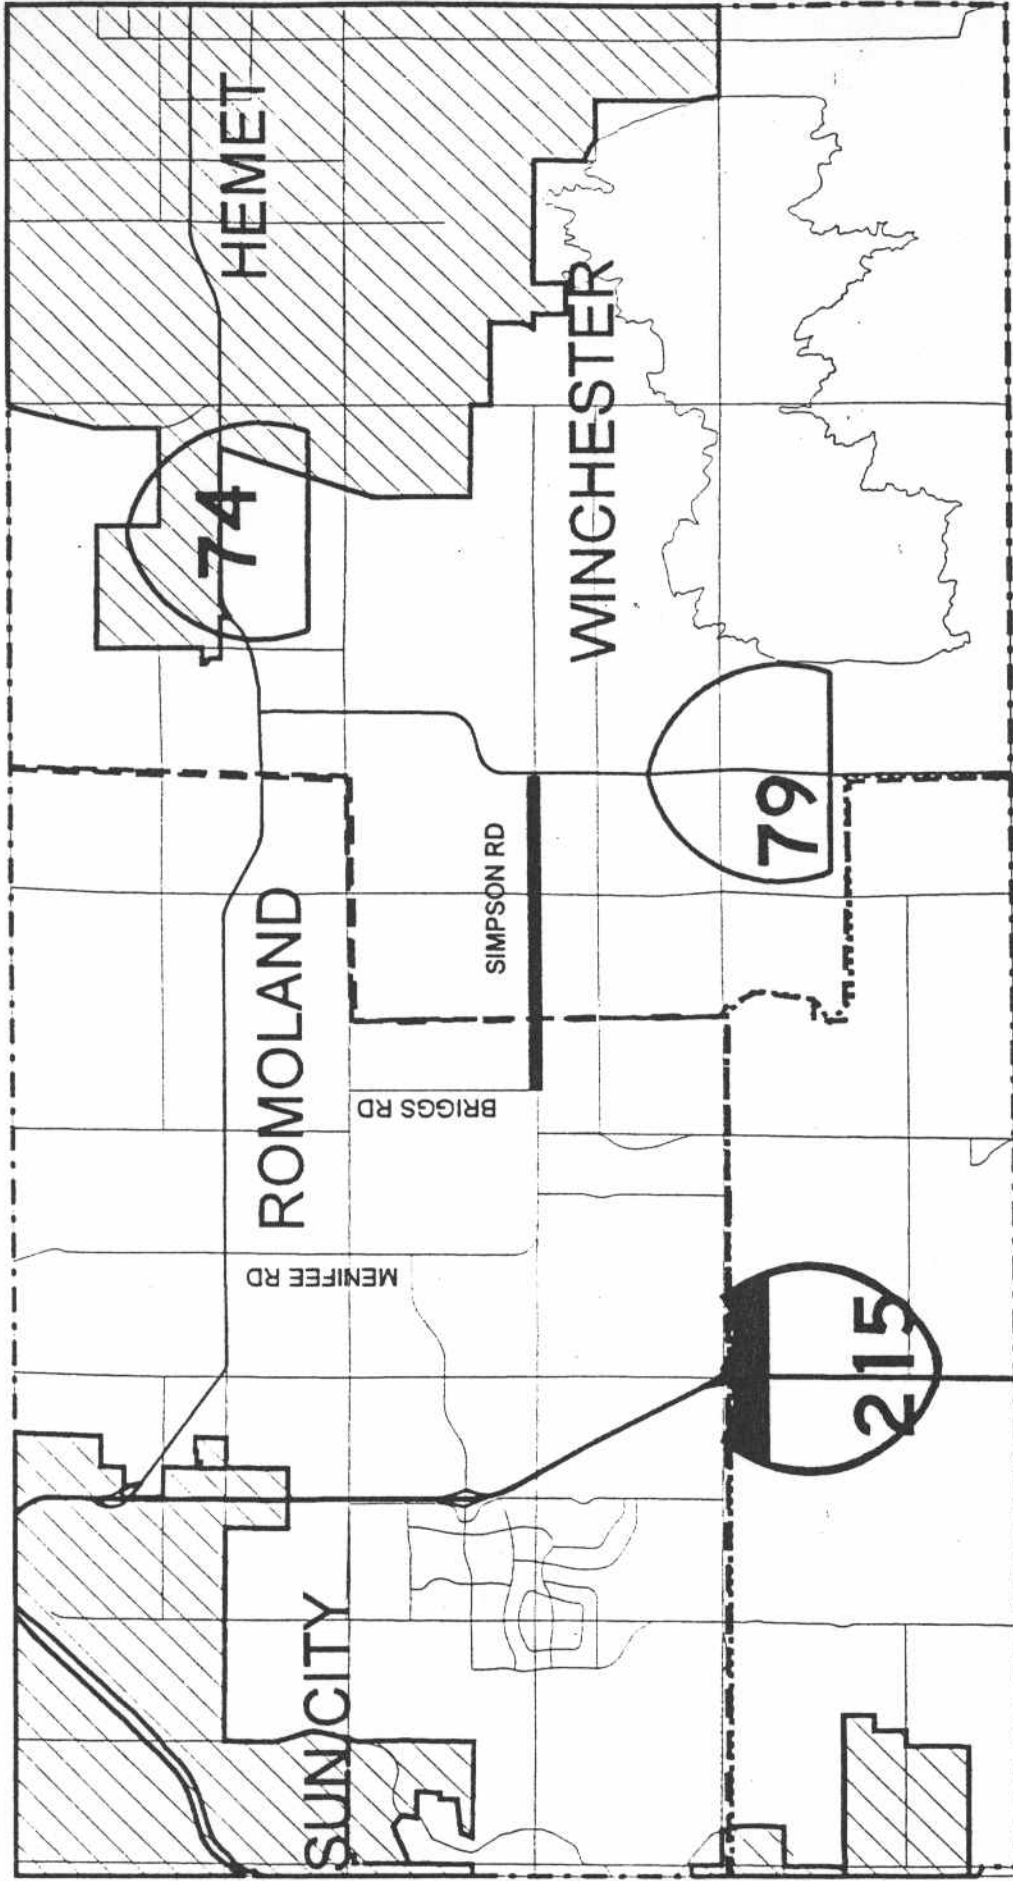

HEMET

WINCHESTER

ROMOLAND

SUN CITY

74

79

215

SIMPSON RD

BRIGGS RD

MENIFEE RD
