

230B



**SUBMITTAL TO THE FLOOD CONTROL AND WATER CONSERVATION DISTRICT BOARD
COUNTY OF RIVERSIDE, STATE OF CALIFORNIA**

FROM: General Manager-Chief Engineer

SUBMITTAL DATE:
January 10, 2006

SUBJECT: Notice of Completion
Hemet MDP Line D, Stage 6
Project No. 4-0-0211

RECOMMENDED MOTION:

The Board accept the referenced project as constructed; authorize the Chairman to execute the attached Notice of Completion; and direct the Clerk of the Board to record the executed Notice of Completion with the Riverside County Clerk and Recorder's Office within 10 calendar days in accordance with Section 3093 of the Civil Code.

BACKGROUND:

Continued on Page 2.

Departmental Concurrence

WARREN D. WILLIAMS
General Manager-Chief Engineer

mcv

| | | | | |
|-----------------------|-----------------------------|-----|-------------------------|-----|
| FINANCIAL DATA | Current F.Y. District Cost: | N/A | In Current Year Budget: | N/A |
| | Current F.Y. County Cost: | N/A | Budget Adjustment: | N/A |
| | Annual Net District Cost: | N/A | For Fiscal Year: | N/A |

| | | |
|-----------------------------|----------------------------------|--------------------------|
| SOURCE OF FUNDS: N/A | Positions To Be Deleted Per A-30 | <input type="checkbox"/> |
| | Requires 4/5 Vote | <input type="checkbox"/> |

C.E.O. RECOMMENDATION:

APPROVE

County Executive Office Signature

- Policy
- Policy
- Consent
- Consent
- Dept't Recomm.:
- Per Exec. Ofc.:

**FLOOD CONTROL AND WATER CONSERVATION DISTRICT BOARD SUBMITTAL
COUNTY OF RIVERSIDE, STATE OF CALIFORNIA**

SUBJECT: Notice of Completion
Hemet MDP Line D, Stage 6
Project No. 4-0-0211

SUBMITTAL DATE: January 10, 2006


Page 2

BACKGROUND:

The Board approved the original contract with K.C. Construction as Agenda Item Number 11.7 on March 1, 2005 in an amount of \$669,100.00. The District is also in receipt of \$13,092.60 of requests for additional compensation associated with additional material costs incurred by K.C. Construction during the construction of the project. Additionally, due to a reduction of the actual construction quantities installed, the total project construction cost is estimated not to exceed the original contract amount, including all the costs associated with the aforementioned additional material costs.

Final inspection of the above referenced project was made, and the project was found to be complete according to plans and specifications. A brief project description and location map is attached.

HEMET MDP LINE D STAGE 6 PROJECT NO. 4-0-0211

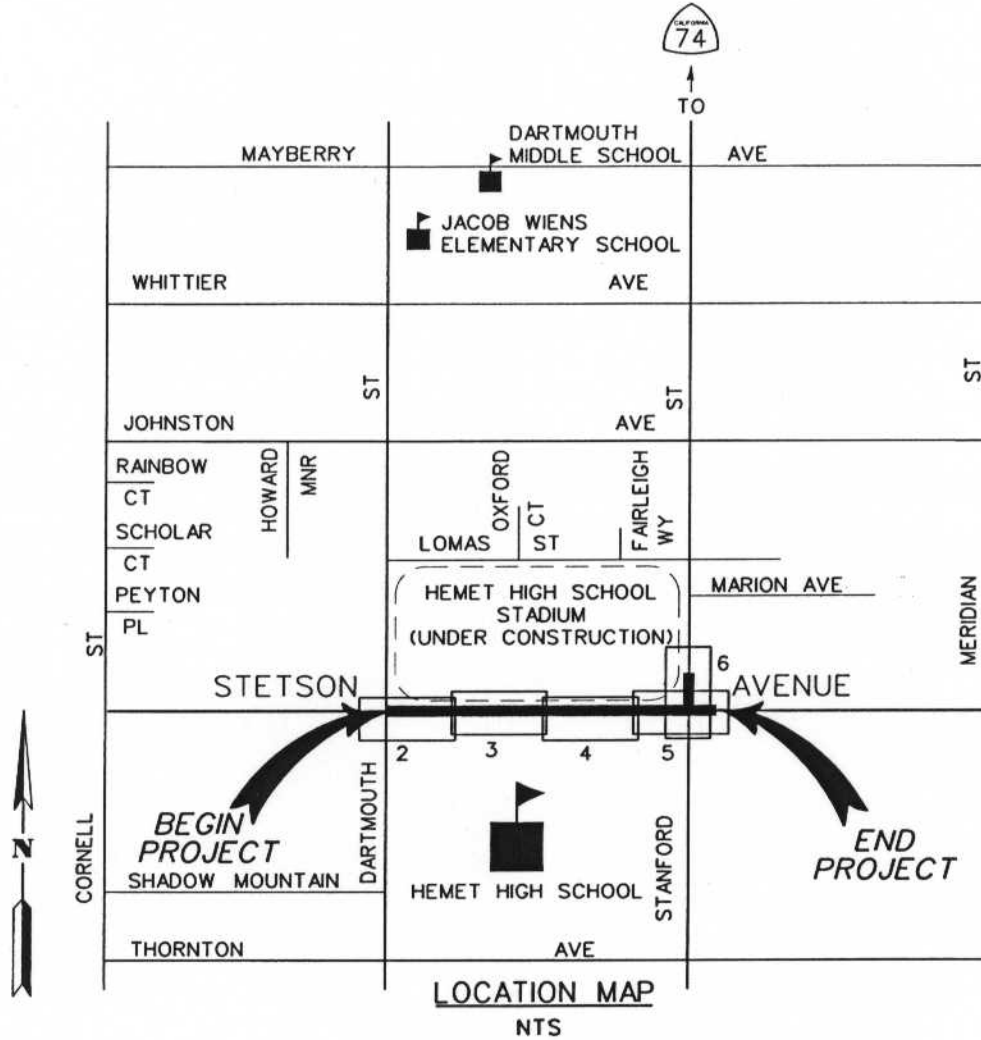

This project will construct approximately 1,600 feet of underground reinforced concrete pipe storm drain, ranging in size from 72 inches to 24 inches in diameter. This storm drain will be constructed within street right of way in front of Hemet High School along Stetson Avenue between Dartmouth and Stanford Streets, and will construct Lateral Line D-4 on Stanford Street. This stage of the project is being constructed out of sequence with stages 4 and 5 to allow installation of the storm drain before the construction of street improvements that will be done by Hemet Unified School District, thus avoiding the need to trench through the newly improved street. No inlets to this storm drain will be constructed until the downstream stages 4 and 5 of Hemet MDP Line D are constructed.
