

536A

**SUBMITTAL TO THE BOARD OF SUPERVISORS
COUNTY OF RIVERSIDE, STATE OF CALIFORNIA**



FROM: TLMA – Transportation Dept.

SUBMITTAL DATE:
January 30, 2006

SUBJECT: Notice of Completion – Construction of Interim Asphalt Concrete Sidewalk, South Side of Mission Boulevard, Pedley Road to Valley Way, West Riverside area

RECOMMENDED MOTION: That the Board execute and file the attached "Notice of Completion"

BACKGROUND: By Minute Order dated August 23, 2005 (Agenda item no. 3.95), the Board received and filed an agreement with R. J. Noble Company to construct interim asphalt concrete sidewalk on the south side of Mission Boulevard, from Pedley Road to Valley Way, in the West Riverside area of Riverside County. The agreement was executed by the Director of Transportation in accordance with authority that the Board has delegated to the Director of Transportation by Resolution no. 93-047. The Transportation Department entered into this agreement with R. J. Noble Company on July 6, 2005. The original estimate of costs for the work was \$380,163.00, and the original amount of the contract was \$274,480.00. The total amended contract amount (including Change Orders and quantity adjustments) is \$244,131.74, which is 11.06% less than the originally authorized amount.

This work was completed in conformance with the plans and specifications on August 5, 2005. The work was inspected by the Construction Engineering Section of the Transportation Department. Work Order B5-0690.

Continued on Page 2...

Departmental Concurrence

HS:js

Attachments: Notice of Completion

George A. Johnson
Director of Transportation

FINANCIAL DATA	Current F.Y. Total Cost:	\$ 244,131.74	In Current Year Budget:	NA
	Current F.Y. Net County Cost:	\$ 0.00	Budget Adjustment:	No
	Annual Net County Cost:	\$ 0.00	For Fiscal Year:	2005/2006

SOURCE OF FUNDS: Economic Development Agency	Positions To Be Deleted Per A-30	<input type="checkbox"/>
	Requires 4/5 Vote	<input type="checkbox"/>

C.E.O. RECOMMENDATION: APPROVE

County Executive Office Signature

- Policy
- Policy
- Consent
- Consent
- Dep't Recomm.:
- Per Exec. Ofc.:

Prev. Agn. Ref.: 8/23/05 (3.95)

District: 2

Agenda Number:

3.42

Budget

Original Contract Amount			\$274,480.00
Tot. Chg Orders Authorized -	1	-5.92%	(\$16,252.00)
Est. Pending Change Orders		0.00%	\$0.00
Amended Contract Amount			\$258,228.00
* Quantity Adjustments		-5.10%	(\$13,989.60)
+ CCO FA Adjustments		-0.04%	<u>(\$106.66)</u>
Total Amended Contract Amount		88.94%	\$244,131.74

Expenditures

Total Progress Payments -	3		\$244,131.74
Estimated Pending Payments			<u>\$0.00</u>
Total Expenditures			\$244,131.74

(Over)\Under Contract Amount \$0.00

+ Change Orders using the Force Account method of payment issued prior to the work being completed generally do not use the total authorized amount.

* CAL-Trans Standard Specifications 4-1.03B. Increases or decreases in the quantity of a contract item of work will be determined by comparing the total pay quantity of such item of work with the Engineer's Estimate therefor. If the total pay quantity of any item of work required under the contract varies from the Engineers Estimate therefor by 25 percent or less, payment will be made for the quantity of work of said item performed at contract unit price, therefor, unless eligible for adjustment pursuant to Section 4-1.03C, "Changes in Character of Work."

<p>When recorded, return to:</p> <p>After Recording, deliver to: Clerk of Board of Supervisors</p>
<p>Notice of Completion</p>
<p>(Civil Code § 3093 - Public Works)</p>

(For Recorder's use)

To be recorded with County Recorder within 10 days after completion.
 No recording fee.

Notice is hereby given by the undersigned owner, a public entity of the State of California, that a public work of improvement has been completed, as follows:

Project title or description of work: Mission Boulevard Interim Sidewalk

Date of Completion: Date of this notice

Nature of owner: County of Riverside

Interest or estate of owner: Public Roadway

Address of owner: 4080 Lemon Street, 8th Floor, Riverside, CA 92501

Name of contractor: R. J. Noble Company

Street or legal description of site: South side of Mission Boulevard between Pedley Road and Valley Way, Rubidoux area

Dated: _____

Owner: County of Riverside
 (Name of Public Entity)

By: _____
 Chairman, Board of Supervisors


STATE OF CALIFORNIA)

ss

COUNTY OF RIVERSIDE)

I am the Chairman of the governing board of the County of Riverside, the public entity which executed the foregoing notice and on whose behalf I make this verification; I have read this notice, know its contents, and the same is true. I certify under penalty of perjury that the foregoing is true and correct.

Executed at Riverside, California on _____ (Date)

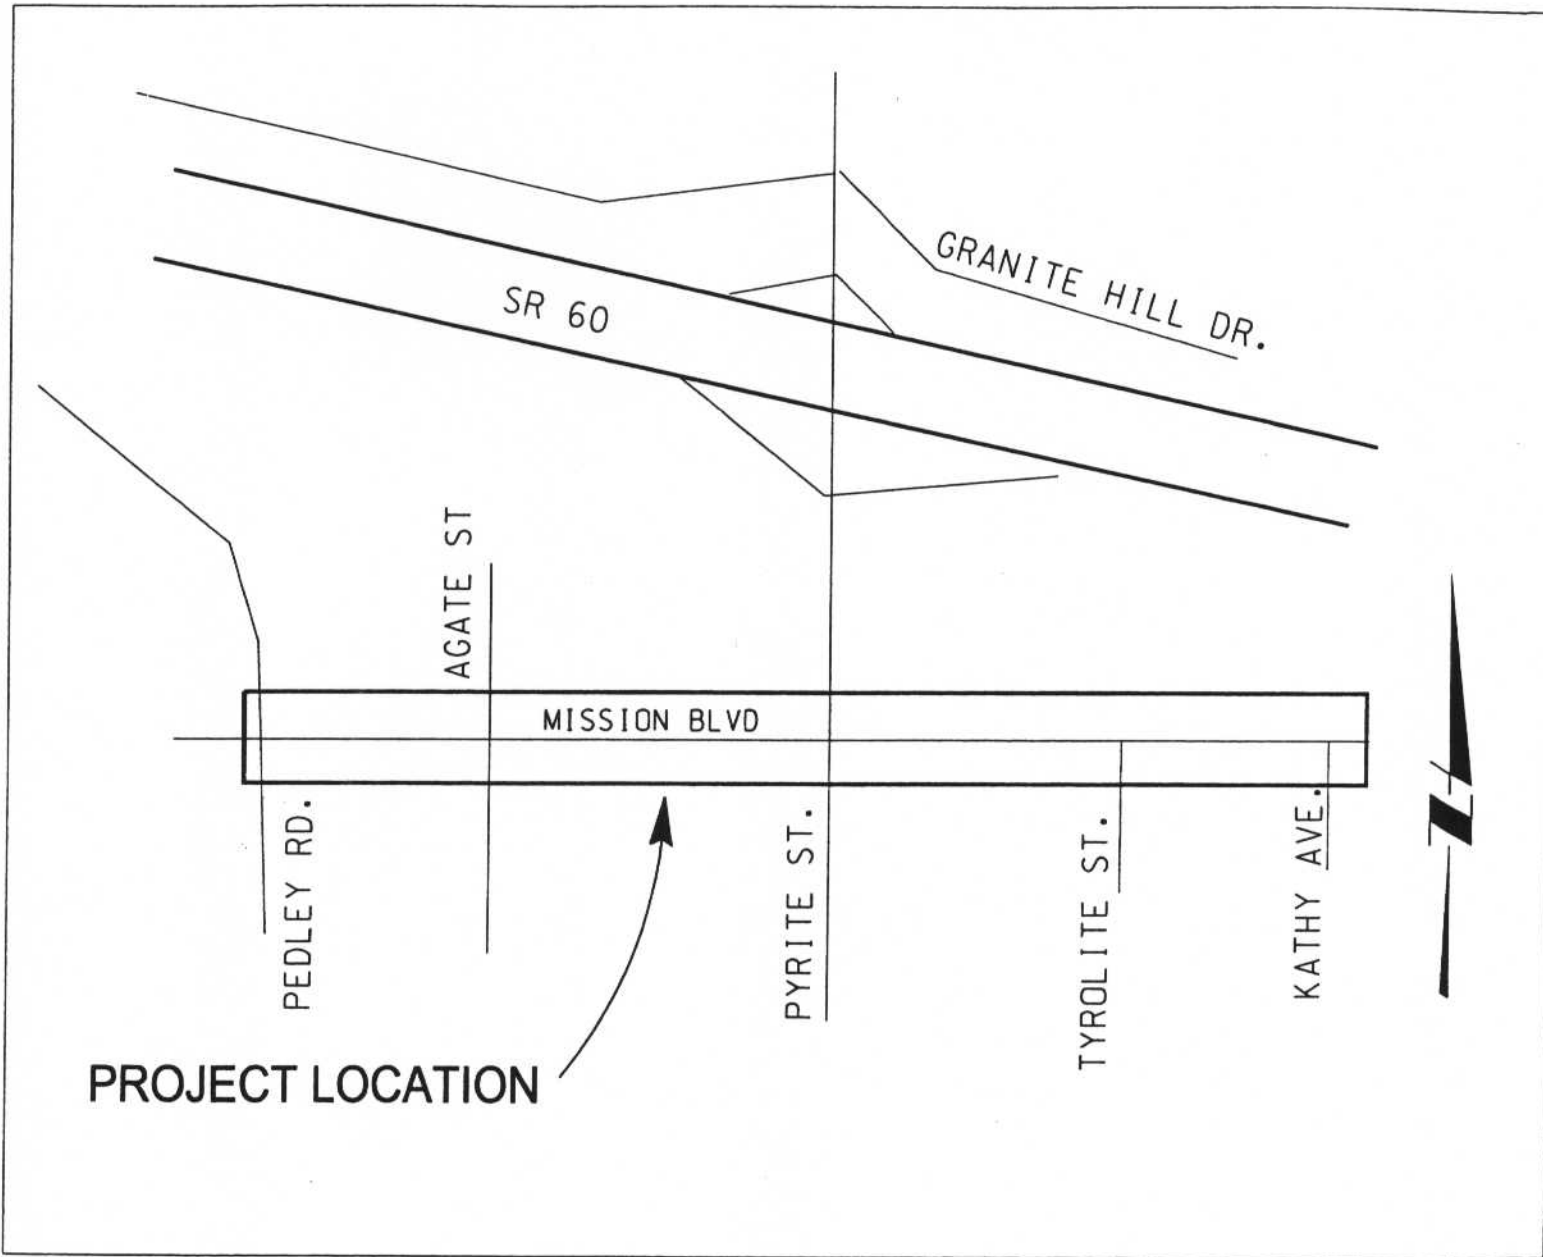

VICINITY MAP

N.T.S.

T2S R6W SEC11
