

**SUBMITTAL TO THE BOARD OF SUPERVISORS  
COUNTY OF RIVERSIDE, STATE OF CALIFORNIA**

840 A



**FROM:** TLMA – Transportation Dept.

**SUBMITTAL DATE:**

**SUBJECT:** Notice of Completion – Resurfacing of various roads in the East Pedley area

**RECOMMENDED MOTION:** That the Board execute and file the attached "Notice of Completion"


**BACKGROUND:** By Minute Order 3.29 of August 15, 2006, the Board entered into an agreement with All American Asphalt of Corona, CA for the resurfacing of various roads in the East Pedley area of Riverside County. The authorized amount of the contract was \$645,700.00. The total amended contract amount (including quantity adjustments) is \$663,471.45, which is 2.8% more than the originally authorized amount.

This work was completed in conformance with the plans and specifications on February 22, 2007. The work was inspected by the Construction Engineering Section of the Transportation Department. Work Order X-0308.

Continued on Page 2...

Departmental Concurrence

HS: tn  
Attachments: Notice of Completion


  
George A. Johnson  
Director of Transportation

<b>FINANCIAL DATA</b>	Current F.Y. Total Cost:	\$663,471.45	In Current Year Budget:	Yes
	Current F.Y. Net County Cost:	\$ 0.00	Budget Adjustment:	No
	Annual Net County Cost:	\$ 0.00	For Fiscal Year:	2006/2007

<b>SOURCE OF FUNDS:</b> Measure A/Western, Combined Improvement Fund, Rubidoux Community Services District	Positions To Be Deleted Per A-30	<input type="checkbox"/>
	Requires 4/5 Vote	<input type="checkbox"/>

**C.E.O. RECOMMENDATION: APPROVE**

County Executive Office Signature



- Policy  Policy
- Consent  Consent
- Dept't Recomm.: Per Exec. Ofc.:

Prev. Agn. Ref.: 8/15/06 (3.29) | District: 2 | Agenda Number:

3.36

The Honorable Board of Supervisors  
RE: Notice of Completion

Page 2 of 2

**Budget**

Original Contract Amount			\$645,700.00
Tot. Chg Orders Authorized -	1	3.3%	\$21,264.00
Est. Pending Change Orders		0.0%	\$0.00
Amended Contract Amount			\$666,964.00
* Quantity Adjustments		-0.5%	(\$3,492.55)
+ CCO FA Adjustments		0.0%	\$0.00
Total Amended Contract Amount		102.8%	\$663,471.45

**Expenditures**

Total Progress Payments -	2		\$605,814.51
Estimated Pending Payments	3 - Final		\$57,656.94
Total Expenditures			\$663,471.45

**(Over)\Under Contract Amount** \$0.00





+ Change Orders using the Force Account method of payment issued prior to the work being completed generally do not use the total authorized amount.

\* CAL-Trans Standard Specifications 4-1.03B. Increases or decreases in the quantity of a contract item of work will be determined by comparing the total pay quantity of such item of work with the Engineer's Estimate therefor. If the total pay quantity of any item of work required under the contract varies from the Engineers Estimate therefor by 25 percent or less, payment will be made for the quantity of work of said item performed at contract unit price, therefor, unless eligible for adjustment pursuant to Section 4-1.03C, "Changes in Character of Work."

# COUNTY OF RIVERSIDE

## EAST PEDLEY AREA

### RESURFACING PROJECT

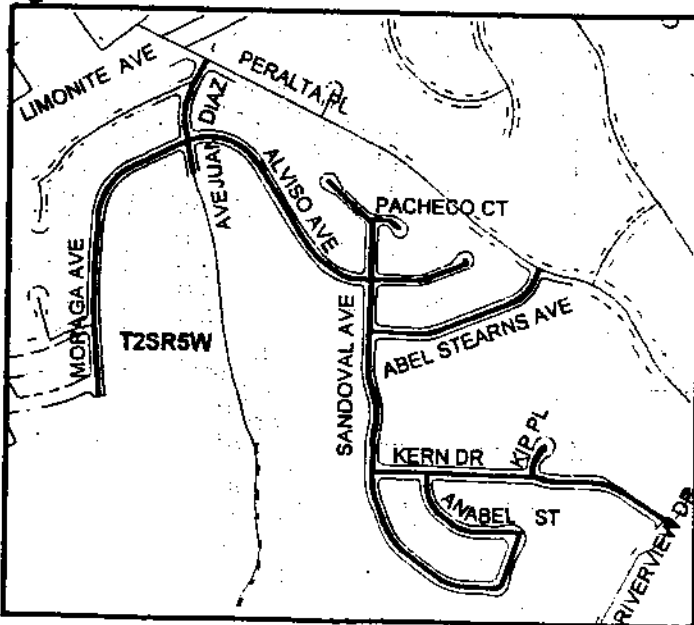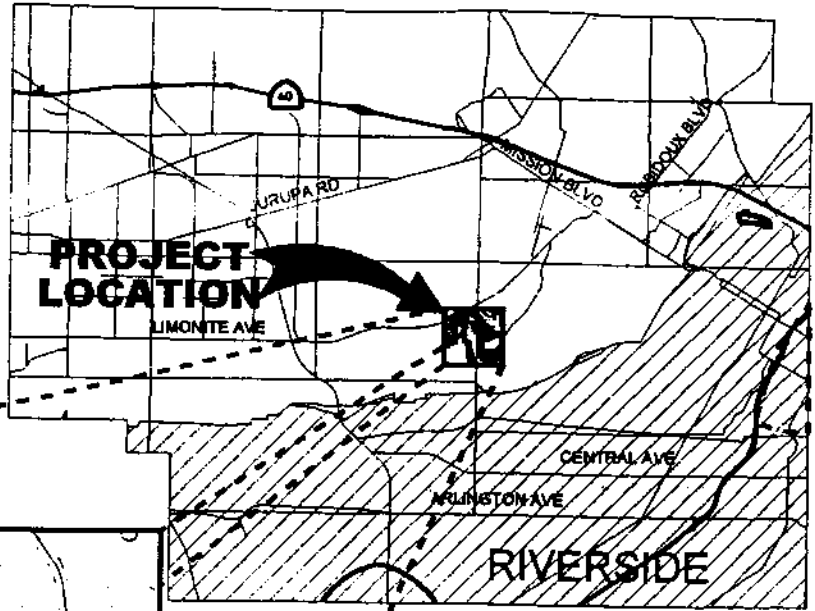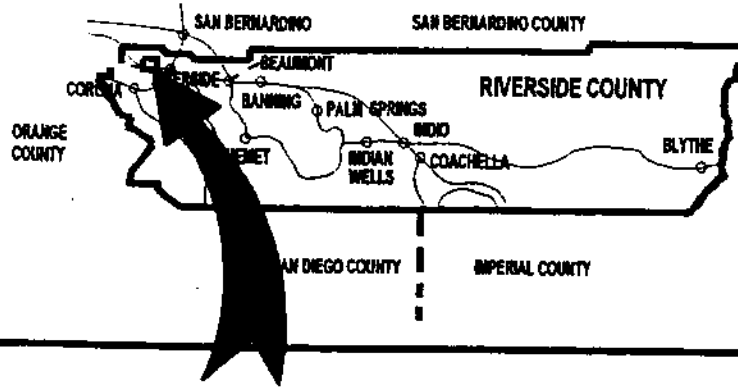

PROJECT LENGTH = 1.90 MI.  
T2SR5W SECTIONS 19, 20, 29, & 30

### VICINITY MAP

<p><b>When recorded, return to:</b></p> <p><b>After Recording, deliver to:</b>  <b>Clerk of Board of Supervisors</b></p>
<p><b>Notice of Completion</b></p>
<p><b>(Civil Code § 3093 - Public Works)</b></p>

**(For Recorder's use)**

To be recorded with County Recorder within 10 days after completion.  
 No recording fee.

**Notice is hereby given by the undersigned owner, a public entity of the State of California, that a public work of improvement has been completed, as follows:**

**Project title or description of work:** Resurfacing of various roads in the East Pedley area of Riverside County.

**Date of Completion:** Date of this notice

**Nature of owner:** County

**Interest or estate of owner:** Public Roadway

**Address of owner:** 4080 Lemon Street, 8th Floor, Riverside, CA 92501

**Name of contractor:** All American Asphalt of Corona, CA.

**Street or legal description of site:** East Pedley area

Dated: \_\_\_\_\_

Owner: County of Riverside  
 (Name of Public Entity)

By: \_\_\_\_\_  
 Chairman, Board of Supervisors

**STATE OF CALIFORNIA )**

**ss**

**COUNTY OF RIVERSIDE )**

I am the Chairman of the governing board of the County of Riverside, the public entity which executed the foregoing notice and on whose behalf I make this verification; I have read this notice, know its contents, and the same is true. I certify under penalty of perjury that the foregoing is true and correct.

Executed at Riverside, California on \_\_\_\_\_ (Date)
