

**SUBMITTAL TO THE BOARD OF SUPERVISORS
COUNTY OF RIVERSIDE, STATE OF CALIFORNIA**

868



FROM: TLMA – Transportation Dept.

SUBMITTAL DATE:

May 25, 2007

SUBJECT: Notice of Completion – Storm Damage Repair, Reconstruction of San Jacinto Avenue, from Old Elsinore Road to approximately 1 mile Easterly, and reconstruction of Old Elsinore Road, from San Jacinto Avenue to approximately 3,000 feet Northerly, Mead Valley area

RECOMMENDED MOTION: That the Board execute and file the attached "Notice of Completion"

BACKGROUND: By Minute Order 3.45 of October 17, 2006, the Board entered into an agreement with McKenna General Engineering Inc. of Corona, CA for the reconstruction of San Jacinto Avenue, from Old Elsinore Road to approximately 1 mile Easterly, and reconstruction of Old Elsinore Road, from San Jacinto Avenue to approximately 3,000 feet Northerly in the Mead Valley area of Riverside County. The authorized amount of the contract was \$1,360,866.50. The total amended contract amount (including quantity adjustments) is \$1,370,388.44, which is 0.7% more than the originally authorized amount.

This work was completed in conformance with the plans and specifications on March 23, 2007. The work was inspected by the Construction Engineering Section of the Transportation Department. Work Order 4505140104 and 4505140105.

Continued on Page 2...

HS:tn

Attachments: Notice of Completion

George A. Johnson
George A. Johnson

Director of Transportation

FINANCIAL DATA	Current F.Y. Total Cost:	\$1,370,388.44	In Current Year Budget:	Yes
	Current F.Y. Net County Cost:	\$ 0.00	Budget Adjustment:	No
	Annual Net County Cost:	\$ 0.00	For Fiscal Year:	2006/2007

SOURCE OF FUNDS: FHWA (Storm Damage Funds), State Office of Emergency Services, Gas Tax	Positions To Be Deleted Per A-30	<input type="checkbox"/>
	Requires 4/5 Vote	<input type="checkbox"/>

C.E.O. RECOMMENDATION:

APPROVE

BY: *Tina Grande*
Tina Grande

County Executive Office Signature

Dept't Recomm.: Consent Policy

Per Exec. Ofc.: Consent Policy

Prev. Agn. Ref.: 10/17/2006 (3.45)

District: 5

Agenda Number:

3.67

Budget

Original Contract Amount			\$1,360,866.50
Tot. Chg Orders Authorized -	2	-1.0%	(\$13,360.86)
Est. Pending Change Orders		0.0%	\$0.00
Amended Contract Amount			\$1,347,505.64
* Quantity Adjustments		1.7%	\$22,882.80
+ CCO FA Adjustments		0.0%	\$0.00
Total Amended Contract Amount		100.7%	\$1,370,388.44

Expenditures

Total Progress Payments -	3		\$1,240,705.56
Estimated Pending Payments	4 Final		\$129,682.88
Total Expenditures			\$1,370,388.44

(Over)\Under Contract Amount \$0.00

+ Change Orders using the Force Account method of payment issued prior to the work being completed generally do not use the total authorized amount.

* CAL-Trans Standard Specifications 4-1.03B. Increases or decreases in the quantity of a contract item of work will be determined by comparing the total pay quantity of such item of work with the Engineer's Estimate. If the total pay quantity of any item of work required under the contract varies from the Engineers Estimate by 25 percent or less, payment will be made for the quantity of work of said item performed at contract unit price, unless eligible for adjustment pursuant to Section 4-1.03C, "Changes in Character of Work."

<p>When recorded, return to:</p> <p>After Recording, deliver to: Clerk of Board of Supervisors</p>
<p>Notice of Completion</p>
<p>(Civil Code § 3093 - Public Works)</p>

(For Recorder's use)

To be recorded with County Recorder within 10 days after completion. No recording fee.

Notice is hereby given by the undersigned owner, a public entity of the State of California, that a public work of improvement has been completed, as follows:

Project title or description of work: Reconstruction Storm Damaged sections of San Jacinto Avenue and Old Elsinore Road in the Mead Valley area of Riverside County

Date of Completion: Date of this notice

Nature of owner: County of Riverside, public entity

Interest or estate of owner: Public Roadway

Address of owner: 4080 Lemon Street, 8th Floor, Riverside, CA 92501

Name of contractor: McKenna General Engineering, INC. Corona, CA

Street or legal description of site: San Jacinto Avenue and Old Elsinore Road, Mead Valley area

Dated: _____

Owner: County of Riverside
(Name of Public Entity)

By: _____
Chairman, Board of Supervisors

STATE OF CALIFORNIA)

ss

COUNTY OF RIVERSIDE)



I am the Chairman of the governing board of the County of Riverside, the public entity which executed the foregoing notice and on whose behalf I make this verification; I have read this notice, know its contents, and the same is true. I certify under penalty of perjury that the foregoing is true and correct.

Executed at Riverside, California on _____ (Date)

COUNTY OF RIVERSIDE

SAN JACINTO AVENUE
RECONSTRUCTION OF STORM DAMAGED
ROAD SEGMENT

FROM OLD ELSINORE ROAD
TO PERRIS CITY LIMITS

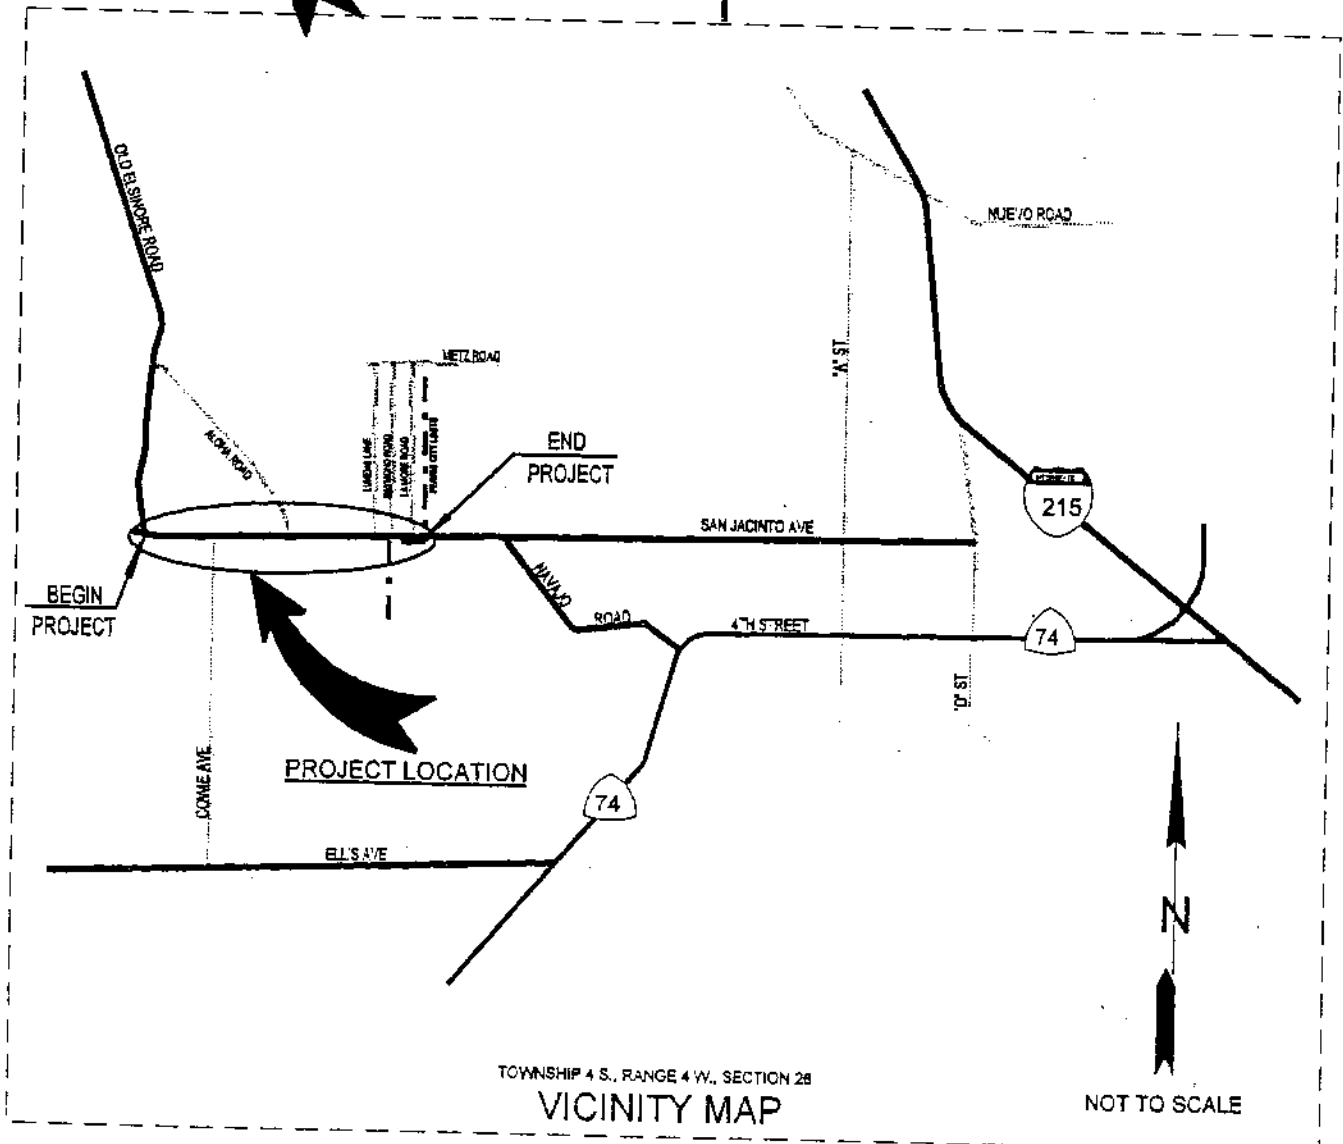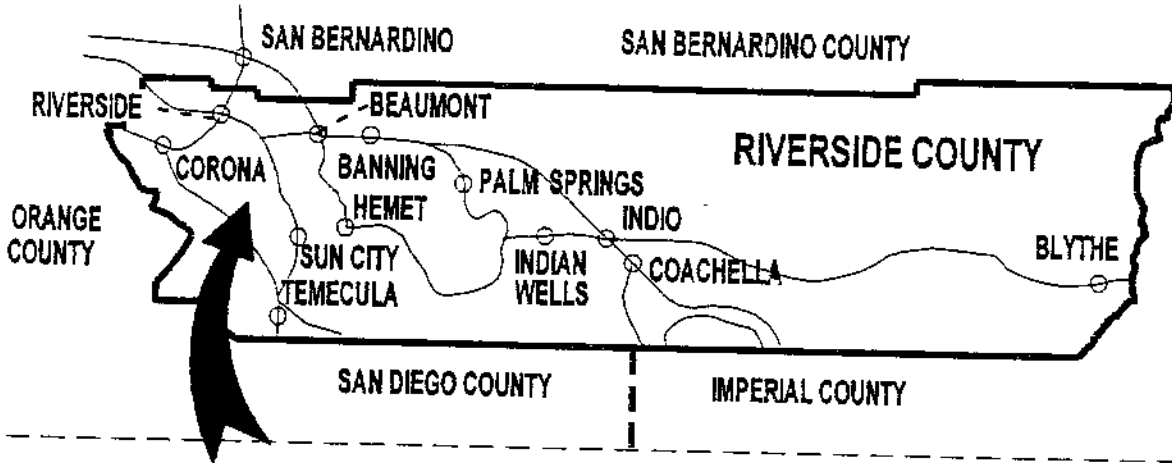

COUNTY OF RIVERSIDE

OLD ELSINORE ROAD

RECONSTRUCTION OF STORM DAMAGED
ROAD SEGMENT

FROM SAN JACINTO AVENUE
TO N'LY OF ALOHA ROAD

