

**SUBMITTAL TO THE BOARD OF SUPERVISORS
COUNTY OF RIVERSIDE, STATE OF CALIFORNIA**

823A



FROM: TLMA - Transportation Department

SUBMITTAL DATE:

SUBJECT: Notice of Completion - Coachella Valley 5 in 1

RECOMMENDED MOTION: That the Board execute and file the attached "Notice of Completion"

BACKGROUND: By Minute Order 3.114 of July 31, 2007, the Board entered into an agreement with Skanska USA Civil West California District Inc. of Riverside, CA for the construction of 1.) Old Morongo Road, Painted Hills Road, Desert Hot Springs area and 2.) 53rd Avenue, Calhoun Street to Van Buren Street, Coachella area and 3.) 54th Avenue, Pierce Street to the All American Canal, Coachella area and 4.) Signal modifications, roadway widening and the installation of left turn lanes at Dillon Road and Mountain View Road, Desert Hot Springs area and 5.) Roadway widening and the installation of left turn lanes at Dillon Road and Little Morongo Road, Desert Hot Springs area of Riverside County.



Juan C. Perez
Director of Transportation


dj
(Continued On Attached Page)

FINANCIAL DATA	Current F.Y. Total Cost:	\$ 1,024,351.15	In Current Year Budget:	Yes
	Current F.Y. Net County Cost:	\$ 0	Budget Adjustment:	No
	Annual Net County Cost:	\$ 0	For Fiscal Year:	2007/2008

SOURCE OF FUNDS: PM10/CMAQ (46%), Gas Tax (15%), Measure A/Coachella Valley (5%), Hazard Elimination Safety Program (13%), State Exchange Funds (6%), Misc. Funds, Coachella Valley Air Quality (COLMAC) (8%), Eastern County DIF - Traffic Signal (7%)	Positions To Be Deleted Per A-30	<input type="checkbox"/>
	Requires 4/5 Vote	<input type="checkbox"/>

C.E.O. RECOMMENDATION:

APPROVE

BY: 
Tina Grande

County Executive Office Signature

Policy



Policy



Consent



Consent



Dep't Recomm.:

Per Exec. Ofc.:

Prev. Agn. Ref. 7/31/07 (3.114)

District: 4,5

Agenda Number:

The authorized amount of the contract was \$1,007,764.75. The total amended contract amount (including quantity adjustments) is \$1,024,351.15 which is 1.6% more than the originally authorized amount.

This work was completed in conformance with the plans and specifications on December 4, 2007. The work was inspected by the Construction Engineering Section of the Transportation Department. Work Orders B3-0655, B3-0699, B3-0681, B3-0682, B4-0496.

Budget

Original Contract Amount		\$1,007,764.75
Tot. Chg Orders Authorized -	0.0%	\$0.00
Est. Pending Change Orders	3.1%	\$31,358.76
Amended Contract Amount		\$1,039,123.51
* Quantity Adjustments	-1.5%	(\$14,772.36)
+ CCO FA Adjustments	0.0%	\$0.00
Total Amended Contract Amount	101.6%	\$1,024,351.15

Expenditures

Total Progress Payments -	6	\$958,481.39
Estimated Pending Payments	7 Final	\$65,869.76
Total Expenditures		\$1,024,351.15

(Over)Under Contract Amount \$0.00

+ Change Orders using the Force Account method of payment issued prior to the work being completed generally do not use the total authorized amount.

* CAL-Trans Standard Specifications 4-1.03B. Increases or decreases in the quantity of a contract item of work will be determined by comparing the total pay quantity of such item of work with the Engineer's Estimate. If the total pay quantity of any item of work required under the contact varies from the Engineers Estimate by 25 percent or less, payment will be made for the quantity of work of said item performed at contract unit price, unless eligible for adjustment pursuant to Section 4-1.03C, "Changes in Character of Work."

When recorded, return to: After Recording, deliver to: Clerk of Board of Supervisors
Notice of Completion
(Civil Code § 3093 - Public Works)

(For Recorder's use)

To be recorded with County Recorder within 10 days after completion.
 No recording fee.

Notice is hereby given by the undersigned owner, a public entity of the State of California, that a public work of improvement has been completed, as follows:

Project title or description of work: Coachella Valley 5 in 1

Date of Completion: Date of this notice

Nature of owner: County of Riverside, public entity

Interest or estate of owner: Public Roadway

Address of owner: 4080 Lemon Street, 8th Floor, Riverside, CA 92501

Name of contractor: Skanska

Street or legal description of site: Old Morongo, 53rd Ave., 54th Ave., Dillon Rd & Mountain View Rd., and Dillon Rd & Little Morongo Rd., Coachella Valley

Dated: _____

Owner: County of Riverside
 (Name of Public Entity)

By: _____
 Chairman, Board of Supervisors

STATE OF CALIFORNIA)

ss

COUNTY OF RIVERSIDE)

I am the Chairman of the governing board of the County of Riverside, the public entity which executed the foregoing notice and on whose behalf I make this verification; I have read this notice, know its contents, and the same is true. I certify under penalty of perjury that the foregoing is true and correct.

Executed at Riverside, California on _____ (Date)

**Coachella Valley
Contract CCO History**

Contract No. 07-06-015
 Work Order No. B3-0681, B3-0682, B3-0699, B4-0496, B3-0655
 Contract Amount \$1,007,764.75

Single Maximum CCO \$32,577.65
 Maximum CCO's \$100,776.48
 Tip Budget N/A Tip Comments:
No Change

CCO No.	Amount This CCO	Authority	Cumulative CCO's	% Original Authorized	Cumulative CCO %	Classification
1	\$14,497.09	Trans. Director	\$14,497.09	1.44%	1.44%	Unavoidable
2	\$16,861.67	Trans. Director	\$31,358.76	1.67%	3.11%	Unavoidable

\$31,358.76



3.11%

New Authorized Contract Total	\$1,039,123.51
Total CCO Dollars To Date	\$31,358.76
Total % Increased by CCO's	3.11%

COUNTY OF RIVERSIDE

INTERSECTION OF DILLON ROAD AND MOUNTAIN VIEW AVENUE

TRAFFIC SIGNAL MODIFICATION AND STREET IMPROVEMENTS
FEDERAL I.D. NO. STPL-5956 (157)

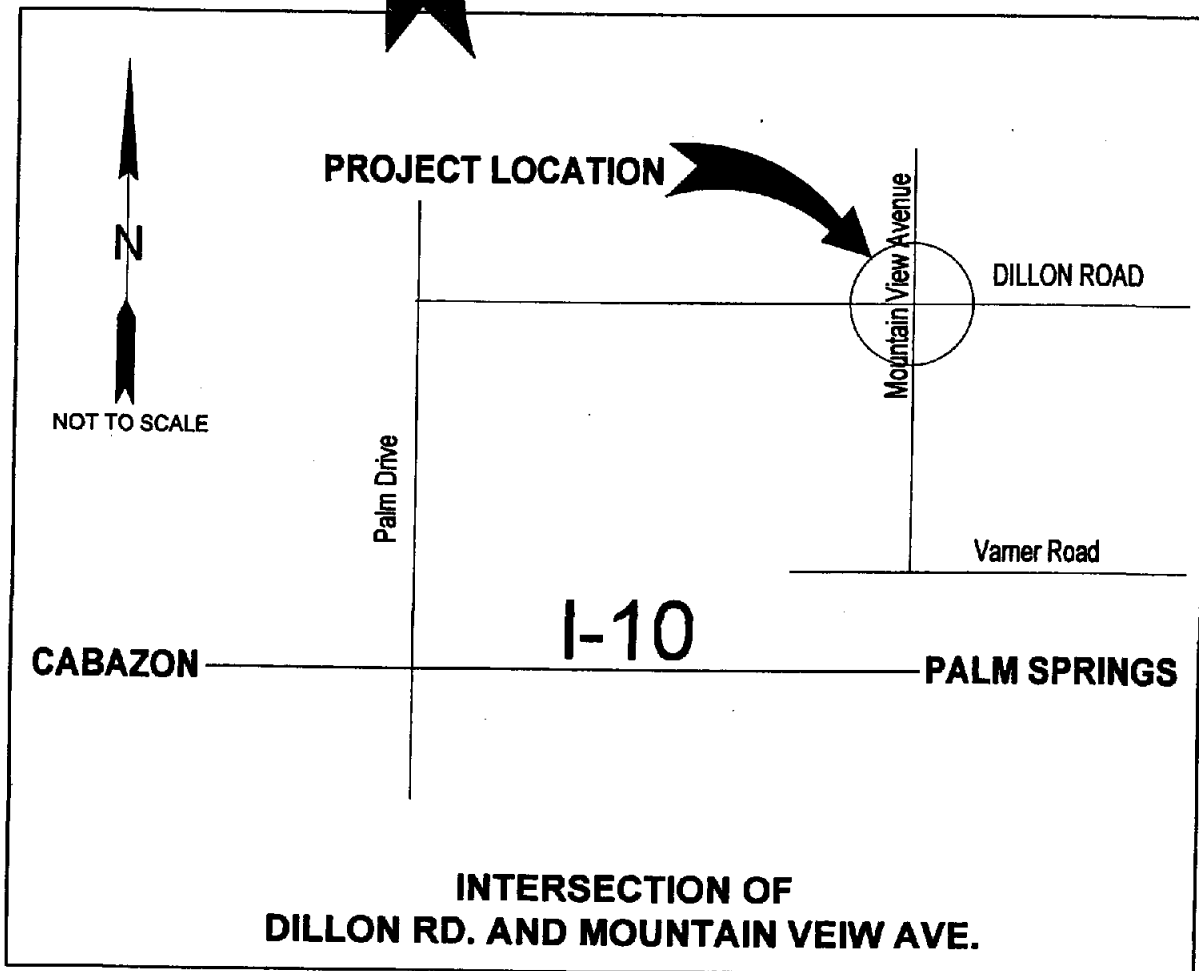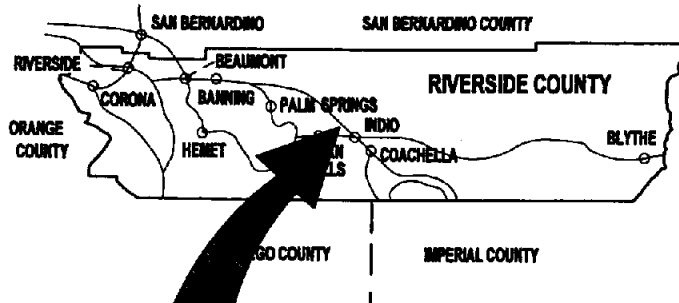

VICINITY MAP

T.3S.,R.5E.,SEC'S. 8&9

COUNTY OF RIVERSIDE



**DILLON ROAD
REHABILITATION PROJECT**

@

LITTLE MORONGO ROAD

FEDERAL AID PROJECT NO. STPLH-5956 (149)

WORK ORDER NUMBER: B3-0655

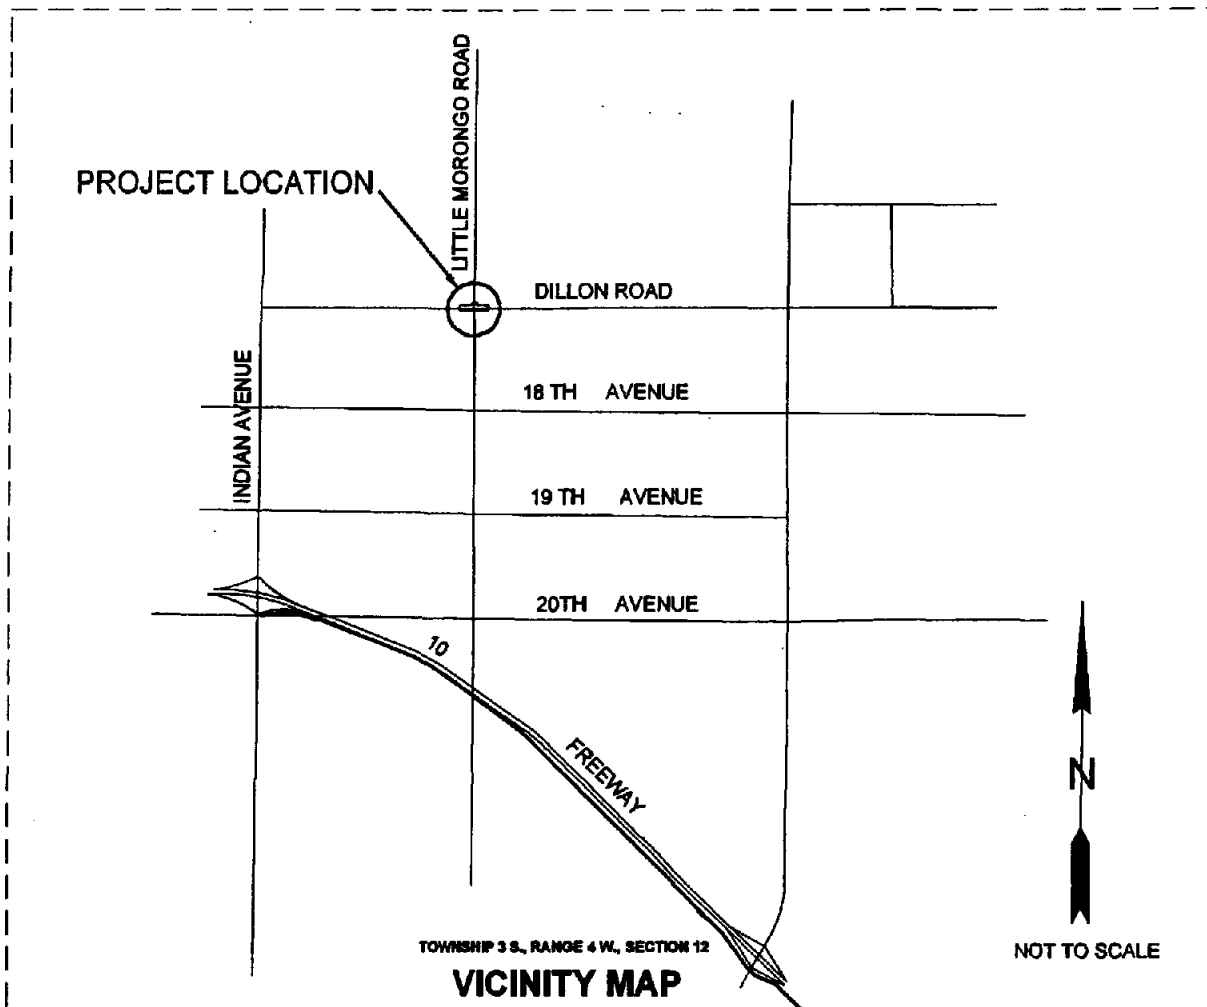
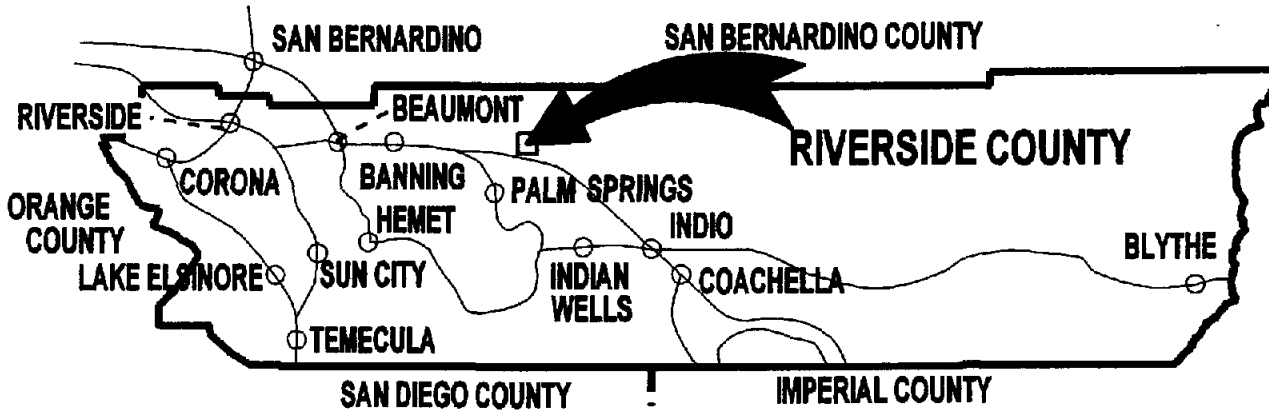


COUNTY OF RIVERSIDE

OLD MORONGO ROAD

STREET IMPROVEMENTS

PAINTED HILLS ROAD TO 0.4 MILE NORTHERLY
FEDERAL I.D. NO. CML 6164 (012)

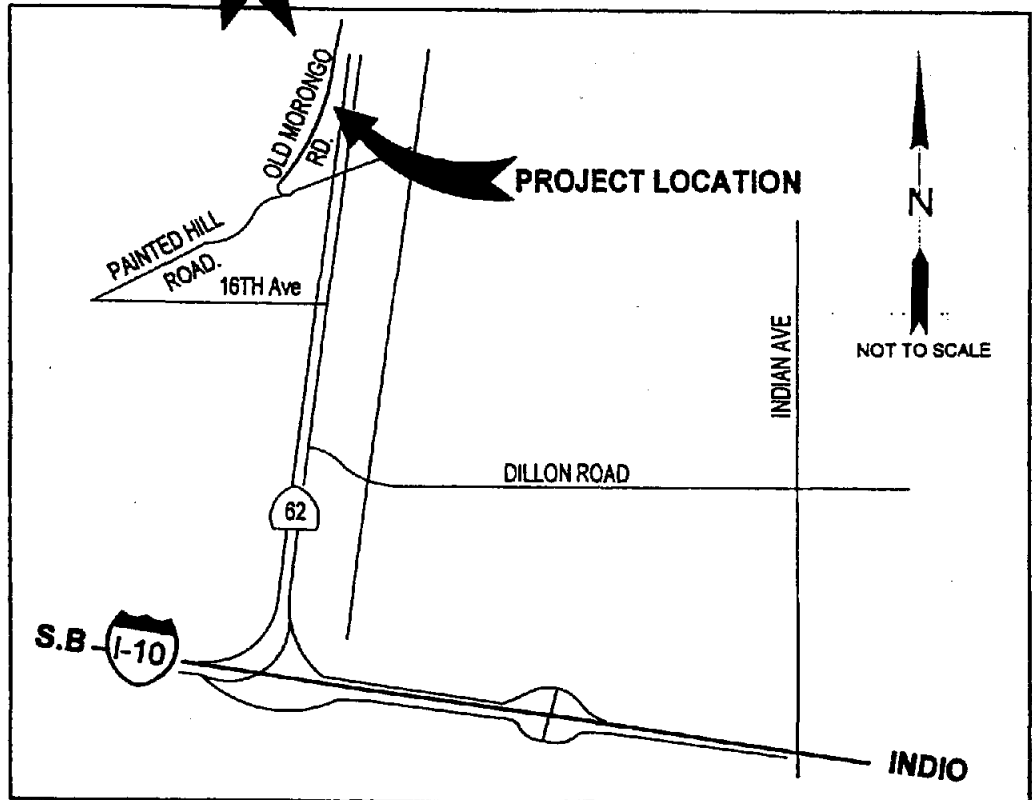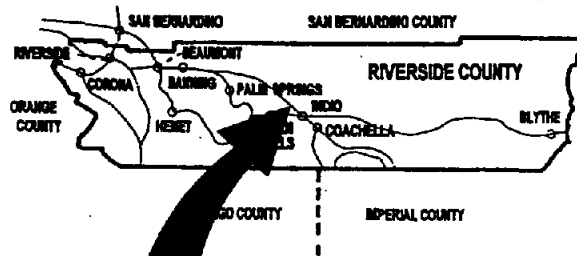

VICINITY MAP



T.28, R.4E, SEC 8
1-9-88

COUNTY OF RIVERSIDE

53RD AVENUE

CALHOUN STREET TO VAN BUREN STREET

CONSTRUCTION PROJECTS
FEDERAL I.D. NO. CML 6164 (012)

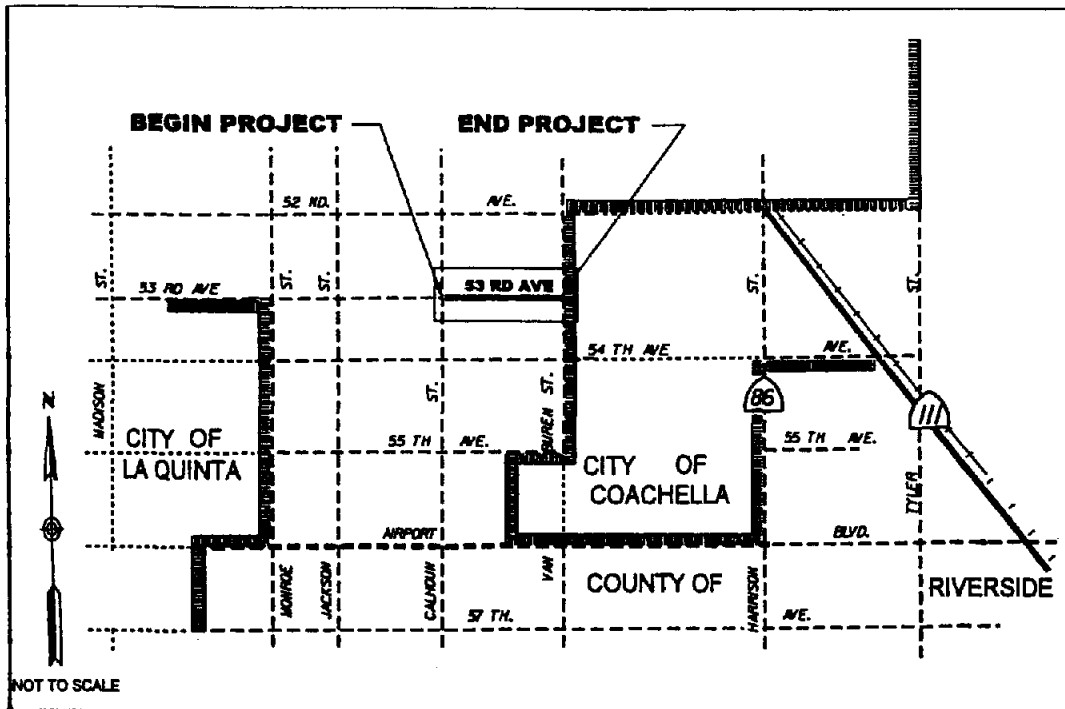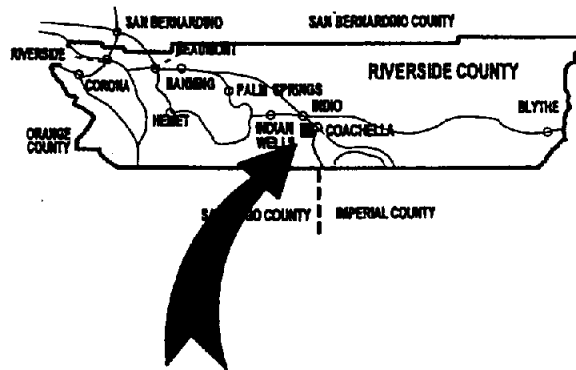

PROJECT LENGTH—0.6 MILE
TOWNSHIP 8 S RANGE 7 E SECTION 12
VICINITY MAP

COUNTY OF RIVERSIDE



54 TH AVENUE

ROAD CONSTRUCTION

FROM

PIERCE STREET TO ALL AMERICAN CANAL

FEDERAL AIDE NO. CML- 5956 (164)

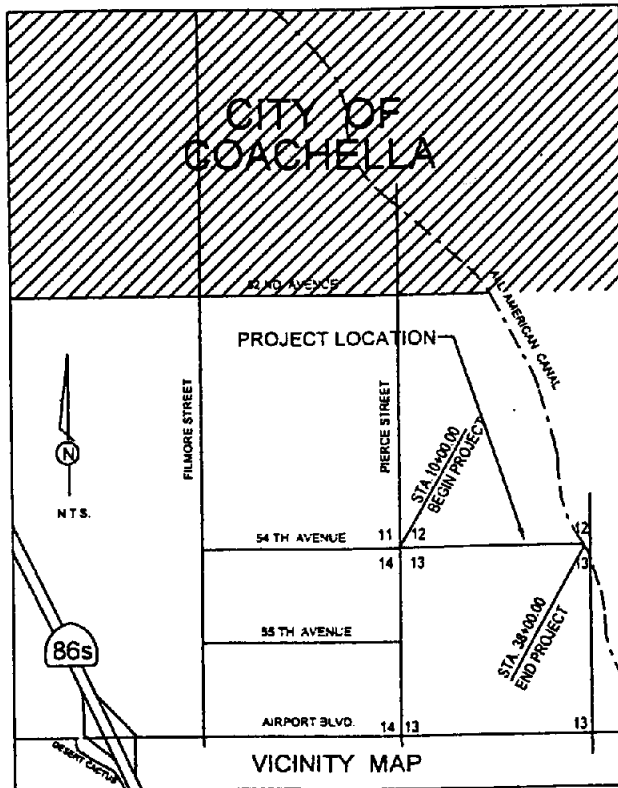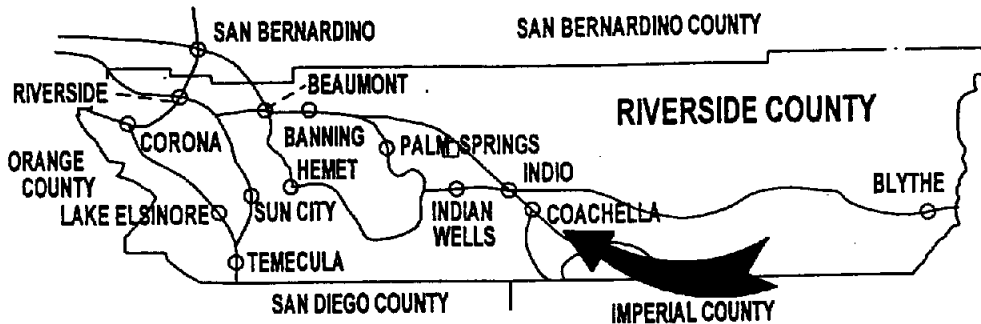

T6S,R0E SEC.12 & 13
LENGTH = .56 MILES
