

**SUBMITTAL TO THE BOARD OF SUPERVISORS
COUNTY OF RIVERSIDE, STATE OF CALIFORNIA**

314
A



FROM: TLMA - Transportation Department

SUBMITTAL DATE:
August 21, 2008

SUBJECT: Notice of Completion - Jefferson Street, State Highway 111 to Indio Boulevard, La Quinta / Indio Area

RECOMMENDED MOTION: That the Board execute and file the attached "Notice of Completion"

BACKGROUND: By Minute Order 3.35 of April 5, 2005, the Board entered into an agreement with Yeager Skanska, Inc. of Riverside, CA for the construction of Jefferson Street, from State Highway 111 to Indio Blvd., in the La Quinta and Indio area of Riverside County. The project includes the reconstruction and widening of Jefferson Street to provide 6 lanes of traffic between State Highway 111 and Indio Blvd., and includes the construction of a bridge over the Whitewater River, traffic signals and associated improvements.

Departmental Concurrence

Juan C. Perez
Director of Transportation

dj
(Continued On Attached Page)

FINANCIAL DATA	Current F.Y. Total Cost:	\$ 19,520,762	In Current Year Budget:	Yes
	Current F.Y. Net County Cost:	\$ 0	Budget Adjustment:	No
	Annual Net County Cost:	\$ 0	For Fiscal Year:	2007/2008
SOURCE OF FUNDS: TUMF (CVAG) (95.6%), City of Indio (2.5%), City of La Quinta (0.2%), Coachella Valley Water District (1.7%)				Positions To Be Deleted Per A-30 <input type="checkbox"/>
				Requires 4/5 Vote <input type="checkbox"/>

C.E.O. RECOMMENDATION:

APPROVE

BY:
Tina Grande

County Executive Office Signature

Policy Policy

Consent Consent

Dep't Recomm.:
Per Exec. Ofc.:

Prev. Agn. Ref. 4/5/05 (3.35)

District: 4

Agenda Number:

3.160

The Honorable Board of Supervisors

RE: Notice of Completion - Jefferson Street, State Highway 111 to Indio Boulevard, La Quinta / Indio Area

Page 2 of 2

The authorized amount of the contract was \$19,050,186.30. The total amended contract amount (including quantity adjustments) is \$ 19,520,762.35 which is 2.5% more than the originally authorized amount.

This work was completed in conformance with the plans and specifications on January 26, 2007. The work was inspected by the Construction Engineering Section of the Transportation Department. Work Order B2-0473.

Budget

Original Contract Amount		\$19,050,186.30
Tot. Chg Orders Authorized -	3.2%	\$606,970.25
Est. Pending Change Orders	0.0%	\$0.00
Amended Contract Amount		\$19,657,156.55
* Quantity Adjustments	-0.7%	(\$136,394.20)
+ CCO FA Adjustments	0.0%	\$0.00
Total Amended Contract Amount	102.5%	\$19,520,762.35

Expenditures

Total Progress Payments -	29	\$19,445,744.30
Estimated Pending Payments	30F	\$75,018.05
Total Expenditures		\$19,520,762.35

(Over)\Under Contract Amount \$0.00

+ Change Orders using the Force Account method of payment issued prior to the work being completed generally do not use the total authorized amount.

* CAL-Trans Standard Specifications 4-1.03B. Increases or decreases in the quantity of a contract item of work will be determined by comparing the total pay quantity of such item of work with the Engineer's Estimate. If the total pay quantity of any item of work required under the contract varies from the Engineers Estimate by 25 percent or less, payment will be made for the quantity of work of said item performed at contract unit price, unless eligible for adjustment pursuant to Section 4-1.03C, "Changes in Character of Work."

When recorded, return to: After Recording, deliver to: Clerk of Board of Supervisors
Notice of Completion
(Civil Code § 3093 - Public Works)

(For Recorder's use)

To be recorded with County Recorder within 10 days after completion.
 No recording fee.

Notice is hereby given by the undersigned owner, a public entity of the State of California, that a public work of improvement has been completed, as follows:

Project title or description of work: Jefferson Street Reconstruction and Widening

Date of Completion: Date of this notice

Nature of owner: County of Riverside, public entity

Interest or estate of owner: Public Roadway

Address of owner: 4080 Lemon Street, 8th Floor, Riverside, CA 92501

Name of contractor: Yeager Skanska, Inc.

Street or legal description of site: Jefferson Street, State Highway 111 to Indio Blvd., La Quinta / Indio Area

Dated: _____

Owner: County of Riverside
 (Name of Public Entity)

By: _____
 Chairman, Board of Supervisors


STATE OF CALIFORNIA)

ss

COUNTY OF RIVERSIDE)

I am the Chairman of the governing board of the County of Riverside, the public entity which executed the foregoing notice and on whose behalf I make this verification; I have read this notice, know its contents, and the same is true. I certify under penalty of perjury that the foregoing is true and correct.

Executed at Riverside, California on _____ (Date)

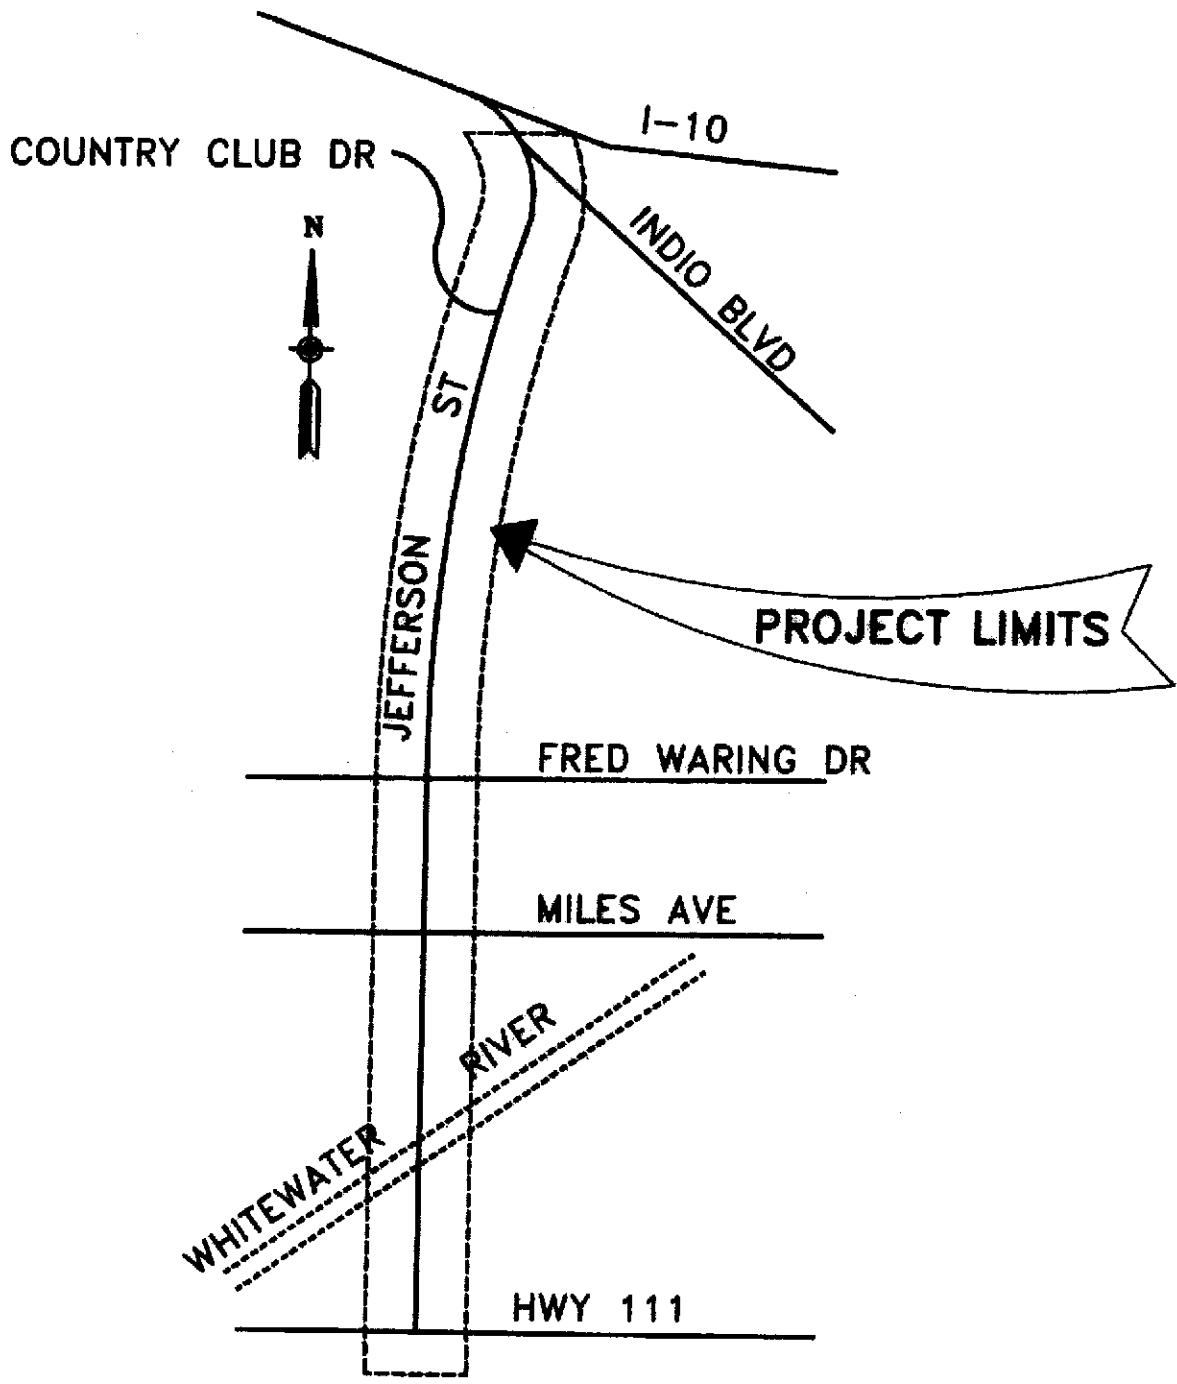

PROJECT LOCATION
NOT TO SCALE
