


**SUBMITTAL TO THE BOARD OF SUPERVISORS
COUNTY OF RIVERSIDE, STATE OF CALIFORNIA**

848



FROM: TLMA - Transportation Department

SUBMITTAL DATE:
January 28, 2010

SUBJECT: Notice of Completion - Construction of pedestrian sidewalk, installation of new fencing on the 68th Street Bridge over Interstate 15

RECOMMENDED MOTION: That the Board execute and file the attached "Notice of Completion"

BACKGROUND: By Minute Order 3.33 of April 21, 2009, the Board entered into an agreement with Trinity Construction of Blue Jay, CA for the construction of pedestrian sidewalk, installation of new fencing on the 68th Street Bridge over Interstate 15 and associated improvements in the Mira Loma area. The authorized amount of the contract was \$119,826. The total amended contract amount (including quantity adjustments) is \$114,934 which is 4.1% less than the originally authorized amount.

Departmental Concurrence

Juan C. Perez
Director of Transportation

dj
(Continued On Attached Page)

FINANCIAL DATA	Current F.Y. Total Cost:	\$114,934	In Current Year Budget:	Yes				
	Current F.Y. Net County Cost:	\$ 0	Budget Adjustment:	No				
	Annual Net County Cost:	\$ 0	For Fiscal Year:	2009/2010				
SOURCE OF FUNDS: State Safe Route to Schools (52%), Measure A/Western (48%)				<table border="1"> <tr> <td>Positions To Be Deleted Per A-30</td> <td align="center"><input type="checkbox"/></td> </tr> <tr> <td>Requires 4/5 Vote</td> <td align="center"><input type="checkbox"/></td> </tr> </table>	Positions To Be Deleted Per A-30	<input type="checkbox"/>	Requires 4/5 Vote	<input type="checkbox"/>
Positions To Be Deleted Per A-30	<input type="checkbox"/>							
Requires 4/5 Vote	<input type="checkbox"/>							

C.E.O. RECOMMENDATION:

APPROVE

BY:

Tina Grande

County Executive Office Signature

Policy	<input checked="" type="checkbox"/>
Policy	<input checked="" type="checkbox"/>
Consent	<input type="checkbox"/>
Consent	<input type="checkbox"/>
Dept't Recomm.:	
Per Exec. Ofc.:	

Prev. Agn. Ref. 4/21/09, Item 3.33 | **District:** 2 | **Agenda Number:**

3.57

The Honorable Board of Supervisors

RE: Notice of Completion - Construction of pedestrian sidewalk, installation of new fencing on the 68th Street Bridge over Interstate 15

January 28, 2010

Page 2 of 2

This work was completed in conformance with the plans and specifications on November 20, 2009. The work was inspected by the Construction Engineering Section of the Transportation Department. Work Order B8-0661.

Budget

Original Contract Amount		\$119,826.00
Tot. Chg Orders Authorized -	0.0%	\$0.00
Est. Pending Change Orders	0.0%	\$0.00
Amended Contract Amount		\$119,826.00
* Quantity Adjustments	-4.1%	(\$4,892.00)
+ CCO FA Adjustments	0.0%	\$0.00
Total Amended Contract Amount	95.9%	\$114,934.00

Expenditures

Total Progress Payments -		\$114,934.00
Estimated Pending Payments		
Total Expenditures		\$114,934.00
(Over)\Under Contract Amount		\$0.00

+ Change Orders using the Force Account method of payment issued prior to the work being completed generally do not use the total authorized amount.

* CAL-Trans Standard Specifications 4-1.03B. Increases or decreases in the quantity of a contract item of work will be determined by comparing the total pay quantity of such item of work with the Engineer's Estimate. If the total pay quantity of any item of work required under the contract varies from the Engineers Estimate by 25 percent or less, payment will be made for the quantity of work of said item performed at contract unit price, unless eligible for adjustment pursuant to Section 4-1.03C, "Changes in Character of Work."

PLEASE COMPLETE THIS INFORMATION
RECORDING REQUESTED BY:

**KECIA HARPER-IHEM, CLERK OF THE BOARD
RIVERSIDE CO. CLERK OF THE BOARD
4080 LEMON STREET, 1ST FLOOR CAC
P O BOX 1147 – RIVERSIDE, CA 92502
MAIL STOP # 1010**

AND WHEN RECORDED MAIL TO:
RETURN TO: _____ STOP #1010
RIVERSIDE COUNTY CLERK OF THE BOARD
P. O. BOX 1147 – RIVERSIDE, CA 92502

THIS SPACE FOR RECORDERS USE ONLY

NOTICE OF COMPLETION

To be recorded with County Recorder
within 10 days after completion.
No recording fee.

Notice is hereby given by the undersigned owner, a public entity of the State of California, that a public work of improvement has been completed, as follows:

Project title or description of work: pedestrian sidewalk and new fencing over I15

Date of Completion: Date of this notice

Nature of owner: County of Riverside, public entity

Interest or estate of owner: Public Roadway

Address of owner: 4080 Lemon Street, 8th Floor, Riverside, CA 92501

Name of contractor: Trinity Construction

Street or legal description of site: 68th Street Bridge over Interstate 15

Dated: _____

Owner: County of Riverside
(Name of Public Entity)

By: _____
Jeff Stone, Chairman, Board of Supervisors

STATE OF CALIFORNIA)

ss

COUNTY OF RIVERSIDE)



I am the Chairman of the governing board of the County of Riverside, the public entity which executed the foregoing notice and on whose behalf I make this verification; I have read this notice, know its contents, and the same is true. I certify under penalty of perjury that the foregoing is true and correct.

Executed at Riverside, California on _____ (Date)

_____, Jeff Stone, Chairman of the Board of Supervisors

COUNTY OF RIVERSIDE DEPARTMENT OF TRANSPORTATION

68TH STREET PEDESTRIAN WALKWAY AND BRIDGE RAILING / FENCES

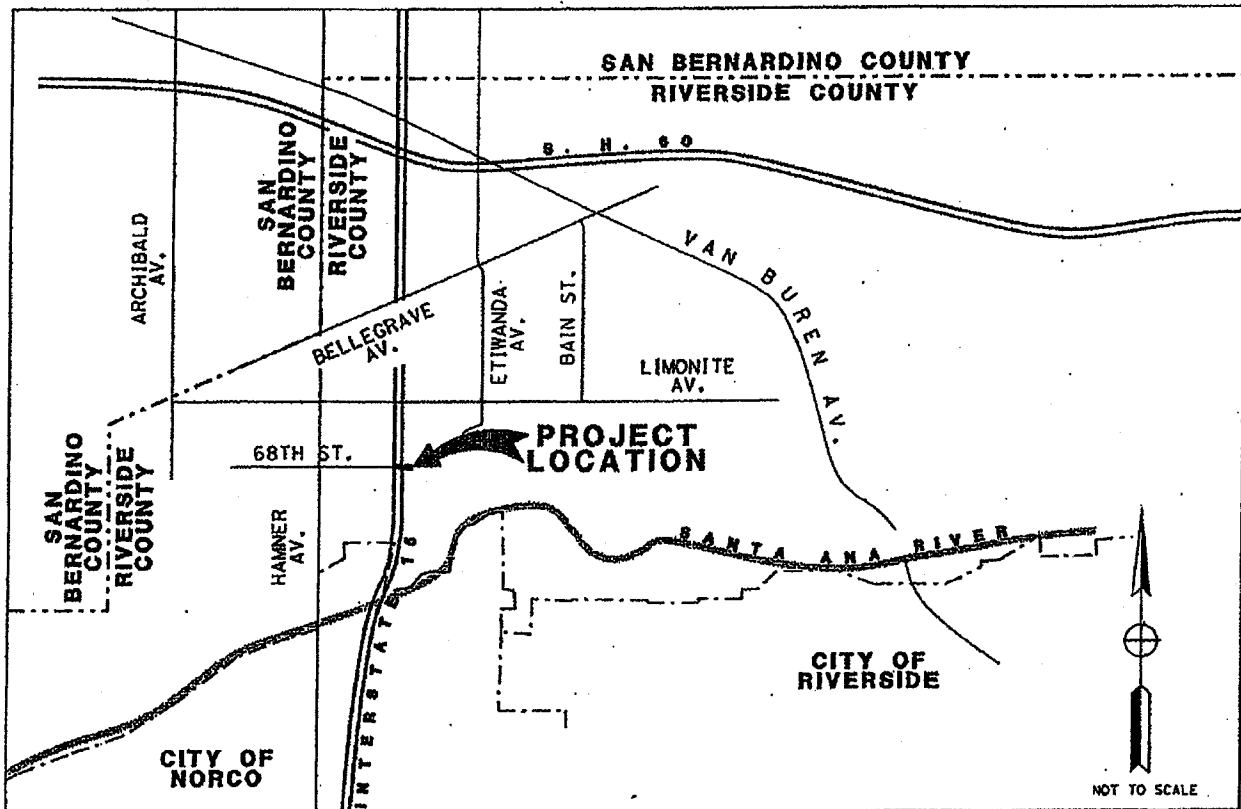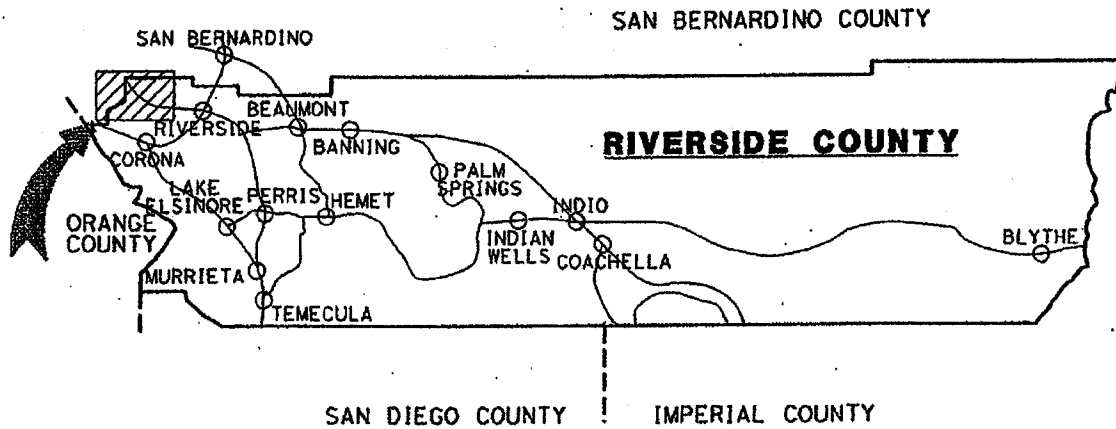

PROJECT LENGTH = 762'
RANCHO JURUPA (STEARNS)
2008 THOMAS GUIDE PG 684, F-7
VICINITY MAP

Contractor: Trinity Construction
 Address: P.O. Box 246
 City, State, Zip: Blue Jay, CA 92317

Estimate No. 3 Final
 From: October 28, 2009
 To: November 25, 2009



Item No.	Item Description	Units	Quantity	Unit Price	Original Contract		Change Authorized		Total Authorized		This Estimate		Previous		Total Estimate To Date		% Auth.
					Amount	Quantity	Amount	Quantity	Amount	Quantity	Amount	Quantity	Amount	Quantity	Amount	Quantity	
					119,826.00	0.00	119,826.00		119,826.00		34,283.00		114,934.00				
PROJECT TOTAL																	

Made by: George Boyden

Checked by:
 OK Const. Supv.

Working Days: 30 Start Date: 6-15-09
 Days Added: 0 End Date: 7-28-09
 Subtotal: 30 % Complete: 96%
 Days Used: 30 Original Contract: \$119,826.00
 % Time Elapsed: 100% Amended Contract: \$119,826.00

TOTAL VALUE OF WORK TO DATE: \$114,934.00
 LESS RETENTION: 10% 11,493.40
 TOTAL DUE TO DATE: \$103,440.60
 LESS PREVIOUSLY INVOICED: 72,585.90
 LESS LABOR NON COMPLIANCE: 0.00
 TOTAL DUE THIS PAYMENT: \$30,854.70

This Estimate Approved _____ Date: _____ for: _____

Juan C. Perez, Director of Transportation

Trinity Construction

Quantities on This Estimate Approved _____ Date: 12-16-09

Received by Accounts Payable: _____
 By: _____

PAYMENT APPROVAL

Fund 20000
 Dept ID 3130500000
 Account 527980
 Project Z68-0661E
 Activity ID Z3600
 Resource Type CNT
 Signature
 Date 12/17/09



Item No.	Item Description	Units	Quantity	Unit Price	Original Contract		Change Authorized		Total Authorized		This Estimate	Previous	Total Estimate To Date		% Auth.
					Amount	Quantity	Amount	Quantity	Amount	Quantity			Amount	Quantity	
1	Place Asphalt Concrete Dike (CRS 212) (6")	LF	450	7.00	3,150.00	450.00	3,150.00	430.00	3,150.00	430.00	430.00	430.00	3,010.00	96%	
2	Asphalt Concrete (Driveway Approach with Asphalt Concrete Dike (CRS 206)	EA	1	500.00	500.00	1.00	500.00	1.00	500.00	1.00	1.00	1.00	500.00	100%	
3	Dust Abatement	LS	1	2,500.00	2,500.00	1.00	2,500.00	0.95	2,500.00	0.95	0.95	0.95	2,500.00	100%	
4	Water Pollution Control	LS	1	1,250.00	1,250.00	1.00	1,250.00	0.90	1,250.00	0.90	0.90	0.90	1,250.00	100%	
5	Traffic Control System	LS	1	25,850.00	25,850.00	1.00	25,850.00	0.90	25,850.00	0.90	0.90	0.90	25,850.00	100%	
6	Remove Traffic Stripe and Pavement Marking	SOFT	1,400	1.50	2,100.00	1,400.00	2,100.00	1,400.00	2,100.00	1,400.00	1,400.00	1,400.00	2,100.00	100%	
7	Salvage Roadside Sign	EA	2	100.00	200.00	2.00	200.00	2.00	200.00	2.00	2.00	2.00	200.00	100%	
8	Clearing and Grubbing	LS	1	500.00	500.00	1.00	500.00	1.00	500.00	1.00	1.00	1.00	500.00	100%	
9	Roadway Excavation	CY	160	44.00	7,040.00	160.00	7,040.00	160.00	7,040.00	160.00	160.00	160.00	7,040.00	100%	
10	Class 2 Aggregate Base	CY	26	60.00	1,560.00	26.00	1,560.00	26.00	1,560.00	26.00	26.00	26.00	1,200.00	77%	
11	Hot Asphalt Mix	TON	88	100.00	8,800.00	88.00	8,800.00	40.20	4,722.00	47.22	40.20	40.20	8,742.00	99%	
12	Place Asphalt Concrete (Misc. Area)	SQYD	290	21.00	6,090.00	290.00	6,090.00	7.00	1,050.00	7.00	7.00	7.00	1,050.00	100%	
13	Roadside Sign - One Post	EA	7	150.00	1,050.00	7.00	1,050.00	7.00	1,050.00	7.00	7.00	7.00	1,050.00	100%	
14	Chain Link Fence (Type CL-6)	LF	180	38.00	6,840.00	180.00	6,840.00	72.00	2,736.00	72.00	120.00	120.00	7,296.00	107%	
15	Chain Link Fence [Type 3 Modified]	LF	256	71.00	18,176.00	256.00	18,176.00	130.00	9,230.00	130.00	120.00	120.00	17,750.00	98%	
16	Chain Link Railing (Type 7)	LF	256	90.00	23,040.00	256.00	23,040.00	131.00	11,790.00	131.00	120.00	120.00	22,590.00	98%	
17	Thermoplastic Crosswalk and Pavement Marking	SOFT	860	2.50	2,150.00	860.00	2,150.00	860.00	2,150.00	860.00	860.00	860.00	2,150.00	100%	
18	Paint Traffic Stripe (2-Coat)	LF	3,400	0.30	1,020.00	3,400.00	1,020.00	3,400.00	1,020.00	3,400.00	3,400.00	3,400.00	1,020.00	100%	
19	Remove Fence Fabric and Railing	LF	256	10.00	2,560.00	256.00	2,560.00	70.00	700.00	70.00	180.00	180.00	2,500.00	98%	
20	Pavement Marker (Reflective)	EA	200	2.25	450.00	200.00	450.00	200.00	450.00	200.00	200.00	200.00	450.00	100%	
21	Obtain Encroachment Permit	FA	1	5,000.00	5,000.00	1.00	5,000.00	0.33	1,650.00	0.33	0.33	0.33	1,650.00	33%	

Contractor: Trinity Construction
 Address: P.O. Box 248
 City, State, Zip: Blue Jay, CA 92317

Estimate No. 3 Final
 From: October 26, 2009
 To: November 25, 2009
