


**SUBMITTAL TO THE BOARD OF SUPERVISORS
COUNTY OF RIVERSIDE, STATE OF CALIFORNIA**

453 A



FROM: TLMA - Transportation Department

SUBMITTAL DATE:
March 25, 2010

SUBJECT: Notice of Completion - Rehabilitation and widening of Cajalco Road from La Sierra Avenue to Temescal Canyon Road

RECOMMENDED MOTION: That the Board execute and file the attached "Notice of Completion".

BACKGROUND: By Minute Order 3.70 of June 30, 2009, the Board entered into an agreement with R.J. Noble Company, Inc. of Orange, CA for the rehabilitation and minor spot widening of Cajalco Road from La Sierra Avenue to Temescal Canyon Road, installation of new traffic signal and associated improvements. The authorized amount of the contract was \$1,562,632. The total amended contract amount (including quantity adjustments) is \$1,724,515.20 which is 10.4% more than the originally authorized amount.

Juan C. Perez
Director of Transportation

dj
(Continued On Attached Page)

FINANCIAL DATA	Current F.Y. Total Cost:	\$1,724,515	In Current Year Budget:	Yes
	Current F.Y. Net County Cost:	\$ 0	Budget Adjustment:	No
	Annual Net County Cost:	\$ 0	For Fiscal Year:	2009/2010

SOURCE OF FUNDS: Measure A / Western (100%)	Positions To Be Deleted Per A-30	<input type="checkbox"/>
	Requires 4/5 Vote	<input type="checkbox"/>

C.E.O. RECOMMENDATION: APPROVE

BY:
Tina Grande

County Executive Office Signature

- Policy
- Consent
- Policy
- Consent
- Dept Recomm.:
- Per Exec. Ofc.:

The Honorable Board of Supervisors
 RE: Notice of Completion - Rehabilitation and widening of Cajalco Road from La Sierra Avenue to Temescal Canyon Road
 March 25, 2010
 Page 2 of 2

The Change Orders authorized were for signal modifications to accommodate requests by residents of Silverton Court to improve turning onto Cajalco Road and additional shoulder grading.

The Quantity Adjustments were for an additional 2,324 tons of hot mix asphalt that were provided to increase the final quality of the 2.8 mile project. The nightly grinding and paving did not allow for importation of base material to compensate for inconsistencies in the compaction of the sub base. The thickness of the final lifts of pavement varied to provide a smooth driving surface. The additional asphalt quantity also included a full depth pavement section under the asphalt berms and additional pavement for adjacent driveways.

This work was completed in conformance with the plans and specifications on September 24, 2009. The work was inspected by the Construction Engineering Section of the Transportation Department. Work Order A7-0346.

Budget

Original Contract Amount		\$1,562,632.00
Tot. Chg Orders Authorized -	2.4%	\$36,999.45
Est. Pending Change Orders	0.0%	\$0.00
Amended Contract Amount		\$1,599,631.45
* Quantity Adjustments	8.0%	\$124,883.75
+ CCO FA Adjustments	0.0%	\$0.00
Total Amended Contract Amount	110.4%	\$1,724,515.20

Expenditures

Total Progress Payments -	\$1,724,515.20
Estimated Pending Payments	
Total Expenditures	\$1,724,515.20
(Over)\Under Contract Amount	\$0.00

+ Change Orders using the Force Account method of payment issued prior to the work being completed generally do not use the total authorized amount.

* CAL-Trans Standard Specifications 4-1.03B. Increases or decreases in the quantity of a contract item of work will be determined by comparing the total pay quantity of such item of work with the Engineer's Estimate. If the total pay quantity of any item of work required under the contract varies from the Engineers Estimate by 25 percent or less, payment will be made for the quantity of work of said item performed at contract unit price, unless eligible for adjustment pursuant to Section 4-1.03C, "Changes in Character of Work."

PLEASE COMPLETE THIS INFORMATION
RECORDING REQUESTED BY:

**KECIA HARPER-IHEM, CLERK OF THE BOARD
RIVERSIDE CO. CLERK OF THE BOARD
4080 LEMON STREET, 1ST FLOOR CAC
P O BOX 1147 – RIVERSIDE, CA 92502
MAIL STOP # 1010**

AND WHEN RECORDED MAIL TO:

**RETURN TO: STOP #1010
RIVERSIDE COUNTY CLERK OF THE BOARD
P. O. BOX 1147 – RIVERSIDE, CA 92502**

THIS SPACE FOR RECORDERS USE ONLY

NOTICE OF COMPLETION

To be recorded with County Recorder
within 10 days after completion.
No recording fee.

Notice is hereby given by the undersigned owner, a public entity of the State of California, that a public work of improvement has been completed, as follows:

Project title or description of work: Rehabilitation, widening, traffic signal and associated improvements

Date of Completion: Date of this notice

Nature of owner: County of Riverside, public entity

Interest or estate of owner: Public Roadway

Address of owner: 4080 Lemon Street, 8th Floor, Riverside, CA 92501

Name of contractor: All American Asphalt

Street or legal description of site: Cajalco Road from Temescal Canyon Road to La Sierra Avenue

Dated: _____

Owner: County of Riverside
(Name of Public Entity)

By: _____
Jeff Stone, Chairman, Board of Supervisors

STATE OF CALIFORNIA)


ss

COUNTY OF RIVERSIDE)

I am the Chairman of the governing board of the County of Riverside, the public entity which executed the foregoing notice and on whose behalf I make this verification; I have read this notice, know its contents, and the same is true. I certify under penalty of perjury that the foregoing is true and correct.


Executed at Riverside, California on _____ (Date)

_____, Jeff Stone, Chairman of the Board of Supervisors

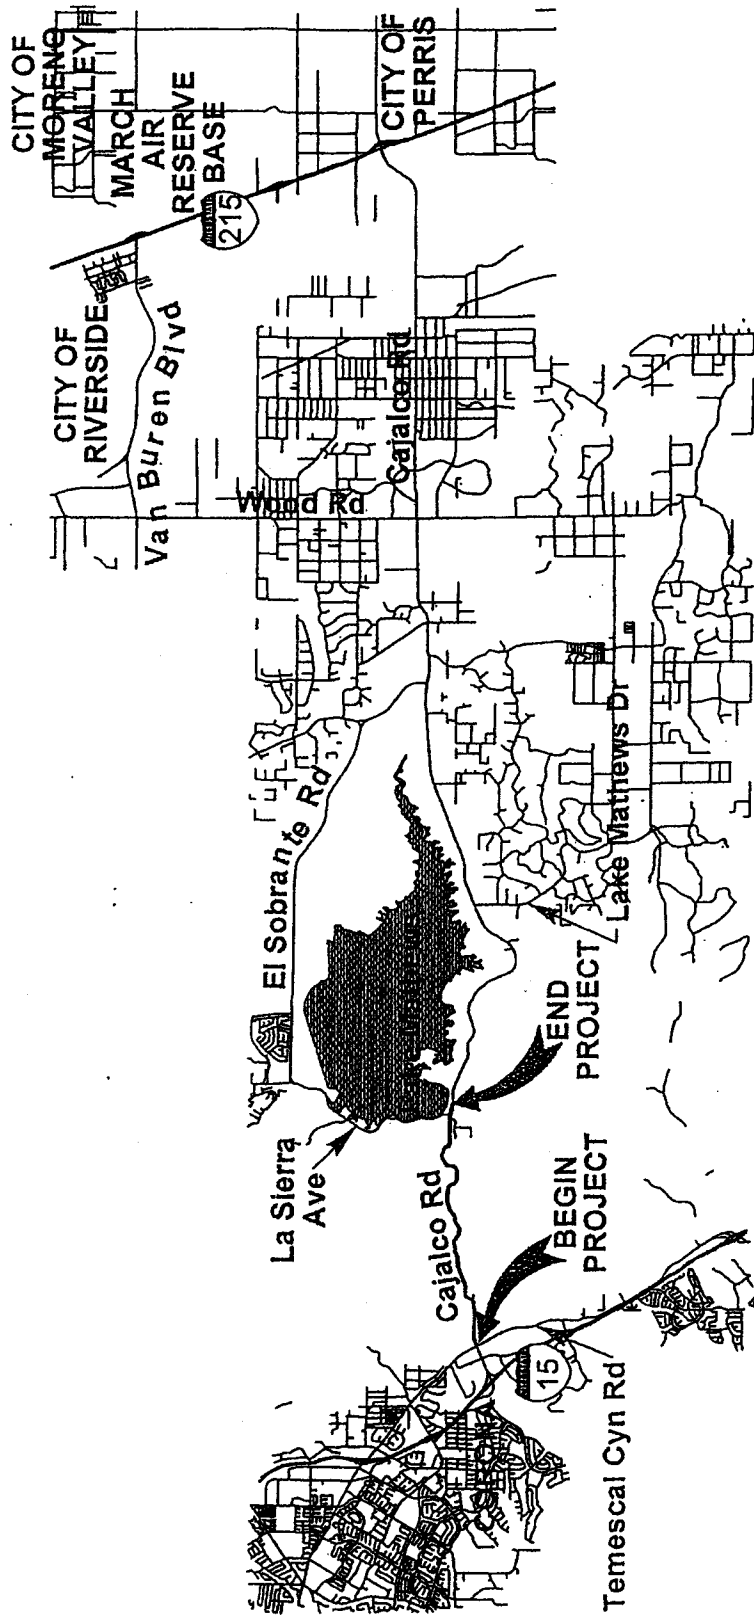

PROJECT LENGTH = 17,703.37 FEET, 3.353 MILES
 WITHIN RANCHO EL SOBRANTE DE SAN JACINTO
 AND T. 4 S., R. 6 W., SEC. 16.

VICINITY MAP

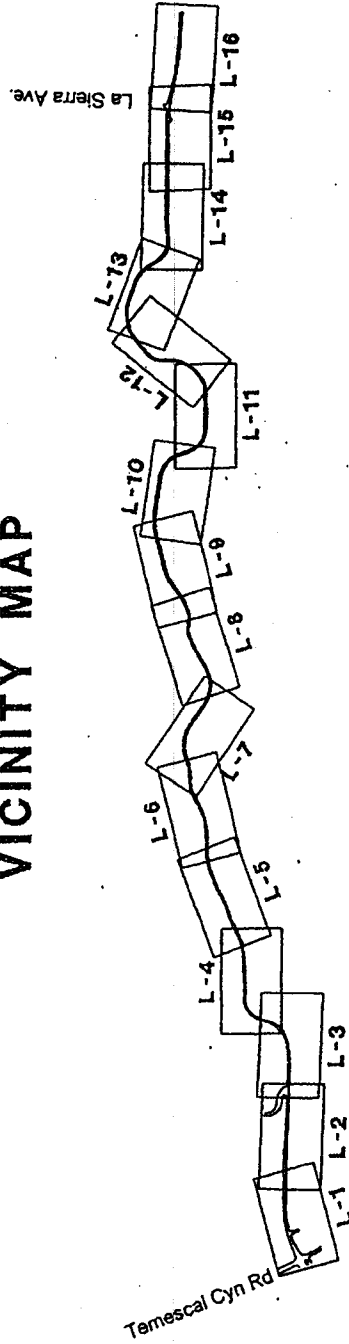

PLAN SHEET INDEX
