

**SUBMITTAL TO THE BOARD OF SUPERVISORS  
COUNTY OF RIVERSIDE, STATE OF CALIFORNIA**



665 A

**FROM:** TLMA - Transportation Department


**SUBMITTAL DATE:**  
April 22, 2010

**SUBJECT:** Notice of Completion - Construction of Traffic Signal and Lighting, at Limonite Avenue and Lucretia Avenue, Mira Loma area.

**RECOMMENDED MOTION:** That the Board execute and file the attached "Notice of Completion".

**BACKGROUND:** By Minute Order 3.48 of October 27, 2009, the Board entered into an agreement with DBX, Inc. of Temecula, CA for the construction of traffic signal and lighting, signing and striping at intersection of Limonite Avenue and Lucretia Avenue, in the Mira Loma area. The authorized amount of the contract was \$358,393. The total amended contract amount is \$386,269 which is 7.8% more than the originally authorized amount.

The cost increase was due to a minor quantity adjustment for asphalt concrete.

  
 \_\_\_\_\_  
 Juan C. Perez  
 Director of Transportation

dj  
(Continued On Attached Page)

<b>FINANCIAL DATA</b>	Current F.Y. Total Cost:	\$386,269	In Current Year Budget:	Yes
	Current F.Y. Net County Cost:	\$ 0	Budget Adjustment:	No
	Annual Net County Cost:	\$ 0	For Fiscal Year:	2009/2010
<b>SOURCE OF FUNDS:</b> Measure A / Western (99%), Jurupa Community Service District (JCSD) (1%)				Positions To Be Deleted Per A-30 <input type="checkbox"/>
				Requires 4/5 Vote <input type="checkbox"/>

**C.E.O. RECOMMENDATION:**

APPROVE

BY:   
 Tina Grande

**County Executive Office Signature**

Policy  
 Policy

Consent  
 Consent

Dep't Recomm.:  
 Per Exec. Ofc.:

**Prev. Agn. Ref.** 10/27/09, Item 3.48 | **District:** 2 | **Agenda Number:**

**3.80**

The Honorable Board of Supervisors

RE: Notice of Completion - Construction of Traffic Signal and Lighting, at Limonite Avenue and Lucretia Avenue, Mira Loma area.

April 22, 2010

Page 2 of 2

All work, including the minor quantity adjustment, was completed in conformance with the plans and specifications on December 2, 2009. The work was inspected by the Construction Engineering Section of the Transportation Department. Work Order B6-0563.

**Budget**

Original Contract Amount		\$358,393.00
Tot. Chg Orders Authorized -	0.0%	\$0.00
Est. Pending Change Orders	0.0%	\$0.00
Amended Contract Amount		\$358,393.00
* Quantity Adjustments	7.8%	\$27,875.93
+ CCO FA Adjustments	0.0%	\$0.00
Total Amended Contract Amount	107.8%	\$386,268.93

**Expenditures**

Total Progress Payments -		\$386,268.93
Estimated Pending Payments		
Total Expenditures		\$386,268.93
<b>(Over)\Under Contract Amount</b>		<b>\$0.00</b>

+ Change Orders using the Force Account method of payment issued prior to the work being completed generally do not use the total authorized amount.

\* CAL-Trans Standard Specifications 4-1.03B. Increases or decreases in the quantity of a contract item of work will be determined by comparing the total pay quantity of such item of work with the Engineer's Estimate. If the total pay quantity of any item of work required under the contract varies from the Engineers Estimate by 25 percent or less, payment will be made for the quantity of work of said item performed at contract unit price, unless eligible for adjustment pursuant to Section 4-1.03C, "Changes in Character of Work."

PLEASE COMPLETE THIS INFORMATION  
RECORDING REQUESTED BY:

**KECIA HARPER-IHEM, CLERK OF THE BOARD  
RIVERSIDE CO. CLERK OF THE BOARD  
4080 LEMON STREET, 1<sup>ST</sup> FLOOR CAC  
P O BOX 1147 – RIVERSIDE, CA 92502  
MAIL STOP # 1010**

AND WHEN RECORDED MAIL TO:

**RETURN TO: STOP #1010**  
RIVERSIDE COUNTY CLERK OF THE BOARD  
P. O. BOX 1147 – RIVERSIDE, CA 92502

THIS SPACE FOR RECORDERS USE ONLY

**NOTICE OF COMPLETION**

To be recorded with County Recorder  
within 10 days after completion.  
No recording fee.

**Notice is hereby given by the undersigned owner, a public entity of the State of California, that a public work of improvement has been completed, as follows:**

**Project title or description of work:** Construction of traffic signal and lighting, signing and striping

**Date of Completion:** Date of this notice

**Nature of owner:** County of Riverside, public entity

**Interest or estate of owner:** Public Roadway

**Address of owner:** 4080 Lemon Street, 8th Floor, Riverside, CA 92501

**Name of contractor:** DBX, Inc.

**Street or legal description of site:** Limonite Avenue and Lucretia Avenue

Dated: \_\_\_\_\_

Owner: County of Riverside  
(Name of Public Entity)

By: \_\_\_\_\_  
Jeff Stone, Chairman, Board of Supervisors

STATE OF CALIFORNIA )

ss

COUNTY OF RIVERSIDE )

I am the Chairman of the governing board of the County of Riverside, the public entity which executed the foregoing notice and on whose behalf I make this verification; I have read this notice, know its contents, and the same is true. I certify under penalty of perjury that the foregoing is true and correct.

Executed at Riverside, California on \_\_\_\_\_ (Date)

\_\_\_\_\_, Jeff Stone, Chairman of the Board of Supervisors

PROJECT: Limonite Ave. & Lucetta Ave. 7/5 and Lighting Project  
 County Project No.: B6-0583  
 Contract No.: 09-08-005

Contractor: DBX, Inc.  
 Address: 42086 Avenida Avencado  
 City, State, Zip: Temecula, CA 92590



Estimate No. 3 Final  
 From: December 25, 2009  
 To: February 25, 2010

Item No.	Item Description	Units	Quantity	Unit Price	Original Contract Amount	Change Authorized Quantity	Change Authorized Amount	Total Authorized Quantity	Total Authorized Amount	This Estimate Quantity	This Estimate Amount	Previous Quantity	Total Estimate To Date Quantity	Total Estimate To Date Amount	% Auth.

Made by: Yvan Mendoza  
 Checked by: \_\_\_\_\_  
 OK Const. Supv. \_\_\_\_\_

Working Days: 35  
 Days Added: 0  
 Subtotal: 35  
 Days Used: 30  
 % Time Elapsed: 86%

Start Date: 11-9-09  
 End Date: 12-2-09  
 % \$ Complete: 108%  
 Original Contract: \$358,393.00  
 Amended Contract: \$358,393.00

TOTAL VALUE OF WORK TO DATE: \$386,268.93  
 LESS RETENTION: 38,628.89  
 TOTAL DUE TO DATE: \$347,642.04  
 LESS PREVIOUSLY INVOICED: 306,971.04  
 LESS LABOR NON COMPLIANCE: 0.00  
 TOTAL DUE THIS PAYMENT: \$40,671.00

This Estimate Approved \_\_\_\_\_ Date: \_\_\_\_\_ for: \$40,671.00

Received by Accounts Payable: \_\_\_\_\_  
 By: \_\_\_\_\_

Quantities on This Estimate Approved [Signature] Date: 3/18/10  
 DBX, Inc.

**PAYMENT APPROVAL**

Fund 20006  
 Dept ID 313050000  
 Account 527980  
 Project Z B6-0583E  
 Activity ID Z3500  
 Resource Type CNT  
 Signature [Signature]  
 Date 3/18/10

PROGRESS ESTIMATE RECORD - COUNTY OF RIVERSIDE

PROJECT: Limonite Ave. & Lurstedla Ave. T/S and Lighting Project  
 County Project No.: 86-0583  
 Contract No.: 09-09-005

Contractor: DBX, Inc.  
 Address: 4206 Avenida Alvarado  
 City, State, Zip: Temecula, CA 92590



Estimate No. 3 Final  
 From: December 25, 2009  
 To: February 25, 2010

Item No.	Item Description	Units	Quantity	Unit Price	Original Contract Amount	Change Authorized Quantity	Change Authorized Amount	Total Authorized Quantity	Total Authorized Amount	This Estimate Quantity	This Estimate Amount	Previous Quantity	Total Estimate To Date Quantity	Total Estimate To Date Amount	% Auth.
1	A) MINOR CONCRETE (CURB RAMP) (CRS 403 -CASE	EA	2	4,670.00	9,340.00			2.00	9,340.00			2.00	2.00	9,340.00	100%
2	MINOR CONCRETE (CURB RAMP) (403 - CASE B)	EA	1	2,660.00	2,660.00			1.00	2,660.00			1.00	1.00	2,660.00	100%
3	DUST ABATEMENT	LS	1	800.00	800.00			1.00	800.00			1.00	1.00	800.00	100%
4	RELOCATE SIGN	EA	1	200.00	200.00			1.00	200.00			1.00	1.00	200.00	100%
5	WATER POLLUTION CONTROL	LS	1	1,500.00	1,500.00			1.00	1,500.00			1.00	1.00	1,500.00	100%
6	TRAFFIC CONTROL SYSTEM	LS	1	4,200.00	4,200.00			1.00	4,200.00			1.00	1.00	4,200.00	100%
7	REMOVE TRAFFIC STRIPE AND PAVEMENT MARKING	SOFT	7,900	0.70	5,530.00			7,900.00	5,530.00	509.00	356.30	6,000.00	6,509.00	4,556.30	82%
8	SALVAGE ROADSIDE SIGN	EA	6	40.00	240.00			6.00	240.00			6.00	6.00	240.00	100%
9	COLD PLANE ASPHALT CONCRETE PAVEMENT	SOYD.	580	13.00	7,540.00			580.00	7,540.00			625.10	625.10	8,126.30	108%
10	CLEARING AND GRUBBING	LS	1	3,000.00	3,000.00			1.00	3,000.00			1.00	1.00	3,000.00	100%
11	DEVELOP WATER SUPPLY	LS	1	1,000.00	1,000.00			1.00	1,000.00			1.00	1.00	1,000.00	100%
12	ROADWAY EXCAVATION	CY	1,590	19.00	30,210.00			1,590.00	30,210.00	454.00	8,626.00	1,501.67	1,955.67	37,157.73	123%
13	CLASS 2 AGGREGATE BASE	CY	1,110	33.00	36,630.00			1,110.00	36,630.00	305.00	10,065.00	1,060.00	1,365.00	45,045.00	123%
14	HOT ASPHALT MIX	TON	640	80.00	51,200.00			640.00	51,200.00	72.50	5,800.00	691.52	764.02	61,121.80	119%
15	ASPHALT RUBBER HOT MIX	TON	360	99.00	35,640.00			360.00	35,640.00			391.40	391.40	38,748.80	109%
16	PLACE ASPHALT CONCRETE DIKE (CRS 212)(8')	LF	1,104	10.00	11,040.00			1,104.00	11,040.00			1,153.00	1,153.00	11,530.00	104%
17	ROADSIDE SIGN - ONE POST	EA	4	240.00	960.00			4.00	960.00			4.00	4.00	960.00	100%
18	THERMOPLASTIC PAVEMENT MARKING & CROSSWALK	SOFT	410	3.00	1,230.00			410.00	1,230.00	418.00	1,254.00	4.00	418.00	1,254.00	102%
19	PAINT TRAFFIC STRIPE 2 COAT	LF	19,800	0.35	6,930.00			19,800.00	6,930.00	21,894.00	7,662.90	21,894.00	21,894.00	7,662.90	111%
20	PAVEMENT MARKER (REFLECTIVE)	EA	596	3.25	1,937.00			596.00	1,937.00	634.00	2,060.50	634.00	634.00	2,060.50	106%
21	SIGNAL AND LIGHTING	LS	1	141,306.00	141,306.00			1.00	141,306.00	0.05	7,065.30	0.95	1.00	141,306.00	100%
22	RELOCATE CATHODIC TEST STATION (JCSD)	EA	1	800.00	800.00			1.00	800.00	1.00	800.00		1.00	800.00	100%

PROGRESS ESTIMATE RECORD - COUNTY OF RIVERSIDE

SHEET 2 of 3

Processed Construction Inspection 3/3/2010


PROJECT: Limonite Ave. & Lucetta Ave. TRS and Lighting Project  
 County Project No.: B6-0583  
 Contract No.: 09-09-005

Contractor: DBX, Inc.  
 Address: 4206 Avenida Alvarado  
 City, State, Zip: Temecula, CA 92590



Estimate No. 3 Final  
 From: December 25, 2009  
 To: February 25, 2010


Item No.	Item Description	Units	Quantity	Unit Price	Original Contract		Change Authorized		Total Authorized		This Estimate		Previous Quantity	Total Estimate To Date		% Auth.
					Amount	Quantity	Amount	Quantity	Amount	Quantity	Amount	Quantity		Amount	Quantity	
23	RELOCATE EXISTING AIR VALVE (JCSD)	EA	1	1,500.00	1,500.00				1.00	1,500.00			1.00	1,500.00	100%	
24	RAISE EXISTING AIR VALVE (JCSD)	EA	1	1,500.00	1,500.00				1.00	1,500.00				1,500.00	100%	
25	RAISE EXISTING BLOW OFF VALVE (JCSD)	EA	1	1,500.00	1,500.00				1.00	1,500.00					0%	

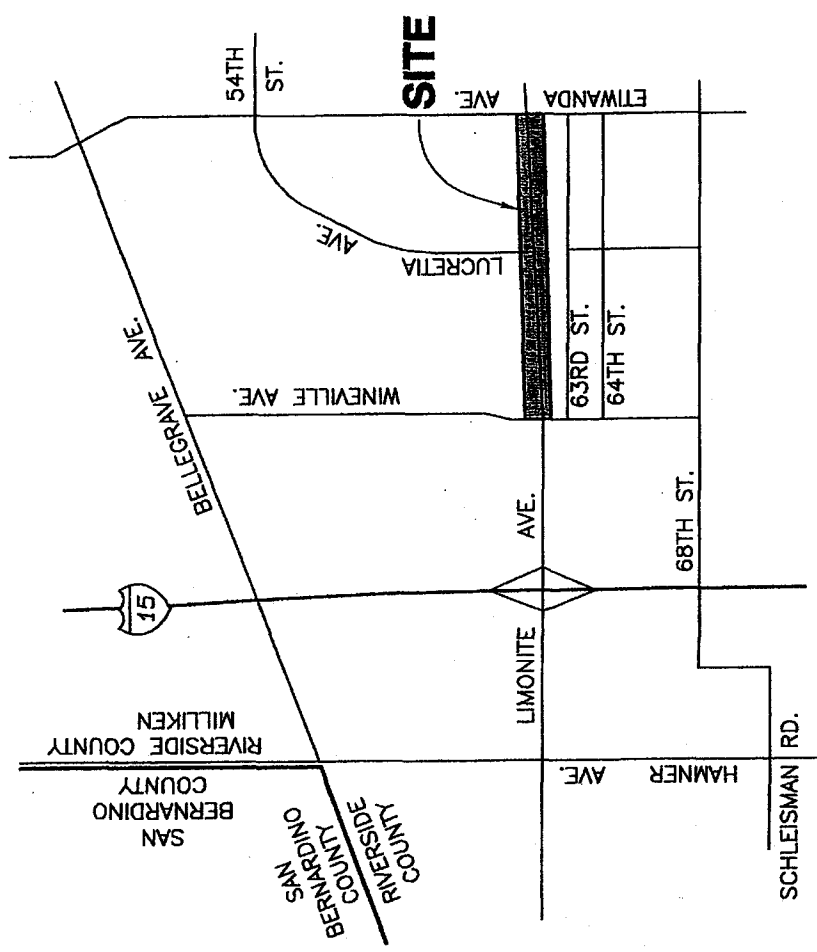

**SITE**

**VICINITY MAP**

PROJECT LENGTH = 5,200 FT  
 SECTION 29, TOWNSHIP 2 S., RANGE 6 W.  
 2008 THOMAS GUIDE PG 683, G5



NOT TO SCALE
