SUBMITTAL TO THE BOARD OF SUPERVISORS COUNTY OF RIVERSIDE, STATE OF CALIFORNIA

9H6



FROM: TLMA - Transportation Department

SUBMITTAL DATE:

August 19, 2010

SUBJECT: Notice of Completion - Resurfacing of various roads, East La Quinta area.

RECOMMENDED MOTION: That the Board execute and file the attached "Notice of Completion".

BACKGROUND: By Minute Order 3.50 of June 16, 2009, the Board entered into an agreement with Hardy & Harper, Inc. of Santa Ana, CA for the resurfacing of various roads in the East La Quinta Area of Riverside County. The originally authorized amount of the contract was \$555,000. The total amended contract amount (including quantity adjustments) is \$711,264.25 which is 28.2% more than the originally authorized amount because extra work had to be performed for grading and re-compaction of the underlying base material in order to achieve a better finished product that will last longer.

Juan C. Perez
Director of Transportation

Director of Transportation (Continued On Attached Page) **Current F.Y. Total Cost:** \$711,264 In Current Year Budget: Yes **FINANCIAL Current F.Y. Net County Cost: Budget Adjustment:** \$0 No **DATA Annual Net County Cost:** \$0 For Fiscal Year: 2010/2011 SOURCE OF FUNDS: Proposition 42 [Sales tax on Gasoline] (4.8%), Prop. **Positions To Be Deleted Per A-30** 1B [State Bond Funds] (94.3%), Measure A [Coachella Valley] (0.9%) Requires 4/5 Vote C.E.O. RECOMMENDATION:

County Executive Office Signature

Consent 🔀 Policy

Departmental Concurrence

Oep't Recomm.: Per Exec. Ofc.:

Prev. Agn. Ref. 06/16/09, Item 3.50

District: 4

Agenda Number:

3.79

The Honorable Board of Supervisors
RE: Notice of Completion - Resurfacing of various roads, East La Quinta area.
August 19, 2010
Page 2 of 2

The existing AC pavement was of such variable thickness that fine grading of the underlying surface was necessary prior to AC paving. Once the pavement was removed it was found that several unstable sub-grade areas existed and had to be stabilized.

In addition, the adjustment in compensation due to price index fluctuations of paving asphalt was applied as specified in the Special Provisions. The California Statewide Paving Asphalt Price Index was at a lower rate at the time of bid (April 2009) vs. the month and year when the asphalt concrete was placed (August 2009) which resulted in the increased compensation.

This work was completed in conformance with the plans and specifications on September 11, 2009. The work was inspected by the Construction Engineering Section of the Transportation Department. Work Order X0504.

Budget		
Original Contract Amount		\$555,000.00
Tot. Chg Orders Authorized -	9.4%	\$52,392.15
Est. Pending Change Orders	0.0%	\$0.00
Amended Contract Amount		\$607,392.15
* Quantity Adjustments	18.7%	\$103,872.10
+ CCO FA Adjustments	0.0%	\$0.00
Total Amended Contract Amount	128.2%	\$711,264.25
Expenditures		
Total Progress Payments -		\$711,264.25
Estimated Pending Payments		\$0.00
Total Expenditures		\$711,264.25
(Over)\Under Contract Amount		\$0.00

- + Change Orders using the Force Account method of payment issued prior to the work being completed generally do not use the total authorized amount.
- * <u>CAL-Trans Standard Specifications 4-1.03B</u>. Increases or decreases in the quantity of a contract item of work will be determined by comparing the total pay quantity of such item of work with the Engineer's Estimate. If the total pay quantity of any item of work required under the contract varies from the Engineers Estimate by 25 percent or less, payment will be made for the quantity of work of said item performed at contract unit price, unless eligible for adjustment pursuant to Section 4-1.03C, "Changes in Character of Work."

PLEASE COMPLETE THIS INFORMATION RECORDING REQUESTED BY:

KECIA HARPER-IHEM, CLERK OF THE BOARD RIVERSIDE CO. CLERK OF THE BOARD 4080 LEMON STREET, 1ST FLOOR CAC P O BOX 1147 - RIVERSIDE, CA 92502

MAIL STOP # 1010

AND WHEN RECORDED MAIL TO:

RETURN TO:

STOP #1010

RIVERSIDE COUNTY CLERK OF THE BOARD P. O. BOX 1147 - RIVERSIDE, CA 92502

THIS SPACE FOR RECORDERS USE ONLY

NOTICE OF COMPLETION

To be recorded with County Recorder within 10 days after completion. No recording fee.

Notice is hereby given by the undersigned owner, a public entity of the State of California, that a public work of improvement has been completed, as follows:

Project title or description of work: Resurfacing of various roads and streets

Date of Completion:

Date of this notice

Nature of owner:

County of Riverside, public entity

Interest or estate of owner:

Public Roadway

Address of owner:

4080 Lemon Street, 8th Floor, Riverside, CA 92501

Name of contractor:

Hardy & Harper, Inc.

Street or legal description of site:

Rosa Ave., Ella Ave., Rue Chateau, Rue Paray, Alvarado Avenue, Sun Swept St.,

Rue Marande, Rue Montigny, Wade St. Rue Marne, Cecil St.

Dated:	Owner: County of Riverside	
	(Name of Public Entity)	
	By:	
	Jeff Stone, Chairman, Board of Supervisors	

STATE OF CALIFORNIA)


COUNTY OF RIVERSIDE)


I am the <u>Chairman</u> of the governing board of the <u>County of Riverside</u>, the public entity which executed the foregoing notice and on whose behalf I make this verification; I have read this notice, know its contents, and the same is true. I certify under penalty of perjury that the foregoing is true and correct.

Executed at _	Riverside	, California on	(Date)
			, Jeff Stone, Chairman of the Board of Supervisors

EAST LA QUINTA AREA

RESURFACING PROJECT.



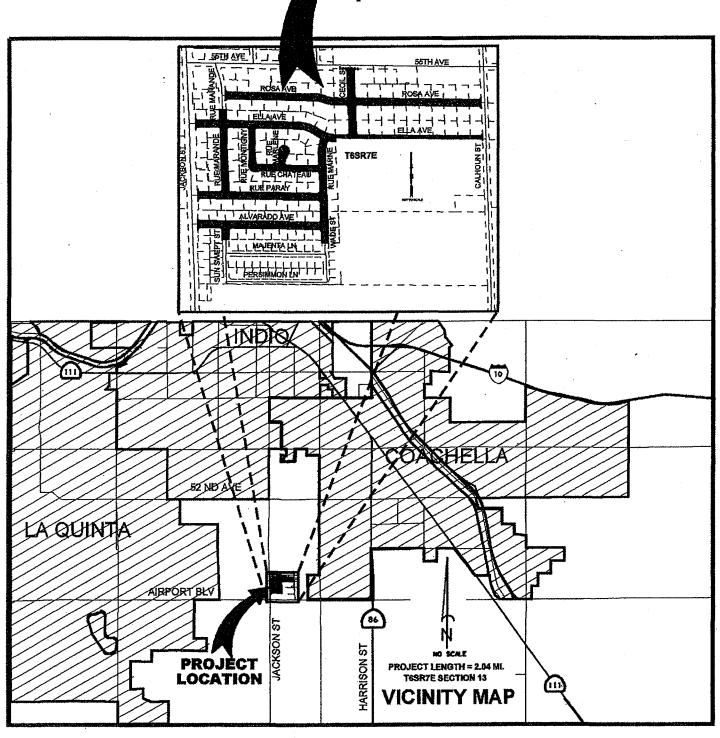

East La Quinta Ave. Contract CCO History

Contract No.	09-05-010
Work Order No.	X0504
Contract Amount	\$555,000.00
Single Maximum CCO Maximum CCO's Tip Budget	\$28,050.00 \$55,500.00

Tip Comments: No Change

CCO No.	Amount This CCO	Authority	Cumulative CCO's	% Original (Authorized		Classification
1	\$15,128.97	Trans. Director	\$15,128.97	2.73%	2.73%	Extra/Unaviodable
2	\$20,673.66	Trans. Director	\$35,802.63	3.72%	6.45%	Extra/Unaviodable
3	\$16,589.52	Trans. Director	\$52,392.15	2.99%	9.44%	Extra/Unaviodable

\$52,392.15

9.44%

New Authorized Contract Total Total CCO Dollars To Date Total % Increased by CCO's \$607,392.15 \$52,392.15 9.44%

Processed Construction Inspection 4/8/2010 January 26, 2010 March 25, 2010 711,264.25 \$711,264.25 0.0 71,126.43 \$640,137.82 96.009'909 \$33,536.86 Total Estimate To Date
Quantity Amount From: 10% ë Previous Quantity TOTAL VALUE OF WORK TO DATE: LESS RETENTION: TOTAL DUE TO DATE: LESS PREVIOUSLY INVOICED: LESS LABOR NON COMPLIANCE: TOTAL DUE THIS PAYMENT: Received by Accounts Payable: SHEET 2 of 2 37,263.18 This Estimate

Quantity Amount 607,392.15 PAYMENT APPROVAL Total Authorized Quantity Amount \$555,000.00 \$607,392.15 117% 9-11-09 Change Authorized Quantity Amount End Date: 52,392.15 Start Date: % \$ Complete: Original Contract: Amended Contract: Santa Ana, CA 92705 Hardy & Harper 1312 E. Warner Ave. \$33,536.86 555,000.00 Original Contract Amount Contractor: Address: City, State, Zip: Date: 3.40-10 25 25 100% 9 2 Ď. Days Added: Working Days: Subtotal: Days Used: % Time Elapsed: Unit Price Quantity Date: Chits Juan C. Perez, Director of Transportation Hardy & Harper PROGRESS ESTIMATE RECORD - COUNTY OF RIVERSIDE PROJECT: East La Quinta Area Resurfacing County Project No.: X0504 Item Description Quantities on This Estimate Approved Made by: Jesse Mendors Checked by: This Estimate Approved _ OK Const. Supv. _ PROJECT TOTAL Contract No.: 09-05-010

20000 Find

527980 Dept ID 31305 Account 7 X0504 F Project ___

Activity ID 23500 50

Resource Type_

Signature_

200

PROGRESS ESTIMATE RECORD - COUNTY OF RIVERSIDE PROJECT: East La Quinta Area Resurfacing

	O I I O I I I I I I I I I I I I I I I I										SHEET 1 of 2		Topessed Const	Processed Construction Inspection 6/9/2010	0,000,0
Count	Frocedor : East La Quinta Area Hesuffacing County Project No.: X0604				Contractor: Address:	Hardy & Harper					Silve I		Estimate No.	3 Final	01028
Contr	Contract No.: 09-05-010				City, State, Zip:	Santa Ana, CA 92705	92705						From:	January 26, 2010 March 25, 2010	2010
te di					Original Contract	Change Authorized	ithorized	Total Authorized	rized	This Fetimate	atemi	200			3
2	nem Lescription	Onits	Quantity	Unit Price	Amount	Quantity	Amount	Quantity	Amount	Quantity	Amount	Quantity	Quantity	Quantity Amount	Auth %
-	Class 2 Aggregate Base [Subgrade] & CCO 1	Շ	8	100.00	3,000.00	-24.00	-2,400.00	00:9	00:009		,,,,	9.00	6.00		600.00 100%
8	Hot Asphait Mix	NO.	096'9	63.00	438,480.00			6,960.00	438,480.00			8 529 20	8	537	òòò
က	Minor Concrete (Cross Gutter & Spandrel) & CCO 1	SOFT	1,110	13.00	14,430.00	-810.00	-10,530.00	300.00	3,900.00	:		300.00	300.00	3.900.00 100%	100%
4	Cold Plane Asphalt Concrete Pavement	SQYD	41,000	1.35	55,350.00			41,000.00	55,350.00			51,250.00	51,250.00	69,187.50 125%	125%
ις	Thermoplastic Pavement Marking & CCO 1	SOFT	205	2.00	1,025.00	565.00	2,825.00	770.00	3,850.00			205.00	205.00	1.025.00	27%
9	Rout and Seal Random Cracks & CCO 1	S	-	2,000.00	2,000.00	-1.00	-2,000.00								₹
^	Water Pollution Control	ST	-	2,000.00	2,000.00			1.00	2,000.00			1.00	.00	2.000.00	100%
œ	Dust Abatement	-S	-	200.00	900.00	_		1.00	200.00			1.00	100		100%
6	Traffic Control System	S	-	26,215.00	26,215.00		,	1.80	26,215.00	-		5	5	26 245 00 100%	2 %
6	Finishing Roadway [Including Match Existing Driveways	S	-	12,000.00	12,000.00			1.00	12,000.00			0.50	0:50	6,000.00	20%
8 1	CCO 1 Grading and Compaction	Ā	0	1.00	0.00	27,233.97	27,233.97	27,233.97	27,233.97			27,233.97	27,233.97	27,233.97	100%
000	Price Index Fluctuation of Paving Asphalt	AD	0	1:00	0.00	20,673.66	20,673.66	20,673.66	20,673.66	20,673.66	20,673.66		20,673.66	20,673.66	100%
CCO 3	OCO 3 Price Index Fluctuation of Paving Asphalt	AD	0	1.00	0.00	16,589.52	16,589.52	16,589.52	16,589.52	16,589.52	16,589.52		16,589.52	16,589.52 100%	,000
