

**SUBMITTAL TO THE BOARD OF SUPERVISORS
COUNTY OF RIVERSIDE, STATE OF CALIFORNIA**

439A



FROM: TLMA - Transportation Department

SUBMITTAL DATE:
July 14, 2011

SUBJECT: Notice of Completion - Emergency Storm Damage Repair, Reche Canyon Road,
North of the City of Moreno Valley

RECOMMENDED MOTION: That the Board execute and file the attached "Notice of Completion".

BACKGROUND: By Minute Order 3.37 of February 8, 2011, the Board entered into an emergency contract, with R.J. Noble, Company of Orange County, California, to provide emergency storm repair work on Reche Canyon Road, from Reche Vista to San Bernardino County Line and from Reche Vista to approximately 0.5 miles southerly of Reche Vista. The originally authorized amount of the contract was \$400,000.

Juan C. Perez
Director of Transportation

dj
(Continued On Attached Page)

FINANCIAL DATA	Current F.Y. Total Cost:	\$488,133	In Current Year Budget:	Yes
	Current F.Y. Net County Cost:	\$ 0	Budget Adjustment:	No
	Annual Net County Cost:	\$ 0	For Fiscal Year:	2011/2012

SOURCE OF FUNDS: Gas Tax (100%)	Positions To Be Deleted Per A-30	<input type="checkbox"/>
There are no general funds used in this project	Requires 4/5 Vote	<input type="checkbox"/>

C.E.O. RECOMMENDATION:

APPROVE

BY:
Tina Grande

County Executive Office Signature

Policy Policy

Consent Consent

Dept's Recomm.:
Per Exec. Ofc.:

Prev. Agn. Ref. 2/8/11, Item 3.37 | District: 5 | Agenda Number:

The Honorable Board of Supervisors

RE: Notice of Completion - Emergency Storm Damage Repair, Reche Canyon Road, North of the City of Moreno Valley

July 14, 2011

Page 2 of 2

Due to the nature of the project, repairing a storm damaged road, the actual extent of the damage could not be fully determined at time of award, and additional work needed to be done to remove sediment, restore road side ditches, and connect to driveways. The contract was based on time and materials for work performed in accordance with Caltrans Standard Specifications.

After all repairs were completed the total amended contract is \$488,133 which is 22% more than the originally authorized amount. Although the work is being paid by gas tax, we are submitting this project for Federal reimbursement due to the emergency declaration.

This work was completed at the direction of the Department on March 14, 2011, and was inspected by the Construction Engineering Section of the Transportation Department. Work Order 45-111301.

Budget

Original Contract Amount		\$400,000.00
Tot. Chg Orders Authorized -	0.0%	\$0.00
Est. Pending Change Orders	0.0%	\$0.00
Amended Contract Amount		\$400,000.00
* Quantity Adjustments	22.0%	\$88,133.20
+ CCO FA Adjustments	0.0%	\$0.00
Total Amended Contract Amount	122.0%	\$488,133.20

Expenditures

Total Progress Payments -	\$488,133.20
Estimated Pending Payments	
Total Expenditures	\$488,133.20

(Over)\Under Contract Amount \$0.00

+ Change Orders using the Force Account method of payment issued prior to the work being completed generally do not use the total authorized amount.

* CAL-Trans Standard Specifications 4-1.03B. Increases or decreases in the quantity of a contract item of work will be determined by comparing the total pay quantity of such item of work with the Engineer's Estimate. If the total pay quantity of any item of work required under the contract varies from the Engineers Estimate by 25 percent or less, payment will be made for the quantity of work of said item performed at contract unit price, unless eligible for adjustment pursuant to Section 4-1.03C, "Changes in Character of Work."

PLEASE COMPLETE THIS INFORMATION
RECORDING REQUESTED BY:

**KECIA HARPER-IHEM, CLERK OF THE BOARD
RIVERSIDE CO. CLERK OF THE BOARD
4080 LEMON STREET, 1ST FLOOR CAC
P O BOX 1147 – RIVERSIDE, CA 92502**

MAIL STOP # 1010

AND WHEN RECORDED MAIL TO:

RETURN TO: STOP #1010
RIVERSIDE COUNTY CLERK OF THE BOARD
P. O. BOX 1147 – RIVERSIDE, CA 92502

THIS SPACE FOR RECORDERS USE ONLY

NOTICE OF COMPLETION

To be recorded with County Recorder
within 10 days after completion.
No recording fee.

Notice is hereby given by the undersigned owner, a public entity of the State of California, that a public work of improvement has been completed, as follows:

Project title or description of work: Storm Damage Repairs

Date of Completion: Date of this notice

Nature of owner: County of Riverside, public entity

Interest or estate of owner: Public Roadway

Address of owner: 4080 Lemon Street, 8th Floor, Riverside, CA 92501

Name of contractor: R.J. Noble, Company

Street or legal description of site: Reche Canyon Road

Dated: _____

Owner: County of Riverside
(Name of Public Entity)

By: _____
Chairman, Board of Supervisors

STATE OF CALIFORNIA)

ss

COUNTY OF RIVERSIDE)

I am the Chairman of the governing board of the County of Riverside, the public entity which executed the foregoing notice and on whose behalf I make this verification; I have read this notice, know its contents, and the same is true. I certify under penalty of perjury that the foregoing is true and correct.

Executed at Riverside, California on _____ (Date)

_____, Chairman of the Board of Supervisors

Contractor: R.J. Noble Corporation
 Address: P.O. Box 620
 City, State, Zip: Orange, CA 92656



Estimate No. 3 Final
 From: February 28, 2011
 To: April 25, 2011

PROJECT: Reche Canyon Storm Damage Repairs
 County Project No.: 45-111301
 Contract No. 11-01-005

Item No.	Item Description	Units	Quantity	Unit Price	Original Contract Amount	Change Authorized		Total Authorized		This Estimate Quantity	Amount	Previous Quantity	Total Estimate To Date Quantity	Amount	% Auth.
						Quantity	Amount	Quantity	Amount						
1	Emergency Road Repairs, CSP, and Rip Rap	FA	400,000	1.00	400,000.00			400,000.00	400,000.00	133,570.27	133,570.27	354,562.93	488,133.20	488,133.20	122%
PROJECT TOTAL					400,000.00	0.00	400,000.00	400,000.00	400,000.00	133,570.27	133,570.27	488,133.20	488,133.20	488,133.20	122%

Made by: Trai Nguyen/Tom Nowak (Vallicoooper)

Checked by:
 OK Const. Supv.

Working Days: 30
 Days Added: 15
 Subtotal: 45
 Days Used: 45
 % Time Elapsed: 100%

Start Date: 1-10-11
 End Date: 3-14-11
 % Complete: 122%

Original Contract: \$400,000.00
 Amended Contract: \$400,000.00

TOTAL VALUE OF WORK TO DATE: \$488,133.20
 LESS RETENTION: 0% 0.00
 TOTAL DUE TO DATE: \$488,133.20
 LESS PREVIOUSLY INVOICED: 354,562.93
 LESS LABOR NON COMPLIANCE: 0.00
 TOTAL DUE THIS PAYMENT: \$133,570.27

PAYMENT APPROVAL

This Estimate Approved _____ Date: _____ for _____
 Juan Perez, Director of Transportation

Received by Accounts Payable: _____
 By: _____

Quantities on This Estimate Approved Kou Inapstad, Project Date: 5/12/11
Coordinator
 R.J. Noble Corporation

Fund 20000
 Dept ID 31305
 Account 524660
 Project Z45111301E
 Activity ID Z3602
 Resource Type CNT
 Signature
 Date 5/17/11

County of Riverside

Department of Transportation


Emergency Storm Damage Repair Work

Reche Canyon Road

**from Reche Vista Drive to San Bernardino County Line and from
Reche Vista Drive to approximately 0.5 miles southerly of Reche Vista Drive**

Project No. 45-111301

Vicinity Map

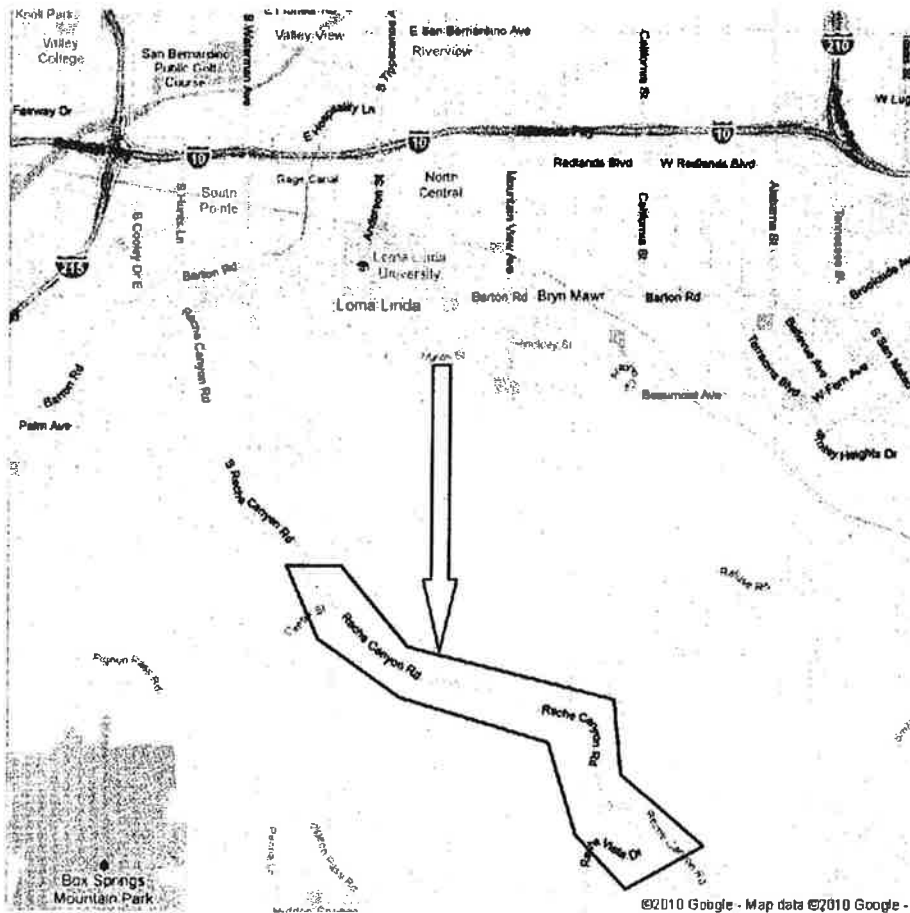

Project No. 45-111301
