

**SUBMITTAL TO THE BOARD OF SUPERVISORS
COUNTY OF RIVERSIDE, STATE OF CALIFORNIA**

719A



FROM: TLMA - Transportation Department


SUBMITTAL DATE:
October 27, 2011

SUBJECT: Notice of Completion - Limonite Avenue Median Landscape Improvements

RECOMMENDED MOTION: That the Board execute and file the attached "Notice of Completion"

BACKGROUND: By Minute Order 3.41 of February 8, 2011, the Board entered into a contract with Adame Landscape, Inc. of San Bernardino, California, for landscaping of an existing median island on Limonite Avenue, from Cedar Creek Road to Sumner Avenue in the City of Eastvale. The originally authorized amount of the contract was \$48,417. The total amended contract is \$46,458 which is 4.0% under than the originally authorized amount.

Departmental Concurrence



Juan C. Perez
Director of Transportation

dj
(Continued On Attached Page)

FINANCIAL DATA	Current F.Y. Total Cost:	\$46,458	In Current Year Budget:	Yes
	Current F.Y. Net County Cost:	\$ 0	Budget Adjustment:	No
	Annual Net County Cost:	\$ 0	For Fiscal Year:	2011/2012
SOURCE OF FUNDS: Mira Loma RBBB (88.4%), Gas Tax (11.6%)				Positions To Be Deleted Per A-30 <input type="checkbox"/>
There are no general funds used in this project				Requires 4/5 Vote <input type="checkbox"/>

C.E.O. RECOMMENDATION:

APPROVE
BY: 
Tina Grande

County Executive Office Signature

- Dep't Recomm.: Consent Policy
- Per Exec. Ofc.: Consent Policy

Prev. Agn. Ref. 2/8/11, Item 3.41 | **District:** 2 | **Agenda Number:**

3.22

This work was completed at the direction of the Department on April 20, 2011, and was inspected by the Construction Engineering Section of the Transportation Department. Work Order ZMS0006.

Budget

Original Contract Amount		\$48,417.41
Tot. Chg Orders Authorized -	0.0%	\$0.00
Est. Pending Change Orders	0.0%	\$0.00
Amended Contract Amount		\$48,417.41
* Quantity Adjustments	-4.0%	(\$1,959.08)
+ CCO FA Adjustments	0.0%	\$0.00
Total Amended Contract Amount	96.0%	<u>\$46,458.33</u>

Expenditures

Total Progress Payments -		\$46,458.33
Estimated Pending Payments		<u>\$0.00</u>
Total Expenditures		<u>\$46,458.33</u>

(Over)\Under Contract Amount \$0.00

+ Change Orders using the Force Account method of payment issued prior to the work being completed generally do not use the total authorized amount.

* CAL-Trans Standard Specifications 4-1.03B. Increases or decreases in the quantity of a contract item of work will be determined by comparing the total pay quantity of such item of work with the Engineer's Estimate. If the total pay quantity of any item of work required under the contract varies from the Engineers Estimate by 25 percent or less, payment will be made for the quantity of work of said item performed at contract unit price, unless eligible for adjustment pursuant to Section 4-1.03C, "Changes in Character of Work."

PLEASE COMPLETE THIS INFORMATION
RECORDING REQUESTED BY:

**KECIA HARPER-IHEM, CLERK OF THE BOARD
RIVERSIDE CO. CLERK OF THE BOARD
4080 LEMON STREET, 1ST FLOOR CAC
P O BOX 1147 – RIVERSIDE, CA 92502
MAIL STOP # 1010**

AND WHEN RECORDED MAIL TO:

**RETURN TO: _____ STOP #1010
RIVERSIDE COUNTY CLERK OF THE BOARD
P. O. BOX 1147 – RIVERSIDE, CA 92502**

THIS SPACE FOR RECORDERS USE ONLY

NOTICE OF COMPLETION

To be recorded with County Recorder
within 10 days after completion.
No recording fee.

Notice is hereby given by the undersigned owner, a public entity of the State of California, that a public work of improvement has been completed, as follows:

Project title or description of work: Landscape Median Improvements

Date of Completion: Date of this notice

Nature of owner: County of Riverside, public entity

Interest or estate of owner: Public Roadway

Address of owner: 4080 Lemon Street, 8th Floor, Riverside, CA 92501

Name of contractor: Adame Landscape, Inc.

Street or legal description of site: Limonite Avenue from Cedar Creek Road to Sumner Avenue

Dated: _____

Owner: County of Riverside
(Name of Public Entity)

By: _____
Chairman, Board of Supervisors

STATE OF CALIFORNIA)

ss

COUNTY OF RIVERSIDE)

I am the Chairman of the governing board of the County of Riverside, the public entity which executed the foregoing notice and on whose behalf I make this verification; I have read this notice, know its contents, and the same is true. I certify under penalty of perjury that the foregoing is true and correct.

Executed at Riverside, California on _____ (Date)

_____, Chairman of the Board of Supervisors

PROGRESS ESTIMATE RECORD - COUNTY OF RIVERSIDE

PROJECT: Lincoln Avenue Landscaping Median Improvements from Cedar Creek Road to Summer Avenue, City of Escondido
 County Project No.: Z1480008
 Contract No.: 11-01-008

Contractor: Adams Landscapes, Inc.
 Address: 41863 Juniper St., Murrieta, CA 92562
 City, State, Zip: Murrieta, CA 92562

SHEET 2 of 2 Processed Construction Inspection 7/26/2011



Estimate No. 3 Final

From: April 24, 2011
 To: July 24, 2011

Item No.	Item Description	Units	Quantity	Unit Price	Original Contract Amount	Change Authorized		Total Authorized		This Estimate		Total Estimate To Date		% Auth.
						Quantity	Amount	Quantity	Amount	Quantity	Amount	Quantity	Amount	
22	14 GAUGE DIRECT BURIAL WIRE	LF	2,300	0.45	1,035.00			2,300.00	1,035.00			2,300.00	1,035.00	100%
23	MISC. FITTINGS AND THRUST BLOCKS	LS	1	280.58	280.58			1.00	280.58			1.00	280.58	100%
PROJECT TOTAL									48,417.41				46,456.33	

Made by: Bill Jackson
 Checked by:
 OK Const. Supv.

Working Days: 25
 Days Added: 0
 Subtotal: 25
 Days Used: 23
 % Time Elapsed: 92%

Start Date: 3-14-11
 End Date: 4-20-11
 % Complete: 96%
 Original Contract: \$48,417.41
 Amended Contract: \$48,417.41

TOTAL VALUE OF WORK TO DATE: \$46,456.33
 LESS RETENTION: 10% 4,645.63
 TOTAL DUE TO DATE: \$41,812.50
 LESS PREVIOUSLY INVOICED: 41,208.45
 TOTAL DUE THIS PAYMENT: 608.05

This Estimate Approved _____ Date: _____ for _____

Juan C. Perez, Director of Transportation

PAYMENT APPROVAL

Received by Accounts Payable: _____
 By: _____

Fund 20000

Dept ID 31304

Account 527980

Project ZMS0006

Activity ID Z5515

Quantities on This Estimate Approved Date: 10-14-11

Adams Landscapes, Inc.

Resource Type CLM

Signature

Date 10/17/11




Contractor: Adams Landscapes, Inc.
 Address: 41883 Juniper St., Murrieta, CA 92562
 City, State, Zip: Murrieta, CA 92562

Estimate No. 3 Final
 From: April 26, 2011
 To: July 26, 2011

Item No.	Item Description	Units	Quantity	Unit Price	Original Contract Amount	Change Authorized		Total Authorized		This Estimate		Previous		% Auth.
						Quantity	Amount	Quantity	Amount	Quantity	Amount	Quantity	Amount	
1	DUST ABATEMENT	LS	1	1,122.30	1,122.30			1.00	1,122.30			1.00	1,122.30	100%
2	WATER POLLUTION CONTROLS	LS	1	5,611.50	5,611.50			1.00	5,611.50			1.00	5,611.50	100%
3	FINE GRADING	SOFT	9,655	0.08	772.40			9,655.00	772.40			9,655.00	772.40	100%
4	SOIL PREPARATION (AMENDMENTS, FERTILIZERS & WEED PREPARATION)	SOFT	9,655	0.08	772.40			9,655.00	772.40			9,655.00	772.40	100%
5	MULCHING (RECYCLED ORGANIC) - 3" THICK	SOFT	9,655	0.37	3,572.35			9,655.00	3,572.35			9,655.00	3,572.35	100%
6	5 GALLON SHRUBS	E	244	15.71	3,833.24			244.00	3,833.24			244.00	3,833.24	100%
7	1 GALLON SHRUBS	E	1,644	5.05	8,302.20			1,644.00	8,302.20			1,644.00	8,302.20	100%
8	12" MAINTENANCE STRIP/WALK - NATURAL COLOR WITH BRDM FINISH	SOFT	1,625	7.07	11,488.75			1,625.00	11,488.75			1,625.00	11,488.75	81%
9	MAINTENANCE (3 MONTHS)	LS	1	673.38	673.38			1.00	673.38	1.00	673.38		673.38	100%
10	1812 POP-UP SPRAY HEAD, SWING JOINT, CHECK VALVE, PRESSURE REGULATOR, ROTATING NOZZLE	EA	144	37.60	5,414.40			144.00	5,414.40			144.00	5,414.40	100%
11	ELECTRIC CONTROL VALVE W/FITTINGS - 1 1/2"	EA	2	280.58	561.16			2.00	561.16			2.00	561.16	100%
12	PVC BALL VALVE AT QUICK COUPLER - 1"	EA	3	58.12	168.36			3.00	168.36			3.00	168.36	100%
13	PVC BALL VALVE AT VALVE - 1 1/2"	EA	2	28.08	56.12			2.00	56.12			2.00	56.12	100%
14	NIBCO T-113-K BRONZE GATE VALVE - 2"	EA	1	505.04	505.04			1.00	505.04			1.00	505.04	100%
15	QUICK COUPLING VALVE	EA	3	168.35	505.05			3.00	505.05			3.00	505.05	100%
16	PURPLE PLASTIC 10" ROUND VALVE BOX W/SUMP, FILTER FABRIC	EA	7	15.15	106.05			7.00	106.05			7.00	106.05	100%
17	PURPLE PLASTIC STANDARD RECTANGULAR VALVE BOX W/SUMP, FILTER FABRIC	EA	3	28.08	84.18			3.00	84.18			3.00	84.18	100%
18	PURPLE NON-PRESSURE LATERAL LINE - SCH 40 - 3/4"	LF	950	0.39	370.50			950.00	370.50			950.00	370.50	100%
19	PURPLE NON-PRESSURE LATERAL LINE - SCH 40 - 1"	LF	850	0.62	527.00			850.00	527.00			850.00	527.00	86%
20	PURPLE NON-PRESSURE LATERAL LINE - SCH 40 - 1 1/4"	LF	50	0.84	42.00			50.00	42.00			50.00	42.00	100%
21	PURPLE NON-PRESSURE LATERAL LINE - SCH 40 - 2 1/2"	LF	665	3.83	2,613.45			665.00	2,613.45			665.00	2,613.45	89%

LIMONITE AVE. LANDSCAPE MEDIAN
FROM CEDAR CREEK ROAD TO SUMNER AVENUE
PROJECT NO. ZMS0006

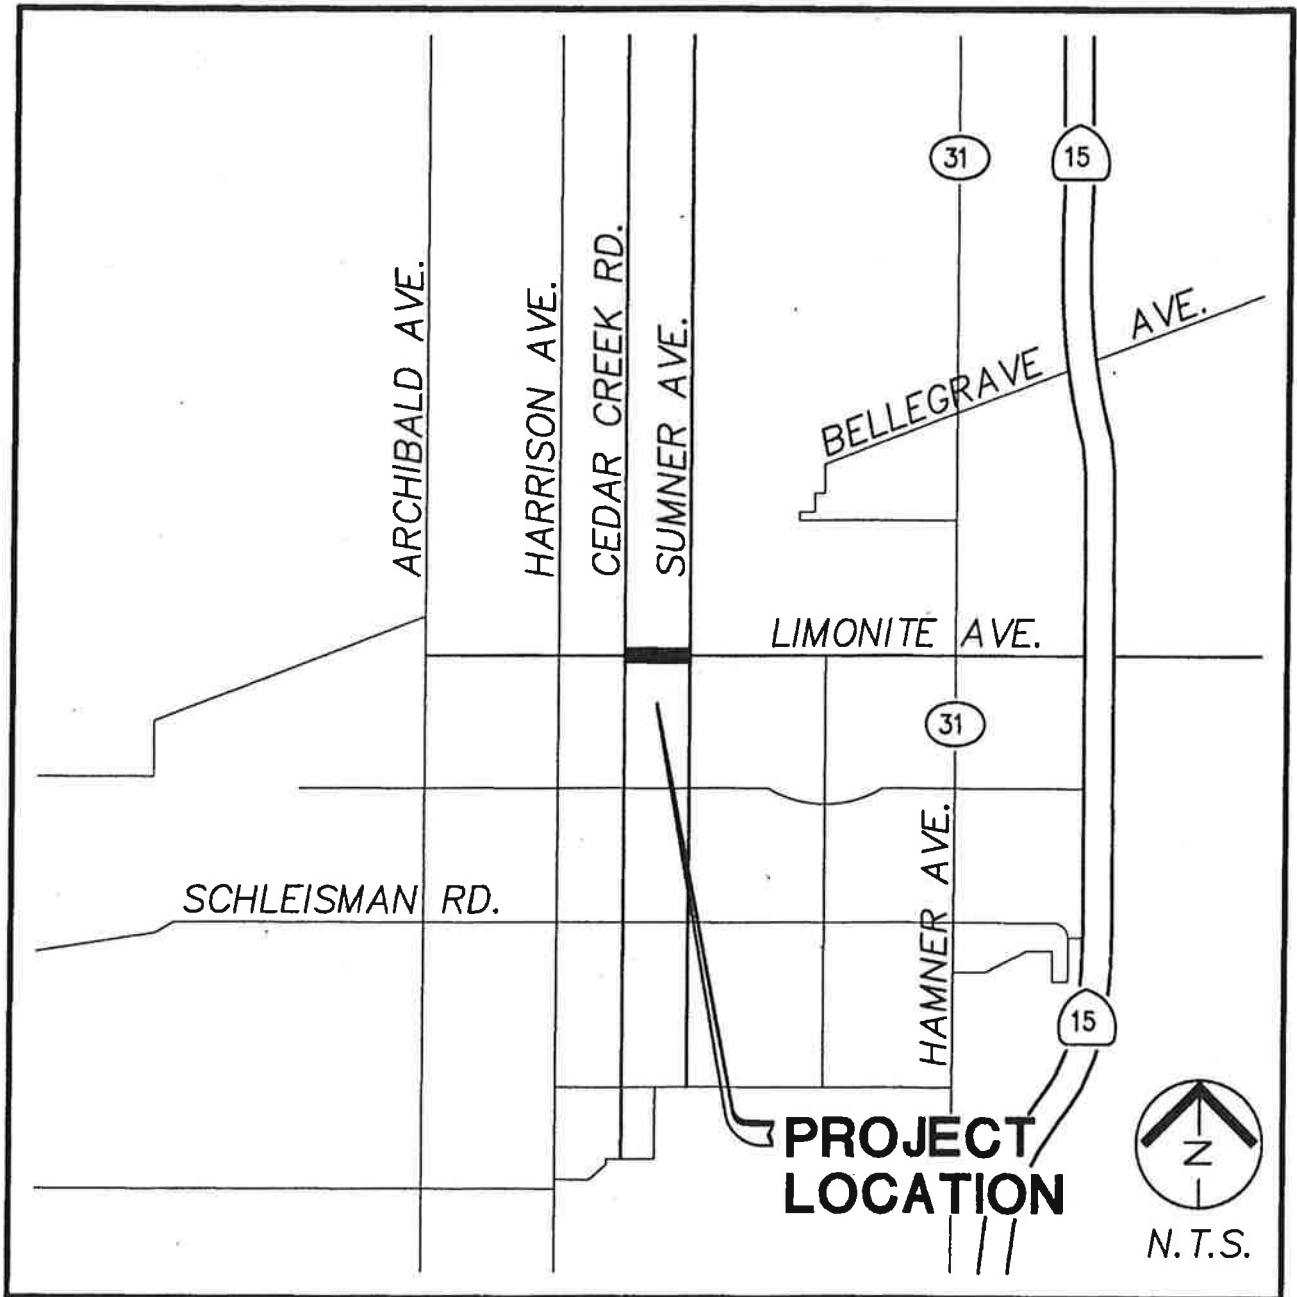

SECTION 23, TOWNSHIP 2 SOUTH, RANGE 7 WEST
VICINITY MAP
