

**SUBMITTAL TO THE BOARD OF SUPERVISORS  
COUNTY OF RIVERSIDE, STATE OF CALIFORNIA**

401A



**FROM:** TLMA – Transportation Department

**SUBMITTAL DATE:**  
September 2, 2014

**SUBJECT:** Notice of Completion – Gilman Springs Road Roadway Improvements, Eastern Moreno Valley, 5th/5th District [\$4,774,024]; Federal Funds 19%, Local Funds 81%

**RECOMMENDED MOTION:** That the Board of Supervisors execute and file the attached “Notice of Completion.”

**BACKGROUND:**

**Summary**

By Minute Order 3-92 of September 10, 2013, the Board of Supervisors entered into a contract with Griffith Company of Santa Fe Springs, CA for the construction of safety and maintenance improvements along Gilman Springs Road in the eastern Moreno Valley area of Riverside County.

Patricia Romo  
Assistant Director of Transportation  
for Juan C. Perez  
Director of Transportation and Land Management

Departmental Concurrence

FINANCIAL DATA	Current Fiscal Year:	Next Fiscal Year:	Total Cost:	Ongoing Cost:	POLICY/CONSENT (Per Exec. Office)
<b>COST</b>	\$ 4,774,024	\$ 0	\$ 4,774,024	\$ 0	Consent <input type="checkbox"/> Policy <input checked="" type="checkbox"/>
<b>NET COUNTY COST</b>	\$ 0	\$ 0	\$ 0	\$ 0	
<b>SOURCE OF FUNDS:</b> HSIP-Highway Safety Improvement Program (19%); Proposition 42, Sales Tax on Gasoline (0.8%), Proposition 1B (State Bond Funds-Local Roads) (16.3%); Gas Tax (ABX8-9 Mar 2010 New HUTA) (35.7%); Measure A/Western (18.8%); City of Moreno Valley (9.4%) There were no general funds used in this project.					<b>Budget Adjustment:</b> No
					<b>For Fiscal Year:</b> 2014-2015

**C.E.O. RECOMMENDATION:**

APPROVE

BY:

Tina Grande

County Executive Office Signature

**MINUTES OF THE BOARD OF SUPERVISORS**

- Positions Added
- Change Order
- A-30
- 4/5 Vote

Prev. Agn. Ref.: 09/10/13, Item 3-92

District: 5/5

Agenda Number:

3-65

**SUBMITTAL TO THE BOARD OF SUPERVISORS, COUNTY OF RIVERSIDE, STATE OF CALIFORNIA**  
**FORM 11:** Notice of Completion – Gilman Springs Road Roadway Improvements, Eastern Moreno Valley, 5th/5th District [\$4,774,024]; Federal Funds 19%, Local Funds 81%  
**DATE:** September 2, 1014  
**PAGE:** 2 of 3

**BACKGROUND:**

**Summary (continued)**

The originally authorized amount of the contract was \$4,985,803. The total amended contract is \$4,774,024, which is 4.2% less than the originally authorized amount.

This work was completed at the direction of the Transportation Department on December 13, 2013, Work Order numbers C0-0531 and C2-0140, HSIPL-5956(204).

**Impact on Residents and Businesses**

This project consisted of improvements, which have increased commuter safety. These improvements include curve realignments, shoulder widening, construction of passing lane, construction of a left turn pocket at Alessandro Boulevard, pavement rehabilitation, and installation of drainage and safety improvements.

**SUPPLEMENTAL:**

**Additional Fiscal Information**

**Budget**

Original Contract Amount		\$4,985,803
Total Change Orders Authorized	0.0%	\$0
Estimated Pending Change Orders	0.0%	\$0
Authorized Contract Amount		\$4,985,803
* Quantity Adjustments	-4.2%	(\$211,779)
+ CCO FA Adjustments	0.0%	\$0
Total Amended Contract Amount	95.8%	\$4,774,024

**Expenditures**

Total Progress Payments	\$4,774,024
Estimated Pending Payments	\$0
Total Expenditures	\$4,774,024

**(Over)/Under Contract Amount** \$0

+ Change Orders using the Force Account method of payment issued prior to the work being completed generally do not use the total authorized amount.

\* CAL-Trans Standard Specifications 4-1.03B. Increases or decreases in the quantity of a contract item of work will be determined by comparing the total pay quantity of such item of work with the Engineer's Estimate. If the total pay quantity of any item of work required under the contract varies from the Engineer's Estimate by 25 percent or less, payment will be made for the quantity of work of said item performed at the contract unit price, unless eligible for adjustment pursuant to Section 4-1.03C, "Changes in Character of Work."

**SUBMITTAL TO THE BOARD OF SUPERVISORS, COUNTY OF RIVERSIDE, STATE OF CALIFORNIA**  
**FORM 11:** Notice of Completion – Gilman Springs Road Roadway Improvements, Eastern Moreno Valley, 5th/5th District [\$4,774,024]; Federal Funds 19%, Local Funds 81%  
**DATE:** September 2, 1014  
**PAGE:** 3 of 3

The Gilman Springs Road Improvements Project was funded with \$907,064 of Highway Safety Improvement Program funds, \$38,192 of Proposition 42 funds, \$778,166 of Proposition 1B funds, \$1,704,327 of Gas Tax funds, \$897,517 of Measure A/Western funds and \$448,758 of City of Moreno Valley funds.

**Contract History and Price Reasonableness**


N/A

COUNTY OF RIVERSIDE  
DEPARTMENT OF TRANSPORTATION

GILMAN SPRINGS ROAD

ROADWAY IMPROVEMENTS  
EASTERN MORENO VALLEY AREA

PROJECT No. C2-0140 AND  
PROJECT No. C0-0531, FEDERAL AID No. HSIPL-5956 (204)

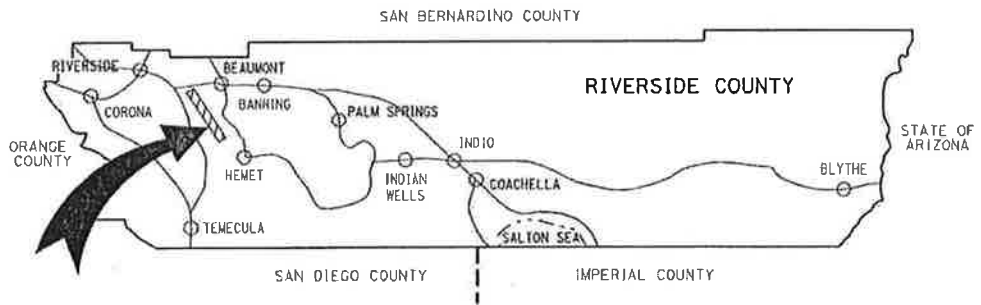

VICINITY MAP

TOWNSHIP 3S RANGE 2W BETWEEN SECTIONS 8 AND 28  
COUNTY ROAD BOOK PAGES No. 87 AND 95

PROJECT: Gilman Springs Road (Eastern Moreno Valley)  
 County Project No.: CD-4531(HS/PL-5956(204)) & C2-0140  
 Contract No. 13-08-006

Contractor: Griffin Company  
 Address: 12200 Bloomfield Ave.  
 City, State, Zip: Santa Fe Springs, CA 90670

Item No.	Item Description	Units	Quantity	Unit Price	Original Contract Amount	Change Authorized Quantity	Change Authorized Amount	Total Authorized Quantity	Total Authorized Amount	This Estimate Quantity	This Estimate Amount	Previous Quantity	Total Estimate To Date Quantity	Total Estimate To Date Amount	% Auth.
					4,985,802.50	0.00	0.00	4,985,802.50	4,985,802.50		13,665.41			4,774,023.67	
<b>PROJECT TOTAL</b>															

Made by: Gabriel Munoz/Alec Yzaquiere  
 Checked by: [Signature] 4-9-14  
 OK Const. Supv: [Signature] 4-9-14

Working Days: 10-15-13  
 Days Added: 12-13-13  
 Subtotal: 96%  
 Days Used: 60  
 % Time Elapsed: 100%

Start Date: 10-15-13  
 End Date: 12-13-13  
 % Complete: 96%  
 Original Contract: \$4,985,802.50  
 Amended Contract: \$4,985,802.50

TOTAL VALUE OF WORK TO DATE: \$4,774,023.67  
 LESS RETENTION: 0%  
 TOTAL DUE TO DATE: \$4,774,023.67  
 LESS PREVIOUSLY INVOICED: 4,760,358.26  
 LESS LABOR NON COMPLIANCE: 0.00  
 TOTAL DUE THIS PAYMENT: \$13,665.41


This Estimate Approved \_\_\_\_\_ Date: \_\_\_\_\_ for: \_\_\_\_\_  
 Juan Perez, Director of Transportation and Land Management

Received by Accounts Payable: \_\_\_\_\_  
 By: \_\_\_\_\_

Quantities on This Estimate Approved [Signature] Date: 8/11/14  
 Griffin Company

**PAYMENT APPROVAL**  
 Fund 20000  
 Dept ID 31305  
 Account 527980  
 Project ZCO-0531E  
 Activity ID Z3500

Resource Type CNT  
 Signature [Signature]  
 Date 8/11/14



Contractor:  
Griffith Company  
12200 Bloomfield Ave.  
Santa Fe Springs, CA 90670

Estimate No. 7 Final  
From: February 26, 2014  
To: March 25, 2014

PROJECT: Gilman Springs Road (Eastern Moreno Valley)  
County Project No.: CD-0631(11S)PL-5956(204) & C2-0140  
Contract No. 13-06-005

Item No.	Item Description	Units	Quantity	Unit Price	Original Contract Amount	Change Authorized		Total Authorized		This Estimate Quantity	This Estimate Amount	Previous Quantity	Total Estimate To Date		% Auth.
						Quantity	Amount	Quantity	Amount				Quantity	Amount	
1	DUST ABATEMENT	LS	1	15,000.00	15,000.00			1.00	15,000.00	1.00		1.00	1.00	15,000.00	100%
2	TRAFFIC CONTROL SYSTEM	LS	1	349,500.00	349,500.00			1.00	349,500.00	1.00		1.00	1.00	349,500.00	100%
3	WATER POLLUTION CONTROL	LS	1	75,000.00	75,000.00			1.00	75,000.00	1.00		1.00	1.00	75,000.00	100%
4	PORTABLE CHANGEABLE MESSAGE SIGNS	EA	8	4,000.00	32,000.00			8.00	32,000.00	7.00		7.00	7.00	28,000.00	88%
5(F)	IMPORTED BORROW	CY	13,320	17.00	226,440.00			13,320.00	226,440.00	13,268.80		13,268.80	13,268.80	225,569.60	100%
6(F)	ROADWAY EXCAVATION	CY	8,000	20.00	160,000.00			8,000.00	160,000.00	8,000.00		8,000.00	8,000.00	160,000.00	100%
7	CLEARING AND GRUBBING	LS	1	15,000.00	15,000.00			1.00	15,000.00	1.00		1.00	1.00	15,000.00	100%
8	DEVELOP WATER SUPPLY	LS	1	10,000.00	10,000.00			1.00	10,000.00	1.00		1.00	1.00	10,000.00	100%
9	CLASS 2 AGGREGATE BASE	CY	14,390	20.00	287,800.00			14,390.00	287,800.00	14,778.26		14,778.26	14,778.26	295,565.20	103%
10	HOT MIX ASPHALT (TYPE C)	TON	21,224	60.00	1,273,440.00			21,224.00	1,273,440.00	21,505.17		21,505.17	21,505.17	1,290,310.20	101%
11	METAL BEAM GUARD RAILING (7" WOOD POST)	LF	712	75.00	53,400.00			712.00	53,400.00	726.00		726.00	726.00	54,450.00	102%
12	TERMINAL SYSTEM (TYPE SRT)	EA	10	3,500.00	35,000.00			10.00	35,000.00	10.00		10.00	10.00	35,000.00	100%
13	TERMINAL SYSTEM (TYPE SKT)	EA	2	4,500.00	9,000.00			2.00	9,000.00	2.00		2.00	2.00	9,000.00	100%
14	36" CORRUGATED STEEL PIPE (.064" THICK)	LF	324	300.00	97,200.00			324.00	97,200.00	391.00		391.00	391.00	117,300.00	121%
15	24" CORRUGATED STEEL PIPE (.064" THICK)	LF	199	200.00	39,800.00			199.00	39,800.00	199.00		199.00	199.00	39,800.00	100%
16	PLACE ASPHALT CONCRETE DIKE (CRS 2'12")	LF	720	8.00	5,760.00			720.00	5,760.00	885.00		885.00	885.00	7,080.00	123%
17	PLACE ASPHALT CONCRETE DIKE (TYPE E)	LF	505	8.00	4,040.00			505.00	4,040.00	601.00		601.00	601.00	4,808.00	119%
18	PLACE ASPHALT CONCRETE DIKE (TYPE C)	LF	170	8.00	1,360.00			170.00	1,360.00	169.00		169.00	169.00	1,352.00	99%
19	PLACE ASPHALT CONCRETE DIKE (TYPE F)	LF	535	8.00	4,280.00			535.00	4,280.00	534.00		534.00	534.00	4,272.00	100%
20	EXTEND 4' X 4' REINFORCED CONCRETE BOX CULVERT	LF	39	2,000.00	78,000.00			39.00	78,000.00	39.00		39.00	39.00	78,000.00	100%

PROJECT: Gilman Springs Road (Eastern Moreno Valley)  
 County Project No.: C0-0531(HSPL-5856(2014)) & C2-0140  
 Contract No. 13-08-005

Contractor: Griffin, Company  
 Address: 12200 Bloomfield Ave.  
 City, State, Zip: Santa Fe Springs, CA 90670

Estimate No. 7 Final  
 From: February 26, 2014  
 To: March 25, 2014

Item No.	Item Description	Units	Quantity	Unit Price	Original Contract Amount	Change Authorized		Total Authorized		This Estimate Quantity	This Estimate Amount	Previous Quantity	Total Estimate To Date Quantity	Total Estimate To Date Amount	% Auth.
						Quantity	Amount	Quantity	Amount						
21	EXTEND 7x6' REINFORCED CONCRETE BOX CULVERT	LF	50	3,500.00	175,000.00			50.00	175,000.00			52.00	52.00	182,000.00	104%
22	ASPHALT CONCRETE OVERSIDE DRAIN	EA	7	3,000.00	21,000.00			7.00	21,000.00			7.00	7.00	21,000.00	100%
23	Class 1 CONCRETE STRUCTURE HEADWALL PER CALTF	EA	15	7,500.00	112,500.00			15.00	112,500.00			17.00	17.00	127,500.00	113%
24	ROADSIDE SIGN - ONE POST	EA	25	400.00	10,000.00			25.00	10,000.00			25.00	25.00	10,000.00	100%
25	SALVAGE ROADSIDE SIGN	EA	19	45.00	855.00			19.00	855.00			19.00	19.00	855.00	100%
26	RELOCATE SIGN	EA	4	100.00	400.00			4.00	400.00			4.00	4.00	400.00	100%
27	DELINEATOR (CLASS 1)(TYPE F)	EA	45	65.00	2,925.00			45.00	2,925.00			55.00	55.00	3,575.00	122%
28	RUMBLE STRIP AND STRIPE	LF	38,260	0.50	19,130.00			38,260.00	19,130.00			39,370.00	39,370.00	19,685.00	103%
29	CONSTRUCT MODIFIED TYPE 1-A (18") FOUNDATION AND	LS	1	5,000.00	5,000.00			1.00	5,000.00			1.00	1.00	5,000.00	100%
30	INSTALL SIGN (STRAP AND SADDLE BRACKET METHOD)	EA	1	250.00	250.00			1.00	250.00			1.00	1.00	250.00	100%
31	THERMOPLASTIC CROSSWALK AND PAVEMENT MARKIN	SOFT	210	6.00	1,260.00			210.00	1,260.00			240.00	240.00	1,440.00	114%
32	PAINT TRAFFIC STRIPE (2-COAT)	LF	43,000	0.25	10,750.00			43,000.00	10,750.00			43,465.00	43,465.00	10,871.50	101%
33	PAVEMENT MAKERS (REFLECTIVE)	EA	1,170	3.00	3,510.00			1,170.00	3,510.00			1,109.00	1,109.00	3,327.00	95%
34	DE-MOBILIZATION	LS	1	218,000.00	218,000.00			1.00	218,000.00			1.00	1.00	218,000.00	100%
35	MOBILIZATION	LS	1	213,000.00	213,000.00			1.00	213,000.00			1.00	1.00	213,000.00	100%
36	HOT MIX ASPHALT (TYPE A)	TON	60	300.00	18,000.00			60.00	18,000.00			50.43	50.43	15,129.00	84%
37	12" CORRUGATED STEEL PIPE DOWNDRAIN (.064" THICK)	LF	80	200.00	16,000.00			80.00	16,000.00			80.00	80.00	16,000.00	100%
38	OBJECT MARKER (TYPE L-1)	EA	20	60.00	1,200.00			20.00	1,200.00			25.00	25.00	1,500.00	125%
39	EROSION CONTROL (BONDED FIBER MATRIX WITH SEED)	ACRE	4	5,000.00	20,000.00			4.00	20,000.00			5.00	5.00	25,000.00	125%
40	ROCK SLOPE PROTECTION (1/4 TON, METHOD B)	CY	8	750.00	6,000.00			8.00	6,000.00			8.00	8.00	6,000.00	100%

PROJECT: Gilman Springs Road (Eastern Moreno Valley)  
 County Project No.: C0-4531(HS)PL-5556(204) & C2-0140  
 Contract No. 13-08-005



Contractor: Griffin Company  
 Address: 12300 Bloomfield Ave.  
 City, State, Zip: Santa Fe Springs, CA 90670

Estimate No. 7 Final  
 From: February 26, 2014  
 To: March 26, 2014

Item No.	Item Description	Units	Quantity	Unit Price	Original Contract Amount	Change Authorized Quantity	Amount	Total Authorized Quantity	Amount	This Estimate Quantity	Amount	Previous Quantity	Total Estimate To Date Quantity	Amount	% Auth.
41	RESIDENT ENGINEER'S OFFICE	LS	1	20,000.00	20,000.00	1.00	20,000.00	1.00	20,000.00			1.00	1.00	20,000.00	100%
42	CONSTRUCTION PROJECT FUNDING IDENTIFICATION SIGN	EA	2	2,500.00	5,000.00	2.00	5,000.00	2.00	5,000.00			2.00	2.00	5,000.00	100%
43	ENCROACHMENT PERMIT	FA	1	10,000.00	10,000.00	1.00	10,000.00	1.00	10,000.00			0.11	0.11	1,066.00	11%
44	SUBGRADE ENHANCEMENT FABRIC (GEOGRID)	SQYD	6,550	2.50	16,375.00	6,550.00	16,375.00	6,550.00	16,375.00			6,572.00	6,572.00	16,430.00	100%
45 A	MISCELLANEOUS DIRECTED WORK	FA	1	250,000.00	250,000.00	1.00	250,000.00	1.00	250,000.00	0.05	13,665.41	0.14352884	0.19819048	49,547.62	20%
45 B	TEMPORARY FENCE (TYPE ESA)	LF	4,820	6.00	28,920.00	4,820.00	28,920.00	4,820.00	28,920.00			4,825.00	4,825.00	28,950.00	100%
45 C	CONSTRUCTION ZONE ENHANCEMENT ENFORCEMENT	FA	1	50,000.00	50,000.00	1.00	50,000.00	1.00	50,000.00			1.00	1.00	49,975.80	100%
46(F)	IMPORTED BORROW	CY	70	17.00	1,190.00	70.00	1,190.00	70.00	1,190.00			70.00	70.00	1,190.00	100%
47(F)	ROADWAY EXCAVATION	CY	1,170	20.00	23,400.00	1,170.00	23,400.00	1,170.00	23,400.00			1,170.00	1,170.00	23,400.00	100%
48	CLASS 2 AGGREGATE BASE	CY	760	20.00	15,200.00	760.00	15,200.00	760.00	15,200.00			785.00	785.00	15,700.00	103%
49	HOT MIX ASPHALT (TYPE C)	TON	5,725	60.00	343,500.00	5,725.00	343,500.00	5,725.00	343,500.00			4,480.22	4,480.22	268,813.20	78%
50	PLACE ASPHALT CONCRETE DIKE (CRS 212) (6")	LF	430	8.00	3,440.00	430.00	3,440.00	430.00	3,440.00			535.00	535.00	4,280.00	124%
51	ASPHALT CONCRETE OVERSIDE DRAIN	EA	2	3,000.00	6,000.00	2.00	6,000.00	2.00	6,000.00			2.00	2.00	6,000.00	100%
52	ROADSIDE SIGN - ONE POST	EA	5	400.00	2,000.00	5.00	2,000.00	5.00	2,000.00			5.00	5.00	2,000.00	100%
53	SALVAGE ROADSIDE SIGN	EA	1	45.00	45.00	1.00	45.00	1.00	45.00			1.00	1.00	45.00	100%
54	RELOCATE SIGN	EA	4	100.00	400.00	4.00	400.00	4.00	400.00			4.00	4.00	400.00	100%
55	DELINEATOR (CLASS 1) (TYPE F)	EA	5	65.00	325.00	5.00	325.00	5.00	325.00			6.00	6.00	390.00	120%
56	RUMBLE STRIP AND STRIPE	LF	12,650	0.50	6,325.00	12,650.00	6,325.00	12,650.00	6,325.00			12,700.00	12,700.00	6,350.00	100%
57	THERMOPLASTIC CROSSWALK AND PAVEMENT MARKING	SQFT	160	6.00	960.00	160.00	960.00	160.00	960.00			197.00	197.00	1,182.00	123%
58	PAINT TRAFFIC STRIPE (2-COAT)	LF	14,800	0.25	3,700.00	14,800.00	3,700.00	14,800.00	3,700.00			14,800.00	14,800.00	3,700.00	100%





PROJECT: Gilman Springs Road (Eastern Moreno Valley)  
 County Project No.: CO-0631(HS/PL-5968(204)) & C2-0140  
 Contract No. 13-08-005

Contractor: Griffith Company  
 12200 Bloomfield Ave.  
 Santa Fe Springs, CA 90670

Estimate No. 7 Final  
 From: February 26, 2014  
 To: March 25, 2014

Item No.	Item Description	Units	Quantity	Unit Price	Original Contract Amount	Change Authorized Quantity	Change Authorized Amount	Total Authorized Quantity	Total Authorized Amount	This Estimate		Total Estimate To Date		% Auth.
										Quantity	Amount	Quantity	Amount	
59	PAVEMENT MAKERS (REFLECTIVE)	EA	365	3.00	1,095.00			365.00	1,095.00	365.00	365.00	1,095.00	100%	
60	HOT MIX ASPHALT (TYPE A)	TON	40	300.00	12,000.00			40.00	12,000.00	35.00	35.00	10,500.00	88%	
61	12" CORRUGATED STEEL PIPE DOWNDRAIN (.064" THICK)	LF	27	200.00	5,400.00			27.00	5,400.00	27.00	27.00	5,400.00	100%	
62	OBJECT MARKER (TYPE L-1)	EA	8	60.00	480.00			8.00	480.00	8.00	8.00	480.00	100%	
63	SHOULDER BACKING	LF	9,350	4.00	37,400.00			9,350.00	37,400.00	9,320.00	9,320.00	37,280.00	100%	
64	EROSION CONTROL (TYPE D)	ACRE	2	5,000.00	10,000.00			2.00	10,000.00	2.00	2.00	10,000.00	100%	
65A	GRINDING ASPHALT CONCRETE IN PLACE	SQYD	13,900	0.60	8,340.00			13,900.00	8,340.00	14,215.00	14,215.00	8,529.00	102%	
65B	TEMPORARY FENCE (TYPE ESA)	LF	670	6.00	4,020.00			570.00	4,020.00	780.00	780.00	4,680.00	116%	
66(F)	ROADWAY EXCAVATION	CY	2,570	20.00	51,400.00			2,570.00	51,400.00	2,570.00	2,570.00	51,400.00	100%	
67	CLASS 2 AGGREGATE BASE	CY	2,420	20.00	48,400.00			2,420.00	48,400.00	2,259.00	2,259.00	45,180.00	93%	
68	HOT MIX ASPHALT (TYPE C)	TON	3,304	60.00	198,240.00			3,304.00	198,240.00	3,414.98	3,414.98	204,898.80	103%	
69	PLACE ASPHALT CONCRETE DIKE (TYPE E)	LF	1,200	8.00	9,600.00			1,200.00	9,600.00	1,412.00	1,412.00	11,296.00	116%	
70	ASPHALT CONCRETE OVERSIDE DRAIN	EA	3	3,000.00	9,000.00			3.00	9,000.00	3.00	3.00	9,000.00	100%	
71	SALVAGE ROADSIDE SIGN	EA	1	45.00	45.00			1.00	45.00	1.00	1.00	45.00	100%	
72	DELINEATOR (CLASS 1) (TYPE F)	EA	7	65.00	455.00			7.00	455.00	8.00	8.00	520.00	114%	
73	THERMOPLASTIC CROSSWALK AND PAVEMENT MARKIN	SQFT	70	6.00	420.00			70.00	420.00	75.00	75.00	450.00	107%	
74	PAINT TRAFFIC STRIPE (2-COAT)	LF	6,850	0.25	1,712.50			6,850.00	1,712.50	6,631.00	6,631.00	1,657.75	97%	
75	PAVEMENT MAKERS (REFLECTIVE)	EA	230	3.00	690.00			230.00	690.00	190.00	190.00	570.00	83%	
76	HOT MIX ASPHALT (TYPE A)	TON	40	300.00	12,000.00			40.00	12,000.00	35.00	35.00	10,500.00	88%	
77	SUBGRADE ENHANCEMENT FABRIC (GEOGRID)	SQYD	10,900	2.50	27,250.00			10,900.00	27,250.00	10,880.00	10,880.00	27,200.00	100%	



Griffith Company  
12200 Bloomfield Ave.  
Santa Fe Springs, CA 90670

Estimate No. 7 Final  
From: February 26, 2014  
To: March 25, 2014

PROJECT: Gilman Springs Road (Eastern Moreno Valley)  
County Project No.: CO-0531(HIS/PL-5566(204)) & C2-0140  
Contract No. 13-08-005

Contractor:  
Address:  
City, State, Zip:

Item No.	Item Description	Units	Quantity	Unit Price	Original Contract Amount	Change Authorized Quantity	Change Authorized Amount	Total Authorized Quantity	Total Authorized Amount	This Estimate Quantity	This Estimate Amount	Previous Quantity	Total Estimate To Date Quantity	Total Estimate To Date Amount	% Auth.
78	SHOULDER BACKING	LF	4,170	4.00	16,680.00			4,170.00	16,680.00			4,200.00	4,200.00	16,800.00	101%
79	EROSION CONTROL (TYPE D)	ACRE	1	5,000.00	5,000.00			1.00	5,000.00			1.00	1.00	5,000.00	100%
80	GRINDING ASPHALT CONCRETE IN PLACE	SQYD	5,950	0.60	3,570.00			5,950.00	3,570.00			4,920.00	4,920.00	2,952.00	83%
81	PLACE HOT MIX ASPHALT (MISCELLANEOUS AREA)	SQYD	260	15.00	3,900.00			260.00	3,900.00						0%
82	ROADSIDE SIGN - TWO POST	EA	2	750.00	1,500.00			2.00	1,500.00			2.00	2.00	1,500.00	100%
83A	GEOTEXTILE	SQYD	3,970	8.00	31,760.00			3,970.00	31,760.00			4,362.00	4,362.00	34,895.00	110%
83B	PLACE ASPHALT COCRETE DIKE (CRS 2'x2) (6")	LF	80	8.00	640.00			80.00	640.00			95.00	95.00	760.00	119%
84	48" CORRUGATED STEEL PIPE (.064" THICK)	LF	57	225.00	12,825.00			57.00	12,825.00			59.00	59.00	13,275.00	104%
85	36" CORRUGATED STEEL PIPE (.064" THICK)	LF	74	300.00	22,200.00			74.00	22,200.00			74.00	74.00	22,200.00	100%
86	30" CORRUGATED STEEL PIPE (.064" THICK)	LF	61	200.00	12,200.00			61.00	12,200.00			60.00	60.00	12,000.00	99%
87	CLASS 1 CONCRETE STRUCTURE (HEADWALL & WARPE	EA	2	12,000.00	24,000.00			2.00	24,000.00			2.00	2.00	24,000.00	100%

PLEASE COMPLETE THIS INFORMATION  
RECORDING REQUESTED BY:

**KECIA HARPER-IHEM, CLERK OF THE BOARD  
RIVERSIDE CO. CLERK OF THE BOARD  
4080 LEMON STREET, 1<sup>ST</sup> FLOOR CAC  
P.O. BOX 1147 – RIVERSIDE, CA 92502  
MAIL STOP # 1010**

AND WHEN RECORDED MAIL TO:

**RETURN TO: STOP #1010**  
RIVERSIDE COUNTY CLERK OF THE BOARD  
P. O. BOX 1147 – RIVERSIDE, CA 92502

**THIS SPACE FOR RECORDERS USE ONLY**

**NOTICE OF COMPLETION**

To be recorded with County Recorder  
within 10 days after completion.  
No recording fee.

**Notice is hereby given by the undersigned owner, a public entity of the State of California, that a public work of improvement has been completed, as follows:**

**Project title or description of work:** Gilman Springs Roadway Improvements

**Date of Completion:** Date of this notice

**Nature of owner:** County of Riverside, public entity

**Interest or estate of owner:** Public Roadway

**Address of owner:** 4080 Lemon Street, 8th Floor, Riverside, CA 92501

**Name of contractor:** Griffith Company

**Street or legal description of site:** Gilman Springs Road

Dated: \_\_\_\_\_

Owner: County of Riverside  
(Name of Public Entity)

By: \_\_\_\_\_  
Chairman, Board of Supervisors

**STATE OF CALIFORNIA )**  
**COUNTY OF RIVERSIDE )** <sup>ss</sup>

I am the Chairman of the governing board of the County of Riverside, the public entity, which executed the foregoing notice and on whose behalf I make this verification; I have read this notice, know its contents, and the same is true. I certify under penalty of perjury that the foregoing is true and correct.

Executed at Riverside, California on \_\_\_\_\_ (Date)

\_\_\_\_\_, Chairman of the Board of Supervisors
