

FORM APPROVED COUNTY COUNSEL
 BY: GREGORY P. PRIAMOS
 DATE: 3/9/16



**SUBMITTAL TO THE BOARD OF SUPERVISORS
 COUNTY OF RIVERSIDE, STATE OF CALIFORNIA**

1/2

FROM: TLMA – Transportation Department

SUBMITTAL DATE:
 March 1, 2016

SUBJECT: Notice of Completion – Emergency Storm Damage Repair Work, Tex Wash Bridge No. 56C0119 on Ragsdale Road in the Community of Desert Center. 4th District; [\$253,156]; Local Funds 100%

RECOMMENDED MOTION: That the Board of Supervisors:

1. Accept Emergency Storm Damage Repair Work, Tex Wash Bridge No. 56C0119 as completed; and
2. Authorize the Chairman of the board to execute the Notice of Completion and the Clerk of the Board to record the Notice.

BACKGROUND:

Summary

By Minute Order 3-27 of September 22, 2015, the Board of Supervisors entered into a contract with Granite Construction Company of Indio, CA for the Emergency Storm Damage Repair Work, Tex Wash Bridge No. 56C0119.

Patricia Romo

Juan C. Perez

Patricia Romo
 Assistant Director of Transportation

Juan C. Perez
 Director of Transportation and Land Management

| FINANCIAL DATA | Current Fiscal Year: | Next Fiscal Year: | Total Cost: | Ongoing Cost: | POLICY/CONSENT (Per Exec. Office) |
|------------------------|----------------------|-------------------|-------------|---------------|-----------------------------------------------------------------------------|
| COST | \$ 253,156 | \$ 0 | \$ 253,156 | \$ 0 | Consent <input type="checkbox"/> Policy <input checked="" type="checkbox"/> |
| NET COUNTY COST | \$ 0 | \$ 0 | \$ 0 | \$ 0 | |

SOURCE OF FUNDS: Gas Tax (100%)
 There are no General funds used in this Project.

Budget Adjustment: N/A
For Fiscal Year: 15/16

C.E.O. RECOMMENDATION:

APPROVE

BY: *Tina Grande*
 Tina Grande

County Executive Office Signature

MINUTES OF THE BOARD OF SUPERVISORS

- A-30
- 4/5 Vote
- Positions Added
- Change Order

Prev. Agn. Ref.: 9/22/15, Item 3-27

District: 4

Agenda Number:

3-33

SUBMITTAL TO THE BOARD OF SUPERVISORS, COUNTY OF RIVERSIDE, STATE OF CALIFORNIA
FORM 11: Notice of Completion – Emergency Storm Damage Repair Work, Tex Wash Bridge No. 56C0119 on Ragsdale Road in the Community of Desert Center. 4th District; [\$253,156]; Local Funds 100%

DATE: March 1, 2016

PAGE: 2 of 2

BACKGROUND:

Summary (continued)

The originally authorized amount of the contract was \$390,000. The total amended contract is \$253,156, which is 35.1% less than the originally authorized amount. The reason for the reduction in the total contract price was the damage to the existing bridge was not as extensive as originally anticipated.

Work Order number 45-162001

Impact on Residents and Businesses

The emergency bridge repairs will ensure that the public has a safe local road travel option between Eagle Mountain Road and Desert Center.

SUPPLEMENTAL:

Additional Fiscal Information

Budget

| | | |
|---------------------------------|--------|-------------|
| Original Contract Amount | | \$390,000 |
| Total Change Orders Authorized | 0.0% | \$0 |
| Estimated Pending Change Orders | 0.0% | \$0 |
| Authorized Contract Amount | | \$390,000 |
| * Quantity Adjustments | -35.1% | (\$136,844) |
| + CCO FA Adjustments | 0.0% | \$0 |
| Total Amended Contract Amount | 64.9% | \$253,156 |

Expenditures

| | |
|----------------------------|-----------|
| Total Progress Payments | \$253,156 |
| Estimated Pending Payments | \$0 |
| Total Expenditures | \$253,156 |

(Over)/Under Contract Amount \$0

+ Change Orders using the Force Account method of payment issued prior to the work being completed generally do not use the total authorized amount.

* CAL-Trans Standard Specifications 4-1.03B. Increases or decreases in the quantity of a contract item of work will be determined by comparing the total pay quantity of such item of work with the Engineer's Estimate. If the total pay quantity of any item of work required under the contract varies from the Engineer's Estimate by 25 percent or less, payment will be made for the quantity of work of said item performed at the contract unit price, unless eligible for adjustment pursuant to Section 4-1.03C, "Changes in Character of Work."

This project was funded with \$253,156 of Gas Tax funds.

Contract History and Price Reasonableness

N/A

ATTACHMENTS:

Vicinity Map
Progress Estimate Report
Notice of Completion



COUNTY OF RIVERSIDE
TRANSPORTATION DEPARTMENT

EMERGENCY STORM DAMAGE REPAIR WORK

TEX WASH BRIDGE No. 56C0119 ON RAGSDALE ROAD

COMMUNITY OF DESERT CENTER

PROJECT No. 45-162001

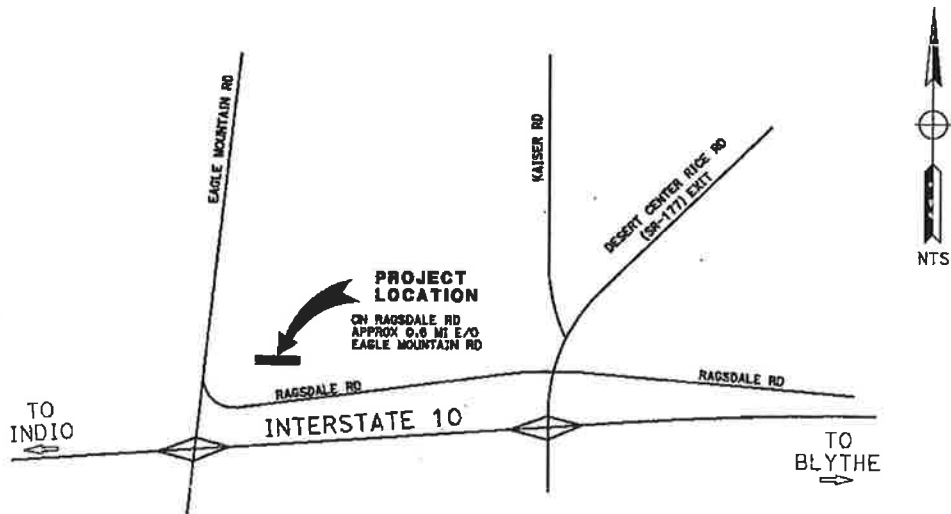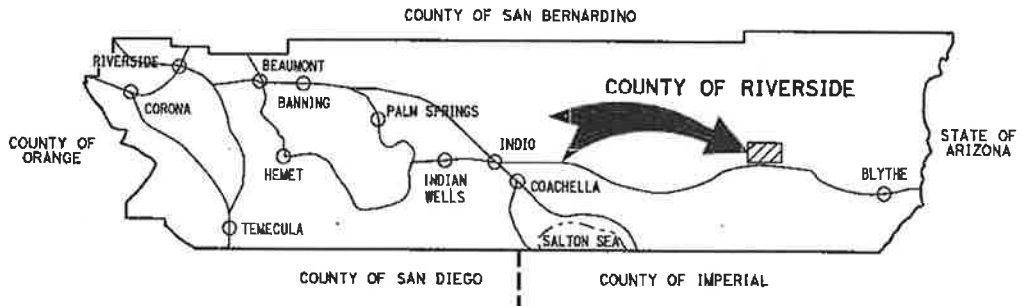


VICINITY MAP
COUNTY ROAD BOOK PAGE No. 265

PROGRESS ESTIMATE RECORD - COUNTY OF RIVERSIDE
 County Project No.: 45-162001
 Contract No. 15-08-001

Contractor: Granite Construction Company
 Address: 38000 Monroe St.
 City, State, Zip: Indio, CA 92203

Estimate No. 2 Final
 From: December 25, 2015
 To: January 21, 2016

SHEET 1 of 1



| Item No. | Item Description | Units | Quantity | Unit Price | Original Contract | | Change Orders | | Amended Contract | | This Estimate Quantity | This Estimate Amount | Previous Quantity | Total Estimate To Date Quantity | Total Estimate To Date Amount | % Aufr. |
|----------------------|----------------------------------|-------|----------|------------|-------------------|------------|---------------|------------|------------------|-----------|------------------------|----------------------|-------------------|---------------------------------|-------------------------------|---------|
| | | | | | Quantity | Amount | Quantity | Amount | Quantity | Amount | | | | | | |
| 1 | EMERGENCY REPAIRS (BENT 12 & 13) | FA | 300,000 | 1.00 | 300,000.00 | 300,000.00 | 300,000.00 | 300,000.00 | 30,172.41 | 30,172.41 | 30,172.41 | 190,793.35 | 220,965.76 | 220,965.76 | 74% | |
| 2 | OTHER REPAIRS (BENT 4 & 8) | FA | 90,000 | 1.00 | 90,000.00 | 90,000.00 | 90,000.00 | 90,000.00 | 32,189.77 | 32,189.77 | 32,189.77 | 32,189.77 | 32,189.77 | 32,189.77 | 36% | |
| PROJECT TOTAL | | | | | | 390,000.00 | 390,000.00 | 390,000.00 | 0.00 | 30,172.41 | 30,172.41 | | | 253,155.53 | | |

Made by: Ira Nquyed
 Checked by: [Signature] 1-21-16
 OK Const. Supv. [Signature] 1-21-16

Working Days: Start Date: 8-19-15
 Days Added: 0 End Date: 11-5-15
 Subtotal: 20 % \$ Complete: 65%
 Days Used: 20 Original Contract: \$390,000.00
 % Time Elapsed: 100% Amended Contract: \$390,000.00

TOTAL VALUE OF WORK TO DATE: \$253,155.53
 LESS RETENTION: 0% 0.00
 TOTAL DUE TO DATE: \$253,155.53
 LESS PREVIOUSLY INVOICED: 222,983.12
 LESS LABOR NON COMPLIANCE: 0.00
 TOTAL DUE THIS PAYMENT: \$30,172.41

This Estimate Approved [Signature] Date: 2/3/16 for: Patricia Romo, Assistant Director of Transportation
 Received by Accounts Payable: _____ By: _____

Quantities on This Estimate Approved [Signature] Date: 1/26/16
 Granite Construction Company

PAYMENT APPROVAL
 Fund 20000
 Dept ID 31005 31301
 Account 527980
 Project 245-1620016
 Activity ID 23500
 Resource Type CNT
 Signature [Signature]
 Date 2/2/16

TRANSFISCAL APPROVED
 By: Crystal Potter 5-3461
 FEB 04 2016

Norma Larson
 951-955-2783
 2.2.16

PLEASE COMPLETE THIS INFORMATION
RECORDING REQUESTED BY:

**KECIA HARPER-IHEM, CLERK OF THE BOARD
RIVERSIDE CO. CLERK OF THE BOARD
4080 LEMON STREET, 1ST FLOOR CAC
P O BOX 1147 – RIVERSIDE, CA 92502
MAIL STOP # 1010**

AND WHEN RECORDED MAIL TO:

RETURN TO: STOP #1010
RIVERSIDE COUNTY CLERK OF THE BOARD
P. O. BOX 1147 – RIVERSIDE, CA 92502

THIS SPACE FOR RECORDERS USE ONLY

NOTICE OF COMPLETION

To be recorded with County Recorder
within 10 days after completion.
No recording fee.

Notice is hereby given by the undersigned owner, a public entity of the State of California, that a public work of improvement has been completed, as follows:

Project title or description of work: Emergency Storm Damage Repair Work, Tex Wash Bridge No. 56C0119

Date of Completion: Date of this notice

Nature of owner: County of Riverside, public entity

Interest or estate of owner: Public Roadway

Address of owner: 4080 Lemon Street, 8th Floor, Riverside, CA 92501

Name of contractor: Granite Construction Company

Street or legal description of site: Tex Wash Brige No. 56C0119

Dated: _____

Owner: County of Riverside
(Name of Public Entity)

By: _____
Chairman, Board of Supervisors

STATE OF CALIFORNIA)

ss

COUNTY OF RIVERSIDE)

I am the Chairman of the governing board of the County of Riverside, the public entity which executed the foregoing notice and on whose behalf I make this verification; I have read this notice, know its contents, and the same is true. I certify under penalty of perjury that the foregoing is true and correct.

Executed at Riverside, California on _____ (Date)

_____, Chairman of the Board of Supervisors

FORM APPROVED COUNTY COUNSEL
BY: Marsha L Victor 3/9/16
MARSHA L. VICTOR DATE
