

**SUBMITTAL TO THE BOARD OF SUPERVISORS  
COUNTY OF RIVERSIDE, STATE OF CALIFORNIA**

848



**FROM:** TLMA - Transportation Department

**SUBMITTAL DATE:**  
January 28, 2010

**SUBJECT:** Notice of Completion - Construction of pedestrian sidewalk, installation of new fencing on the 68<sup>th</sup> Street Bridge over Interstate 15

**RECOMMENDED MOTION:** That the Board execute and file the attached "Notice of Completion"

**BACKGROUND:** By Minute Order 3.33 of April 21, 2009, the Board entered into an agreement with Trinity Construction of Blue Jay, CA for the construction of pedestrian sidewalk, installation of new fencing on the 68<sup>th</sup> Street Bridge over Interstate 15 and associated improvements in the Mira Loma area. The authorized amount of the contract was \$119,826. The total amended contract amount (including quantity adjustments) is \$114,934 which is 4.1% less than the originally authorized amount.

Departmental Concurrence

Juan C. Perez  
Director of Transportation

dj  
(Continued On Attached Page)

|  |                               |           |                         |   |
|--|-------------------------------|-----------|-------------------------|---|
| <b>FINANCIAL DATA</b>  | Current F.Y. Total Cost:      | \$114,934 | In Current Year Budget: | Yes   |
|  | Current F.Y. Net County Cost: | \$ 0      | Budget Adjustment:      | No  |
|  | Annual Net County Cost:       | \$ 0      | For Fiscal Year:        | 2009/2010   |
| <b>SOURCE OF FUNDS:</b> State Safe Route to Schools (52%), Measure A/Western (48%) |                               |           |                         | <b>Positions To Be Deleted Per A-30</b> <input type="checkbox"/><br><b>Requires 4/5 Vote</b> <input type="checkbox"/> |

**C.E.O. RECOMMENDATION:**

APPROVE

BY   
Tina Grande

County Executive Office Signature

**MINUTES OF THE BOARD OF SUPERVISORS**

On motion of Supervisor Benoit, seconded by Supervisor Buster and duly carried by unanimous vote, IT WAS ORDERED that the above matter is approved as recommended.

Ayes: Buster, Tavaglione, Stone, Benoit and Ashley  
 Nays: None  
 Absent: None  
 Date: February 9, 2010  
 xc: Transp., Recorder

Kecia Harper-Ihem  
Clerk of the Board  
By   
Deputy

**Prev. Agn. Ref.** 4/21/09, Item 3.33 **District:** 2 **Agenda Number:**

ATTACHMENTS FILED  
WITH THE CLERK OF THE BOARD

**3.57**

Policy ☒ Policy ☒

Consent ☐ Consent ☐

Dep't Recomm.: Per Exec. Ofc.:

The Honorable Board of Supervisors

RE: Notice of Completion - Construction of pedestrian sidewalk, installation of new fencing on the 68th Street Bridge over Interstate 15

January 28, 2010

Page 2 of 2

This work was completed in conformance with the plans and specifications on November 20, 2009. The work was inspected by the Construction Engineering Section of the Transportation Department. Work Order B8-0661.

**Budget**

|                               |       |              |
|-------------------------------|-------|--------------|
| Original Contract Amount      |       | \$119,826.00 |
| Tot. Chg Orders Authorized -  | 0.0%  | \$0.00       |
| Est. Pending Change Orders    | 0.0%  | \$0.00       |
| Amended Contract Amount       |       | \$119,826.00 |
| * Quantity Adjustments        | -4.1% | (\$4,892.00) |
| + CCO FA Adjustments          | 0.0%  | \$0.00       |
| Total Amended Contract Amount | 95.9% | \$114,934.00 |

**Expenditures**

|                            |              |
|----------------------------|--------------|
| Total Progress Payments -  | \$114,934.00 |
| Estimated Pending Payments |              |
| Total Expenditures         | \$114,934.00 |

|                              |        |
|------------------------------|--------|
| (Over)\Under Contract Amount | \$0.00 |
|------------------------------|--------|

+ Change Orders using the Force Account method of payment issued prior to the work being completed generally do not use the total authorized amount.

\* CAL-Trans Standard Specifications 4-1.03B. Increases or decreases in the quantity of a contract item of work will be determined by comparing the total pay quantity of such item of work with the Engineer's Estimate. If the total pay quantity of any item of work required under the contract varies from the Engineers Estimate by 25 percent or less, payment will be made for the quantity of work of said item performed at contract unit price, unless eligible for adjustment pursuant to Section 4-1.03C, "Changes in Character of Work."

PLEASE COMPLETE THIS INFORMATION  
RECORDING REQUESTED BY:

KECIA HARPER-IHEM, CLERK OF THE BOARD  
RIVERSIDE CO. CLERK OF THE BOARD  
4080 LEMON STREET, 1<sup>ST</sup> FLOOR CAC  
P O BOX 1147 - RIVERSIDE, CA 92502

MAIL STOP # 1010

DOC # 2010-0073156

02/18/2010 08:00A Fee:NC

Page 1 of 2

Recorded in Official Records

County of Riverside

Larry W. Ward

Assessor, County Clerk & Recorder



AND WHEN RECORDED MAIL TO:

RETURN TO: STOP #1010

RIVERSIDE COUNTY CLERK OF THE BOARD

P. O. BOX 1147 - RIVERSIDE, CA 92502

| S       | R | U | PAGE | SIZE | DA   | MISC | LONG | RFD  | COPY |
|---------|---|---|------|------|------|------|------|------|------|
|         |   |   | 2    |      |      |      |      |      |      |
| M       | A | L | 465  | 426  | PCOR | NCOR | SMF  | NCHG | EXAM |
| nchg cc |   |   |      |      |      | T:   | CTY  | UNI  | 509  |

### NOTICE OF COMPLETION

To be recorded with County Recorder  
within 10 days after completion.  
No recording fee.



Notice is hereby given by the undersigned owner, a public entity of the State of California, that a public work of improvement has been completed, as follows:

Project title or description of work: pedestrian sidewalk and new fencing over I15

Date of Completion: Date of this notice 02/09/10

Nature of owner: County of Riverside, public entity

Interest or estate of owner: Public Roadway

Address of owner: 4080 Lemon Street, 8th Floor, Riverside, CA 92501

Name of contractor: Trinity Construction

Street or legal description of site: 68<sup>th</sup> Street Bridge over Interstate 15

Dated: February 9, 2010

Owner: County of Riverside  
(Name of Public Entity)

By: Marion Ashley  
Marion Ashley, Chairman, Board of Supervisors

STATE OF CALIFORNIA )

ss

COUNTY OF RIVERSIDE )

I am the Chairman of the governing board of the County of Riverside, the public entity which executed the foregoing notice and on whose behalf I make this verification; I have read this notice, know its contents, and the same is true. I certify under penalty of perjury that the foregoing is true and correct.

Executed at Riverside, California on February 9, 2010 (Date)

Marion Ashley  
Marion Ashley,  
Chairman of the Board of Supervisors

ATTEST: KECIA HARPER-IHEM, Clerk of the Board by: Landerahmond Deputy Clerk

02.09.10 3.57

2010 13 1989410



**LARRY W. WARD  
COUNTY OF RIVERSIDE  
ASSESSOR-COUNTY CLERK-RECORDER**

**Recorder**  
P.O. Box 751  
Riverside, CA 92502-0751  
(951) 486-7000  
<http://riverside.asrclrec.com>

**CERTIFICATION**

Pursuant to the provisions of Government Code 27361.7, I certify under the penalty of perjury that the following is a true copy of illegible wording found in the attached document:

(Print or type the page number(s) and wording below):

CLARIFICATION OF THE SEAL for the Riverside County Board of Supervisors  
(embossed on document)



Date:

2-9-10

Signature:

*Sandi Schlemmer*



Print Name:

Sandi Schlemmer, Deputy Clerk - Riverside County Clerk of the Board



**COUNTY OF RIVERSIDE  
DEPARTMENT OF TRANSPORTATION**

**68TH STREET  
PEDESTRIAN WALKWAY  
AND  
BRIDGE RAILING / FENCES**

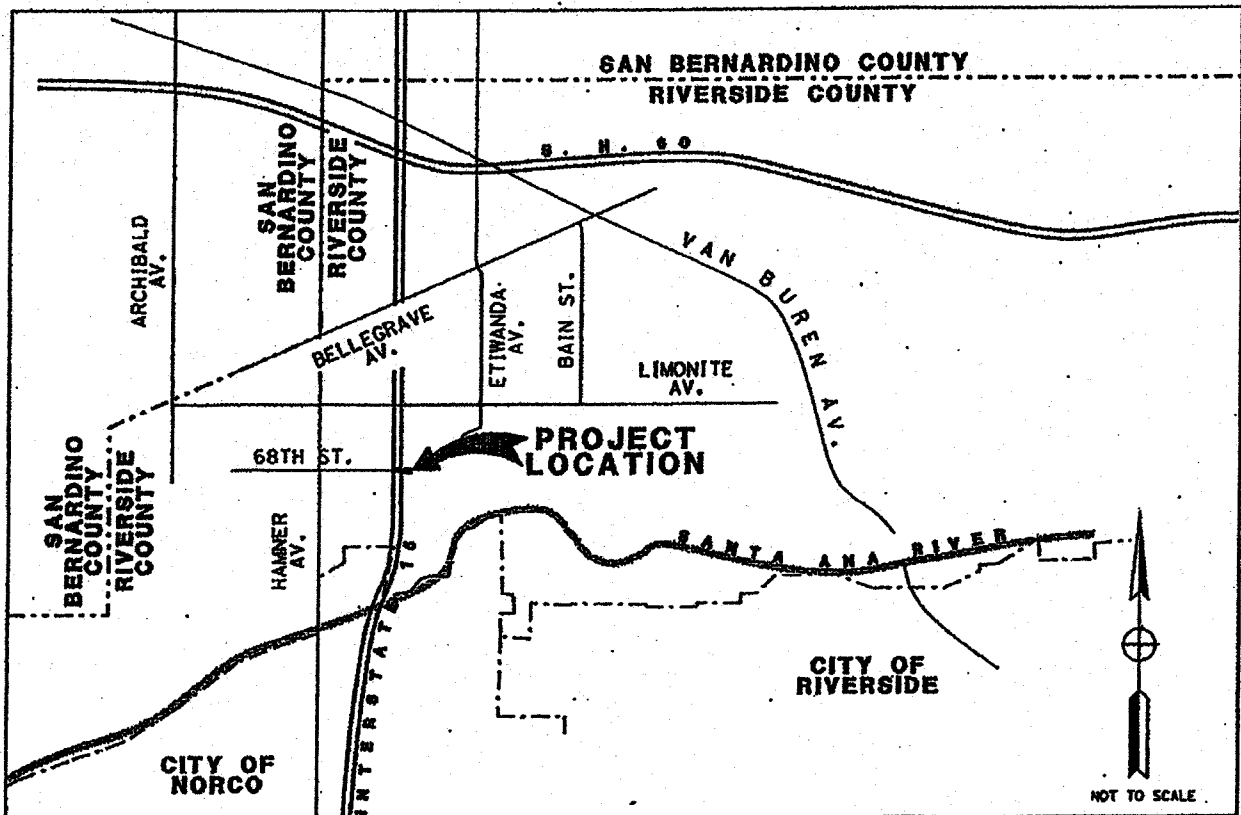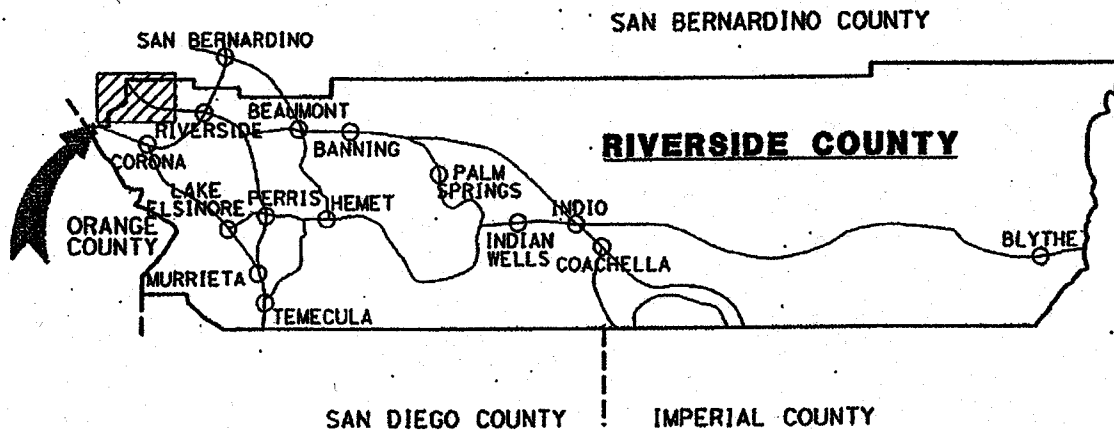

PROJECT LENGTH = 762'  
RANCHO JURUPA (STEARNS)  
2008 THOMAS GUIDE PG 684, F-7  
**VICINITY MAP**

PROJECT: 48th Street Pedestrian Walkway and Bridge Railing  
County Project No.: 88-0461  
Contract No.: 08-03-018

Contractor: Trinity Construction  
Address: P.O. Box 246  
City, State, Zip: Blue Jay, CA 92317

Estimate No. 3 Final  
From: October 28, 2009  
To: November 28, 2009

| Item No. | Item Description | Units | Quantity | Unit Price | Original Contract Amount | Change Authorized Quantity | Change Authorized Amount | Total Authorized Quantity | Total Authorized Amount | This Estimate Quantity | This Estimate Amount | Previous Quantity | Total Estimate To Date Quantity | Total Estimate To Date Amount | % Auth. |
|----------|------------------|-------|----------|------------|--------------------------|----------------------------|--------------------------|---------------------------|-------------------------|------------------------|----------------------|-------------------|---------------------------------|-------------------------------|---------|
|          |                  |       |          |            | 119,828.00               |                            | 0.00                     |                           | 119,828.00              |                        |                      |                   |                                 | 114,934.00                    |         |

PROJECT TOTAL

Made by: George Bowden

Checked by: GW

OK Const. Supv. GW

Working Days: 8-15-09  
Days Added: 7-28-09  
Subtotal: 96%  
Days Used: \$119,828.00  
% Time Elapsed: \$119,828.00  
Original Contract: 100%  
Amended Contract:

TOTAL VALUE OF WORK TO DATE: \$114,934.00  
LESS RETENTION: 10%  
TOTAL DUE TO DATE: \$11,493.40  
LESS PREVIOUSLY INVOICED: \$103,440.60  
LESS LABOR NON COMPLIANCE: 72,595.90  
TOTAL DUE THIS PAYMENT: \$30,854.70

This Estimate Approved \_\_\_\_\_ Date: \_\_\_\_\_ for: \_\_\_\_\_  
\$30,854.70

Juan C. Perez, Director of Transportation

Quantities on This Estimate Approved \_\_\_\_\_ Date: 12-16-09  
Trinity Construction

PAYMENT APPROVAL

FUND 20000

Dept ID 3130500000

Account 527980

Project 268-0661E

Activity ID 23500

Resource Type CNT

Signature [Signature]

Date 12/17/09

Received by Accounts Payable: \_\_\_\_\_  
By: \_\_\_\_\_

Contractor: Trinity Construction  
 Address: P.O. Box 246  
 City, State, Zip: Blue Jay, CA 92317

Estimate No. 3 Final  
 From: October 24, 2009  
 To: November 25, 2009



| Item No. | Item Description   | Units | Quantity | Unit Price | Original Contract Amount | Change Authorized Quantity | Change Authorized Amount | Total Authorized Quantity | Total Authorized Amount | This Estimate Quantity | This Estimate Amount | Previous Quantity | Total Estimate To Date Quantity | Total Estimate To Date Amount | % Auth. |
|----------|--|-------|----------|------------|--------------------------|----------------------------|--------------------------|---------------------------|-------------------------|------------------------|----------------------|-------------------|---------------------------------|-------------------------------|---------|
| 1        | Place Asphalt Concrete Dike (CRS 212) (6")                               | LF    | 450      | 7.00       | 3,150.00                 |                            |                          | 450.00                    | 3,150.00                |                        |                      | 430.00            | 430.00                          | 3,010.00                      | 98%     |
| 2        | Asphalt Concrete (Driveway Approach with Asphalt Concrete Dike (CRS 206) | EA    | 1        | 500.00     | 500.00                   |                            |                          | 1.00                      | 500.00                  |                        |                      |                   | 1.00                            | 500.00                        | 100%    |
| 3        | Dust Abatement   | LS    | 1        | 2,500.00   | 2,500.00                 |                            |                          | 1.00                      | 2,500.00                |                        |                      | 0.95              | 1.00                            | 2,500.00                      | 100%    |
| 4        | Water Pollution Control  | LS    | 1        | 1,250.00   | 1,250.00                 |                            |                          | 1.00                      | 1,250.00                |                        |                      | 0.90              | 1.00                            | 1,250.00                      | 100%    |
| 5        | Traffic Control System   | LS    | 1        | 25,850.00  | 25,850.00                |                            |                          | 1.00                      | 25,850.00               |                        |                      | 0.90              | 1.00                            | 25,850.00                     | 100%    |
| 6        | Remove Traffic Stripe and Pavement Marking                               | SQFT  | 1,400    | 1.50       | 2,100.00                 |                            |                          | 1,400.00                  | 2,100.00                |                        |                      | 1,400.00          | 1,400.00                        | 2,100.00                      | 100%    |
| 7        | Salvage Roadside Sign  | EA    | 2        | 100.00     | 200.00                   |                            |                          | 2.00                      | 200.00                  |                        |                      | 2.00              | 2.00                            | 200.00                        | 100%    |
| 8        | Clearing and Grubbing  | LS    | 1        | 500.00     | 500.00                   |                            |                          | 1.00                      | 500.00                  |                        |                      | 1.00              | 1.00                            | 500.00                        | 100%    |
| 9        | Roadway Excavation   | CY    | 180      | 44.00      | 7,040.00                 |                            |                          | 180.00                    | 7,040.00                |                        |                      | 180.00            | 180.00                          | 7,040.00                      | 100%    |
| 10       | Class 2 Aggregate Base   | CY    | 26       | 60.00      | 1,560.00                 |                            |                          | 26.00                     | 1,560.00                |                        |                      | 18.00             | 20.00                           | 1,200.00                      | 77%     |
| 11       | Hot Asphalt Mix  | TON   | 88       | 100.00     | 8,800.00                 |                            |                          | 88.00                     | 8,800.00                |                        |                      | 40.20             | 87.42                           | 8,742.00                      | 99%     |
| 12       | Place Asphalt Concrete (Misc. Area)                                      | SQYD  | 290      | 21.00      | 6,090.00                 |                            |                          | 290.00                    | 6,090.00                |                        |                      | 288.00            | 288.00                          | 5,586.00                      | 92%     |
| 13       | Roadside Sign - One Post   | EA    | 7        | 150.00     | 1,050.00                 |                            |                          | 7.00                      | 1,050.00                |                        |                      | 7.00              | 7.00                            | 1,050.00                      | 100%    |
| 14       | Chain Link Fence (Type CL-6)   | LF    | 180      | 38.00      | 6,840.00                 |                            |                          | 180.00                    | 6,840.00                |                        |                      | 120.00            | 182.00                          | 7,298.00                      | 107%    |
| 15       | Chain Link Fence (Type 3 Modified)                                       | LF    | 256      | 71.00      | 18,176.00                |                            |                          | 256.00                    | 18,176.00               |                        |                      | 120.00            | 250.00                          | 17,750.00                     | 98%     |
| 16       | Chain Link Railing (Type 7)  | LF    | 256      | 90.00      | 23,040.00                |                            |                          | 256.00                    | 23,040.00               |                        |                      | 120.00            | 251.00                          | 22,590.00                     | 98%     |
| 17       | Thermoplastic Crosswalk and Pavement Marking                             | SQFT  | 860      | 2.50       | 2,150.00                 |                            |                          | 860.00                    | 2,150.00                |                        |                      | 860.00            | 860.00                          | 2,150.00                      | 100%    |
| 18       | Paint Traffic Stripe (2-Coat)  | LF    | 3,400    | 0.30       | 1,020.00                 |                            |                          | 3,400.00                  | 1,020.00                |                        |                      | 3,400.00          | 3,400.00                        | 1,020.00                      | 100%    |
| 19       | Remove Fence Fabric and Railing  | LF    | 256      | 10.00      | 2,560.00                 |                            |                          | 256.00                    | 2,560.00                |                        |                      | 180.00            | 250.00                          | 2,500.00                      | 98%     |
| 20       | Pavement Marker (Reflective)   | EA    | 200      | 2.25       | 450.00                   |                            |                          | 200.00                    | 450.00                  |                        |                      | 200.00            | 200.00                          | 450.00                        | 100%    |
| 21       | Obtain Encroachment Permit   | FA    | 1        | 5,000.00   | 5,000.00                 |                            |                          | 1.00                      | 5,000.00                |                        |                      |                   | 0.33                            | 1,650.00                      | 33%     |
