

**SUBMITTAL TO THE BOARD OF SUPERVISORS  
COUNTY OF RIVERSIDE, STATE OF CALIFORNIA**

422A



**FROM:** TLMA - Transportation Department

**SUBMITTAL DATE:**  
June 10, 2010

**SUBJECT:** Notice of Completion - Construction of Raised Median Improvements on Camino Real from Mission Boulevard to Avenida Baja/River Glen Drive, in the Rubidoux area.

**RECOMMENDED MOTION:** That the Board execute and file the attached "Notice of Completion"

**BACKGROUND:** By Minute Order 3.58 of March 16, 2010, the Board entered into an agreement with S&S Grading and Paving, Inc. of Norco, CA for the construction of raised median improvements on Camino Real from Mission Boulevard to Avenida Baja/River Glen Drive, in the Rubidoux area. The authorized amount of the contract was \$162,269. The total amended contract amount (including quantity adjustments) is \$152,585.45 which is 6.0% less

Juan C. Perez  
Director of Transportation

dj  
(Continued On Attached Page)

<b>FINANCIAL DATA</b>	Current F.Y. Total Cost:	\$152,585	In Current Year Budget:	Yes
	Current F.Y. Net County Cost:	\$ 0	Budget Adjustment:	No
	Annual Net County Cost:	\$ 0	For Fiscal Year:	2009/2010
<b>SOURCE OF FUNDS:</b> Redevelopment Agency (RDA) (100%)				Positions To Be Deleted Per A-30 <input type="checkbox"/>
				Requires 4/5 Vote <input type="checkbox"/>

**C.E.O. RECOMMENDATION:**

APPROVE

BY: *Tina Grande*  
Tina Grande

County Executive Office Signature

**MINUTES OF THE BOARD OF SUPERVISORS**

On motion of Supervisor Stone, seconded by Supervisor Buster and duly carried by unanimous vote, IT WAS ORDERED that the above matter is approved as recommended.

Ayes: Buster, Tavaglione, Stone, Benoit and Ashley  
Nays: None  
Absent: None  
Date: July 13, 2010  
xc: Transp., Recorder

Kecia Harper-Ihem  
Clerk of the Board  
By: *[Signature]*  
Deputy

Prev. Agn. Ref. 03/16/10, Item 3.58 | District: 2 | Agenda Number:

ATTACHMENTS FILED  
WITH THE CLERK OF THE BOARD

3.83

Dept's Recomm.:  Consent  Policy   
Per Exec. Ofc.:  Consent  Policy

The Honorable Board of Supervisors

RE: Notice of Completion - Construction of Raised Median Improvements on Camino Real from Mission Boulevard to Avenida Baja/River Glen Drive, in the Rubidoux area.

June 10, 2010

Page 2 of 2

than the originally authorized amount.

This work was completed in conformance with the plans and specifications on April 22, 2010. The work was inspected by the Construction Engineering Section of the Transportation Department. Work Order B7-0774.

**Budget**

Original Contract Amount		\$162,269.00
Tot. Chg Orders Authorized -	0.0%	\$0.00
Est. Pending Change Orders	0.0%	\$0.00
Amended Contract Amount		\$162,269.00
* Quantity Adjustments	-6.0%	(\$9,683.55)
+ CCO FA Adjustments	0.0%	\$0.00
Total Amended Contract Amount	94.0%	\$152,585.45

**Expenditures**

Total Progress Payments -	\$152,585.45
Estimated Pending Payments	
Total Expenditures	\$152,585.45


**(Over)\Under Contract Amount** \$0.00

+ Change Orders using the Force Account method of payment issued prior to the work being completed generally do not use the total authorized amount.

\* CAL-Trans Standard Specifications 4-1.03B. Increases or decreases in the quantity of a contract item of work will be determined by comparing the total pay quantity of such item of work with the Engineer's Estimate. If the total pay quantity of any item of work required under the contract varies from the Engineers Estimate by 25 percent or less, payment will be made for the quantity of work of said item performed at contract unit price, unless eligible for adjustment pursuant to Section 4-1.03C, "Changes in Character of Work."

# CAMINO REAL


from RIVER GLEN DRIVE to MISSION BLVD.  
in the COMMUNITY OF RUBIDOUX

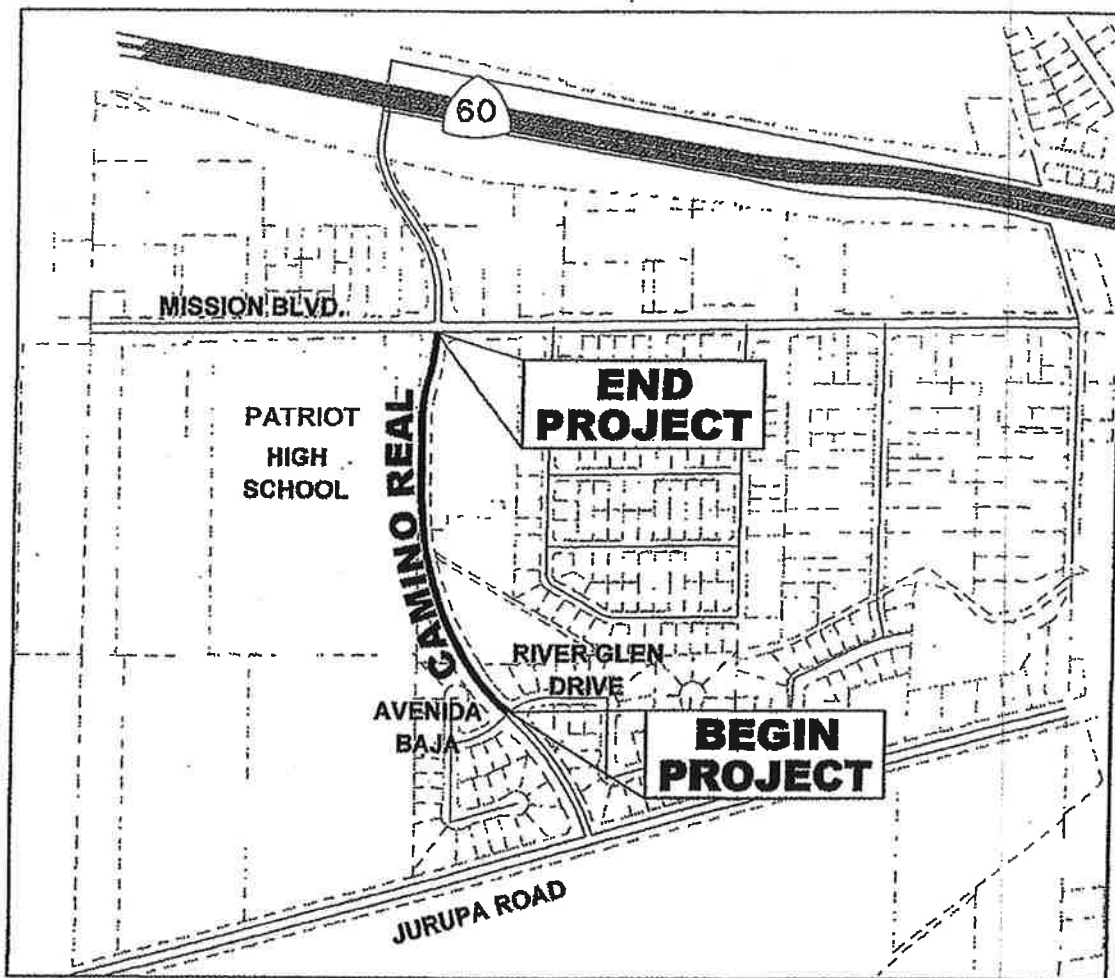

VICINITY MAP

Contractor: S.S. Grading & Paving, Inc.  
 Address: 1221 5th Street  
 City, State, Zip: Norco, CA 92860

Estimate No. 1 Final  
 From: April 3, 2010  
 To: April 18, 2010



Item No.	Item Description	Units	Quantity	Unit Price	Original Contract Amount	Change Authorized Quantity	Change Authorized Amount	Total Authorized Quantity	Total Authorized Amount	This Estimate Quantity	This Estimate Amount	Previous Quantity	Previous Amount	Total Estimate To Date		% Auth.
														Quantity	Amount	
					162,269.00		0.00		162,269.00		152,585.45				152,585.45	
<b>PROJECT TOTAL</b>																

Made by: Trai Nguyen  
 Checked by: [Signature]  
 OK Const. Supv. \_\_\_\_\_

Working Days:  
 Days Added: 3  
 Subtotal: 12  
 Days Used: 12  
 % Time Elapsed: 100%

Start Date: 4-3-10  
 End Date: 4-22-10  
 % Complete: 94%  
 Original Contract: \$162,269.00  
 Amended Contract: \$162,269.00

TOTAL VALUE OF WORK TO DATE: \$152,585.45  
 LESS RETENTION: 10% 15,258.55  
 TOTAL DUE TO DATE: \$137,326.90  
 LESS PREVIOUSLY INVOICED: 0.00  
 LESS LABOR NON COMPLIANCE: 0.00  
 TOTAL DUE THIS PAYMENT: \$137,326.90

This Estimate Approved \_\_\_\_\_ Date: \_\_\_\_\_ for: \_\_\_\_\_  
 Juan C. Perez, Director of Transportation

Received by Accounts Payable: \_\_\_\_\_  
 By: \_\_\_\_\_

**PAYMENT APPROVAL**

Fund 20 000

Dept ID 31305 00000

Account 527 9 80

Project 267-0774E

Activity ID 23500

Resource Type CNT

Signature [Signature]

Date 5/5/10

Quantities on This Estimate Approved \_\_\_\_\_ Date: 5/4/10  
 S.S. Grading & Paving, Inc.



Contractor: S.S. Grading & Paving, Inc.  
 Address: 1221 5th Street  
 City, State, Zip: Norco, CA 92860

Estimate No. 1 Final  
 From: April 3, 2010  
 To: April 18, 2010

Item No.	Item Description	Units	Quantity	Unit Price	Original Contract Amount	Change Authorized Quantity	Change Authorized Amount	Total Authorized Quantity	Total Authorized Amount	This Estimate Quantity	This Estimate Amount	Previous Quantity	Total Estimate To Date		% Auth.
													Quantity	Amount	
1	DUST ABATEMENT	LS	1	7,000.00	7,000.00			1.00	7,000.00	1.00	7,000.00	1.00	7,000.00	100%	
2	WATER POLLUTION CONTROL	LS	1	4,500.00	4,500.00			1.00	4,500.00	1.00	4,500.00		4,500.00	100%	
3	TRAFFIC CONTROL SYSTEM	LS	1	10,200.00	10,200.00			1.00	10,200.00	1.00	10,200.00		10,200.00	100%	
4	CLEARING AND GRUBBING	LS	1	10,000.00	10,000.00			1.00	10,000.00	1.00	10,000.00		10,000.00	100%	
5	ROADWAY EXCAVATION	CY	260	32.00	8,320.00			260.00	8,320.00	267.70	8,566.40		8,566.40	103%	
6	IMPORTED BORROW	CY	80	65.00	5,200.00			80.00	5,200.00	100.00	6,500.00		6,500.00	125%	
7	IMPORTED TOPSOIL	CY	180	76.25	13,725.00			180.00	13,725.00	174.91	13,336.89		13,336.89	97%	
8	SLURRY CEMENT BACKFILL (TWO SACK SLURRY BASE)	CY	35	98.00	3,430.00			35.00	3,430.00	30.00	2,940.00		2,940.00	86%	
9	HOT MIX ASPHALT	TON	95	168.00	15,960.00			95.00	15,960.00	51.87	8,714.16		8,714.16	55%	
10	MINOR CONCRETE [MEDIAN PAVING-DECORATIVE PAVERS]	SQFT	3,110	7.50	23,325.00			3,110.00	23,325.00	3,052.00	22,890.00		22,890.00	98%	
11	MINOR CONCRETE [COBBLE ISLAND PAVING-RIVER ROCK INCLUDING CONCRETE BED]	SQFT	860	9.25	7,955.00			860.00	7,955.00	730.00	6,752.50		6,752.50	85%	
12	MINOR CONCRETE [6" WIDE CONCRETE HEADER]	LF	160	16.25	2,600.00			160.00	2,600.00	160.00	2,600.00		2,600.00	100%	
13	MINOR CONCRETE (TYPE "D" CURB CRS) (204)	LF	3,100	6.50	20,150.00			3,100.00	20,150.00	2,932.00	19,058.00		19,058.00	95%	
14	INSTALL 4" DIAMETER PVC SCH 40 UTILITY SLEEVE	LF	320	23.25	7,440.00			320.00	7,440.00	330.00	7,672.50		7,672.50	103%	
15	INSTALL 3" DIAMETER PVC SCH 40 UTILITY SLEEVE	LF	570	20.30	11,571.00			570.00	11,571.00	540.00	10,962.00		10,962.00	95%	
16	INSTALL 2" DIAMETER PVC SCH 40 UTILITY SLEEVE	LF	30	40.00	1,200.00			30.00	1,200.00	30.00	1,200.00		1,200.00	100%	
17	REMOVE TRAFFIC STRIPE AND PAVEMENT MARKING	SQFT	585	3.00	1,755.00			585.00	1,755.00	585.00	1,755.00		1,755.00	100%	
18	ROADSIDE SIGN-ONE POST	EA	15	195.00	2,925.00			15.00	2,925.00	15.00	2,925.00		2,925.00	100%	
19	THERMOPLASTIC CROSSWALK AND PAVEMENT MARKING (INCLUDING THERMOPLASTIC TRAFFIC	SQFT	630	4.50	2,835.00			630.00	2,835.00	630.00	2,835.00		2,835.00	100%	
20	PAINT TRAFFIC STRIPE (2-COAT)	LF	5,760	0.30	1,728.00			5,760.00	1,728.00	5,760.00	1,728.00		1,728.00	100%	
21	PAVEMENT MARKER (REFLECTIVE)	EA	120	3.75	450.00			120.00	450.00	120.00	450.00		450.00	100%	

PLEASE COMPLETE THIS INFORMATION  
RECORDING REQUESTED BY:

**KECIA HARPER-IHEM, CLERK OF THE BOARD  
RIVERSIDE CO. CLERK OF THE BOARD  
4080 LEMON STREET, 1<sup>ST</sup> FLOOR CAC  
P O BOX 1147 – RIVERSIDE, CA 92502  
MAIL STOP # 1010**

AND WHEN RECORDED MAIL TO:

**RETURN TO: STOP #1010  
RIVERSIDE COUNTY CLERK OF THE BOARD  
P. O. BOX 1147 – RIVERSIDE, CA 92502**

DOC # 2010-0336132

07/19/2010 08:00A Fee:NC

Page 1 of 2

Recorded in Official Records

County of Riverside

Larry W. Ward

Assessor, County Clerk & Recorder



S	R	U	PAGE	SIZE	DA	MISC	LONG	RFD	COPY
			2						
M	A	L	465	426	PCOR	NCOR	SMF	NCHG	EXAM
Notice					T:		CTY	UNI	508

**NOTICE OF COMPLETION**

To be recorded with County Recorder  
within 10 days after completion.  
No recording fee.

**C**  
508

Notice is hereby given by the undersigned owner, a public entity of the State of California, that a public work of improvement has been completed, as follows:

**Project title or description of work:** Raised median improvements

**Date of Completion:** Date of this notice 07/13/10

**Nature of owner:** County of Riverside, public entity

**Interest or estate of owner:** Public Roadway

**Address of owner:** 4080 Lemon Street, 8th Floor, Riverside, CA 92501

**Name of contractor:** S&S Grading and Paving, Inc.

**Street or legal description of site:** Camino Real from Mission Blvd. to Avenida Baja/River Glen Drive

Dated: July 13, 2010

Owner: County of Riverside  
(Name of Public Entity)

By: Marion Ashley  
Marion Ashley Chairman, Board of Supervisors

STATE OF CALIFORNIA )

ss

COUNTY OF RIVERSIDE )

I am the Chairman of the governing board of the County of Riverside, the public entity which executed the foregoing notice and on whose behalf I make this verification; I have read this notice, know its contents, and the same is true. I certify under penalty of perjury that the foregoing is true and correct.

Executed at Riverside, California on 07/13/10 (Date)

Marion Ashley, Marion Ashley, Chairman of the Board of Supervisors

ATTEST:  
KECIA HARPER-IHEM, Clerk of the Board

by: [Signature]  
Deputy

07.13.10 3.83

2010-07-10 2096



**LARRY W. WARD**  
**COUNTY OF RIVERSIDE**  
**ASSESSOR-COUNTY CLERK-RECORDER**

**Recorder**  
P.O. Box 751  
Riverside, CA 92502-0751  
(951) 486-7000

<http://riverside.asrelkrec.com>

**CERTIFICATION**

Pursuant to the provisions of Government Code 27361.7, I certify under the penalty of perjury that the following is a true copy of illegible wording found in the attached document:

(Print or type the page number(s) and wording below):

CLARIFICATION OF THE SEAL for the Riverside County Board of Supervisors  
(embossed on document)



Date:

7-13-10

Signature:

Karen Barton

Print Name:

Karen Barton, Board Assistant, Riverside County Clerk of the Board

