

**SUBMITTAL TO THE BOARD OF SUPERVISORS
COUNTY OF RIVERSIDE, STATE OF CALIFORNIA**

636 A



FROM: TLMA - Transportation Department

SUBMITTAL DATE:
July 15, 2010

SUBJECT: Notice of Completion - Construction of street improvements for the Mecca Streets Revitalization Project Phase 1.

RECOMMENDED MOTION: That the Board execute and file the attached "Notice of Completion"

BACKGROUND: By Minute Order 3.50 of November 3, 2009, the Board entered into an agreement with Match Corporation of San Bernardino, CA for the construction of street improvements for the Mecca Streets Revitalization Project - Phase 1, including 2nd Street and Hammond Road in the unincorporated community of Mecca. The originally authorized amount of the contract was \$1,731,371. The total amended contract amount (including quantity adjustments) is \$1,914,361.58 which is 10.6% more than the originally authorized amount.

Juan C. Perez
Director of Transportation


dj
(Continued On Attached Page)

FINANCIAL DATA	Current F.Y. Total Cost:	\$1,914,362	In Current Year Budget:	Yes
	Current F.Y. Net County Cost:	\$ 0	Budget Adjustment:	No
	Annual Net County Cost:	\$ 0	For Fiscal Year:	2010/2011

SOURCE OF FUNDS: Redevelopment Agency funds (RDA) (100%)	Positions To Be Deleted Per A-30	<input type="checkbox"/>
	Requires 4/5 Vote	<input type="checkbox"/>

C.E.O. RECOMMENDATION:

APPROVE

BY: 
Tina Grande


County Executive Office Signature

- Dept't Recomm.: Policy
- Per Exec. Ofc.: Policy
- Consent
- Consent

MINUTES OF THE BOARD OF SUPERVISORS

On motion of Supervisor Stone, seconded by Supervisor Benoit and duly carried, IT WAS ORDERED that the above matter is approved as recommended.

Ayes: Buster, Stone, Benoit and Ashley
Nays: None
Absent: Tavaglione
Date: July 27, 2010
xc: Transp., Recorder

Kecia Harper-Ihem
Clerk of the Board
By: 
Deputy

Prev. Agn. Ref. 11/3/09, Item 3.50 | District: 4 | Agenda Number:

ATTACHMENTS FILED WITH
THE CLERK OF THE BOARD

3.76

This work was completed in conformance with the plans and specifications on April 30, 2010. The work was inspected by the Construction Engineering Section of the Transportation Department. Work Order X1002.

Budget

Original Contract Amount		\$1,731,371.00
Tot. Chg Orders Authorized -	0.0%	\$0.00
Est. Pending Change Orders	0.0%	\$0.00
Amended Contract Amount		\$1,731,371.00
* Quantity Adjustments	10.6%	\$182,990.58
+ CCO FA Adjustments	0.0%	\$0.00
Total Amended Contract Amount	110.6%	\$1,914,361.58

Expenditures

Total Progress Payments -	\$1,914,361.58
Estimated Pending Payments	\$0.00
Total Expenditures	\$1,914,361.58

(Over)\Under Contract Amount \$0.00

+ Change Orders using the Force Account method of payment issued prior to the work being completed generally do not use the total authorized amount.

* CAL-Trans Standard Specifications 4-1.03B. Increases or decreases in the quantity of a contract item of work will be determined by comparing the total pay quantity of such item of work with the Engineer's Estimate. If the total pay quantity of any item of work required under the contract varies from the Engineers Estimate by 25 percent or less, payment will be made for the quantity of work of said item performed at contract unit price, unless eligible for adjustment pursuant to Section 4-1.03C, "Changes in Character of Work."

PLEASE COMPLETE THIS INFORMATION
RECORDING REQUESTED BY:

**KECIA HARPER-IHEM, CLERK OF THE BOARD
RIVERSIDE CO. CLERK OF THE BOARD
4080 LEMON STREET, 1ST FLOOR CAC
P O BOX 1147 - RIVERSIDE, CA 92502**

MAIL STOP # 1010

AND WHEN RECORDED MAIL TO:

**RETURN TO: STOP #1010
RIVERSIDE COUNTY CLERK OF THE BOARD
P. O. BOX 1147 - RIVERSIDE, CA 92502**

DOC # 2010-0352211

07/28/2010 08:00A Fee:NC

Page 1 of 2

Recorded in Official Records

County of Riverside

Larry W. Ward

Assessor, County Clerk & Recorder



S	R	U	PAGE	SIZE	DA	MISC	LONG	RFD	COPY
			2						
M	A	L	465	426	PCOR	NCOR	SMF	NCHG	EXAM
M 513						T:	CTY	UNI	513

NOTICE OF COMPLETION

To be recorded with County Recorder
within 10 days after completion.
No recording fee.

**C
513**

Notice is hereby given by the undersigned owner, a public entity of the State of California, that a public work of improvement has been completed, as follows:

Project title or description of work: Various street improvements

Date of Completion: Date of this notice 07/27/10

Nature of owner: County of Riverside, public entity

Interest or estate of owner: Public Roadway

Address of owner: 4080 Lemon Street, 8th Floor, Riverside, CA 92501


Name of contractor: Match Corporation

Street or legal description of site: 2nd Street and Hammond Road

Dated: July 27, 2010

Owner: County of Riverside
(Name of Public Entity)

By: Marion Ashley
Marion Ashley Chairman, Board of Supervisors



STATE OF CALIFORNIA)

ss

COUNTY OF RIVERSIDE)

I am the Chairman of the governing board of the County of Riverside, the public entity which executed the foregoing notice and on whose behalf I make this verification; I have read this notice, know its contents, and the same is true. I certify under penalty of perjury that the foregoing is true and correct.

Executed at Riverside, California on 07/27/10 (Date)

Marion Ashley Marion Ashley
Chairman of the Board of Supervisors

ATTEST:

Kecia Harper-Ihem, Clerk of the Board

By: [Signature]
Deputy

2010-08-102784

07.27.10 3.76



LARRY W. WARD
COUNTY OF RIVERSIDE
ASSESSOR-COUNTY CLERK-RECORDER

Recorder
P.O. Box 751
Riverside, CA 92502-0751
(951) 486-7000


<http://riverside.asrclrec.com>

CERTIFICATION

Pursuant to the provisions of Government Code 27361.7, I certify under the penalty of perjury that the following is a true copy of illegible wording found in the attached document:

(Print or type the page number(s) and wording below):

CLARIFICATION OF THE SEAL for the Riverside County Board of Supervisors
(embossed on document)



Date:

7-27-10


Signature:

Karen Barton

Print Name:

Karen Barton, Board Assistant, Riverside County Clerk of the Board



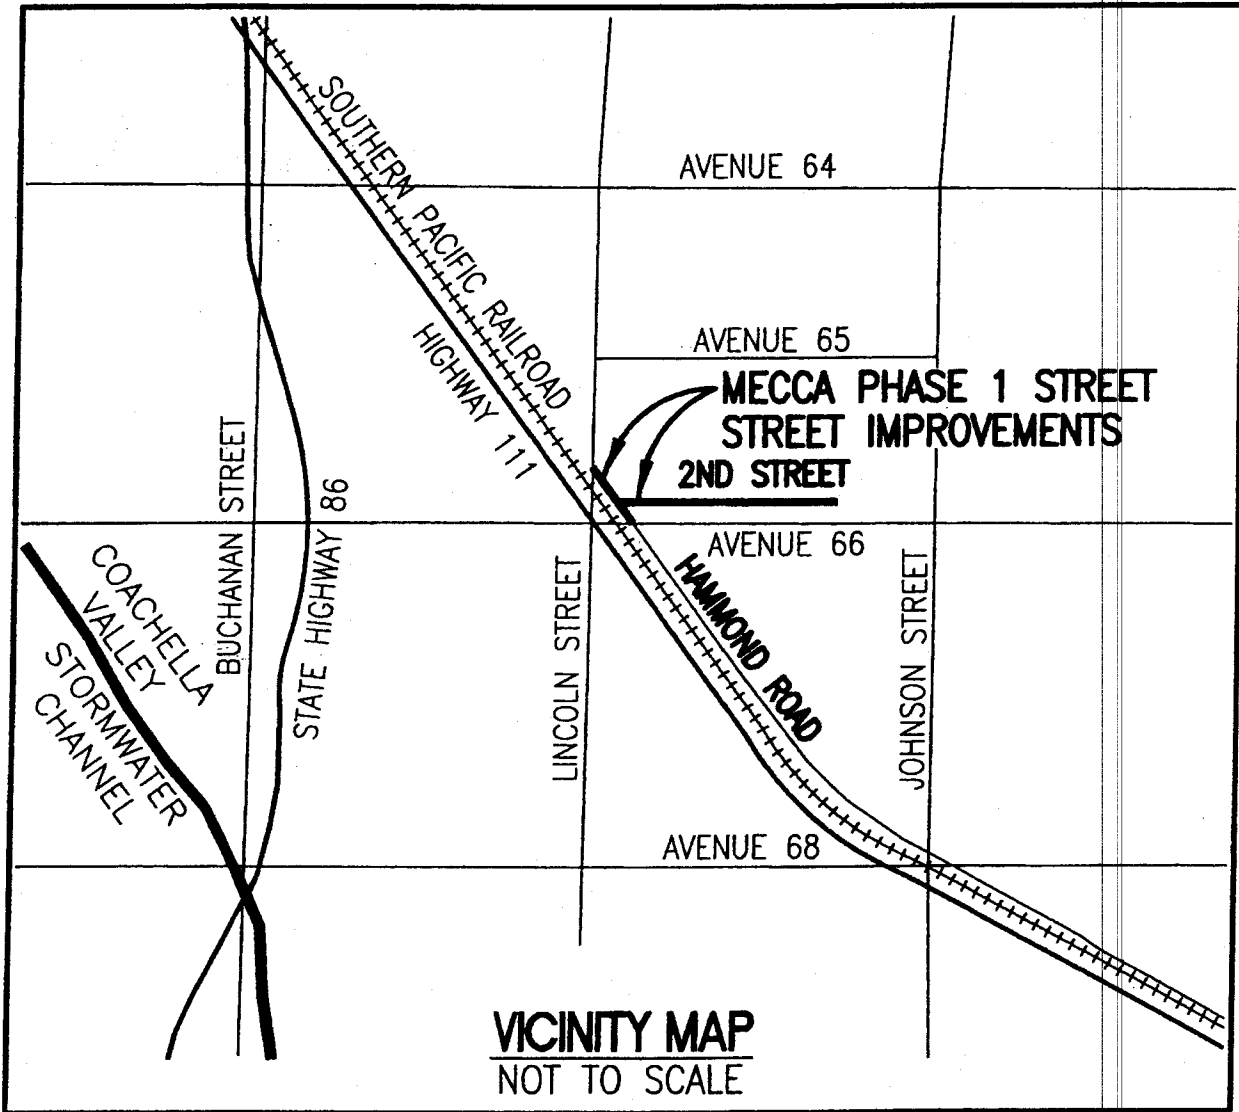

PROJECT: Mecca Streets Revitalization Project Phase 1 2nd St. and Hammond Rd
 County Project No.: X1002
 Contract No.: 09-10-004

Contractor: Match Corporation
 Address: P.O. Box 50,000
 City, State, Zip: San Bernardino, CA 92412



Estimate No. 5 Final
 From: April 26, 2010
 To: May 25, 2010

Item No.	Item Description	Units	Quantity	Unit Price	Original Contract		Change Authorized		Total Authorized		This Estimate		Previous		Total Estimate To Date		% Auth.
					Amount	Quantity	Amount	Quantity	Amount	Quantity	Amount	Quantity	Amount	Quantity	Amount	Quantity	
					1,731,371.00	0.00	1,731,371.00	0.00	1,731,371.00		59,826.90					1,914,361.58	
PROJECT TOTAL																	

Made by: Jesse Mendoza
 Checked by: [Signature]
 OK Const. Supv. _____

Working Days: 60
 Days Added: 26
 Subtotal: 86
 Days Used: 86
 % Time Elapsed: 100%

Start Date: 12-21-09
 End Date: 4-30-10
 % Complete: 111%
 Original Contract: \$1,731,371.00
 Amended Contract: \$1,731,371.00

TOTAL VALUE OF WORK TO DATE: \$1,914,361.58
 LESS RETENTION: 10% 191,436.16
 TOTAL DUE TO DATE: \$1,722,925.42
 LESS PREVIOUSLY INVOICED: 1,669,081.21
 LESS LABOR NON COMPLIANCE: 0.00
 TOTAL DUE THIS PAYMENT: \$53,844.21

This Estimate Approved _____ Date: _____ for: _____
 Juan C. Perez, Director of Transportation

Received by Accounts Payable: _____
 By: _____

Quantities on This Estimate Approved _____ Date: 6/19/10
 Match Corporation

Signature: [Signature]
 Date: 6/24/10
 Resource Type: CNT

Activity ID: 23600
 Project: ZX1002E
 Account: 527980
 Dept ID: 31305
 Fund: 80000

PAYMENT APPROVAL

PROJECT: Mecca Streets Revitalization Project Phase 1 2nd St. and Hammond Rd
 County Project No.: X1002
 Contract No.: 09-10-004

Contractor: Match Corporation
 Address: P.O. Box 50,000
 City, State, Zip: San Bernardino, CA 92412

Estimate No. 5 Final
 From: April 26, 2010
 To: May 25, 2010



Item No.	Item Description	Units	Quantity	Unit Price	Original Contract Amount	Change Authorized		Total Authorized		This Estimate		Previous Quantity	Total Estimate To Date		% Auth
						Quantity	Amount	Quantity	Amount	Quantity	Amount		Quantity	Amount	
23	REMOVE EXISTING FENCE/ REPLACE WITH TUBULAR STEEL FENCE	LF	1,050	60.00	63,000.00			1,050.00	63,000.00	262.00	15,720.00	1,050.00	1,312.00	78,720.00	125%
24	REMOVE REPLACE EXISTING FENCEWALL	LF	390	170.00	66,300.00			390.00	66,300.00	30.00	5,100.00	391.00	421.00	71,570.00	108%
25	SUBGRADE ENHANCEMENT TREATMENT	SQYD	7,500	8.10	60,750.00			7,500.00	60,750.00			9,375.00	9,375.00	75,937.50	125%
26	PAINT TRAFFIC STRIPE (2-COAT)	LF	4,400	0.35	1,540.00			4,400.00	1,540.00	4,756.00	1,664.60	4,756.00	4,756.00	1,664.60	108%
27	THERMO CROSSWALK & PAVEMENT MARKING	SQYD	1,850	3.00	5,550.00			1,850.00	5,550.00	1,848.00	5,544.00	1,848.00	1,848.00	5,544.00	100%
28	ROADSIDE SIGN - ONE POST	EA	13	155.00	2,015.00			13.00	2,015.00	14.00	2,170.00	14.00	14.00	2,170.00	108%
29	RELOCATE ROADSIDE SIGN	EA	16	155.00	2,480.00			16.00	2,480.00	18.00	2,790.00	18.00	18.00	2,790.00	113%
30	PAVEMENT MARKER (REFLECTIVE)	EA	75	5.10	382.50			75.00	382.50	93.00	474.30	93.00	93.00	474.30	124%
31	MISC DIRECTED WORK	FA	1	100,000.00	100,000.00			1.00	100,000.00	0.00000000		0.9991912	0.9991912	99,919.12	100%
32	LIGHTING [RESIDENTIAL STREET LIGHT SYSTEM]	LS	1	102,000.00	102,000.00			1.00	102,000.00	0.05	5,100.00	0.95	1.00	102,000.00	100%
33	CONCRETE-ROCK SLOPE PROTECTION [COBBLE, METHOD A]	CY	10	700.00	7,000.00			10.00	7,000.00			10.00	10.00	7,000.00	100%
34	MINOR CONCRETE (COMMERCIAL DRIVEWAY APPROACH) (CRS207A)	EA	11	1,500.00	16,500.00			11.00	16,500.00			13.00	13.00	19,500.00	118%
