

**SUBMITTAL TO THE BOARD OF SUPERVISORS
COUNTY OF RIVERSIDE, STATE OF CALIFORNIA**

904A



FROM: TLMA - Transportation Department

SUBMITTAL DATE:
March 10, 2011

SUBJECT: Notice of Completion - Emergency Storm Damage Repair, Bautista Road, near the Hemet Area

RECOMMENDED MOTION: That the Board of Supervisors execute and file the attached "Notice of Completion".

BACKGROUND: By Minute Order 3.36 of February 8, 2011, the Board entered into an emergency contract, with All American Asphalt to provide emergency storm repair work on Bautista Road, approximately 4 miles southeasterly of Fairview Avenue near the Hemet area. The originally authorized amount of the contract was \$280,000.

Juan C. Perez
Director of Transportation

dj
(Continued On Attached Page)

FINANCIAL DATA	Current F.Y. Total Cost:	\$166,429	In Current Year Budget:	Yes
	Current F.Y. Net County Cost:	\$ 0	Budget Adjustment:	No
	Annual Net County Cost:	\$ 0	For Fiscal Year:	2010/2011
SOURCE OF FUNDS: Gas Tax (100%)				Positions To Be Deleted Per A-30 <input type="checkbox"/> Requires 4/5 Vote <input type="checkbox"/>

C.E.O. RECOMMENDATION:

APPROVE

Tina Grande

County Executive Office Signature

MINUTES OF THE BOARD OF SUPERVISORS

On motion of Supervisor Buster, seconded by Supervisor Benoit and duly carried, IT WAS ORDERED that the above matter is approved as recommended.

Ayes: Buster, Stone, Benoit and Ashley
Nays: None
Absent: Tavaglione
Date: March 29, 2011
xc: Transp., Recorder

Kecia Harper-Ihem
Clerk of the Board
By: Deputy

Prev. Agn. Ref. 2/8/11, Item 3.36 | **District:** 3 | **Agenda Number:**

3.32

Departmental Concurrence

Dept't Recomm.: Consent Policy
 Per Exec. Ofc.: Consent Policy

The Honorable Board of Supervisors

RE: Notice of Completion - Emergency Storm Damage Repair, Bautista Road, near the Hemet Area

March 10, 2011

Page 2 of 2

The total amended contract amount (including quantity adjustments) is \$166,429 which is 41% less than the originally authorized amount.

This work was completed in conformance with the plans and specifications on January 31, 2011. The work was inspected by the Construction Engineering Section of the Transportation Department. Work Order 45111501.

Budget

Original Contract Amount		\$280,000.00
Tot. Chg Orders Authorized -	0.0%	\$0.00
Est. Pending Change Orders	0.0%	\$0.00
Amended Contract Amount		\$280,000.00
* Quantity Adjustments	-40.6%	(\$113,570.95)
+ CCO FA Adjustments	0.0%	\$0.00
Total Amended Contract Amount	59.4%	\$166,429.05

Expenditures

Total Progress Payments -		\$166,429.05
Estimated Pending Payments		
Total Expenditures		\$166,429.05

(Over)\Under Contract Amount \$0.00

+ Change Orders using the Force Account method of payment issued prior to the work being completed generally do not use the total authorized amount.

* CAL-Trans Standard Specifications 4-1.03B. Increases or decreases in the quantity of a contract item of work will be determined by comparing the total pay quantity of such item of work with the Engineer's Estimate. If the total pay quantity of any item of work required under the contract varies from the Engineers Estimate by 25 percent or less, payment will be made for the quantity of work of said item performed at contract unit price, unless eligible for adjustment pursuant to Section 4-1.03C, "Changes in Character of Work."

PLEASE COMPLETE THIS INFORMATION
RECORDING REQUESTED BY:

**KECIA HARPER-IHEM, CLERK OF THE BOARD
RIVERSIDE CO. CLERK OF THE BOARD
4080 LEMON STREET, 1ST FLOOR CAC
P O BOX 1147 - RIVERSIDE, CA 92502
MAIL STOP # 1010**

AND WHEN RECORDED MAIL TO:
RETURN TO: STOP #1010
RIVERSIDE COUNTY CLERK OF THE BOARD
P. O. BOX 1147 - RIVERSIDE, CA 92502

DOC # 2011-0147805

04/04/2011 02:40P Fee:NC

Page 1 of 2

Recorded in Official Records

County of Riverside

Larry W. Ward

Assessor, County Clerk & Recorder



S	R	U	PAGE	SIZE	DA	MISC	LONG	RFD	COPY
1			2						
M	A	L	465	426	PCOR	NCOR	SMF	NCHG	EXAM
nchgc						T:	CTY	UNI	518

NOTICE OF COMPLETION



To be recorded with County Recorder
within 10 days after completion.
No recording fee.

Notice is hereby given by the undersigned owner, a public entity of the State of California, that a public work of improvement has been completed, as follows:

Project title or description of work: Emergency Storm Damage Repair

Date of Completion: Date of this notice 3/29/11

Nature of owner: County of Riverside, public entity

Interest or estate of owner: Public Roadway

Address of owner: 4080 Lemon Street, 8th Floor, Riverside, CA 92501

Name of contractor: All American Asphalt

Street or legal description of site: Bautista Road

Dated: March 29, 2011

Owner: County of Riverside
(Name of Public Entity)

By: Bob Buster
Chairman, Board of Supervisors
Bob Buster

STATE OF CALIFORNIA)

ss

COUNTY OF RIVERSIDE)

I am the Chairman of the governing board of the County of Riverside, the public entity which executed the foregoing notice and on whose behalf I make this verification; I have read this notice, know its contents, and the same is true. I certify under penalty of perjury that the foregoing is true and correct.

Executed at Riverside, California on 3/29/11 (Date)

Bob Buster, Chairman of the Board of Supervisors
Bob Buster

ATTEST:
Kecia Harper-Ihem, Clerk

By Kecia Harper-Ihem
Deputy

03.29.11 3.32

2011-4-106824



**LARRY W. WARD
COUNTY OF RIVERSIDE
ASSESSOR-COUNTY CLERK-RECORDER**

Recorder
P.O. Box 751
Riverside, CA 92502-0751
(951) 486-7000

<http://riverside.asrclkrec.com>

CERTIFICATION

Pursuant to the provisions of Government Code 27361.7, I certify under the penalty of perjury that the following is a true copy of illegible wording found in the attached document:

(Print or type the page number(s) and wording below):

CLARIFICATION OF THE SEAL for the Riverside County Board of Supervisors
(embossed on document)



Date:

3-29-11

Signature:

Karen Barton

Print Name:

Karen Barton, Board Assistant, Riverside County Clerk of the Board



County of Riverside

Department of Transportation


Emergency Storm Damage Repair Work

Bautista Road

**Approximately 4 miles southeasterly of Fairview Avenue
near the Hemet area**

Project No. 45-111501

Vicinity Map

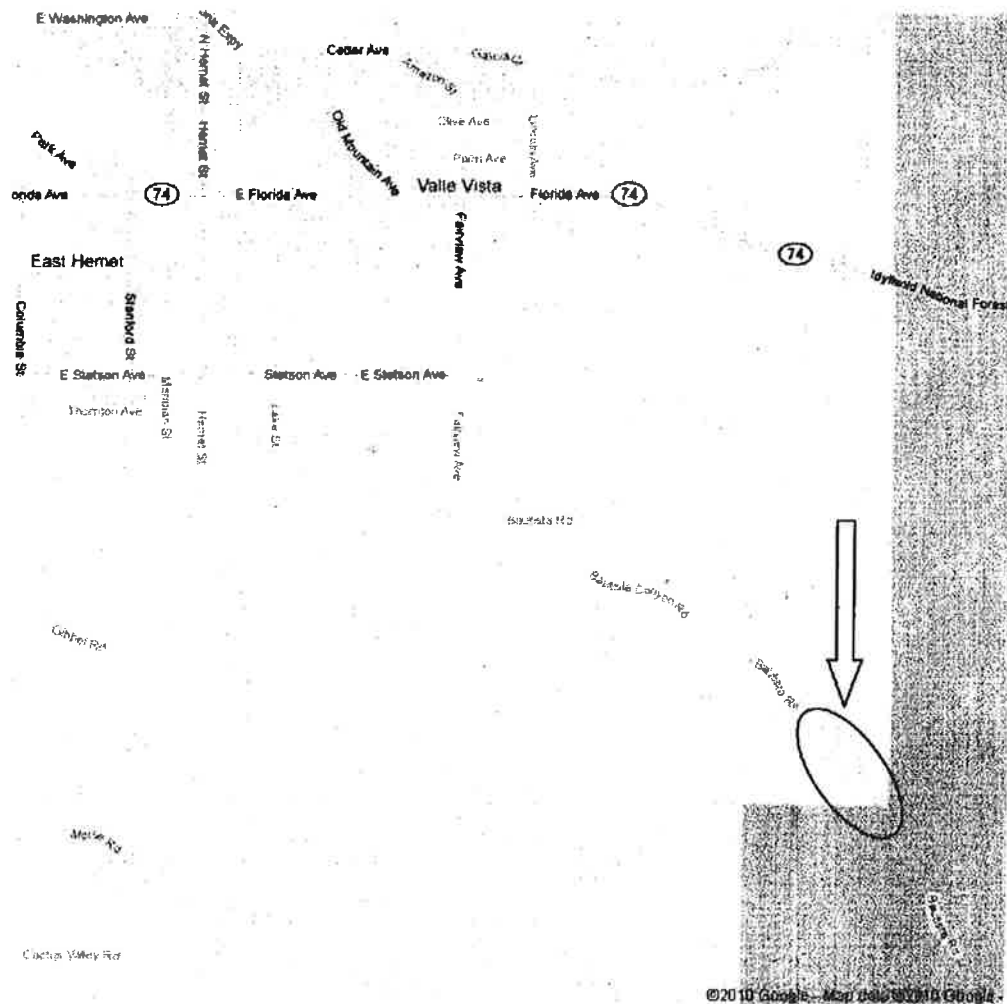

Project No. 45-111501

Contractor: All American Asphalt
 Address: P.O. Box 2228
 City, State, Zip: Corona, CA 92678

Estimate No. 1 FINAL
 From: January 11, 2011
 To: February 25, 2011



Item No.	Item Description	Units	Quantity	Unit Price	Original Contract Amount	Change Authorized Quantity	Total Authorized Quantity	This Estimate		Previous Quantity	Total Estimate To Date		% Auth.
								Quantity	Amount		Quantity	Amount	
1	Emergency Road Repairs, Replace CSPs, Concrete	FA	280,000	1.00	280,000.00		280,000.00	166,429.05	166,429.05		166,429.05	166,429.05	59%
PROJECT TOTAL					280,000.00	0.00	280,000.00	166,429.05	166,429.05		166,429.05	166,429.05	

Made by: Trai Nguyen

Checked by:

OK Const Supv.

Working Days: 30
 Days Added: 0
 Subtotal: 30
 Days Used: 18
 % Time Elapsed: 60%

Start Date: 1-11-11
 End Date: 1-31-11
 % Complete: 59%

Original Contract: \$280,000.00
 Amended Contract: \$280,000.00

TOTAL VALUE OF WORK TO DATE: \$166,429.05
 LESS RETENTION: 0%
 TOTAL DUE TO DATE: \$166,429.05
 LESS PREVIOUSLY INVOICED: 0.00
 LESS LABOR NON COMPLIANCE: 0.00
 TOTAL DUE THIS PAYMENT: \$166,429.05 ✓

This Estimate Approved _____ Date: _____ for: \$166,429.05

Juan Perez, Director of Transportation

All American Asphalt

Quantities on This Estimate Approved _____ Date: 02/25/2011

PAYMENT APPROVAL

Fund 20000

Dept ID 31305

Account 527980

Project 245111501E

Activity ID 23500

Resource Type CNT

Signature

Date 2/28/11

Received by Accounts Payable: _____
 By: _____
