

**SUBMITTAL TO THE BOARD OF SUPERVISORS
COUNTY OF RIVERSIDE, STATE OF CALIFORNIA**

210



FROM: TLMA - Transportation Department

SUBMITTAL DATE:
January 3, 2013

SUBJECT: Notice of Completion - Camino Real Resurfacing in the City of Jurupa Valley

RECOMMENDED MOTION: That the Board of Supervisors execute and file the attached "Notice of Completion"

BACKGROUND: By Minute Order 3.70 Dated July 31, 2012, the Board of Supervisors entered into a contract with All American Asphalt of Corona, CA for the construction of Camino Real Resurfacing Project in the City of Jurupa Valley.

The originally authorized amount of the contract was \$1,570,000. The total amended contract is \$1,573,516, which is 0.2% more than the originally authorized amount.

Juan C. Perez
Director of Transportation and Land Management

dj
(Continued On Attached Page)

FINANCIAL DATA	Current F.Y. Total Cost:	\$1,573,516	In Current Year Budget:	Yes
	Current F.Y. Net County Cost:	\$ 0	Budget Adjustment:	No
	Annual Net County Cost:	\$ 0	For Fiscal Year:	2012/2013

SOURCE OF FUNDS: Proposition 1B (State Bond Funds-Local Roads) (62.2%), ABX8 9 (Gas Tax Mar 2010) (37.4%), Jurupa Community Services Dist. (0.4%) There were no General Funds used in this project	Positions To Be Deleted Per A-30	<input type="checkbox"/>
	Requires 4/5 Vote	<input type="checkbox"/>

C.E.O. RECOMMENDATION:

APPROVE
BY:
Tina Grande

County Executive Office Signature

- Dept's Recomm.: Consent Policy
- Per Exec. Ofc.: Consent Policy

MINUTES OF THE BOARD OF SUPERVISORS

On motion of Supervisor Ashley, seconded by Supervisor Stone and duly carried by unanimous vote, IT WAS ORDERED that the above matter is approved as recommended.

Ayes: Jeffries, Tavaglione, Stone, Benoit and Ashley
 Nays: None
 Absent: None
 Date: January 15, 2013
 xc: Transp., Recorder

Kecia Harper-Ihem
Clerk of the Board
By:
Deputy

Prev. Agn. Ref. 07/31/12, Item 3.70 | District: 2/2 | Agenda Number:

ATTACHMENTS FILED
WITH THE CLERK OF THE BOARD

3-17

The Honorable Board of Supervisors
RE: Notice of Completion - Camino Real Resurfacing in the City of Jurupa Valley

Page 2 of 2

This work was completed at the direction of the Department on October 26, 2012, and was inspected by the Construction Engineering Section of the Transportation Department. Work Order C1-0503.

Budget

Original Contract Amount		\$1,570,000.00
Tot. Chg Orders Authorized -	0.0%	\$0.00
Est. Pending Change Orders	0.0%	\$0.00
Amended Contract Amount		\$1,570,000.00
* Quantity Adjustments	0.2%	\$3,516.31
+ CCO FA Adjustments	0.0%	\$0.00
Total Amended Contract Amount	100.2%	<u>\$1,573,516.31</u>

Expenditures

Total Progress Payments -		\$1,573,516.31
Estimated Pending Payments		
Total Expenditures		<u>\$1,573,516.31</u>

(Over)\Under Contract Amount \$0.00

+ Change Orders using the Force Account method of payment issued prior to the work being completed generally do not use the total authorized amount.

* CAL-Trans Standard Specifications 4-1.03B. Increases or decreases in the quantity of a contract item of work will be determined by comparing the total pay quantity of such item of work with the Engineer's Estimate. If the total pay quantity of any item of work required under the contract varies from the Engineer's Estimate by 25 percent or less, payment will be made for the quantity of work of said item performed at contract unit price, unless eligible for adjustment pursuant to Section 4-1.03C, "Changes in Character of Work."

PLEASE COMPLETE THIS INFORMATION
RECORDING REQUESTED BY:

KECIA HARPER-IHEM, CLERK OF THE BOARD
RIVERSIDE CO. CLERK OF THE BOARD
4080 LEMON STREET, 1ST FLOOR CAC
P O BOX 1147 - RIVERSIDE, CA 92502
MAIL STOP # 1010

DOC # 2013-0024969
01/16/2013

Customer Copy Label
The paper to which this label is
affixed has not been compared
with the filed/recorded document

Larry W Ward
County of Riverside
Assessor, County Clerk & Recorder

AND WHEN RECORDED MAIL TO:

RETURN TO: STOP #1010
RIVERSIDE COUNTY CLERK OF THE BOARD
P. O. BOX 1147 - RIVERSIDE, CA 92502

THIS SPACE FOR RECORDERS USE ONLY

NOTICE OF COMPLETION

To be recorded with County Recorder
within 10 days after completion.
No recording fee.

Notice is hereby given by the undersigned owner, a public entity of the State of California, that a public work of
improvement has been completed, as follows:

Project title or description of work: Camino Real Resurfacing Project

Date of Completion: Date of this notice 01/15/13

Nature of owner: County of Riverside, public entity

Interest or estate of owner: Public Roadway


Address of owner: 4080 Lemon Street, 8th Floor, Riverside, CA 92501

Name of contractor: All American Asphalt

Street or legal description of site: Camino Real

Dated: January 15, 2013

Owner: County of Riverside
(Name of Public Entity)

By: 
Chairman, Board of Supervisors
John J. Benoit


STATE OF CALIFORNIA)

ss


COUNTY OF RIVERSIDE)

I am the Chairman of the governing board of the County of Riverside, the public entity which executed the
foregoing notice and on whose behalf I make this verification; I have read this notice, know its contents, and the same is
true. I certify under penalty of perjury that the foregoing is true and correct.

Executed at Riverside California on 01/15/13 (Date)


Chairman of the Board of Supervisors
John J. Benoit

ATTEST:
Kecia Harper-Ihem, Clerk

By  Deputy

01.15.13 3-17

COPY



**LARRY W. WARD
COUNTY OF RIVERSIDE
ASSESSOR-COUNTY CLERK-RECORDER**

Recorder
P.O. Box 751
Riverside, CA 92502-0751
(951) 486-7000


<http://riverside.asrcfrec.com>

CERTIFICATION

Pursuant to the provisions of Government Code 27361.7, I certify under the penalty of perjury that the following is a true copy of illegible wording found in the attached document:

(Print or type the page number(s) and wording below):

CLARIFICATION OF THE SEAL for the Riverside County Board of Supervisors
(embossed on document)



Date:

1-15-13

Signature:



Karen Barton

Print Name:

Karen Barton, Board Assistant, Riverside County Clerk of the Board

COUNTY OF RIVERSIDE
DEPARTMENT OF TRANSPORTATION

CAMINO REAL
RESURFACING PROJECT
IN THE CITY OF JURUPA VALLEY

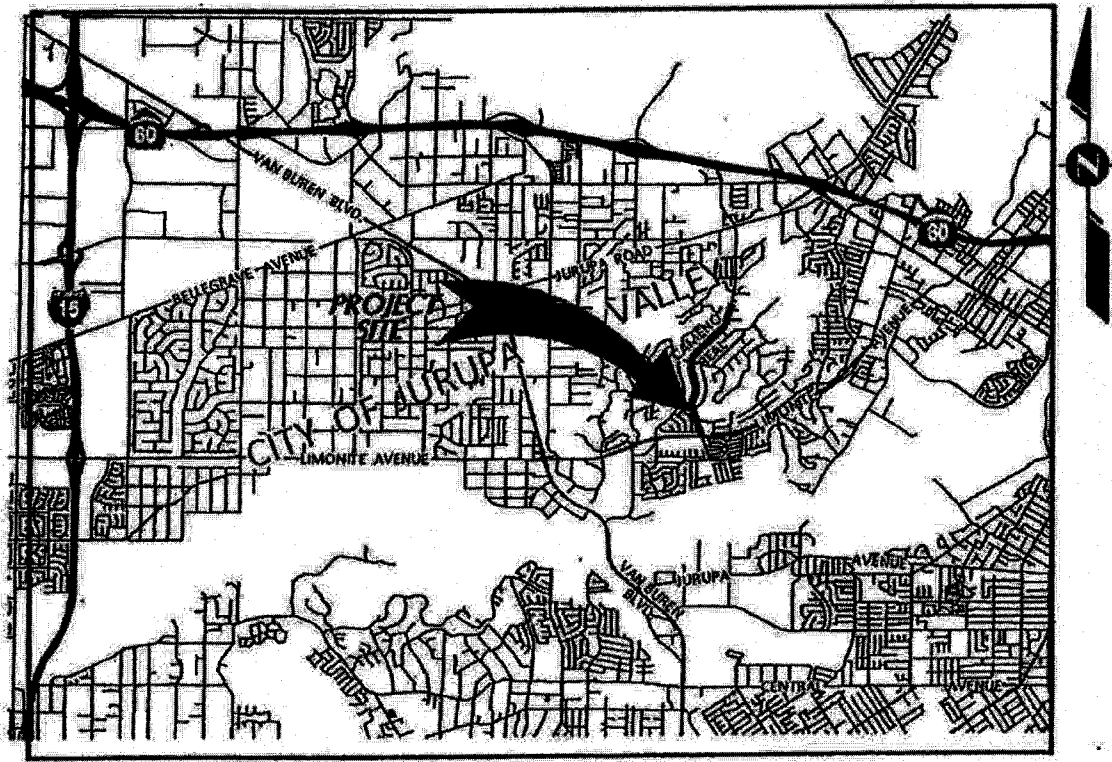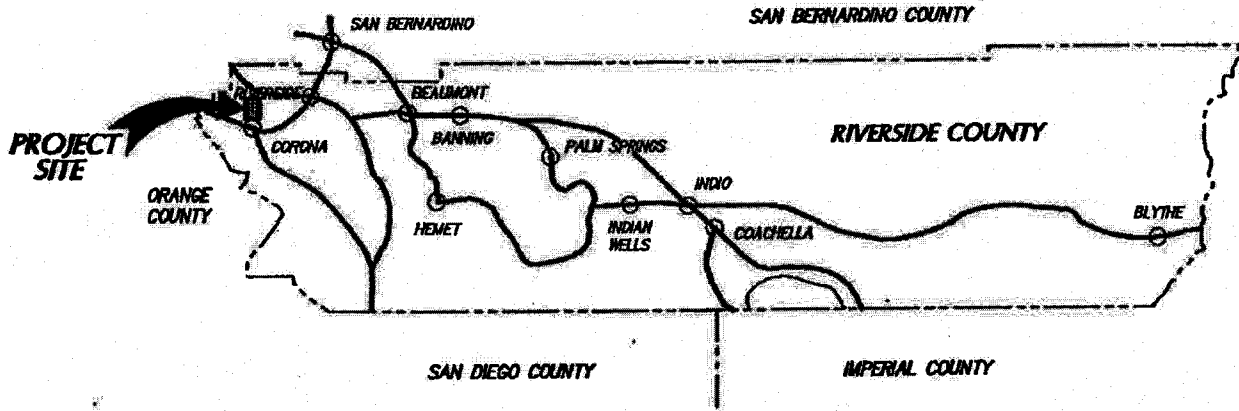

VICINITY MAP

PROJECT LENGTH - 7123 L.F.
TOWNSHIP 2S, SECTIONS 18 & 19, RANGE 5W
2008 THOMAS GUIDE, PAGE 684, H-2 THRU H-5

PROJECT: Camino Real Resurfacing Project in the City of Jurupa Valley
 County Project No.: C1-0503
 Contract No.: 12-06-011

Contractor: All American Asphalt
 Address: P.O. Box 2229, Corona, CA 92878
 City, State, Zip: Corona, CA 92878

Estimate No. 2 Final
 From: September 26, 2012
 To: November 25, 2012



Item No.	Item Description	Units	Quantity	Unit Price	Original Contract Amount	Change Authorized Quantity	Amount	Total Authorized Quantity	Amount	This Estimate Quantity	Amount	Previous Quantity	Amount	Total Estimate To Date Quantity	Amount	% Auth.
24	PAVEMENT MARKER (REFLECTIVE)	EA	1,500	3.00	4,500.00		4,500.00	1,500.00	4,500.00	1,485.00	4,455.00		4,455.00	1,485.00	4,455.00	99%
25	DETECTOR LOOP	EA	20	200.00	4,000.00		4,000.00	20.00	4,000.00	21.00	4,200.00		4,200.00	21.00	4,200.00	105%
26	ADJUST MANHOLE TO GRADE	EA	22	350.00	7,700.00		7,700.00	22.00	7,700.00	23.00	8,050.00	1.00	8,050.00	24.00	8,400.00	109%
PROJECT TOTAL					1,570,000.00		1,570,000.00		1,570,000.00		1,345,619.45		1,345,619.45		1,573,516.31	

Made by: Jesse Mendoza
 Checked by: JY 11-28-12
 OK Const. Supv. JAC

Working Days: 40
 Days Added: 0
 Subtotal: 40
 Days Used: 32
 % Time Elapsed: 80%

Start Date: 9-12-12
 End Date: 10-26-12
 % Complete: 100%
 Original Contract: \$1,570,000.00
 Amended Contract: \$1,570,000.00

TOTAL VALUE OF WORK TO DATE: \$1,573,516.31
 LESS RETENTION: 5% 78,675.81
 TOTAL DUE TO DATE: \$1,494,840.50
 LESS PREVIOUSLY INVOICED: 216,502.02
 LESS LABOR NON COMPLIANCE: 0.00
 TOTAL DUE THIS PAYMENT: \$1,278,338.48

This Estimate Approved _____ Date: _____ for: _____
 Juan C. Perez, Director of Transportation and Land Management
 _____ Date: 11/30/12
 All American Asphalt

Received by Accounts Payable: _____
 By: _____
PAYMENT APPROVAL
 Fund 20000
 Dept ID 31805
 Account 527980

Project ZC1-0503
 Activity ID Z3500
 Resource Type CNT
 Signature [Signature]
 Date 12/10/12

PROJECT: Camino Real Resurfacing Project in the City of Jurupa Valley
 County Project No.: C1-0503
 Contract No.: 12-06-011

Contractor: All American Asphalt
 Address: P.O. Box 2229, Corona, CA 92878
 City, State, Zip: Corona, CA 92878

Estimate No. 2 Final
 From: September 26, 2012
 To: November 25, 2012



Item No.	Item Description	Units	Quantity	Unit Price	Original Contract Amount	Change Authorized Quantity	Change Authorized Amount	Total Authorized Quantity	Total Authorized Amount	This Estimate Quantity	This Estimate Amount	Previous Quantity	Previous Amount	Total Estimate To Date Quantity	Total Estimate To Date Amount	% Auth.
1	DUST ABATEMENT	LS	1	5,000.00	5,000.00			1.00	5,000.00	0.50	2,500.00	0.50	2,500.00	1.00	5,000.00	100%
2	WATER POLLUTION CONTROL	LS	1	7,000.00	7,000.00			1.00	7,000.00	0.50	3,500.00	0.50	3,500.00	1.00	7,000.00	100%
3	TRAFFIC CONTROL SYSTEM	LS	1	38,205.00	38,205.00			1.00	38,205.00	0.50	19,102.50	0.50	19,102.50	1.00	38,205.00	100%
4	CLEARING AND GRUBBING	LS	1	10,000.00	10,000.00			1.00	10,000.00	0.50	5,000.00	0.50	5,000.00	1.00	10,000.00	100%
5	DEVELOP WATER SUPPLY	LS	1	3,250.00	3,250.00			1.00	3,250.00	1.00	3,250.00		3,250.00	1.00	3,250.00	100%
6	ROADWAY EXCAVATION	CY	3,100	17.00	52,700.00			3,100.00	52,700.00	777.00	13,209.00	2,750.00	13,209.00	3,527.00	59,959.00	114%
7	WEDGE PLANE ASPHALT CONCRETE	LF	15,400	0.70	10,780.00			15,400.00	10,780.00	15,599.00	10,919.30		10,919.30	15,599.00	10,919.30	101%
8	WEDGE PLANE ASPHALT CONCRETE - MEDIUM COLD PLANE ASPHALT CONCRETE PAVEMENT	LF	3,200	0.70	2,240.00			3,200.00	2,240.00	3,288.00	2,301.60		2,301.60	3,288.00	2,301.60	103%
9	PAVEMENT REINFORCING FABRIC (FIBER GLASS FABRIC)	SQYD	1,000	1.00	1,000.00			1,000.00	1,000.00	1,250.00	1,250.00		1,250.00	1,250.00	1,250.00	125%
10	CLASS 2 AGGREGATE BASE	SQYD	66,700	1.80	120,060.00			66,700.00	120,060.00	66,033.00	118,859.40		118,859.40	66,033.00	118,859.40	99%
11	HOT MIX ASPHALT	CY	1,700	24.50	41,650.00			1,700.00	41,650.00	1,030.00	25,235.00	1,095.00	25,235.00	2,125.00	52,062.50	125%
12	ASPHALT RUBBER HOT MIX	TON	8,300	63.50	527,050.00			8,300.00	527,050.00	7,224.45	458,752.58	894.36	458,752.58	8,118.81	515,544.44	98%
13	MINOR CONCRETE (CURB & GUTTER) (CRS 201)	TON	8,500	76.00	646,000.00			8,500.00	646,000.00	8,394.22	637,960.72		637,960.72	8,394.22	637,960.72	99%
14	MINOR CONCRETE (CURB RAMP) (CRS 403)	LF	200	45.00	9,000.00			200.00	9,000.00			250.00		250.00	11,250.00	125%
15	MINOR CONCRETE (CROSS-GUTTER AND SPANDREL)	EA	5	2,000.00	10,000.00			5.00	10,000.00	6.00		6.00		6.00	12,000.00	120%
16	MINOR CONCRETE (CURB, GUTTER, SIDEWALK AND DRIVEWAY)	SQFT	3,000	10.00	30,000.00			3,000.00	30,000.00			3,000.00		3,000.00	30,000.00	100%
17	RELOCATE ROADSIDE SIGN	SQFT	2,500	5.00	12,500.00			2,500.00	12,500.00			2,765.00		2,765.00	13,825.00	111%
18	INSTALL ROADSIDE SIGN PANEL ON EXISTING POST	EA	1	200.00	200.00			1.00	200.00	1.00	200.00		200.00	1.00	200.00	100%
19	INSTALL SIGN (STRAP AND SADDLE BRACKET METHOD)	EA	7	200.00	1,400.00			7.00	1,400.00	8.00	1,600.00		1,600.00	8.00	1,600.00	114%
20	REMOVE TRAFFIC STRIPE AND PAVEMENT MARKING	EA	2	200.00	400.00			2.00	400.00	2.00	400.00		400.00	2.00	400.00	100%
21	PAINT TRAFFIC STRIPE 2 COAT	SQFT	1,200	1.50	1,800.00			1,200.00	1,800.00	1,344.00	2,016.00		2,016.00	1,344.00	2,016.00	112%
22	THERMOPLASTIC CROSSWALK AND PAVEMENT MARKING	LF	31,500	0.26	8,190.00			31,500.00	8,190.00	31,335.00	8,147.10		8,147.10	31,335.00	8,147.10	99%
23		SQFT	4,100	3.75	15,375.00			4,100.00	15,375.00	3,923.00	14,711.25		14,711.25	3,923.00	14,711.25	96%
