

**SUBMITTAL TO THE BOARD OF SUPERVISORS  
COUNTY OF RIVERSIDE, STATE OF CALIFORNIA**

530A



**FROM:** TLMA - Transportation Department

**SUBMITTAL DATE:**  
February 13, 2013

**SUBJECT:** Notice of Completion - Mission Boulevard Rehabilitation Project, City of Jurupa Valley

**RECOMMENDED MOTION:** That the Board of Supervisors execute and file the attached "Notice of Completion"

**BACKGROUND:** By Minute Order 3.48 of June 19, 2012, the Board entered into a contract with All American Asphalt of Corona, CA for the rehabilitation of an approximate 900 foot segment of Mission Boulevard between the SR-60 eastbound off-ramp and the SR-60 westbound on-ramp in the City of Jurupa Valley.

Juan C. Perez  
Director of Transportation and Land Management

dj  
(Continued On Attached Page)

<b>FINANCIAL DATA</b>	Current F.Y. Total Cost:	\$195,329	In Current Year Budget:	Yes
	Current F.Y. Net County Cost:	\$ 0	Budget Adjustment:	No
	Annual Net County Cost:	\$ 0	For Fiscal Year:	2012/2013

<b>SOURCE OF FUNDS:</b> ABX8 9 (Gas Tax Mar 2010) (99.4%), Jurupa Community Services District (0.6%) = 100%	<b>Positions To Be Deleted Per A-30</b>	<input type="checkbox"/>
	<b>Requires 4/5 Vote</b>	<input type="checkbox"/>

There were no General Funds used in this project

**C.E.O. RECOMMENDATION:**  
 APPROVE  
 BY:   
 Tina Grande  
 County Executive Office Signature

**MINUTES OF THE BOARD OF SUPERVISORS**

On motion of Supervisor Ashley, seconded by Supervisor Benoit and duly carried by unanimous vote, IT WAS ORDERED that the above matter is approved as recommended.

**Ayes:** Jeffries, Tavaglione, Stone, Benoit and Ashley  
**Nays:** None  
**Absent:** None  
**Date:** February 26, 2013  
**xc:** Transp., Recorder

Kecia Harper-Ihem  
Clerk of the Board  
By:   
Deputy

Prev. Agn. Ref. 06/19/12, Item 3.48 | District: 2/2 | Agenda Number:

3-64

Departmental Concurrence

Dept't Recomm.:  Policy  Consent  
 Per Exec. Ofc.:  Policy  Consent

The originally authorized amount of the contract was \$226,069. The total amended contract is \$195,329, which is 13.6% less than the originally authorized amount. The reduction in the total contract price was the direct result of less asphalt paving and traffic striping required to complete the work than originally determined in the engineers estimate.

This work was completed at the direction of the Department on November 1, 2012, and was inspected by the Construction Engineering Section of the Transportation Department, Work Order C2-0135.

**Budget**

Original Contract Amount		\$226,069.00
Total Change Orders Authorized	0.0%	\$0.00
Estimated Pending Change Orders	0.0%	\$0.00
Amended Contract Amount		\$226,069.00
* Quantity Adjustments	-13.6%	(\$30,740.40)
+ CCO FA Adjustments	0.0%	\$0.00
Total Amended Contract Amount	86.4%	\$195,328.60

**Expenditures**

Total Progress Payments		\$195,328.60
Estimated Pending Payments		
Total Expenditures		\$195,328.60
<b>(Over)/Under Contract Amount</b>		<u><u>\$0.00</u></u>

+ Change Orders using the Force Account method of payment issued prior to the work being completed generally do not use the total authorized amount.

\* CAL-Trans Standard Specifications 4-1.03B. Increases or decreases in the quantity of a contract item of work will be determined by comparing the total pay quantity of such item of work with the Engineer's Estimate. If the total pay quantity of any item of work required under the contract varies from the Engineer's Estimate by 25 percent or less, payment will be made for the quantity of work of said item performed at the contract unit price, unless eligible for adjustment pursuant to Section 4-1.03C, "Changes in Character of Work."

PLEASE COMPLETE THIS INFORMATION  
RECORDING REQUESTED BY:

KECIA HARPER-IHEM, CLERK OF THE BOARD  
RIVERSIDE CO. CLERK OF THE BOARD  
4080 LEMON STREET, 1<sup>ST</sup> FLOOR CAC  
P O BOX 1147 - RIVERSIDE, CA 92502  
MAIL STOP # 1010

DOC # 2013-010007  
02/28/2013

Customer Copy Label  
The paper to which this label is  
affixed has not been compared  
with the filed/recorded document

Larry W Ward  
County of Riverside  
Assessor, County Clerk & Recorder

AND WHEN RECORDED MAIL TO:

RETURN TO: STOP #1010  
RIVERSIDE COUNTY CLERK OF THE BOARD  
P. O. BOX 1147 - RIVERSIDE, CA 92502

THIS SPACE FOR RECORDERS USE ONLY

NOTICE OF COMPLETION

To be recorded with County Recorder  
within 10 days after completion.  
No recording fee.

Notice is hereby given by the undersigned owner, a public entity of the State of California, that a public work of  
improvement has been completed, as follows:

Project title or description of work: Mission Boulevard at SR-60 Rehabilitation Project

Date of Completion: Date of this notice 02/26/13

Nature of owner: County of Riverside, public entity

Interest or estate of owner: Public Roadway

Address of owner: 4080 Lemon Street, 8th Floor, Riverside, CA 92501

Name of contractor: All American Asphalt

Street or legal description of site: Mission Boulevard. at SR-60

Dated: February 26, 2013

Owner: County of Riverside  
(Name of Public Entity)

By: John J. Benoit  
Chairman, Board of Supervisors  
John J. Benoit

STATE OF CALIFORNIA )

ss

COUNTY OF RIVERSIDE )

I am the Chairman of the governing board of the County of Riverside, the public entity which executed the  
foregoing notice and on whose behalf I make this verification; I have read this notice, know its contents, and the same is  
true. I certify under penalty of perjury that the foregoing is true and correct.

Executed at Riverside, California on 02/26/13 (Date)

John J. Benoit, Chairman of the Board of Supervisors  
John J. Benoit

ATTEST:  
Kecia Harper-Ihem, Clerk

By: Kecia Harper-Ihem Deputy

02.26.13 3-64

COPY



**LARRY W. WARD  
COUNTY OF RIVERSIDE  
ASSESSOR-COUNTY CLERK-RECORDER**


**Recorder**  
P.O. Box 751  
Riverside, CA 92502-0751  
(951) 486-7000  
<http://riverside.asrcfrec.com>

**CERTIFICATION**

Pursuant to the provisions of Government Code 27361.7, I certify under the penalty of perjury that the following is a true copy of illegible wording found in the attached document:

(Print or type the page number(s) and wording below):

CLARIFICATION OF THE SEAL for the Riverside County Board of Supervisors  
(embossed on document)



Date:

02/20/13

Signature:

*Karen Barton*

Print Name:

Karen Barton, Board Assistant, Riverside County Clerk of the Board



PROJECT: Mission Blvd. Pavement Rehabilitation Project at SR 60, Between East Bound Off-Ramp and West Bound On-Ramp  
 County Project No.: C2-0135  
 Contract No. 12-05-007

Contractor: All American Asphalt  
 Address: P.O. Box 2229  
 City, State, Zip: Corona, CA 92878

Estimate No. 2 Final  
 From: September 26, 2012  
 To: October 25, 2012

Item No.	Item Description	Units	Quantity	Unit Price	Original Contract		Change Authorized		Total Authorized		This Estimate		Previous		Total Estimate To Date		% Auth.
					Amount	Quantity	Amount	Quantity	Amount	Quantity	Quantity	Amount	Quantity	Quantity	Amount		
					226,069.00	0.00			226,069.00							195,328.60	
<b>PROJECT TOTAL</b>																	

Made by: Steve Kestly

Checked by:   
 OK Const. Supv. 

Working Days: 10 Start Date: 9-10-12 End Date: 11-1-12  
 Days Added: 0  
 Subtotal: 10 % \$ Complete: 86%  
 Days Used: 10 Original Contract: \$226,069.00  
 % Time Elapsed: 100% Amended Contract: \$226,069.00


TOTAL VALUE OF WORK TO DATE: \$195,328.60  
 LESS RETENTION: 5% 9,766.43  
 TOTAL DUE TO DATE: \$185,562.17  
 LESS PREVIOUSLY INVOICED: 164,543.61  
 LESS LABOR NON COMPLIANCE: 0.00  
 TOTAL DUE THIS PAYMENT: \$21,018.56


This Estimate Approved \_\_\_\_\_ Date: \_\_\_\_\_ for: \_\_\_\_\_  
 Juan C. Perez, Director of Transportation and Land Management

Received by Accounts Payable: \_\_\_\_\_  
 By: \_\_\_\_\_

Quantities on This Estimate Approved  Date: 11/13/12  
 All American Asphalt

**PAYMENT APPROVAL**  
 Fund 20000  
 Dept ID 31305  
 Account 527980  
 Project Z-CR-0135E

Activity ID Z3500  
 Resource Type UNIT  
 Signature   
 Date 11/13/12



**PROGRESS ESTIMATE RECORD - COUNTY OF RIVERSIDE**  
**PROJECT:** Mission Blvd. Pavement Rehabilitation Project at SR 60, Between East Bound  
 Off-Ramp and West Bound On-Ramp  
 County Project No.: C2-9136  
 Contract No. 12-05-007



Item No.	Item Description	Units	Quantity	Unit Price	Original Contract Amount	Change Authorized Quantity	Change Authorized Amount	Total Authorized Quantity	Total Authorized Amount	This Estimate		Previous Quantity	Total Estimate To Date		% Auth.
										Quantity	Amount		Quantity	Amount	
1	OBTAIN ENCROACHMENT PERMIT	FA	1	10,000.00	10,000.00			1.00	10,000.00	1.00	1.00	1.00	10,000.00	100%	
2	DUST ABATEMENT	LS	1	520.00	520.00			1.00	520.00	1.00	1.00	1.00	520.00	100%	
3	TRAFFIC CONTROL SYSTEM	LS	1	21,600.00	21,600.00			1.00	21,600.00	0.25	5,400.00	1.00	21,600.00	100%	
4	CLEARING AND GRUBBING	LS	1	1,040.00	1,040.00			1.00	1,040.00		1.00	1.00	1,040.00	100%	
5	FINISHING ROADWAY	LS	1	1,040.00	1,040.00			1.00	1,040.00		1.00	1.00	1,040.00	100%	
6	COLD PLANE ASPHALT CONCRETE PAVEMENT	SQYD	8,900	1.03	9,167.00			8,900.00	9,167.00		8,800.00	8,800.00	9,064.00	99%	
7	SUBGRADE ENHANCEMENT FABRIC	SQYD	8,900	2.60	23,140.00			8,900.00	23,140.00		8,800.00	8,800.00	22,880.00	99%	
8	HOT MIX ASPHALT (TYPE A AND C)	TON	2,140	70.00	149,800.00			2,140.00	149,800.00	150.00	1,564.58	1,714.58	120,020.60	80%	
9	THERMOPLASTIC CROSSWALK AND PAVEMENT MARKING	MA SQFT	300	5.20	1,560.00			300.00	1,560.00	164.00	852.80	164.00	852.80	55%	
10	PAINT TRAFFIC STRIPE	LF	5,500	0.42	2,310.00			5,500.00	2,310.00		5,500.00	5,500.00	2,310.00	100%	
11	PAVEMENT MARKER (REFLECTIVE)	EA	100	5.20	520.00			100.00	520.00		121.00	121.00	629.20	121%	
12	DETECTOR LOOP	EA	14	250.00	3,500.00			14.00	3,500.00	14.00	3,500.00	14.00	3,500.00	100%	
13	ADJUST MANHOLE TO GRADE	EA	3	624.00	1,872.00			3.00	1,872.00	3.00	1,872.00	3.00	1,872.00	100%	

Contractor: All American Asphalt  
 Address: P.O. Box 2229  
 City, State, Zip: Corona, CA 92878

Estimate No.		2 Final	
From:	September 28, 2012	To:	October 25, 2012

**COUNTY OF RIVERSIDE  
DEPARTMENT OF TRANSPORTATION**

**MISSION BLVD  
RESURFACING PROJECT**

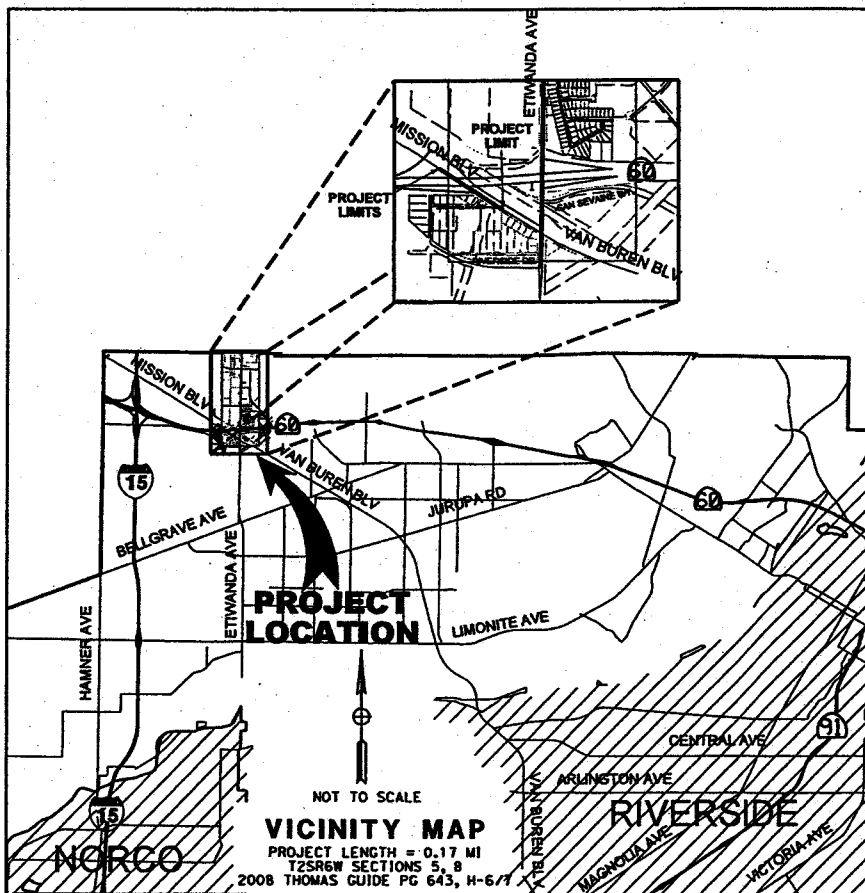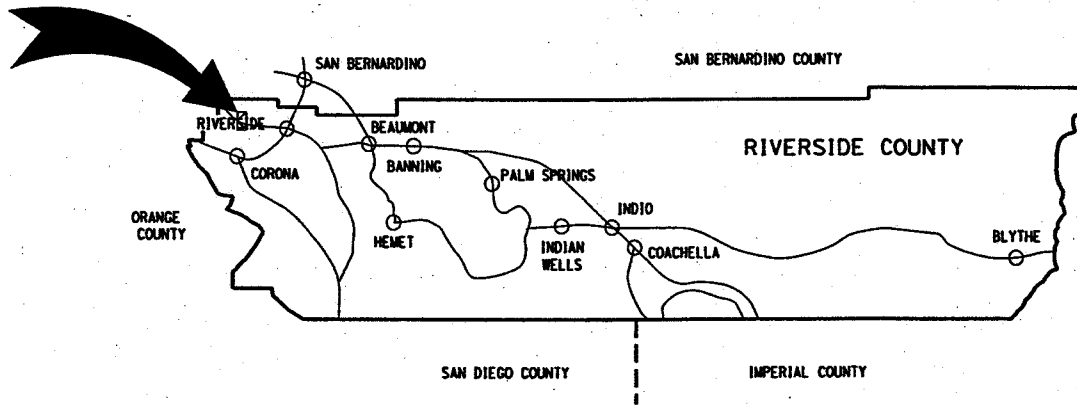

VICINITY MAP

SCALE NONE

EXHIBIT "A"

**MISSION BLVD  
RESURFACING PROJECT**
