SUBMITTAL TO THE BOARD OF SUPERVISORS **COUNTY OF RIVERSIDE, STATE OF CALIFORNIA**

101

FROM: TLMA - Transportation Department

SUBMITTAL DATE: November 27, 2013

SUBJECT: Notice of Completion - Construction of Indiana Avenue and Grant Street Roadway Improvements in the Community of Home Gardens. 2nd/2nd District [\$188,361]; Local Funds 100%

RECOMMENDED MOTION: That the Board of Supervisors execute and file the attached "Notice of Completion."

BACKGROUND:

Summary

Departmental Concurrence

By Minute Order 3-21 of May 21, 2013, the Board entered into a contract with All American Asphalt of Corona, CA for the construction of Indiana Avenue and Grant Street roadway improvements in the community of Home Gardens.

> Patricia Romo Assistant Director of Transportation

Juan C. Perez

Director of Transportation and Land Management

| FINANCIAL DATA | Gurrent Fi | scal Year: | Next Fisc | ál Year; | Total | Costr | ø | ngoing Cost: | 770000000000000000000000000000000000000 | CONSENT ec. Office) |
|---|------------|------------|-----------|------------|--------|-----------------|------|-----------------|---|------------------------|
| COST | \$ | 0.00 | \$ | 0.00 | \$ | 188,361 | \$ | 0.00 | C | Delley Co |
| NET COUNTY COST | \$ | 0.00 | \$ | 0.00 | \$ | 0.00 |) \$ | 0.00 | Consent | Policy - |
| SOURCE OF FUN | DS: Gas | Tax (ABX | 3-9 Mar 2 | 2010 New H | JTA) (| 23.0%), | | Budget Adjustn | nent: No | |
| Community Developme (0.3%). There were no | | | | | aens | Sanitary Distri | ct | For Fiscal Year | : 201 | 3/2014 |
| C.E.O. RECOMME | ENDATION | ON: | | | | <u> </u> | | 1 | | |

County Executive Office Signature

MINUTES OF THE BOARD OF SUPERVISORS

On motion of Supervisor Jeffries, seconded by Supervisor Ashley and duly carried, IT WAS ORDERED that the above matter is approved as recommended.

Ayes:

Jeffries, Stone, Benoit and Ashley

Nays:

None

Tavaglione

Date:

Absent:

December 17, 2013

XC:

Transp., Recorder

Agenda Number:

Kecia Harper-Ihem

Clerk of the Bozard

Positions Added

Change Order

4/5 Vote

SUBMITTAL TO THE BOARD OF SUPERVISORS, COUNTY OF RIVERSIDE, STATE OF CALIFORNIA

FORM 11: Notice of Completion - Construction of Indiana Avenue and Grant Street Roadway Improvements in the Community of Home Gardens. 2nd/2nd District [\$188,361]; Local Funds 100%

DATE: November 14, 2013

PAGE: 2 of 2

BACKGROUND:

Summary (continued)

The originally authorized amount of the contract was \$212,027. The total amended contract is \$188,361, which is 11.2% less than the originally authorized amount.

This work was completed at the direction of the Transportation Department on August 15, 2013, and was inspected by the Construction Engineering Section of the Transportation Department, Work Order C2-0138.

Impact on Residents and Businesses

This project provided for new asphalt concrete resurfacing to repair and extend the life of the roads and various pedestrian improvements in the area.

SUPPLEMENTAL:

Additional Fiscal Information

Budget

| Original Contract Amount | | \$212,027.00 |
|---------------------------------|--------|---------------|
| Total Change Orders Authorized | 0.0% | \$0.00 |
| Estimated Pending Change Orders | 0.0% | \$0.00 |
| Amended Contract Amount | | \$212,027.00 |
| * Quantity Adjustments | -11.2% | (\$23,666.18) |
| + CCO FA Adjustments | 0.0% | \$0.00 |
| Total Amended Contract Amount | 88.8% | \$188,360.82 |
| Expenditures | | |
| Total Progress Payments | | \$188,360.82 |
| Estimated Pending Payments | | \$0.00 |
| Total Expenditures | | \$188,360.82 |
| | | |
| (Over)/Under Contract Amount | · | \$0.00 |

⁺ Change Orders using the Force Account method of payment issued prior to the work being completed generally do not use the total authorized amount.

Contract History and Price Reasonableness


N/A


^{*} CAL-Trans Standard Specifications 4-1.03B. Increases or decreases in the quantity of a contract item of work will be determined by comparing the total pay quantity of such item of work with the Engineer's Estimate. If the total pay quantity of any item of work required under the contract varies from the Engineer's Estimate by 25% or less, payment will be made for the quantity of work of said item performed at the contract unit price, unless eligible for adjustment pursuant to Section 4-1.03C, "Changes in Character of Work."

COUNTY OF RIVERSIDE DEPARTMENT OF TRANSPORTATION

INDIANA AVENUE HOME GARDENS ROAD IMPROVEMENT (PHASE II)

PROJECT No. C2-0138
COMMUNITY DEVELOPMENT BLOCK GRANT, CDBG No. 2.27-09



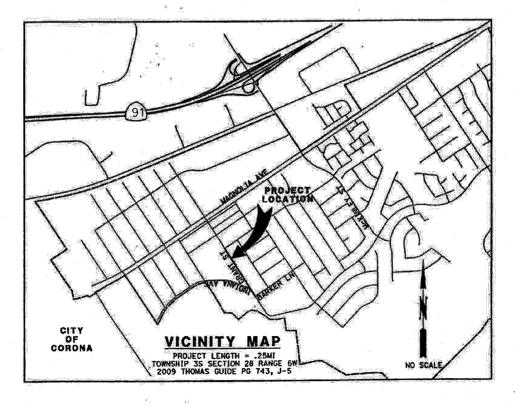

| - | PROGRESS ESTIMATE RECORD - COUNTY OF RIVERSIDE | | | | | | | And the second s | 1,4 | | SHEET 1 of 2 | Process | sed Construction | Processed Construction Inspection 8/28/2013 | 013 |
|-----------|--|------|----------|----------|-------------------------------|-----------------------------------|--|--|-----------|---------------|--------------|--|------------------------|---|----------------|
| ğ | PROJECT: Indiana Avenue Home Gardens Road Improvement (Phase II) | - | | | Contractor: | All American Asphalt | haft | | | | | (SA) | Estimate No. | 1 Final | |
| <u> </u> | Community Development Block Grant County Project No.: C2-0138 | | | | Address: City, Stafe, Zip: | P.O. Box 2229 Corona. CA 92878 | - | | | | | | From: | July 1, 2013 | |
| Š | Contract No. 13-04-004 | | | | | | | | | | | | Ţ. | August 15, 2013 | 013 |
| ltem F | More Description | | 4 | 9 | Original Contract | Change Authorized | ized | Total Authorized | be | This Estimate | imate | Previous | Total Estimate To Date | te To Date | % { |
| | | 5 | + | B | 2002 | \vdash | TINGE TO SERVICE TO SE | Commit | | Control | | Company of the Compan | - Account | 10000 | |
| ~ | DUST ABATEMENT | S | - | 2,650.00 | 2,650.00 | , | | 1.00 | 2,650.00 | 1.00 | 2,650.00 | | 1.00 | 2,650.00 100% | 100% |
| -2 | WATER POLLUTION CONTROL | LS | + | 2,400.00 | 2,400.00 | | | 1.00 | 2,400.00 | 1.00 | 2,400.00 | | 1.00 | 2,400.00 100% | 100% |
| <u>د</u> | TRAFFIC CONTROL SYSTEM | S | - | 4,933.00 | 4,933.00 | | | 1.00 | 4,933.00 | 1.00 | 4,933.00 | | 1.00 | 4,933.00 100% | 100% |
| 4 | CLEARING AND GRUBBING | SJ | . | 1,432.00 | 1,432.00 | | | 1.00 | 1,432.00 | 1.00 | 1,432.00 | | 1.00 | 1,432.00 100% | 100% |
| 2 | 5 DEVELOP WATER SUPPLY | SJ | - | 1,839.00 | 1,839.00 | | <u> </u> | 1.0 | 1,839.00 | 1.80 | 1,839.00 | | 1.00 | 1,839.00 100% | 100% |
| 9 | FINISHING ROADWAY | ST | - | 3,136.00 | 3,136.00 | | | 1.00 | 3,136.00 | 1.00 | 3,136.00 | • | 1.00 | 3,136.00 100% | 100% |
| | ROADWAY EXCAVATION | Շ | 1,300 | 20.45 | 26,585.00 | | y | 1,300.00 | 26,585.00 | 1,268.00 | 25,930.60 | | 1,268.00 | 25,930.60 | %86 |
| | WEDGE PLANE ASPHALT CONCRETE | 5 | 700 | 1.85 | 1,295.00 | * . | | 700.00 | 1,295.00 | 875.00 | 1,618.75 | | 875.00 | 1,618.75 | 125% |
| <u>ი</u> | COLD PLANE ASPHALT CONCRETE PAVEMENT | SQYD | 3,000 | 2.37 | 7,110.00 | | | 3,000.00 | 7,110.00 | 3,695.00 | 8,757.15 | | 3,695.00 | 8,757.15 123% | 123% |
| 2 | CLASS 2 AGGREGATE BASE | Շ | 009 | 23.78 | 14,268.00 | | | 00.009 | 14,268.00 | 638.00 | 15,171.64 | | 638.00 | 15,171.64 106% | 106% |
| E | HOT MIX ASPHALT | NOT | 1,150 | 61.60 | 70,840.00 | | | 1,150.00 | 70,840.00 | 918.84 | 56,600.54 | | 918.84 | 56,600.54 | %08 |
| 12 | PLACE ASPHALT CONCRETE (MISC AREA) | SQYD | 120 | 37.08 | 5,562.00 | | ······································ | 150.00 | 5,562.00 | 91.00 | 3,374.28 | | 91.00 | 3,374.28 | 61% |
| 55 | ASPHALT CONCRETE DIKE | 4 | 1,000 | 4.24 | 4,240.00 | | | 1,000.00 | 4,240.00 | 550.00 | 2,332.00 | | 920.00 | 2,332.00 | 25% |
| 4 | MINOR CONCRETE (CURB AND GUTTER)(CRS 200) | 느 | 700 | 133.00 | 26,600.00 | | | 200:00 | 26,600.00 | 132.00 | 17,556.00 | | 132.00 | 17,556.00 | %99 |
| <u>5</u> | MINOR CONCRETE (CURB AND GUTTER)(CRS 201) | 5 | 09 | 152.00 | 9,120.00 | | | 60.00 | 9,120.00 | 00.09 | 9,120.00 | | 90.00 | 9,120.00 100% | 100% |
| 9 | MINOR CONCRETE (DRIVEWAY APPROACH) (CRS 207) | Æ | - | 2,800.00 | 2,800.00 | | | 1.00 | 2,800.00 | 1.00 | 2,800.00 | | 1.00 | 2,800.00 100% | 100% |
| 14 | MINOR CONCRETE (CROSS-GUTTER AND SPANDREL) | SQFT | 009 | 16.50 | 9,900.00 | • | - | 00.009 | 00.006,6 | 700.00 | 11,550.00 | | 700.00 | 11,550.00 117% | 117% |
| 8 | MINOR CONCRETE (SIDEWALK) | SQFT | 200 | 7.85 | 5,495.00 | | | 200.00 | 5,495.00 | 00.099 | 5,181.00 | | 00.099 | 5,181.00 | 94% |
| € | | Æ | - | 2,040.00 | 2,040.00 | | , , , , , , , | 1.00 | 2,040.00 | 1.00 | 2,040.00 | | 1.00 | 2,040.00 100% | 100% |
| 20 | MINOR CONCRETE (CURB, SIDEWALK AND CURB RAMP) | ā | - | 3,200.00 | 3,200.00 | | | 1.00 | 3,200.00 | 9. | 3,200.00 | | 1.00 | 3,200.00 100% | 100% |
| 72 | CURB DRAIN | Æ | * | 1,790.00 | 1,790.00 | | | 1.00 | 1,790.00 | 1.00 | 1,790.00 | | 1.00 | 1,790.00 100% | 100% |

| ۵ | PROGRESS ESTIMATE RECORD - COUNTY OF RIVERSIDE | | | | | | | | | | SHEET 2 of 2 | | Processed Construction Inspection 8/28/2013 | n Inspection 8/28, | 3/2013 | r |
|-------|--|---------|-----------|-----------------|-------------------------------|--|---|------------------|--------------------|---------------|-------------------------------|------------------------------|---|------------------------|---------------|---|
| PRO. | PROJECT: Indiana Avenue Home Gardens Road Improvement (Phase II) | | | | Contractor: | Ali American Asphalt | | | | | in the second | | Estimate No. | 1 Final | | |
| Count | Community Development Block Grant County Project No.: C2-0138 | | | | Address: City, State, Zip: | P.O. Box 2229 Corona, CA 92878 | | | | | | | From: | July 1, 2013 | 013 | |
| Contr | Contract No. 13-04-004 | | | | | | | | | | | | ĕ | August 15, 2013 | , 2013 | |
| Item | | | | | Original Contract | Change Authorized | | Total Authorized | 7 | This Estimate | imate | Previous | Total Estime | Total Estimate To Date | % | |
| 2 | Item Description | Units | Quantity | Unit Price | Amount | Quantity | e E | ntity | Amount | Quantity | Amount | Quantity | Quantity | Amount | ¥. | T |
| 8 | THERMOPLASTIC CROSSWALK AND PAVEMENT MARKING | SQFT | 400 | 4.77 | 1,908.00 | | | 400.00 | 1,908.00 | 398.00 | 1,898.46 | <u> </u> | 398.00 | · | 1,898.46 100% | |
| 23 | PAINT TRAFFIC STRIPE (2-COAT) | 5 | 1,200 | 1.30 | 1,560.00 | | _ | 1,200.00 | 1,560.00 | 1,328.00 | 1,726.40 | <u>ç</u> | 1,328.00 | 1,726.40 111% | 0 111% | |
| 24 25 | NOT SELECTED FOR AWARD ADJUST FRAME AND COVER TO GRADE | Ę | 8 | 662.00 | 1,324.00 | | | 2.00 | 1,324.00 | 2.00 | 1,324.00 | 0 | 2.00 | N/A 1,324.00 100% | N/A 100% | |
| | | | - | | | | | | | | | | | | | |
| | PROJECT TOTAL | | | | 212,027.00 | | 00:00 | | 212,027.00 | | 188,360.82 | 2 | | 188,360.82 | | |
| | Made by: Jesse Mendoza | | Wo | Working Days: | 70 | Start Date: | | 7-1-13 | | | | | | | | - |
| | Checked by // 8-28 | | ă | Days Added: | 0 | End Date: | | 8-15-13 | - | OTAL VALU | JE OF WOF | TOTAL VALUE OF WORK TO DATE: | | \$188,360.82 | | |
| | OK Const. Supv. | | | Subtotal: | 50 | % \$ Complete: | lete: | %68 | | | LESS | LESS RETENTION: | %9 | 9,418.04 | | - |
| | > | | | Days Used: | 50 | Original Contract: | | \$212,027.00 | 8 | | TOTAL DL | TOTAL DUE TO DATE: | | \$178,942.78 | | - |
| | | | % Tim | % Time Elapsed: | 100% | Amended Contract: | | \$212,027.00 | 8 | LESS PI | REVIOUSLY | LESS PREVIOUSLY INVOICED: | | 0.00 | | |
| | | | ٠. | | | | | | | LESS LAB(| OR NON CC | LESS LABOR NON COMPLIANCE: | | 0.00 | | |
| | | | | | | | PAYA | MENTA | PAYMENT APPROVAL | TOTA | L DUE THIS | TOTAL DUE THIS PAYMENT: | | \$178,942.78 | | - |
| F | This Estimate Approved | | Date: | | for: | \$178,942.78 | Find | Find 2000 | 20, | Poceived | Received by Accounts Payable: | ts Payable: | | | | |
| | Juan C. Perez, Director of Transportation and Land Management | n and L | and Manag | | | | Deat | D 3, | Devil 31305 | | | By: | | | | |
| | | | | | | | Accor | S I | Account 527980 | 0 | | | | | | |
| Ö | Quantities on This Estimate Approved | Z | . , | Date | 9-5-13 | | Projec | N B | Project ZCZ-0138E | 38E | | | | | | |
| | All American Asphalt | | | | | | Activ | Activity ID | 23500 | 8 | | | | | | |
| | | | | | | | Reson | urce Typ. | Resource Type CN 7 | - | | | | | | |
| | | | | | | THE REAL PROPERTY AND ADDRESS OF THE PERSON NAMED IN COLUMN TWO IS NOT THE PERSON NAMED IN COLUMN TWO IS NAMED IN C | *************************************** | | 1 | | | | | | | 7 |

Signature Date

SUBMITTAL TO THE BOARD OF SUPERVISORS COUNTY OF RIVERSIDE, STATE OF CALIFORNIA



FROM: TLMA - Transportation Department

SUBMITTAL DATE:

Construction of Indiana Avenue and Grant Street roadway improvements in the SUBJECT:

January 16, 2013

community of Home Gardens.

RECOMMENDED MOTION: That the Board of Supervisors:

- 1. Approve the plans and specifications for the construction of Indiana Avenue and Grant Street roadway improvements in the community of Home Gardens; and,
- 2. Authorize the Clerk to advertise for bids to be received in the office of the Director of Transportation up to the hour of 2:00 PM, Wednesday, February 20, 2013, at which time bids will be opened.

Director of Transportation and Land Management

JCP:jrj:rr

Departmental Concurrence

(Continued On Attached Page)

| | Current F.Y. Total Cost: | \$ 226,000 | In Current Year Budge | et: Yes |
|-----------|-------------------------------|------------|-----------------------|-----------|
| FINANCIAL | Current F.Y. Net County Cost: | \$ 0 | Budget Adjustment: | No |
| DATA | Annual Net County Cost: | \$ 0 | For Fiscal Year: | 2012/2013 |
| | | | | D |

SOURCE OF FUNDS: Gas Tax (ABX8-9 Mar 2010 New HUTA) (24.4%),

Positions To Be **Deleted Per A-30**

Requires 4/5 Vote

Community Development Block Grant (CDBG) (75.6%)

There are no General Funds used in this project.

C.E.O. RECOMMENDATION:

APPROVE

County Executive Office Signature

Policy

FORM APPROVED COUNTY COURSE

X

Consent

Dep't Recomm. Per Exec. Ofc.

Prev. Agn. Ref.

District: 2/2

Agenda Number:

3-45

The Honorable Board of Supervisors

RE: Construction of Indiana Avenue and Grant Street roadway improvements in the community of Home Gardens.

January 16, 2013

Page 2 of 2

BACKGROUND: The Transportation Improvement Program provides for the construction of Indiana Avenue roadway improvements in the community of Home Gardens.

The reconstruction will improve drainage and pedestrian accessibility.

The proposed improvements include roadway reconstruction, roadway resurfacing, sidewalk, driveway and access ramp reconstruction. The reconstruction includes approximately 500 linear feet of Indiana Avenue and Grant Street. The resurfacing includes approximately 700 linear feet of Grant Street. Additional improvements includes the removal and reconstruction of concrete curb and gutter, driveway approaches, curb ramps and sidewalk, and construction of a new concrete cross gutter and spandrel, placement of asphalt concrete dike and driveways, striping, pavement markings, and associated work improvements. The reconstruction will allow for improved drainage and pedestrian access.

This project received major funding from Community Development Block Grant Program (CDBG 2.27-09).

The submitted plans and specifications have been approved as to form by County Counsel.

Environmental clearance is complete.

Project Number: C2-0138

PLEASE COMPLETE THIS INFORMATION RECORDING REQUESTED BY:

KECIA HARPER-IHEM, CLERK OF THE BOARD RIVERSIDE CO. CLERK OF THE BOARD 4080 LEMON STREET, 1ST FLOOR CAC **P O BOX 1147 - RIVERSIDE, CA 92502**

MAIL STOP # 1010

AND WHEN RECORDED MAIL TO:


RETURN TO: STOP #1010

RIVERSIDE COUNTY CLERK OF THE BOARD P. O. BOX 1147 - RIVERSIDE, CA 92502

DOC # 2013-0584942 12/18/2013 10:27A Fee:NC


Recorded in Official Records County of Riverside Larry W. Ward





NOTICE OF COMPLETION

To be recorded with County Recorder within 10 days after completion. No recording fee.



Notice is hereby given by the undersigned owner, a public entity of the State of California, that a public work of improvement has been completed, as follows:

Project title or description of work:

Indiana Avenue Home Gardens Road Improvement

Date of Completion:

Date of this notice 12/17/13

Nature of owner:

County of Riverside, public entity

Interest or estate of owner:

Public Roadway

Address of owner:

4080 Lemon Street, 8th Floor, Riverside, CA 92501

Name of contractor: All American Asphalt

Street or legal description of site:

Indiana Avenue and Grant Street

Dated:

December 17, 2013

County of Riverside

(Name of Public Entity)

Chairman, Board of Supervisors

John J. Benøit

STATE OF CALIFORNIA)

COUNTY OF RIVERSIDE)

I am the Chairman of the governing board of the County of Riverside, the public entity which executed the foregoing notice and on whose behalf I make this verification; I have read this notice, know its contents, and the same is true. I certify under penalty of perjury that the foregoing is true and correct.

Executed at

California on

12/17/13 (Date)

Chairman of the Board of Supervisors

KECLA PARPER-IHEM, Clerk

12/17/13 3-59

2013-12-120 821



2013-0584942 12/18/2013 10:278 2 of 2



LARRY W. WARD COUNTY OF RIVERSIDE ASSESSOR-COUNTY CLERK-RECORDER

Recorder P.O. Box 751 Riverside, CA 92502-0751 (951) 486-7000

http://riverside.asrcikrec.com

CERTIFICATION

Pursuant to the provisions of Government Code 27361.7, I certify under the penalty of perjury that the following is a true copy of illegible wording found in the attached document:

(Print or type the page number(s) and wording below):

CLARIFICATION OF THE SEAL for the Riverside County Board of Supervisors (embossed on document)



| Date: | 12/17/19 |
|------------|-------------|
| Signature: | Papul Posit |

Print Name:

Raquel Rosete, Board Assistant, Riverside County Clerk of the Board
