

**SUBMITTAL TO THE BOARD OF SUPERVISORS
COUNTY OF RIVERSIDE, STATE OF CALIFORNIA**

911A



FROM: TLMA – Transportation Department

SUBMITTAL DATE:
March 20, 2014

SUBJECT: Notice of Completion – Construction of Traffic Signals and Street Improvements at the Intersection of Ontario Avenue/Temescal Canyon Road and El Cerrito Road/Minnesota Road. El Cerrito Community. 2nd/2nd District. [\$500,678]; Local Funds 100%

RECOMMENDED MOTION: That the Board of Supervisors execute and file the attached “Notice of Completion.”

BACKGROUND:

Summary

By Minute Order 3-90 of April 2, 2013, the Board of Supervisors entered into a contract with United Paving Company of La Mirada, CA for the construction of traffic signals and street improvements at the intersection of Ontario Avenue/Temescal Canyon Road and El Cerrito Road/Minnesota Road in the El Cerrito community.

Departmental Concurrence

Patricia Romo

Assistant Director of Transportation

Juan C. Perez

Director of Transportation and Land Management

FINANCIAL DATA	Current Fiscal Year:	Next Fiscal Year:	Total Cost:	Ongoing Cost:	POLICY/CONSENT (Per Exec. Office)
COST	\$ 0	\$ 0	\$ 500,678	\$ 0	Consent <input type="checkbox"/> Policy <input checked="" type="checkbox"/>
NET COUNTY COST	\$ 0	\$ 0	\$ 0	\$ 0	

SOURCE OF FUNDS: West County DIF Signal Mitigation Fund (100%)
There are no General Funds used in this project.

Budget Adjustment: No

For Fiscal Year: 2013-2014

C.E.O. RECOMMENDATION:

APPROVE

BY Tina Grande

County Executive Office Signature

MINUTES OF THE BOARD OF SUPERVISORS

On motion of Supervisor Stone, seconded by Supervisor Benoit and duly carried, IT WAS ORDERED that the above matter is approved as recommended.

Ayes: Jeffries, Stone, Benoit and Ashley
Nays: None
Absent: Tavaglione
Date: April 8, 2014
xc: Transp., Recorder

Kecia Harper-Ihem
Clerk of the Board

By Deputy

- Positions Added
- Change Order

- A-30
- 4/5 Vote

Prev. Agn. Ref.: 4/2/13, Item 3-90

District: 2/2

Agenda Number:

3-26

SUBMITTAL TO THE BOARD OF SUPERVISORS, COUNTY OF RIVERSIDE, STATE OF CALIFORNIA
FORM 11: Notice of Completion – Construction of Traffic Signals and Street Improvements at the Intersection of Ontario Avenue/Temescal Canyon Road and El Cerrito Road/Minnesota Road. El Cerrito Community. 2nd//2nd District. [\$500,678]; Local Funds 100%

DATE: March 20, 2014

PAGE: 2 of 2

BACKGROUND:

Summary (continued)

The originally authorized amount of the contract was \$522,946. The total amended contract is \$500,678, which is 4.3% less than the originally authorized amount.

This work was completed at the direction of the Transportation Department on July 29, 2013, Work Order B7-0767.

Impact on Residents and Businesses

The project has improved traffic safety.

SUPPLEMENTAL:

Additional Fiscal Information

Budget

Original Contract Amount		\$522,946
Total Change Orders Authorized	0.0%	\$0
Estimated Pending Change Orders	0.0%	\$0
Amended Contract Amount		\$522,946
* Quantity Adjustments	-4.3%	-\$22,268
+ CCO FA Adjustments	0.0%	\$0
Total Amended Contract Amount	95.7%	\$500,678

Expenditures

Total Progress Payments		\$500,678
Estimated Pending Payments		\$0
Total Expenditures		\$500,678

(Over)/Under Contract Amount \$0

+ Change Orders using the Force Account method of payment issued prior to the work being completed generally do not use the total authorized amount.

* CAL-Trans Standard Specifications 4-1.03B. Increases or decreases in the quantity of a contract item of work will be determined by comparing the total pay quantity of such item of work with the Engineer's Estimate. If the total pay quantity of any item of work required under the contract varies from the Engineer's Estimate by 25% or less, payment will be made for the quantity of work of said item performed at the contract unit price, unless eligible for adjustment pursuant to Section 4-1.03C, "Changes in Character of Work."

The construction of the project was funded with \$500,678 of West County DIF Signal Mitigation Fund.

Contract History and Price Reasonableness

N/A

COUNTY OF RIVERSIDE
DEPARTMENT OF TRANSPORTATION



ONTARIO AVENUE / TEMESCAL CANYON ROAD
AND

EL CERRITO ROAD / MINNESOTA ROAD

CONSTRUCTION OF TRAFFIC SIGNALS, PARKING LOT, AND
ASSOCIATED IMPROVEMENTS

EL CERRITO COMMUNITY

PROJECT No. B7-0767

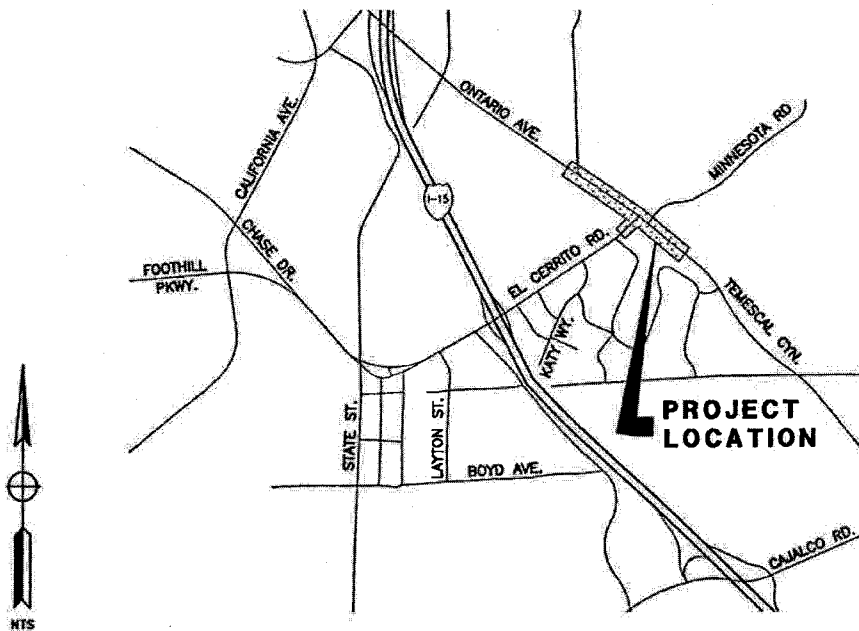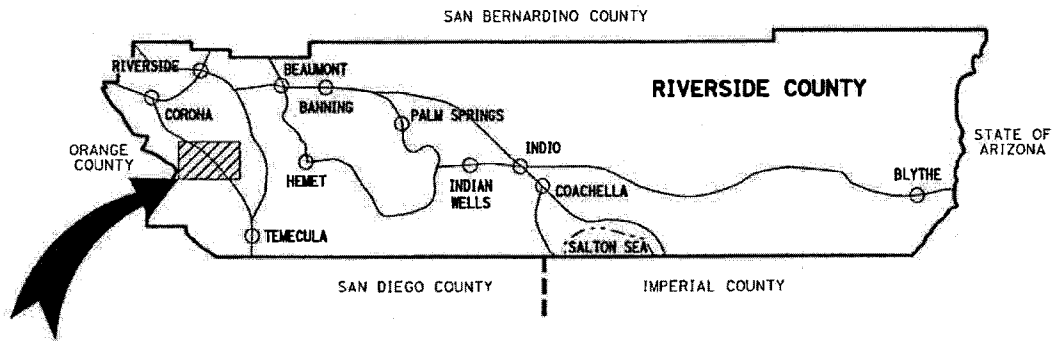

VICINITY MAP

TOWNSHIP 48 RANGE 6W SECTION 8
COUNTY ROAD BOOK PAGE No. 30-B

PLEASE COMPLETE THIS INFORMATION
RECORDING REQUESTED BY:

**KECIA HARPER-IHEM, CLERK OF THE BOARD
RIVERSIDE CO. CLERK OF THE BOARD
4080 LEMON STREET, 1ST FLOOR CAC
P O BOX 1147 – RIVERSIDE, CA 92502**

MAIL STOP # 1010

AND WHEN RECORDED MAIL TO:

**RETURN TO: STOP #1010
RIVERSIDE COUNTY CLERK OF THE BOARD
P. O. BOX 1147 – RIVERSIDE, CA 92502**

DOC # 2014-0130931

04/10/2014 11:24A Fee:NC

Page 1 of 2

Recorded in Official Records

County of Riverside

Larry W. Ward

Assessor, County Clerk & Recorder



S	R	U	PAGE	SIZE	DA	MISC	LONG	RFD	COPY
			2						
M	A	L	465	426	PCOR	NCOR	SMF	NCHB	EXAM
NCHB						T:	CTY	UNI	518



NOTICE OF COMPLETION

To be recorded with County Recorder
within 10 days after completion.
No recording fee.

Notice is hereby given by the undersigned owner, a public entity of the State of California, that a public work of improvement has been completed, as follows:

Project title or description of work: Construction of Traffic Signals, Parking Lot, and Associated Improvements

Date of Completion: Date of this notice 04/08/14

Nature of owner: County of Riverside, public entity

Interest or estate of owner: Public Roadway

Address of owner: 4080 Lemon Street, 8th Floor, Riverside, CA 92501

Name of contractor: Superior Paving Company, Inc. dba United Paving Company

Street or legal description of site: Ontario Aveue/Temescal Canyon Road and el Cerrito Road/Minnesota Road

Dated: April 8, 2014

Owner: County of Riverside
(Name of Public Entity)

By: Jeff Stone
Chairman, Board of Supervisors
Jeff Stone

STATE OF CALIFORNIA)

ss

COUNTY OF RIVERSIDE)

I am the Chairman of the governing board of the County of Riverside, the public entity which executed the foregoing notice and on whose behalf I make this verification; I have read this notice, know its contents, and the same is true. I certify under penalty of perjury that the foregoing is true and correct.

Executed at Riverside, California on 04/08/14 (Date)

Jeff Stone, Chairman of the Board of Supervisors
Jeff Stone

ATTEST:
Kecia Harper-Ihem, Clerk

By Kecia Harper-Ihem Deputy

04.08.14 3-26

2014-4-122420



**LARRY W. WARD
COUNTY OF RIVERSIDE
ASSESSOR-COUNTY CLERK-RECORDER**

Recorder
P.O. Box 751
Riverside, CA 92502-0751
(951) 486-7000
<http://riverside.asrcclrec.com>

CERTIFICATION

Pursuant to the provisions of Government Code 27361.7, I certify under the penalty of perjury that the following is a true copy of illegible wording found in the attached document:

(Print or type the page number(s) and wording below):

CLARIFICATION OF THE SEAL for the Riverside County Board of Supervisors
(embossed on document)



Date: 4-8-14

Signature: *Karen Barton*

Print Name: Karen Barton, Board Assistant, Riverside County Clerk of the Board



PROJECT: Ontario Avenue/Temescal Canyon Road and El Cerrito Road/Minnesota Road
 Construction of Traffic Signals, Parking Lot, and Associated Improvements El Cerrito
 County Project No.: B7-0767
 Contract No. 13-03-002

Contractor: United Paving Co.
 Address: 14660 Industry Circle
 City, State, Zip: La Mirada, CA 90638

Estimate No. 5 Final
 From: August 26, 2013
 To: January 25, 2014



Item No.	Item Description	Units	Quantity	Unit Price	Original Contract Amount	Change Authorized Quantity	Change Authorized Amount	Total Authorized Quantity	Total Authorized Amount	This Estimate Quantity	This Estimate Amount	Previous Quantity	Total Estimate To Date Quantity	Total Estimate To Date Amount	% Auth.
1	DUST ABATEMENT	LS	1	1,000.00	1,000.00			1.00	1,000.00			1.00	1.00	1,000.00	100%
2	WATER POLLUTION CONTROL	LS	1	1,000.00	1,000.00			1.00	1,000.00			1.00	1.00	1,000.00	100%
3	TRAFFIC CONTROL SYSTEM	LS	1	4,000.00	4,000.00			1.00	4,000.00			1.00	1.00	4,000.00	100%
4	CLEARING AND GRUBBING	LS	1	1,000.00	1,000.00			1.00	1,000.00			1.00	1.00	1,000.00	100%
5	REMOVE TREE	EA	18	440.00	7,920.00			18.00	7,920.00			12.00	12.00	5,280.00	67%
6	ROADWAY EXCAVATION	CY	575	45.80	26,335.00			575.00	26,335.00			493.56	493.56	22,605.05	86%
7	CLASS 2 AGGREGATE BASE	CY	380	44.20	16,796.00			380.00	16,796.00			303.29	303.29	13,405.42	80%
8	HOT MIX ASPHALT (TYPE A)	TON	570	107.80	61,446.00			570.00	61,446.00	6.03	650.03	627.48	633.51	68,292.38	111%
9	COLD PLANE ASPHALT CONCRETE PAVEMENT (.17")	SQYD	490	12.80	6,272.00			490.00	6,272.00			490.00	490.00	6,272.00	100%
10	PLACE ASPHALT CONCRETE DIKE (CRS 212)(6")	LF	35	23.00	805.00			35.00	805.00			35.00	35.00	805.00	100%
11	PLACE ASPHALT CONCRETE DIKE (CRS 212)(8")	LF	45	23.00	1,035.00			45.00	1,035.00			42.00	42.00	966.00	93%
12	MINOR CONCRETE (CURB RAMP) (CRS 403 - CASE A)	EA	1	2,310.00	2,310.00			1.00	2,310.00			1.00	1.00	2,310.00	100%
13	MINOR CONCRETE (CURB RAMP) (CRS 403 - CASE B)	EA	4	1,980.00	7,920.00			4.00	7,920.00			4.00	4.00	7,920.00	100%
14	MINOR CONCRETE (DRIVEWAY APPROACH) (CRS 207)	SQFT	400	3.85	1,540.00			400.00	1,540.00			385.00	385.00	1,482.25	96%
15	MINOR CONCRETE (DRIVEWAY APPROACH) (CRS 207 A)	SQFT	2,350	3.90	9,165.00			2,350.00	9,165.00			2,296.25	2,296.25	8,955.38	98%
16	MINOR CONCRETE (CURB AND GUTTER) (CRS 200)	LF	440	17.60	7,744.00			440.00	7,744.00			192.00	192.00	3,379.20	44%
17	MINOR CONCRETE (TYPE D CURB) (CRS 204)	LF	590	15.40	9,086.00			590.00	9,086.00			580.00	580.00	8,932.00	98%
18	MINOR CONCRETE (SIDEWALK)	SQFT	680	3.30	2,244.00			680.00	2,244.00			816.75	816.75	2,695.28	120%
19	MINOR CONCRETE (BUS STOP PAD)	SQFT	540	8.80	4,752.00			540.00	4,752.00			558.00	558.00	4,910.40	103%
20	MINOR CONCRETE (BUS TURNOUT)	SQFT	765	8.80	6,732.00			765.00	6,732.00			956.25	956.25	8,415.00	125%
21	MINOR CONCRETE (STAMPED CONCRETE)	SQFT	300	13.20	3,960.00			300.00	3,960.00			217.00	217.00	2,864.40	72%
22	UNDERSIDEWALK DRAIN CAST IN PLACE (CRS 303)	EA	1	5,720.00	5,720.00			1.00	5,720.00			1.00	1.00	5,720.00	100%

Estimate No. 5 Final

From: August 26, 2013
To: January 26, 2014

Contractor: United Paving Co.
Address: 14860 Industry Circle
City, State, Zip: La Mirada, CA 90638

PROJECT: Ontario Avenue/Temescal Canyon Road and El Cerrito Road/Minnesota Road
Construction of Traffic Signals, Parking Lot, and Associated Improvements El Cerrito
County Project No.: B7-0767
Contract No. 13-03-002



Item No.	Item Description	Units	Quantity	Unit Price	Original Contract Amount	Change Authorized		This Estimate		Total Estimate To Date		% Auth.
						Quantity	Amount	Quantity	Amount	Quantity	Amount	
23	RELOCATE SIGN STRUCTURE	EA	1	3,520.00	3,520.00	1.00	3,520.00	1.00	3,520.00	1.00	3,520.00	100%
24	SIGNAL AND LIGHTING	LS	1	194,000.00	194,000.00	1.00	194,000.00	1.00	194,000.00	1.00	194,000.00	100%
25	REMOVE TRAFFIC STRIPE AND PAVEMENT MARKING	SQFT	2,495	1.56	3,892.20	2,495.00	3,892.20	2,399.00	3,742.44	2,399.00	3,742.44	96%
26	THERMOPLASTIC PAVEMENT MARKING	SQFT	800	4.76	3,808.00	800.00	3,808.00	791.00	3,765.16	791.00	3,765.16	99%
27	PAINT TRAFFIC STRIPE 2 COAT	LF	6,000	0.61	3,660.00	6,000.00	3,660.00	6,776.00	4,133.36	6,776.00	4,133.36	113%
28	REMOVE SIGN	EA	15	44.80	672.00	15.00	672.00	15.00	672.00	15.00	672.00	100%
29	RELOCATE SIGNS	EA	8	196.00	1,568.00	8.00	1,568.00	6.00	1,176.00	6.00	1,176.00	75%
30	ROADSIDE SIGN - ONE POST	EA	17	291.00	4,947.00	17.00	4,947.00	15.00	4,365.00	15.00	4,365.00	88%
31	DELINEATOR (CLASS 1)	EA	4	67.00	268.00	4.00	268.00	4.00	268.00	4.00	268.00	100%
32	INSTALL SIGN (STRAP AND SADDLE BRACKET METHOD)	EA	2	151.00	302.00	2.00	302.00	2.00	302.00	2.00	302.00	100%
33	PAVEMENT MARKER (REFLECTIVE)	EA	290	4.50	1,305.00	290.00	1,305.00	351.00	1,579.50	351.00	1,579.50	121%
34	PARKING BUMPER (PRECAST CONCRETE)	EA	8	32.00	256.00	8.00	256.00	8.00	256.00	8.00	256.00	100%
35	GUARD POST	EA	4	380.00	1,520.00	4.00	1,520.00	4.00	1,520.00	4.00	1,520.00	100%
36	REMOVE CHAIN LINK FENCE	LF	180	13.20	2,376.00	180.00	2,376.00	170.00	2,244.00	170.00	2,244.00	94%
37	CHAIN LINK FENCE (TYPE CL-6)	LF	100	60.50	6,050.00	100.00	6,050.00	95.00	5,747.50	95.00	5,747.50	95%
38	ROOT BARRIER	LF	100	35.20	3,520.00	100.00	3,520.00	100.00	3,520.00	100.00	3,520.00	100%
39	ONSITE WASTEWATER TREATMENT SYSTEM	LS	1	45,500.00	45,500.00	1.00	45,500.00	1.00	45,500.00	1.00	45,500.00	100%
40	MISCELLANEOUS DIRECTED WORK	FA	30,000	1.00	30,000.00	30,000.00	30,000.00	3,264.30	3,264.30	16,892.78	20,157.08	67%
41	DE-MOBILIZATION	LS	1	22,000.00	22,000.00	1.00	22,000.00	1.00	22,000.00	1.00	22,000.00	100%
42	CROSSING GUARDS	FA	1	5,000.00	5,000.00	1.00	5,000.00					0%

PROJECT: Ontario Avenue/Temesca Canyon Road and El Cerrito Road/Minnesota Road
 Construction of Traffic Signage, Parking Lot, and Associated Improvements El Cerrito
 County Project No.: B7-0767
 Contract No. 13-03-002

Contractor: United Paving Co.
 Address: 14660 Industry Circle
 City, State, Zip: La Mirada, CA 90638

Estimate No. 5 Final
 From: August 26, 2013
 To: January 25, 2014



Item No.	Item Description	Units	Quantity	Unit Price	Original Contract		Change Authorized		Total Authorized		This Estimate		Previous		Total Estimate To Date		% Auth.
					Amount	Quantity	Amount	Quantity	Amount	Quantity	Amount	Quantity	Amount	Quantity	Amount	Quantity	
					522,946.20		0.00		522,946.20	29,434.33						500,677.90	
PROJECT TOTAL																	

Made by: Ivan Mendoza
 Checked by: [Signature] 2/19/14
 OK Const. Supv. [Signature]

Working Days: 50
 Days Added: 0
 Subtotal: 50
 Days Used: 50
 % Time Elapsed: 100%

Start Date: 5-20-13
 End Date: 7-29-13
 % \$ Complete: 96%
 Original Contract: \$522,946.20
 Amended Contract: \$522,946.20

TOTAL VALUE OF WORK TO DATE: \$500,677.90
 LESS RETENTION: 5% 25,033.91
 TOTAL DUE TO DATE: \$475,643.89
 LESS PREVIOUSLY INVOICED: 471,557.22
 LESS LABOR NON COMPLIANCE: 0.00
 TOTAL DUE THIS PAYMENT: \$4,086.67

LESS \$23,875.94 OVERPAYMENT- STOP PAYMENT NOTICE HOLD ADDED TO ESTIMATE 4 PAYMENT IN ERROR:
 TOTAL DUE THIS PAYMENT: \$4,086.67

Received by Accounts Payable: _____
 By: _____

PAYMENT APPROVAL

Fund 20000
 Dept ID 31305
 Account 527980
 Project Z-1070767E
 Activity ID Z3500
 Resource Type CNT
 Signature [Signature]
 Date 3/11/14

This Estimate Approved _____ Date: 2-25-14 for: _____
 Juan C. Perez, Director of Transportation and Land Management

Quantities on This Estimate Approved [Signature]
 United Paving Co.
