## SUBMITTAL TO THE BOARD OF SUPERVISORS **COUNTY OF RIVERSIDE, STATE OF CALIFORNIA**





FROM: TLMA - Transportation Department

SUBMITTAL DATE: September 22, 2015

SUBJECT: Notice of Completion – Highland Springs Avenue Resurfacing Project, Community of Cherry Valley. 5th District. [\$239,254]; Local Funds 100%

RECOMMENDED MOTION: That the Board of Supervisors execute and file the attached "Notice of Completion."

## **BACKGROUND:**

## **Summary**

Departmental Concurrence

By Minute Order 3-39 of May 12, 2015, the Board of Supervisors entered into a contract with Matich Corporation of San Bernardino, CA for the construction of Highland Springs Avenue Resurfacing Project between Brookside Avenue and Cherry Valley Boulevard in the community of Cherry Valley.

Patricia Romo

Assistant Director of Transportation

Juan C. Perez

Director of Transportation and Land Management

FINANCIAL DATA	Curre	ent Fiscal Year:	Next F	iscal Year:	Tota	al Cost:	-	Ongo	ing Cost:	(Per Exec. Off	Control of the Contro
COST	\$	239,254	\$	0	\$	23	39,254	\$	0	Consent □ Poli	in. •
NET COUNTY COST	\$	0	\$	0	\$		0	\$	0	Consent - Poli	Cy
SOURCE OF FUNDS: Gas Tax (ABX8-9 Mar 2010 New HUTA) (100%). Budget Adjustment: No											
There are no General Funds used in this project.							F	or Fiscal Year:	15/16		

C.E.O. RECOMMENDATION:

**APPROV** 

**County Executive Office Signature** 

## MINUTES OF THE BOARD OF SUPERVISORS

On motion of Supervisor Jeffries, seconded by Supervisor Tavaglione and duly carried, IT WAS ORDERED that the above matter is approved as recommended.

Ayes:

Jeffries, Tavaglione, Washington and Benoit

Navs:

None

Absent:

Ashley

Date:

October 20, 2015

XC:

Transp., Recorder

Prev. Agn. Ref.: 5/12/15, Item 3-39

District: 5

**Agenda Number:** 

Kecia Harper-Ihem

Clerk of the Board

Positions Added

Change Order

4/5 Vote A-30

П

## SUBMITTAL TO THE BOARD OF SUPERVISORS, COUNTY OF RIVERSIDE, STATE OF CALIFORNIA

**FORM 11:** Notice of Completion – Highland Springs Avenue Resurfacing Project, Community of Cherry Valley.

5th District. [\$239,254]; Local Funds 100%

DATE: September 22, 2015

**PAGE**: 2 of 3

#### **BACKGROUND:**

### Summary (continued)

The originally authorized amount of the contract was \$240,000. The total amended contract is \$239,254, which is 1.3% less than the originally authorized amount.

The work was completed at the direction of the Transportation Department on June 30, 2015, Work Order Number C1-0582.

### **Impact on Residents and Businesses**

The improvements benefit the project area by significantly improving the service life of the existing road, as well as providing upgrades to enhance pedestrian safety with Americans with Disabilities Act (ADA) compliant ramps.

#### SUPPLEMENTAL:

## **Additional Fiscal Information**

Bud	get
-----	-----

Original Contract Amount		\$240,000
Total Change Orders Authorized	1.0%	\$2,300
Estimated Pending Change Orders	0.0%	\$0
Authorized Contract Amount		\$242,300
* Quantity Adjustments	-1.3%	(\$3,046)
+ CCO FA Adjustments	0.0%	\$0
Total Amended Contract Amount	99.7%	\$239,254
Expenditures		
Total Progress Payments		\$239,254
Estimated Pending Payments		\$0
Total Expenditures		\$239,254
(Over)/Under Contract Amount		\$0

<sup>+</sup> Change Orders using the Force Account method of payment issued prior to the work being completed generally do not use the total authorized amount.

This project was funded with \$239,254 of Gas Tax funds.

<sup>\* &</sup>lt;u>CAL-Trans Standard Specifications 4-1.03B</u>. Increases or decreases in the quantity of a contract item of work will be determined by comparing the total pay quantity of such item of work with the Engineer's Estimate. If the total pay quantity of any item of work required under the contract varies from the Engineer's Estimate by 25 percent or less, payment will be made for the quantity of work of said item performed at the contract unit price, unless eligible for adjustment pursuant to Section 4-1.03C, "Changes in Character of Work."

## SUBMITTAL TO THE BOARD OF SUPERVISORS, COUNTY OF RIVERSIDE, STATE OF CALIFORNIA

FORM 11: Notice of Completion – Highland Springs Avenue Resurfacing Project, Community of Cherry Valley.

5th District. [\$239,254]; Local Funds 100%

DATE: September 22, 2015

**PAGE:** 3 of 3

## **Contract History and Price Reasonableness**

Eight bids were received on March 4, 2015 ranging from \$240,000 to \$448,064. The basis for the selection of a contractor is the lowest responsive and responsible bid. The lowest responsible bid was submitted by Matich Corporation in the amount of \$240,000, which is \$40,000 (14%) below the Engineer's Estimate.

#### **ATTACHMENTS:**

Vicinity Map Change Order Report Progress Estimate Record Notice of Completion PLEASE COMPLETE THIS INFORMATION RECORDING REQUESTED BY:

KECIA HARPER-IHEM, CLERK OF THE BOARD RIVERSIDE CO. CLERK OF THE BOARD 4080 LEMON STREET, 1ST FLOOR CAC P O BOX 1147 - RIVERSIDE, CA 92502

**MAIL STOP # 1010** 

AND WHEN RECORDED MAIL TO:

**RETURN TO:** 

STOP #1010

RIVERSIDE COUNTY CLERK OF THE BOARD P. O. BOX 1147 - RIVERSIDE, CA 92502

2015-046148(

10/21/2015 11:33 AM Fee: \$ 0.00

Recorded in Official Records County of Riverside Peter Aldana



126					R	Α	Exam	110	
Page	DA	PCOR	Misc	Long	RFD	1st Pg	Adtl Pg	Cert	CC
2									
SIZE	NCOR	SMF	NCH	T:		Nebace			

### NOTICE OF COMPLETION

To be recorded with County Recorder within 10 days after completion. No recording fee.

Notice is hereby given by the undersigned owner, a public entity of the State of California, that a public work of improvement has been completed, as follows:

Project title or description of work:

Highland Springs Avenue Resurfacing Project

**Date of Completion:** 

Date of this notice 10/20/15

Nature of owner:

County of Riverside, public entity

Interest or estate of owner:

Public Roadway

Address of owner:

4080 Lemon Street, 8th Floor, Riverside, CA 92501

Name of contractor: Matich Corporation

Street or legal description of site:

Highland Springs Avenue, between Brookside Avenue and Cherry Valley Blvd.

Dated: October 20, 2015

County of Riverside (Name of Public Entity)

Marion Ashley

STATE OF CALIFORNIA )

**COUNTY OF RIVERSIDE)** 

I am the <u>Chairman</u> of the governing board of the <u>County of Riverside</u>, the public entity which executed the foregoing notice and on whose behalf I make this verification; I have read this notice, know its contents, and the same is true. I certify under penalty of perjury that the foregoing is true and correct.

Executed at

Riverside

, California on 10/20/15

Marion Ashley

ATTEST:

10.20.15 3-28

2015-11-129505



# PETER ALDANA COUNTY OF RIVERSIDE ASSESSOR-COUNTY CLERK-RECORDER

Recorder P.O. Box 751 Riverside, CA 92502-0751 (951) 486-7000

www.riversideacr.com

## **CERTIFICATION**

Pursuant to the provisions of Government Code 27361.7, I certify under the penalty of perjury that the following is a true copy of illegible wording found in the attached document:

(Print or type the page number(s) and wording below):

CLARIFICATION OF THE SEAL for the Riverside County Board of Supervisors (embossed on document)



Date:

Signature:

Print Name:


Karen Barton, Board Assistant, Riverside County Clerk of the Board


Available in Alternate Formats

## DEPARTMENT OF TRANSPORTATION

## HIGHLAND SPRINGS AVE RESURFACING PROJECT

BROOKSIDE AVE TO CHERRY VALLEY BLVD COMMUNITY OF CHERRY VALLEY PROJECT No. C1-0582

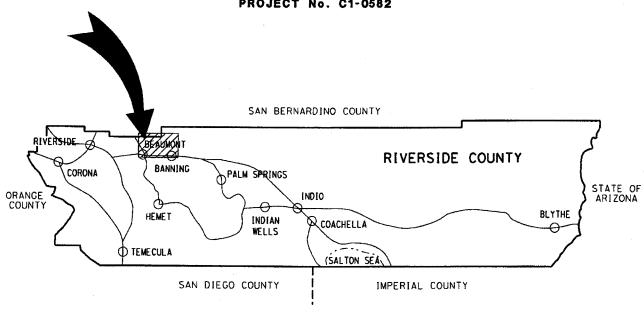

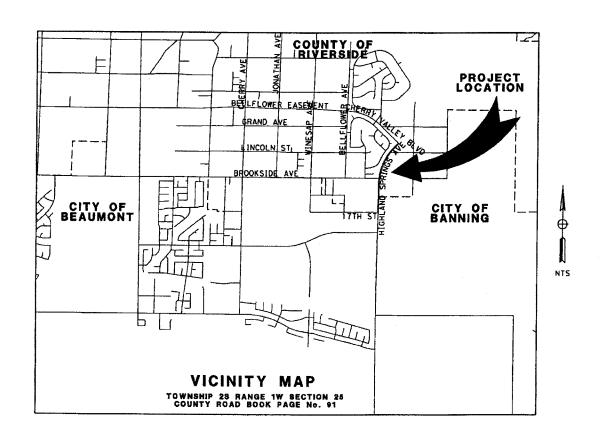

## CHANGE ORDER REPORT (Highland Springs Avenue Resurfacing Project)

Change Order Number	Contract Amount	Percent	Description
	Original Contract Amount		
	\$240,000		
1	\$2,300	0.96%	The contractor encountered an unmarked sewer manhole buried below the existing asphalt pavement during the grinding operation not shown on the plans. It was necessary to repair the damages and to adjust the facility to grade.
Quantity Adjustments	-\$3,046	-1.3%	
Total Change Orders	\$2,300		
Revised Contract Amount	\$239,254		

PROGRESS ESTIMATE RECORD - COUNTY OF RIVERSIDE

PRO	PROGRESS ESTIMATE RECORD - COUNTY OF RIVERSIDE										SHEET 1 of 2		assed Constructi	Processed Construction Inspection 8/11/2015	72015
PROJE County Contra	PROJECT: Highland Springs Avenue Resurfacing Project County Project No.: C1-0582 Contract No. 15-04-002				Contractor: Matich Corporation Address: 1596 Harry Sheppard Blvd. City, State, Zip: San Bernardino, CA 92408	Corporation y Sheppard Blv Bernardino, C.	d. A 92408						Estimate No. From: To:	3 Final July 26, 2015 August 25, 2015	5 15
Item					Original Contract	Change Orders	ers	Amended Contract	tract	This Estimate	l arte	Previous	Total Estimate To Date	e To Date	8
Š	Item Description	Units	Quantity	Unit Price	Amount	Quantity	Amount	Quantity	Amount	Quantity	Amount	Quantity	Quantify	Amount	Auth.
	DUST ABATEMENT	รา	<b>T</b>	1,500.00	1,500.00			1.00	1,500.00			100	1.00	1,500.00 100%	100%
2	WATER POLLUTION CONTROL	2	i <del>.</del>	2,400.00	2,400.00			1.00	2,400.00			90,	1.00	2,400.00 100%	100%
m	TRAFFIC CONTROL SYSTEM	മ		11,000.00	11,000.00			1.00	11,000.00			1.00	1.00	11,000.00 100%	400%
4	DEVELOP WATER SUPPLY	S	~	1,400.00	1,400.00			1.00	1,400.00			9.	4.00	1,400.00 100%	100%
s.	CLEARING AND GRUBBING	ន្ទ	<del>-</del>	27,400.00	27,400.00		THE RESERVE OF THE PARTY OF THE	1.00	27,400.00	0.93	25,482.00	0.07	1.00	27,400.00 100%	100%
g	ROADWAY EXCAVATION	ঠ	1,100	20.00	22,000.00			1,100.00	22,000.00			1,087.21	1,087.21	21,744.20	%66
~	SHOULDER BACKING	<b>5</b>	1,600	2.60	4,160.00			1,600.00	4,160.00			1,700.00	1,700.00	4,420.00 106%	106%
∞	HOT MIX ASPHALT (YPE.C)	TON	2,460	54.40	133,824.00		*** **********************************	2,460.00	133,824.00			2,509.33	2,509.33	136,507.55 102%	102%
0	PLACE ASPHALT CONCRETE DIKE (CRS 212) (6) "	<b>5</b>	20	12.00	00.009			20.00	900.00			53.00	53.00	636.00 106%	106%
9	MINOR CONCRETE (CURB RAMP) (CRS 403)	ង	7	5,000.00	10,000.00		mananan and an annua	2.00	10,000.00		***************************************	2.00	2.00	10,000.00 100%	100%
Ξ	ROADSIDE SIGN - ONE POST	<b>a</b>	-	514.00	514.00			1.00	514.00		-	1.00	1.00	514.00 100%	100%
72	THERMOPLASTIC CROSSWALK AND PAVEMENT MARKING	SOFT	220	5.10	1,122.00			220:00	1,122.00			239.00	239.00	1,218.90 109%	109%
13	PAINT TRAFFIC STRIPE (2-COAT)	4	4,000	0.50	2,000.00			4,000.00	2,000.00	3. rh		4,606.00	4,606.00	2,303.00 115%	115%
4	PAVEMENT MARKER (REFLECTIVE)	Æ	09	3.00	180.00			00:09	180.00			90:00	60.00	180.00 100%	100%
15	FUNDING AWARENESS SIGN	Ę	.73	950.00	1,900.00			2.00	1,900.00			2.00	2.00	1,900.00 100%	100%
9	MISCELLANEOUS DIRECTED WORK	Æ	~	20,000.00	20,000.00			1.00	20,000.00	0.0012465	24.93	0.690266	0.6915125	13,830.25	%69
CCO 1	FURNISH & ADJUST MANHOLE TO GRADE	Ą	0	1.00	0.00	2,300.00	2,300,00	2,300.00	2,300.00	2,300.00	2,300.00		2,300.00	2,300.00 100%	100%
		************************************											-		records.

Processed Construction Inspection 8/11/2015 TOTAL VALUE OF WORK TO DATE: LESS RETENTION: TOTAL DUE TO DATE: Previous Quantity SHEET 2 of 2 27,806.93 This Estimate Quantity Ar 242,300.00 Amended Contract Quantity Amount \$240,000.00 6-30-15 6-15-15 %66 2,300.00 Start Date: End Date: % \$ Complete: Original Contract: Original Contract Change Orders
Amount Quantity Amount Contractor: Matich Corporation Address: 1596 Harry Sheppard Bivd. City, State, Zip: San Bernardino, CA 92408 240,000.00 12 40% 30 0 Days Added: Subtotal: Days Used: Working Days: Unit Price Quantity Units PROGRESS ESTIMATE RECORD - COUNTY OF RIVERSIDE PROJECT: Highland Springs Avenue Resurfacing Project County Project No.: C1-0582 OK Const. Supv. 4 Jun 8/12/15 Made by: Joseph Martinez Checked by W 8-11-N ltem Description PROJECT TOTAL Contract No. 15-04-002

No.

3 Final July 26, 2015 August 25, 2015

From: ĕ Total Estimate To Date
Quantity Amount

239,253.90

\$239,253.90 11,962.70 \$227,291.20 200,874.62

%

LESS PREVIOUSLY INVOICED:

\$242,300.00

Amended Contract:

% Time Elapsed:

\$26,416.58

TOTAL DUE THIS PAYMENT: LESS LABOR NON COMPLIANCE:

Received by Accounts Payable:

Patricia Romo, Assistant Director of Transportation

This Estimate Approved

\$26,416.58

Date: 8/8

Matich Corporation

Quantities on This Estimate Approved

PAYMENT APPROVAL

10000 C 10000

Account 527980 21305 Dept ID

TRANSFISCAL APPROVED By: Crystal Potter 5-3461

Activity ID 28500

Project ZCI- 05 82 E

Resource Type

Signature Date

Norma Larson 951-955-2783 8-94-75

## Highland Springs Ave. Resurfacing Project Contract CCO History

Contract No.	15-04-002
Work Order No.	C1-0582
Contract Amount	\$240,000.00
Single Maximum CCO	\$24,000.00
Maximum CCO's	\$24,000.00

	CCO Category Legend					
AFA	Anticpated Force Account					
CFC	Changed Field Conditon					
CME	Contract Management Error					
DO	Design Omission					
OAM	Outside Agency Mandate					
RWO	Right-of-Way Obligation					
SE	Survey Error					
UB	Upgrade/Betterment					
UI	Utility Interference					

=====					======	=======	
CCO	Amount		Cumulative	% Original (	Cumulative	CCO	
No.	This CCO	Authority	CCO's	Authorized	CCO %	Category	Classification
		44			Barris de la companya de la company		
1 _	\$2,300.00	Director	\$2,300.00	0.96%	0.96%	DO	Avoidable
	\$2,300.00			0.96%			

New Authorized Contract Total Total CCO Dollars To Date Total % Increased by CCO's \$242,300.00 \$2,300.00 0.96%
