

FORM APPROVED COUNTY COUNSEL 3/8/16
 BY: GREGORY P. PRIAMOS DATE

**SUBMITTAL TO THE BOARD OF SUPERVISORS
 COUNTY OF RIVERSIDE, STATE OF CALIFORNIA**

115



FROM: TLMA – Transportation Department

SUBMITTAL DATE:
 December 1, 2015

SUBJECT: Notice of Completion – Sage Road Resurfacing and Reconstruction Project in the Sage Community. 3rd District; [\$772,063]; Local Funds 100%

- RECOMMENDED MOTION:** That the Board of Supervisors:
1. Accept Sage Road Resurfacing and Reconstruction Project in the Sage Community as completed; and
 2. Authorize the Chairman of the Board to execute the Notice of Completion and the Clerk of the Board to record the Notice.


BACKGROUND:

Summary

By Minute Order 3-38 of May 12, 2015, the Board of Supervisors entered into a contract with All American Asphalt of Corona, CA for the resurfacing and reconstruction of three Sage Road segments in the community of Sage.

Departmental Concurrence


 Patricia Romo
 Assistant Director of Transportation


 Juan C. Perez
 Director of Transportation and Land Management

FINANCIAL DATA	Current Fiscal Year:	Next Fiscal Year:	Total Cost:	Ongoing Cost:	POLICY/CONSENT (Per Exec. Office)
COST	\$ 772,063	\$ 0	\$ 772,063	\$ 0	Consent <input type="checkbox"/> Policy <input checked="" type="checkbox"/>
NET COUNTY COST	\$ 0	\$ 0	\$ 0	\$ 0	

SOURCE OF FUNDS: Measure A/Western (100%). There are no General funds used in this Project.

Budget Adjustment: N/A
For Fiscal Year: 15/16

C.E.O. RECOMMENDATION:


APPROVE

 BY: Jina Grady
 County Executive Office Signature

MINUTES OF THE BOARD OF SUPERVISORS

On motion of Supervisor Jeffries, seconded by Supervisor Ashley and duly carried, IT WAS ORDERED that the above matter is approved as recommended.

Ayes: Jeffries, Tavaglione, Benoit and Ashley
 Nays: None
 Absent: Washington
 Date: March 29, 2016
 xc: Transp., Recorder

Kecia Harper-Ihem
 Clerk of the Board
 By: 
 Deputy

- A-30
- Positions Added
- 4/5 Vote
- Change Order

Prev. Agn. Ref.: 5/12/15, Item 3-38 District: 3 Agenda Number:

3-34

BACKGROUND:

Summary (continued)

The originally authorized amount of the contract was \$768,582. The total amended contract is \$772,063, which is 0.5% more than the originally authorized amount.

Work Order numbers C2-0158.

Impact on Residents and Businesses

The improvements benefit the project area by significantly improving the existing infrastructure, preserving and extending the service life, as well as providing upgrades to enhance safety.

SUPPLEMENTAL:

Additional Fiscal Information

Budget

Original Contract Amount		\$768,582
Total Change Orders Authorized	0.0%	\$0
Estimated Pending Change Orders	0.0%	\$0
Authorized Contract Amount		\$768,582
* Quantity Adjustments	0.5%	\$3,481
+ CCO FA Adjustments	0.0%	\$0
Total Amended Contract Amount	100.5%	\$772,063

Expenditures

Total Progress Payments	\$772,063
Estimated Pending Payments	\$0
Total Expenditures	\$772,063

(Over)/Under Contract Amount \$0

+ Change Orders using the Force Account method of payment issued prior to the work being completed generally do not use the total authorized amount.

* *CAL-Trans Standard Specifications 4-1.03B*. Increases or decreases in the quantity of a contract item of work will be determined by comparing the total pay quantity of such item of work with the Engineer's Estimate. If the total pay quantity of any item of work required under the contract varies from the Engineer's Estimate by 25 percent or less, payment will be made for the quantity of work of said item performed at the contract unit price, unless eligible for adjustment pursuant to Section 4-1.03C, "Changes in Character of Work."

This project was funded with \$772,063 of Measure A/Western funds.

Contract History and Price Reasonableness

Six bids were received on February 25, 2015 ranging from \$768,582 to \$1,119,000. The basis for the selection of a contractor is the lowest responsive and responsible bid. The lowest responsive bid was submitted by All American Asphalt in the amount of 768,582, which is \$75,600 (9%) below the Engineer's Estimate.

ATTACHMENTS:

- Vicinity Map
- Progress Estimate Report
- Notice of Completion



C O U N T Y O F R I V E R S I D E
T R A N S P O R T A T I O N D E P A R T M E N T

S A G E R D

RESURFACING AND RECONSTRUCTION PROJECT

SEGMENT 1: 0.18 MILES AT E. BENTON RD
SEGMENT 2: 0.62 MILES AT RED MOUNTAIN RD
SEGMENT 3: 16.6 MILES FROM SH-79 TO CACTUS VALLEY RD

PROJECT No. C2-0158

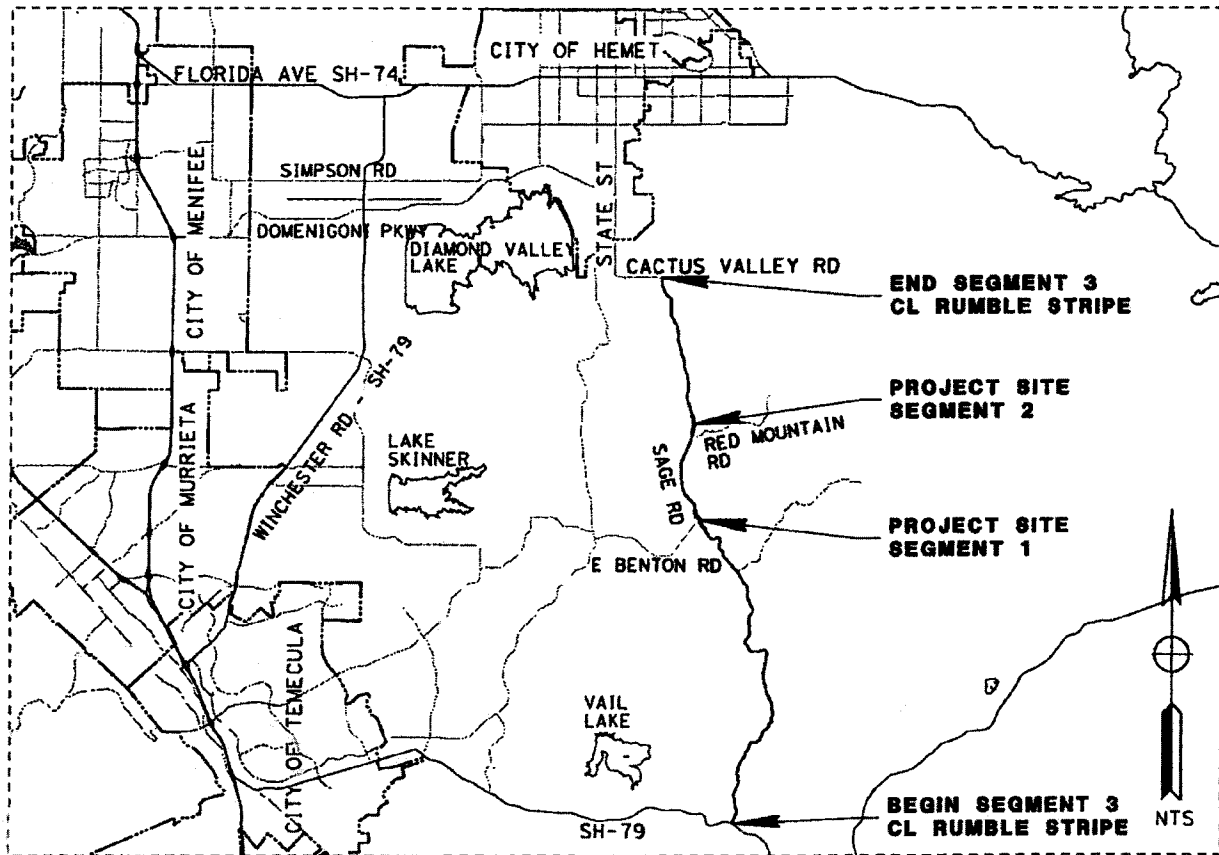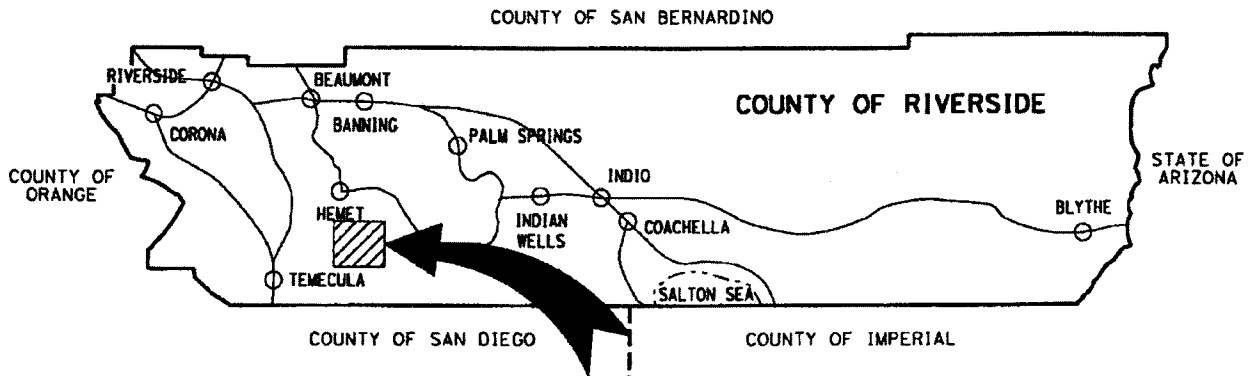

VICINITY MAP

PROGRESS ESTIMATE RECORD - COUNTY OF RIVERSIDE
 PROJECT: Sage Road Resurfacing and Reconstruction Project
 County Project No.: C2-0168
 Contract No. 15-04-003



Contractor: All American Asphalt
 Address: P.O. Box 2229
 City, State, Zip: Corona, CA 92878

Item No.	Item Description	Units	Quantity	Unit Price	Original Contract		Change Orders		Amended Contract		This Estimate		Previous Quantity		Total Estimate To Date		% Auth.
					Amount	Quantity	Amount	Quantity	Amount	Quantity	Amount	Quantity	Amount	Quantity	Amount	Quantity	
1	DUST ABATEMENT	LS	1	6,300.00	6,300.00	1.00				6,300.00	0.10	630.00	0.90	1.00	6,300.00	100%	
2	WATER POLLUTION CONTROL	LS	1	8,900.00	8,900.00	1.00				8,900.00	0.10	890.00	0.90	1.00	8,900.00	100%	
3	TRAFFIC CONTROL SYSTEM	LS	1	43,150.00	43,150.00	1.00				43,150.00	0.10	4,315.00	0.90	1.00	43,150.00	100%	
4	CLEARING AND GRUBBING	LS	1	1,100.00	1,100.00	1.00				1,100.00	0.10	200.00	0.90	1.00	1,100.00	100%	
5	DEVELOP WATER SUPPLY	LS	1	2,000.00	2,000.00	1.00				2,000.00	0.10	200.00	0.90	1.00	2,000.00	100%	
6	FINISHING ROADWAY	LS	1	4,600.00	4,600.00	1.00				4,600.00			1.00	1.00	4,600.00	100%	
7	REPAIR SLOPE	LF	60	516.00	30,960.00	60.00				30,960.00			60.00	60.00	30,960.00	100%	
8	GRINDING ASPHALT CONCRETE IN PLACE	SQYD	11,000	1.10	12,100.00	11,000.00				12,100.00			10,677.78	10,677.78	11,745.56	97%	
9	COLD PLANE ASPHALT CONCRETE PAVEMENT	SQYD	5,100	1.38	7,038.00	5,100.00				7,038.00			5,348.21	5,348.21	7,380.53	105%	
10	SHOULDER BACKING	LF	10,000	1.97	19,700.00	10,000.00				19,700.00			9,156.00	9,156.00	18,037.32	92%	
11	ASPHALT TREATED PERMEABLE BASE	CY	200	165.00	33,000.00	200.00				33,000.00			218.00	218.00	35,970.00	109%	
12	ASPHALT CONCRETE OVERSIDE DRAIN (CRS 306)	EA	10	3,100.00	31,000.00	10.00				31,000.00			11.00	11.00	34,100.00	110%	
13	ASPHALT CONCRETE DIKE	LF	8,000	1.47	11,760.00	8,000.00				11,760.00			8,021.00	8,021.00	11,790.87	100%	
14	HOT MIX ASPHALT	TON	5,200	72.64	377,728.00	5,200.00				377,728.00			5,676.66	5,676.66	412,352.58	109%	
15	18 REINFORCED CONCRETE PIPE "	LF	110	120.00	13,200.00	110.00				13,200.00			112.00	112.00	13,440.00	102%	
16	3 PLASTIC PIPE (EDGE DRAIN) "	LF	510	41.00	20,910.00	510.00				20,910.00			510.00	510.00	20,910.00	100%	
17	DRAINAGE INLET	EA	2	3,600.00	7,200.00	2.00				7,200.00			2.00	2.00	7,200.00	100%	
18	MARKER	EA	25	136.00	3,400.00	25.00				3,400.00			25.00	25.00	3,400.00	100%	
19	METAL BEAM GUARD RAILING	LF	50	255.00	12,750.00	50.00				12,750.00			50.00	50.00	12,750.00	100%	
20	THERMOPLASTIC CROSSWALK AND PAVEMENT MARKING	SQFT	200	6.22	1,244.00	200.00				1,244.00			170.00	170.00	1,057.40	85%	
21	PAINT TRAFFIC STRIPE (2-COAT)	LF	14,000	0.56	7,840.00	14,000.00				7,840.00			14,162.00	14,162.00	7,930.72	101%	

PROGRESS ESTIMATE RECORD - COUNTY OF RIVERSIDE
 PROJECT: Sage Road Resurfacing and Reconstruction Project
 County Project No.: C2-0158
 Contract No. 15-04-003

Contractor: All American Asphalt
 Address: P. O. Box 2229
 City, State, Zip: Corona, CA 92878

Estimate No. 3 Final
 From: September 26, 2015
 To: October 25, 2015



Item No.	Item Description	Units	Quantity	Unit Price	Original Contract		Amended Contract		This Estimate		Previous Quantity		Total Estimate To Date		% Auth.
					Quantity	Amount	Quantity	Amount	Quantity	Amount	Quantity	Amount	Quantity	Amount	
22	PAVEMENT MARKER (REFLECTIVE)	EA	400	4.08	1,632.00	400.00	1,632.00	399.00	399.00	1,627.92	399.00	1,627.92	100%		
23	MISCELLANEOUS WORK (AS DIRECTED)	FA	1	50,000.00	50,000.00	1.00	50,000.00	0.0414010	11,400.09	13,470.14	0.2694028	13,470.14	27%		
24	REMOVE PAVEMENT MARKER	EA	7,000	1.01	7,070.00	7,000.00	7,070.00	5,285.00	5,285.00	5,337.85	5,285.00	5,337.85	76%		
25	RUMBLE STRIP	LF	88,000	0.27	23,760.00	88,000.00	23,760.00	88,306.00	88,306.00	23,842.62	88,306.00	23,842.62	100%		
26	PAINT TRAFFIC STRIPE (2-COAT)	LF	70,000	0.22	15,400.00	70,000.00	15,400.00	82,469.00	82,469.00	18,143.18	82,469.00	18,143.18	118%		
27	PAVEMENT MARKER (REFLECTIVE)	EA	7,000	2.12	14,840.00	7,000.00	14,840.00	6,871.00	6,871.00	14,566.52	6,871.00	14,566.52	98%		
PROJECT TOTAL					768,582.00	0.00	768,582.00	17,435.09	772,063.21						

Made by: Justin Robbins
 Checked by: Justin Robbins 10-21-15
 OK Const. Supv. AB

Working Days: 30 Start Date: 7-27-15
 Days Added: 0 End Date: 9-4-15
 Subtotal: 30 % Complete: 100%
 Days Used: 29 Original Contract: \$768,582.00
 % Time Elapsed: 97% Amended Contract: **PAYMENT APPROVAL**

Fund 20000 LESS LABOR NON COMPLIANCE: 0.00
 Total Due This Payment: \$16,563.34

Dept ID 31305 Received by Accounts Payable: _____
 Account 527980 By: _____
 Project ZC2-0158F

This Estimate Approved Patricia Romo Date: 11/21/15 for: _____
 Patricia Romo, Assistant Director of Transportation

Quantities on This Estimate Approved J. Robbins Date: 10/21/15
 All American Asphalt

TOTAL VALUE OF WORK TO DATE: \$772,063.21
 LESS RETENTION: 5% 38,603.16
 TOTAL DUE TO DATE: \$733,460.05
 LESS PREVIOUSLY INVOICED: 716,896.71
 TOTAL DUE THIS PAYMENT: \$16,563.34

TRANSFISCAL APPROVED
 By: Crystal Potter 5-3461
 NOV 09 2015
 Norma Larson
 951-955-2783
 #12115

PLEASE COMPLETE THIS INFORMATION
RECORDING REQUESTED BY:

**KECIA HARPER-IHEM, CLERK OF THE BOARD
RIVERSIDE CO. CLERK OF THE BOARD
4080 LEMON STREET, 1ST FLOOR CAC
P O BOX 1147 - RIVERSIDE, CA 92502
MAIL STOP # 1010**

AND WHEN RECORDED MAIL TO:
**RETURN TO: STOP #1010
RIVERSIDE COUNTY CLERK OF THE BOARD
P. O. BOX 1147 - RIVERSIDE, CA 92502**

2016-0336760

08/08/2016 11:35 AM Fee: \$ 0.00

Page 1 of 5

Recorded in Official Records
County of Riverside
Peter Aldana
Assessor-County Clerk-Recorder



12/1					R	A	Exam: 087		
Page	DA	PCOR	Misc	Long	RFD	1st Pg	Adtl Pg	Cert	CC
5									
SIZE	NCOR	SMF	NCHG				NCT1000		

NOTICE OF COMPLETION

6

Re-record

To be recorded with County Recorder
within 10 days after completion.
No recording fee.

Notice is hereby given by the undersigned owner, a public entity of the State of California, that a public work of improvement has been completed, as follows:

Project title or description of work: Sage Road Resurfacing and Reconstruction Project

Date of Completion: Date of this notice 5/16/16

Nature of owner: County of Riverside, public entity

Interest or estate of owner: Public Roadway

Address of owner: 4080 Lemon Street, 8th Floor, Riverside, CA 92501

Name of contractor: All American Asphalt

Street or legal description of site: Sage Road at East Benton Rd and from Red Mountain Rd Northerly 3300 Feet

Dated: May 16, 2016

Owner: County of Riverside
(Name of Public Entity)

By: John J. Benoit
Chairman, Board of Supervisors



STATE OF CALIFORNIA)
ss
COUNTY OF RIVERSIDE)

I am the Chairman of the governing board of the County of Riverside, the public entity which executed the foregoing notice and on whose behalf I make this verification; I have read this notice, know its contents, and the same is true. I certify under penalty of perjury that the foregoing is true and correct.

Executed at Riverside, California on 5/16/16 (Date)

John J. Benoit, Chairman of the Board of Supervisors

ATTEST:
KECIA HARPER-IHEM, Clerk
By: [Signature]
DEPUTY

03.29.16 3-34

2016-0-132780



**PETER ALDANA
COUNTY OF RIVERSIDE
ASSESSOR-COUNTY CLERK-RECORDER**

Recorder
P.O. Box 751
Riverside, CA 92502-0751
(951) 486-7000

www.riversideacr.com

CERTIFICATION

Pursuant to the provisions of Government Code 27361.7, I certify under the penalty of perjury that the following is a true copy of illegible wording found in the attached document:

(Print or type the page number(s) and wording below):

CLARIFICATION OF THE SEAL for the Riverside County Board of Supervisors
(embossed on document)



Date:

5-16-16

Signature:

Karen Barton

Print Name:

Karen Barton, Board Assistant, Riverside County Clerk of the Board

PLEASE COMPLETE THIS INFORMATION
RECORDING REQUESTED BY:

KECIA HARPER-IHEM, CLERK OF THE BOARD
RIVERSIDE CO. CLERK OF THE BOARD
4080 LEMON STREET, 1ST FLOOR CAC
P O BOX 1147 - RIVERSIDE, CA 92502

MAIL STOP # 1010

AND WHEN RECORDED MAIL TO:

RETURN TO: STOP #1010
RIVERSIDE COUNTY CLERK OF THE BOARD
P. O. BOX 1147 - RIVERSIDE, CA 92502

2016-0124667

03/31/2016 08:59 AM Fee: \$ 0.00

Page 1 of 2

Recorded in Official Records
County of Riverside
Peter Aldana
Assessor-County Clerk-Recorder



126					R	A	Exam: 110		
Page	DA	PCOR	Misc	Long	RFD	1st Pg	Adtl Pg	Cert	CC
2									
SIZE	NCOR	SMF	NCHG	T:	NCP ACC				

NOTICE OF COMPLETION

To be recorded with County Recorder
within 10 days after completion.
No recording fee.

Notice is hereby given by the undersigned owner, a public entity of the State of California, that a public work of improvement has been completed, as follows:

Project title or description of work: Sage Road Resurfacing and Reconstruction Project

Date of Completion: Date of this notice 3/29/16

Nature of owner: County of Riverside, public entity

Interest or estate of owner: Public Roadway

Address of owner: 4080 Lemon Street, 8th Floor, Riverside, CA 92501

Name of contractor: All American Asphalt

Street or legal description of site: Sage Road ✓

Dated: March 29, 2016

Owner: County of Riverside
(Name of Public Entity)

By: John J. Benoit
Chairman, Board of Supervisors
John J. Benoit

STATE OF CALIFORNIA)
 ss
COUNTY OF RIVERSIDE)

I am the Chairman of the governing board of the County of Riverside, the public entity which executed the foregoing notice and on whose behalf I make this verification; I have read this notice, know its contents, and the same is true. I certify under penalty of perjury that the foregoing is true and correct.

Executed at Riverside, California on 3/29/16 (Date)

John J. Benoit, Chairman of the Board of Supervisors
John J. Benoit

ATTEST:
Kecia Harper-Ihem, Clerk

By: [Signature] Deputy

03.29.16 3-34

FORM APPROVED COUNTY COUNSEL
BY: Yousha Victor 3/8/16
MARSHAL VICTOR DATE

2016-4-131443



PETER ALDANA
COUNTY OF RIVERSIDE
ASSESSOR-COUNTY CLERK-RECORDER

Recorder
P.O. Box 751
Riverside, CA 92502-0751
(951) 486-7000

www.riversideacr.com

CERTIFICATION

Pursuant to the provisions of Government Code 27361.7, I certify under the penalty of perjury that the following is a true copy of illegible wording found in the attached document:

(Print or type the page number(s) and wording below):

CLARIFICATION OF THE SEAL for the Riverside County Board of Supervisors
(embossed on document)



Date:

3-29-16

Signature:

Karen Barton

Print Name:

Karen Barton, Board Assistant, Riverside County Clerk of the Board
