

**SUBMITTAL TO THE BOARD OF SUPERVISORS
COUNTY OF RIVERSIDE, STATE OF CALIFORNIA**

840 A



FROM: TLMA – Transportation Department

SUBMITTAL DATE:
May 2, 2016

SUBJECT: Notice of Completion – Mecca Roundabout Street Improvements Project at the Intersection of 4th Street and Hammond Road. 4th District; [\$1,801,890 - Total Cost]; Local Funds 39% and Federal Funds 61%

RECOMMENDED MOTION: That the Board of Supervisors:

1. Accept the Mecca Roundabout Street Improvements Project as completed; and
2. Authorize the Chairman of the Board to execute the Notice of Completion and the Clerk of the Board to record the Notice.

BACKGROUND:

Summary

By Minute Order 3-73 of July 31, 2012, the Board of Supervisors entered into a contract with Mamco, Inc. of Riverside, CA for the construction of Mecca Roundabout Street Improvements Project at the intersection of 4th Street and Hammond Road, in the unincorporated Community of Mecca.

Patricia Romo
Assistant Director of Transportation

Juan C. Perez
Director of Transportation and Land Management

FINANCIAL DATA	Current Fiscal Year:	Next Fiscal Year:	Total Cost:	Ongoing Cost:	POLICY/CONSENT (Per Exec. Office)
COST	\$ 1,801,890	\$ 0	\$ 1,801,890	\$ 0	Consent <input type="checkbox"/> Policy <input checked="" type="checkbox"/>
NET COUNTY COST	\$ 0	\$ 0	\$ 0	\$ 0	

SOURCE OF FUNDS: Federal Highway (CMAQ) (61%) and Redevelopment Agency funds (39%). There are no General funds used in this Project.

Budget Adjustment: N/A
For Fiscal Year: 15/16

C.E.O. RECOMMENDATION:

APPROVE

BY:
Tina Grande

County Executive Office Signature

MINUTES OF THE BOARD OF SUPERVISORS

On motion of Supervisor Jeffries, seconded by Supervisor Benoit and duly carried, IT WAS ORDERED that the above matter is approved as recommended.

Ayes: Jeffries, Washington and Benoit
Nays: None
Absent: Tavaglione and Ashley
Date: June 7, 2016
xc: Transp., Recorder

Kecia Harper-Ihem
Clerk of the Board
By:
Deputy

Prev. Agn. Ref.: 7/31/12, Item 3-73

District: 4

Agenda Number:

3-44

FORM APPROVED COUNTY COUNSEL 5/17/16
DATE
BY: GREGORY P. PRIAMOS

Departmental Concurrence

- A-30
- Positions Added
- 4/5 Vote
- Change Order

SUBMITTAL TO THE BOARD OF SUPERVISORS, COUNTY OF RIVERSIDE, STATE OF CALIFORNIA
FORM 11: Notice of Completion – Mecca Roundabout Street Improvements Project at the Intersection of 4th Street and Hammond Road. 4th District; [\$1,801,890 - Total Cost]; Local Funds 39% and Federal Funds 61%

DATE: May 2, 2016

PAGE: 2 of 3

BACKGROUND:

Summary (continued)

The originally authorized amount of the contract was \$1,818,018. The total amended contract is \$1,801,890 which is 0.9% less than the originally authorized amount.

The project was completed February 25, 2013, however, it had a three (3) year landscape maintenance period specified in the contract. The landscape maintenance period ended on March 25, 2016. The work was completed in conformance with the plans and specifications and the contractor was granted relief of maintenance on March 25, 2016.

Work Order Number B9-0997, Federal Aid No.: CML-5956 (188)

Impact on Residents and Businesses

The project has improved traffic circulation, pedestrian access, and street drainage by eliminating blight.

SUPPLEMENTAL:

Additional Fiscal Information

Budget

Original Contract Amount		\$1,818,018
Total Change Orders Authorized	0.0%	\$0
Estimated Pending Change Orders	0.0%	\$0
Authorized Contract Amount		\$1,818,018
* Quantity Adjustments	-0.9%	(\$16,128)
+ CCO FA Adjustments	0.0%	\$0
Total Amended Contract Amount	99.1%	\$1,801,890

Expenditures

Total Progress Payments	\$1,801,890
Estimated Pending Payments	\$0
Total Expenditures	\$1,801,890

(Over)/Under Contract Amount \$0

+ Change Orders using the Force Account method of payment issued prior to the work being completed generally do not use the total authorized amount.

* CAL-Trans Standard Specifications 4-1.03B. Increases or decreases in the quantity of a contract item of work will be determined by comparing the total pay quantity of such item of work with the Engineer's Estimate. If the total pay quantity of any item of work required under the contract varies from the Engineer's Estimate by 25 percent or less, payment will be made for the quantity of work of said item performed at the contract unit price, unless eligible for adjustment pursuant to Section 4-1.03C, "Changes in Character of Work."

This project was funded with \$1,099,153 of Federal Highway (CMAQ) funds and \$702,737 of Redevelopment Agency funds.

Contract History and Price Reasonableness

Five bids were received on May 23, 2012 ranging from \$1,818,018 to \$2,354,585. The basis for the selection of a contractor is the lowest responsive and responsible bid of base bid schedules A, B & C. The lowest responsible bid was submitted by Mamco, Inc. in the amount of \$1,818,018, which is \$129,072 (6.63%) below the Engineer's Estimate.

SUBMITTAL TO THE BOARD OF SUPERVISORS, COUNTY OF RIVERSIDE, STATE OF CALIFORNIA
FORM 11: Notice of Completion – Mecca Roundabout Street Improvements Project at the Intersection of 4th Street and Hammond Road. 4th District; [\$1,801,890 - Total Cost]; Local Funds 39% and Federal Funds 61%

DATE: May 2, 2016

PAGE: 3 of 3


ATTACHMENTS:

Vicinity Map

Progress Estimate Report

Notice of Completion

Mecca Roundabout Location Map

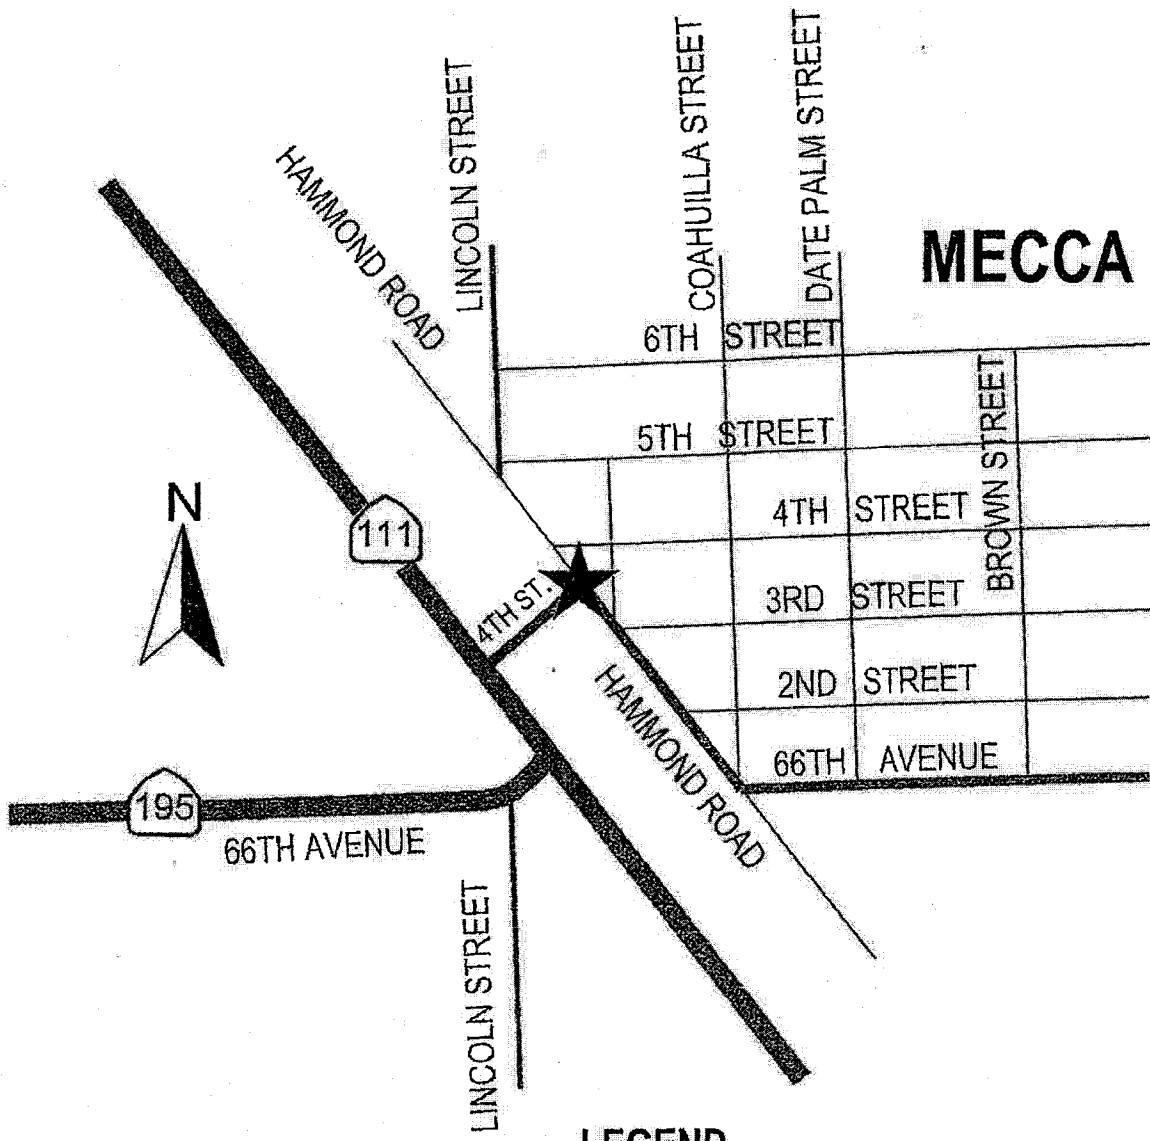

MECCA

LEGEND



Proposed Roundabout Location

PROJECT: Mecca Roundabout Street Improvement Project at 4th street and Hammond Road
 County Project No.: B9-0997 & X1005, CML-5956(188)
 Contract No.: 12-07-004

Contractor: Mamco, Inc.
 Address: 18810 Van Buren Blvd. #200
 City, State, Zip: Riverside, 92504

Estimate No. 19 Final
 From: August 26, 2015
 To: March 25, 2016



Item No.	Item Description	Units	Quantity	Unit Price	Original Contract		Change Authorized		Total Authorized		This Estimate		Previous		Total Estimate To Date		% Auth.
					Quantity	Amount	Quantity	Amount	Quantity	Amount	Quantity	Amount	Quantity	Amount	Quantity	Amount	
Project Subtotals																	
	ROUNDABOUT - B9-0997				1,588,588.00			1,588,588.00			5,000.00					1,601,086.20	
	BLOCKWALL, SIGN REPLACEMENT & ADA PARKING SPACES - X1005				229,430.00			229,430.00								200,803.67	
	PROJECT TOTAL				1,818,018.00	0.00		1,818,018.00			5,000.00					1,801,889.87	

Made by: Alec Yzaquire
 Checked by: NS 3-22-16
 OK Const. Supv. WML 3-23-16

Working Days: 95
 Days Added: 20
 Subtotal: 115
 Days Used: 113
 % Time Elapsed: 98%

Start Date: 8-20-12
 End Date: 2-14-13
 % \$ Complete: 99%
 Original Contract: \$1,818,018.00
 Amended Contract: \$1,818,018.00

TOTAL VALUE OF WORK TO DATE: \$1,801,889.87
 LESS RETENTION: 0%
 TOTAL DUE TO DATE: \$1,801,889.87
 LESS PREVIOUSLY INVOICED: 1,796,889.87
 LESS LABOR NON COMPLIANCE: 0.00
 TOTAL DUE THIS PAYMENT: \$5,000.00

This Estimate Approved _____ Date: _____ for: _____
 Patricia Romo, Assistant Director of Transportation

PAYMENT APPROVAL

Quantities on This Estimate Approved [Signature] Date: 3/29/16
 Mamco, Inc.

Received by Accounts Payable: _____
 By: _____

Fund 20000
 Dept ID 31305
 Account 527980
 Project Z09-09976
 Activity ID Z3500
 Resource Type CNT
 Signature [Signature]
 Date 3/29/16

PROJECT: Mecca Roundabout Street Improvement Project at 4th street and Hammond Road
 County Project No.: B9-0997 & X1005, CML-5986(188)
 Contract No.: 12-07-004

Contractor: Mamco, Inc.
 Address: 16810 Van Buren Blvd. #200
 City, State, Zip: Riverside, 92504

Estimate No. 19 Final
 From: August 26, 2015
 To: March 25, 2016

Item No.	Item Description	Units	Quantity	Unit Price	Original Contract Amount	Change Authorized		Total Authorized		This Estimate Quantity	This Estimate Amount	Previous		% Auth.
						Quantity	Amount	Quantity	Amount			Quantity	Amount	
ROUNDABOUT - B9-0997														
1	MOBILIZATION	LS	1	25,000.00	25,000.00			1.00	25,000.00	1.00	25,000.00	1.00	25,000.00	100%
2	DE-MOBILIZATION	LS	1	50,000.00	50,000.00			1.00	50,000.00	1.00	50,000.00	1.00	50,000.00	100%
3	DUST ABATEMENT	LS	1	5,000.00	5,000.00			1.00	5,000.00	1.00	5,000.00	1.00	5,000.00	100%
4	WATER POLLUTION CONTROL	LS	1	20,000.00	20,000.00			1.00	20,000.00	1.00	20,000.00	1.00	20,000.00	100%
5	TRAFFIC CONTROL SYSTEM	LS	1	25,000.00	25,000.00			1.00	25,000.00	1.00	25,000.00	1.00	25,000.00	100%
6	CLEARING AND GRUBBING	LS	1	25,000.00	25,000.00			1.00	25,000.00	1.00	25,000.00	1.00	25,000.00	100%
7	TEMPORARY CONSTRUCTION PROJECT FUNDING IDENTIFICATION SIGN	EA	1	800.00	800.00			1.00	800.00	1.00	800.00	1.00	800.00	100%
8	ROADWAY EXCAVATION	CY	5,500	36.00	198,000.00			5,500.00	198,000.00	5,500.00	198,000.00	5,500.00	198,000.00	100%
9	HOT MIX ASPHALT	TON	2,150	100.00	215,000.00			2,150.00	215,000.00	2,073.22	207,322.00	2,073.22	207,322.00	96%
10	CLASS 2 AGGREGATE BASE	CY	4,500	46.00	207,000.00			4,500.00	207,000.00	5,029.00	231,334.00	5,029.00	231,334.00	112%
11	SUBGRADE ENHANCEMENT FABRIC (GEOGRID 1 LAYER)	SOYD	11,500	5.00	57,500.00			11,500.00	57,500.00	11,410.76	57,053.80	11,410.76	57,053.80	99%
12	MINOR CONCRETE (CURB AND GUTTER) (CRS 200)	LF	1,450	18.00	26,100.00			1,450.00	26,100.00	1,416.00	25,488.00	1,416.00	25,488.00	98%
13	MINOR CONCRETE (TYPE D CURB) (MODIFIED CRS 204) [6" CF]	LF	1,900	16.00	30,400.00			1,900.00	30,400.00	1,785.00	28,560.00	1,785.00	28,560.00	94%
14	MINOR CONCRETE (TYPE A3-8 CURB) (CT STD A87A) [8" CF]	LF	230	16.00	3,680.00			230.00	3,680.00	219.00	3,504.00	219.00	3,504.00	95%
15	MINOR CONCRETE (TYPE B3-4 CURB) (CT STD A87A) [4" CF]	LF	270	16.00	4,320.00			270.00	4,320.00	241.00	3,856.00	241.00	3,856.00	89%
16	MINOR CONCRETE (CURB) [3" CF, MOUNTABLE CURB PER DETAIL]	LF	260	18.00	4,680.00			260.00	4,680.00	253.00	4,554.00	253.00	4,554.00	97%
17	MINOR CONCRETE [CONCRETE MOW STRIP]	LF	500	16.00	8,000.00			500.00	8,000.00	625.00	10,000.00	625.00	10,000.00	125%
18	MINOR CONCRETE (SIDEWALK) [CRS 401] [4" THICK]	SQFT	9,200	4.00	36,800.00			9,200.00	36,800.00	9,327.50	37,310.00	9,327.50	37,310.00	101%
19	MINOR CONCRETE (CURB RAMP) [PER DETAIL]	SQFT	650	6.00	3,900.00			650.00	3,900.00	806.90	4,841.40	806.90	4,841.40	124%
20	MINOR CONCRETE (MINOR STRUCTURE) [UNDER SIDEWALK DRAIN PER CRS 309, AND U-DRAIN PER DETAIL]	LS	1	4,500.00	4,500.00			1.00	4,500.00	1.00	4,500.00	1.00	4,500.00	100%
21	MINOR CONCRETE (DRIVEWAY) [CRS 207] [8" THICK]	SQFT	90	5.00	450.00			90.00	450.00	110.00	550.00	110.00	550.00	122%
22	MINOR CONCRETE (DRIVEWAY) [CRS 207, COLORED CONCRETE] [8" THICK]	SQFT	105	6.00	630.00			105.00	630.00	90.00	540.00	90.00	540.00	86%

PROJECT: Mecca Roundabout Street Improvement Project at 4th Street and Hammond Road
 County Project No.: B9-0987 & X1005, CML-9986(189)
 Contract No.: 12-07-004

Contractor: Mamco, Inc.
 Address: 16810 Van Buren Blvd. #200
 City, State, Zip: Riverside, 92504

Estimate No. 19 Final
 From: August 26, 2015
 To: March 25, 2016

Item No.	Item Description	Units	Quantity	Unit Price	Original Contract Amount	Change Authorized Quantity	Change Authorized Amount	Total Authorized		This Estimate		Previous Quantity	Total Estimate To Date Quantity	% Auth.
								Quantity	Amount	Quantity	Amount			
23	MINOR CONCRETE [COLORED CONCRETE - BIKE PATH, BIKE RAMP] (4" THICK)	SQFT	1,300	6.00	7,800.00			1,300.00	7,800.00			1,266.00	1,266.00	97%
24	MINOR CONCRETE (STAMPED CONCRETE) [DECORATIVE COLORED - MEDIUM ISLANDS] (4" THICK)	SQFT	6,400	6.00	38,400.00			6,400.00	38,400.00			5,451.25	5,451.25	85%
25	MINOR CONCRETE (STAMPED CONCRETE) [DECORATIVE COLORED- CONCRETE PAVEMENT - TRUCK APRON. (8" THICK)]	CY	110	400.00	44,000.00			110.00	44,000.00			116.78	116.78	106%
26	METAL BEAM GUARD RAILING (WOOD POSTS) [CALTRANS STD PLAN A77A]	LF	60	50.00	3,000.00			60.00	3,000.00			60.00	60.00	100%
27	REMOVE TRAFFIC STRIPE AND PAVEMENT MARKING	SQFT	700	5.50	3,850.00			700.00	3,850.00			701.00	701.00	100%
28	THERMOPLASTIC CROSSWALK AND PAVEMENT MARKINGS	SQFT	4,200	4.00	16,800.00			4,200.00	16,800.00			3,158.00	3,158.00	75%
29	THERMOPLASTIC TRAFFIC STRIPE (SPRAYABLE)	LF	4,000	1.40	5,600.00			4,000.00	5,600.00			3,600.00	3,600.00	90%
30	PAINT TRAFFIC STRIPE (2 COAT)	LF	780	1.10	858.00			780.00	858.00			650.00	650.00	83%
31	ROADWAY SIGN - ONE POST	EA	49	200.00	9,800.00			49.00	9,800.00			49.00	49.00	100%
32	RELOCATE ROADSIDE SIGN AND REPLACE POST	EA	2	200.00	400.00			2.00	400.00			2.00	2.00	100%
33	BARRIER POST [BOLLARD]	EA	4	1,200.00	4,800.00			4.00	4,800.00			4.00	4.00	100%
34	CHAIN LINK FENCE [WITH CURB PER DETAIL]	LF	50	62.00	3,100.00			50.00	3,100.00			62.50	62.50	125%
35	LIGHTING [ROUNDABOUT SAFETY LIGHTING SYSTEM]	LS	1	75,000.00	75,000.00			1.00	75,000.00			1.00	1.00	100%
36	IMPORTED BORROW [FILL AND DECORATIVE MOUNDING]	CY	1,275	18.00	22,950.00			1,275.00	22,950.00			1,000.00	1,000.00	78%
37	IMPORTED BORROW GRANULAR MATERIAL [DECOMPOSED GRANITE (3" THICK)]	CY	415	92.00	38,180.00			415.00	38,180.00			415.00	415.00	100%
38	IMPORTED ROCKY MATERIAL [BOULDERS (SIZE 1-2.5X2X2)]	EA	90	66.00	5,940.00			90.00	5,940.00			90.00	90.00	100%
39	IMPORTED ROCKY MATERIAL [BOULDERS (SIZE 12-3.5X3X2)]	EA	80	105.00	8,400.00			80.00	8,400.00			80.00	80.00	100%
40	REMOVE EXISTING BLOCK WALL [INCLUDING INSTALLATION OF TEMPORARY FENCING]	LF	210	37.00	7,770.00			210.00	7,770.00			210.00	210.00	100%
41	MASONRY BLOCK WALL [6" SLUMP BLOCK WALL W/ROLLED MORTAR CAP]	LF	650	140.00	91,000.00			650.00	91,000.00			650.00	650.00	100%
42	7" PLASTER WITH STONE VENEER AND PRECAST CAP	EA	12	3,600.00	43,200.00			12.00	43,200.00			14.00	14.00	117%
43	ENTRY MONUMENT WALL STRUCTURE	LS	1	9,000.00	9,000.00			1.00	9,000.00			1.00	1.00	100%
44	AGAVE PLANT METAL SCULPTURES (24" X 30") (4 EACH)	FA	1	5,000.00	5,000.00			1.00	5,000.00			1.25	1.25	125%
45	ELECTRIC SERVICE (IRRIGATION) [INCLUDING CONDUIT RUNS BETWEEN CONTROLLER, SERVICE POINT, AND PEDESTAL]	EA	1	8,000.00	8,000.00			1.00	8,000.00			1.00	1.00	100%
46	SOIL PREPARATION (PHASE 1)	LS	1	5,000.00	5,000.00			1.00	5,000.00			1.00	1.00	100%

PROJECT: Mecca Roundabout Street Improvement Project at 4th street and Hammond Road
 County Project No.: 89-0987 & X1005, CML-5956(188)
 Contract No.: 12-07-004

Contractor: Manco, Inc.
 Address: 16810 Van Buren Blvd. #200
 City, State, Zip: Riverside, 92504

Estimate No. 19 Final
 From: August 26, 2015
 To: March 25, 2016

Item No.	Item Description	Units	Quantity	Unit Price	Original Contract Amount	Change Authorized Quantity	Change Authorized Amount	Total Authorized Quantity	Total Authorized Amount	This Estimate Quantity	This Estimate Amount	Previous Quantity	Total Estimate To Date Quantity	Total Estimate To Date Amount	% Auth.
46A	OBTAIN ENCROACHMENT PERMIT	FA	1	1,000.00	1,000.00			1.00	1,000.00			0.82	0.82	820.00	82%
47	PLANT (GROUP Z) (PALM TREE) [6 BTH]	EA	24	395.00	9,480.00			24.00	9,480.00			24.00	24.00	9,480.00	100%
48	PLANT (GROUP Z) (PALM TREE) [10 BTH]	EA	3	2,600.00	7,800.00			3.00	7,800.00			3.00	3.00	7,800.00	100%
49	PLANT (GROUP B) [5 GALLON SHRUB]	EA	200	31.00	6,200.00			200.00	6,200.00			200.00	200.00	6,200.00	100%
50	IRRIGATION SYSTEM (DRIP EMITTER SYSTEM EQUIPMENT, ASSEMBLIES, VALVES, AND PIPING (PHASE 1))	LS	1	53,000.00	53,000.00			1.00	53,000.00			1.00	1.00	53,000.00	100%
51	IRRIGATION CONTROLLER ASSEMBLY (CALSENSE) (INCLUDING ET GAGE, RAIN BUCKET, ANTENNA)	LS	1	25,000.00	25,000.00			1.00	25,000.00			1.00	1.00	25,000.00	100%
52	LANDSCAPE LIGHTING AND SIGN ILLUMINATION (INCLUDING ALL CONDUIT, CONTACTS, RELAYS, AND CONDUIT TO SERVICE POINT)	LS	1	16,500.00	16,500.00			1.00	16,500.00			1.00	1.00	16,500.00	100%
53	PLANT ESTABLISHMENT PERIOD (12 QUARTERS)	LS	60,000	1.00	60,000.00			60,000.00	60,000.00	5,000.00	5,000.00	55,000.00	60,000.00	60,000.00	100%
BLOCKWALL, SIGN REPLACEMENT & ADA PARKING SPACES - X1005															
54	RADAR DRIVER FEEDBACK DISPLAY ASSEMBLIES (ZEACH) AND WIRELESS COMMUNICATION EQUIPMENT	LS	1	81,000.00	81,000.00			1.00	81,000.00			1.00	1.00	81,000.00	100%
55	ITEM RELOCATED TO ALT. BID SCHEDULE "2"				0.00				0.00						N/A
56	ITEM RELOCATED TO ALT. BID SCHEDULE "2"				0.00				0.00						N/A
57	MISCELLANEOUS DIRECTED WORK	FA	100,000	1.00	100,000.00			100,000.00	100,000.00			66,210.67	66,210.67	66,210.67	66%
58	REPLACE EXISTING ROADSIDE SIGNS AND POSTS WITH NEW ROADSIDE SIGNS AND POSTS	EA	120	200.00	24,000.00			120.00	24,000.00			146.00	146.00	29,200.00	122%
59	MODIFY ANGLED PARKING FOR ADA COMPLIANCE (CT STD. A90A)	LS	1	3,500.00	3,500.00			1.00	3,500.00			1.00	1.00	3,500.00	100%
60	REMOVE EXISTING BLOCK WALL (INCLUDING INSTALLATION OF TEMPORARY FENCING)	LF	90	37.00	3,330.00			90.00	3,330.00			89.00	89.00	3,293.00	99%
61	MASONRY BLOCK WALL [6' SLUMP BLOCK WALL WIROLLED MORTAR CAP]	LF	90	140.00	12,600.00			90.00	12,600.00			90.00	90.00	12,600.00	100%
62	MAN GATE	EA	1	5,000.00	5,000.00			1.00	5,000.00			1.00	1.00	5,000.00	100%

PROJECT: Mecca Roundabout Street Improvement Project at 4th street and Hammond Road
County Project No.: B9-0987 & X1005, CHL-4966(188)
Contract No.: 12-07-004

Contractor: Mamco, Inc.
Address: 16810 Van Buren Blvd. #200
City, State, Zip: Riverside, 92504

Estimate No. 19 Final
From: August 26, 2016
To: March 25, 2016



ROUNDABOUT - B9-0997

ESTIMATE TO DATE:	\$1,601,086.20
LESS RETENTION:	0%
LESS PREVIOUSLY INVOICED:	0.00
LESS LABOR NON COMPLIANCE:	1,596,086.20
TOTAL DUE THIS PAYMENT:	0.00
	=====
	\$5,000.00

BLOCKWALL, SIGN REPLACEMENT & ADA PARKING SPACES - X1005

ESTIMATE TO DATE:	\$200,803.67
LESS RETENTION:	0%
LESS PREVIOUSLY INVOICED:	0.00
TOTAL DUE THIS PAYMENT:	200,803.67
	=====
	\$0.00

TOTAL DUE THIS PAYMENT: **\$5,000.00**

PLEASE COMPLETE THIS INFORMATION
RECORDING REQUESTED BY:

**KECIA HARPER-IHEM, CLERK OF THE BOARD
RIVERSIDE CO. CLERK OF THE BOARD
4080 LEMON STREET, 1ST FLOOR CAC
P O BOX 1147 - RIVERSIDE, CA 92502**

MAIL STOP # 1010

AND WHEN RECORDED MAIL TO:

**RETURN TO: STOP #1010
RIVERSIDE COUNTY CLERK OF THE BOARD
P. O. BOX 1147 - RIVERSIDE, CA 92502**

2016-0234666

06/08/2016 04:07 PM Fee: \$ 0.00

Page 1 of 2

Recorded in Official Records
County of Riverside
Peter Aldana
Assessor-County Clerk-Recorder



126					R	A	Exam: 100		
Page	DA	PCOR	Misc	Long	RFD	1st Pg	Adtl Pg	Cert	CC
2	1								
SIZE	NCOR	SMF	(NCHG) T:						N/CCT16

NOTICE OF COMPLETION

To be recorded with County Recorder
within 10 days after completion.
No recording fee.

Notice is hereby given by the undersigned owner, a public entity of the State of California, that a public work of improvement has been completed, as follows:

Project title or description of work: Mecca Roundabout Street Improvements

Date of Completion: Date of this notice 06/07/16

Nature of owner: County of Riverside, public entity

Interest or estate of owner: Public Roadway

Address of owner: 4080 Lemon Street, 8th Floor, Riverside, CA 92501

Name of contractor: Mamco, Inc.

Street or legal description of site: 4th Street and Hammond Road

Dated: June 7, 2016

Owner: County of Riverside
(Name of Public Entity)

By: John J. Benoit
Chairman, Board of Supervisors
John J. Benoit

STATE OF CALIFORNIA)

ss

COUNTY OF RIVERSIDE)

I am the Chairman of the governing board of the County of Riverside, the public entity which executed the foregoing notice and on whose behalf I make this verification; I have read this notice, know its contents, and the same is true. I certify under penalty of perjury that the foregoing is true and correct.

Executed at Riverside, California on 06/07/16 (Date)

John J. Benoit, Chairman of the Board of Supervisors
John J. Benoit

ATTEST:

KECIA HARPER-IHEM, Clerk
By: Kecia Harper-Ihem
DEPUTY

06.07.16 3-44

FORM APPROVED COUNTY COUNSEL

BY: Marsha L. Victor 01/17/16
MARSHA L. VICTOR DATE
2016-7-132274

RECEIVED RIVERSIDE COUNTY
CLERK / BOARD OF SUPERVISORS
2016 JUL - 1 AM 11:35



PETER ALDANA
COUNTY OF RIVERSIDE
ASSESSOR-COUNTY CLERK-RECORDER

Recorder
P.O. Box 751
Riverside, CA 92502-0751
(951) 486-7000
www.riversideacr.com

CERTIFICATION

Pursuant to the provisions of Government Code 27361.7, I certify under the penalty of perjury that the following is a true copy of illegible wording found in the attached document:

(Print or type the page number(s) and wording below):

CLARIFICATION OF THE SEAL for the Riverside County Board of Supervisors
(embossed on document)



Date:

6-7-16

Signature:

Karen Barton

Print Name:

Karen Barton, Board Assistant, Riverside County Clerk of the Board
