

**SUBMITTAL TO THE BOARD OF SUPERVISORS
COUNTY OF RIVERSIDE, STATE OF CALIFORNIA**



2123

FROM : TRANSPORTATION AND LAND MANAGEMENT AGENCY-
TRANSPORTATION

SUBMITTAL DATE:

August 17, 2016

SUBJECT: Notice of Completion – Avenida Rambla and Camino Campesino Sidewalk Safety Project in the Desert of Hot Springs Area. 4th District. [\$208,501 – Total Cost]; State Funds 100%

RECOMMENDED MOTION: That the Board of Supervisors:

1. Accept Avenida Rambla and Camino Campesino Sidewalk Safety Project as completed; and
2. Authorize the Chairman of the Board to execute the Notice of Completion and the Clerk of the Board to record the Notice.

Policy

FINANCIAL DATA	Current Fiscal Year:	Next Fiscal Year:	Total Cost:	Ongoing Cost
COST	\$ 208,501	\$ 0	\$ 208,501	\$ 0
NET COUNTY COST	\$ 0	\$ 0	\$ 0	\$ 0
SOURCE OF FUNDS: Active Transportation Program (ATP) (100%). There are no General funds used in this Project.			Budget Adjustment: N/A	
			For Fiscal Year: 16/17	

C.E.O. RECOMMENDATION:

MINUTES OF THE BOARD OF SUPERVISORS

On motion of Supervisor Benoit, seconded by Supervisor Washington and duly carried by unanimous vote, IT WAS ORDERED that the above matter is approved as recommended.

Ayes: Jeffries, Tavaglione, Washington, Benoit and Ashley
Nays: None
Absent: None
Date: October 25, 2016
xc: Transp., Recorder

Kecia Harper-Ihem
 Clerk of the Board
 By: *[Signature]*
 Deputy

3-43

**SUBMITTAL TO THE BOARD OF SUPERVISORS COUNTY OF RIVERSIDE,
STATE OF CALIFORNIA**

BACKGROUND:

Summary

By Minute Order 3-33 of April 26, 2016, the Board of Supervisors entered into a contract with CT&T Concrete Paving, Inc., Pomona, CA for sidewalk construction at Avenida Rambla and Camino Campesino in the Desert Hot Springs Area.

The originally authorized amount of the contract was \$205,340. The total amended contract is \$208,501 which is 1.5% more than the originally authorized amount. The increase in the total contract price was the result of an increase in the asphalt paving and concrete curb required to complete the work.

The work was completed in conformance with the plans and specifications and the contractor was granted relief of maintenance on July 7, 2016. Work Order Number C5-0076, State Project No. ATPL 5956 (245).

Impact on Residents and Businesses

The project has improved pedestrian safety by providing an American with Disabilities Act (ADA) compliant pedestrian path for students and parents going to and from Bubbling Wells Elementary School.

SUPPLEMENTAL:

Additional Fiscal Information

Budget

Original Contract Amount		\$205,340
Total Change Orders Authorized	0.0%	\$0
Estimated Pending Change Orders	0.0%	\$0
Authorized Contract Amount		\$205,340
* Quantity Adjustments	1.5%	\$3,161
+ CCO FA Adjustments	0.0%	\$0
Total Amended Contract Amount	101.5%	\$208,501

Expenditures

Total Progress Payments		\$208,501
Estimated Pending Payments		\$0
Total Expenditures		\$208,501

(Over)/Under Contract Amount \$0

+ Change Orders using the Force Account method of payment issued prior to the work being completed generally do not use the total authorized amount.

* CAL-Trans Standard Specifications 4-1.03B. Increases or decreases in the quantity of a contract item of work will be determined by comparing the total pay quantity of such item of work with the Engineer's Estimate. If the total pay quantity of any item of work required under the contract varies from the Engineer's Estimate by 25 percent or less, payment will be made for the quantity of work of said item performed at the contract unit price, unless eligible for adjustment pursuant to Section 4-1.03C, "Changes in Character of Work."

**SUBMITTAL TO THE BOARD OF SUPERVISORS COUNTY OF RIVERSIDE,
STATE OF CALIFORNIA**

This project was funded with \$208,501.19 of ATP funds.

Contract History and Price

Six bids were received on February 4, 2016, ranging from \$205,340 to \$320,710. The basis for the selection of a contractor is the lowest responsive and responsible bid. The lowest responsible bid was submitted by CT&T Concrete Paving, Inc. in the amount of \$205,340, which is \$20,935 (9.25%) below the Engineer's Estimate.

ATTACHMENTS:

Vicinity Map

Progress Estimate Report

Notice of Completion

COUNTY OF RIVERSIDE
DEPARTMENT OF TRANSPORTATION



SIDEWALK SAFETY PROJECT

AVENIDA RAMBLA
BUBBLING WELLS ELEMENTARY SCHOOL TO CAMINO AVENTURA
AND

CAMINO CAMPESINO
AVENIDA RAMBLA TO BUBBLING WELLS ROAD

IN THE DESERT HOT SPRINGS AREA

COUNTY PROJECT No. C5-0076
STATE PROJECT No. ATPL-5956 (245)

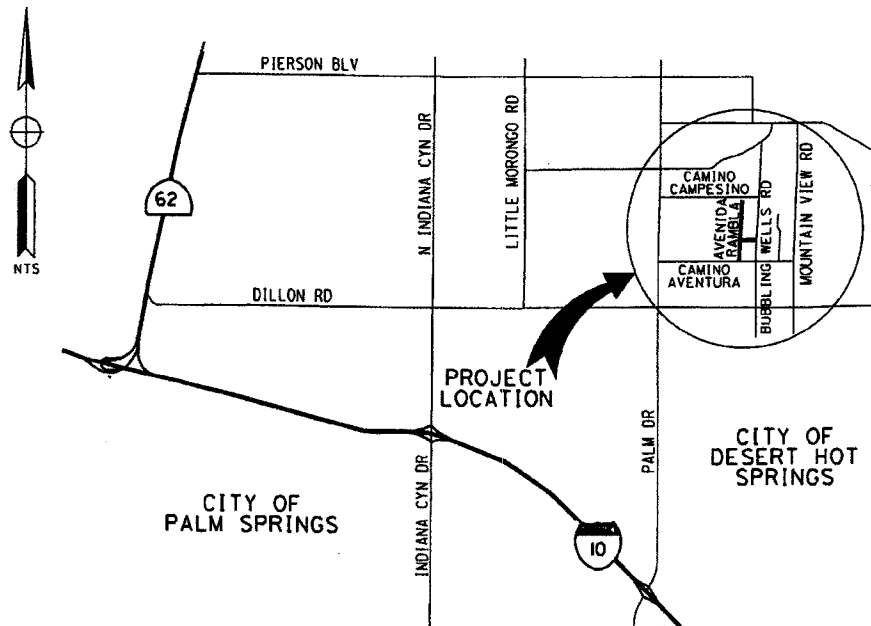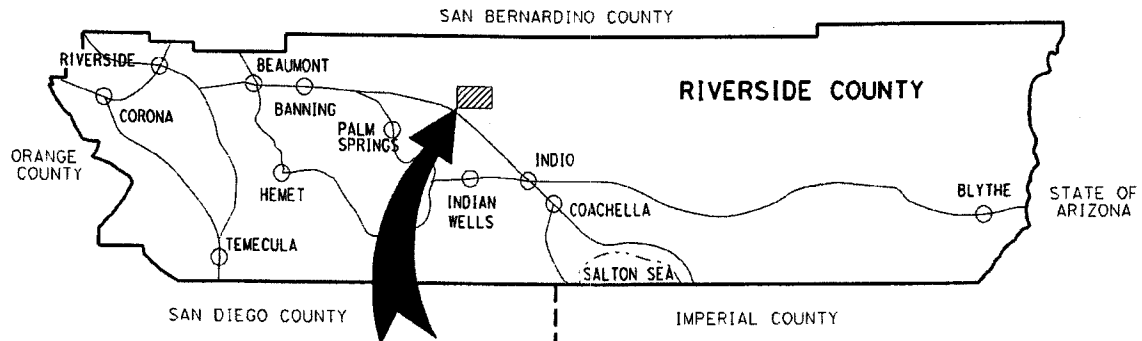

VICINITY MAP

TOWNSHIP 3S RANGE 5E SECTION 5
COUNTY ROAD BOOK PAGE No. 171

PROJECT: Avenida Ramba and Camino Campeano Sidewalk Safety Project
 County Project No.: CS-0076, State Project No. ATPL 5956(245)
 Contract No. 16-03-003

Contractor: CT & T Concrete Paving, Inc.
 Address: 324 S. Diamond Bar Blvd. BHP275
 City, State, Zip: Diamond Bar, CA 91765

Estimate No. 1 Final
 From: June 2, 2016
 To: July 25, 2016

Item No.	Item Description	Units	Quantity	Unit Price	Original Contract		Change Orders		Amended Contract		This Estimate		Previous		Total Estimate To Date		% Auth.
					Amount	Quantity	Amount	Quantity	Amount	Quantity	Amount	Quantity	Amount	Quantity	Amount	Quantity	
					205,340.00	0.00	0.00	205,340.00			208,501.19					208,501.19	
PROJECT TOTAL																	

Made by: Alec Yzaquirre
 Checked by: [Signature] 7/19/16
 OK Const. Supv: [Signature]

Working Days:
 Days Added: 0
 Subtotal: 40
 Days Used: 27
 % Time Elapsed: 68%

Start Date: 6-2-16
 End Date: 7-7-16
 % Complete: 102%
 Original Contract: \$205,340.00
 Amended Contract: \$205,340.00

TOTAL VALUE OF WORK TO DATE: \$208,501.19
 LESS RETENTION: 0%
 TOTAL DUE TO DATE: \$208,501.19
 LESS PREVIOUSLY INVOICED: 0.00
 LESS LABOR NON COMPLIANCE: 0.00
 TOTAL DUE THIS PAYMENT: \$208,501.19

This Estimate Approved [Signature] for: \$208,501.19
 Patricia Robyn, Director of Transportation

Date: 7/29/16

Quantities on This Estimate Approved [Signature] Date: 7-2-16
 CT & T Concrete Paving Inc.

PAYMENT APPROVAL

Fund 20000

Dept ID 31305

Account 527980

Project ZC5-0076E

Activity ID Z3600

Resource Type ENT

Signature [Signature]

Date 7/27/16

TRANSFISCAL APPROVED
 By: Crystal Potter 5-3461

AUG 01 2016

Norma Larson
 951-955-2783
 7-28-16

10-25-16
 MT 2123

PROJECT: Avenida Rambla and Camino Campeonino Sidewalk Safety Project
 County Project No. - CE-0076, State Project NO. ATPL 5996(246)
 Contract No. 16-03-003

Contractor: CT & T Concrete Paving, Inc.
 Address: 324 S. Diamond Bar Blvd. BHP275
 City, State, Zip: Diamond Bar, CA 91765

Estimate No. 1 Final
 From: June 2, 2016
 To: July 25, 2016



Item No.	Item Description	Units	Quantity	Unit Price	Original Contract Amount	Change Orders Quantity	Change Orders Amount	Amended Contract Quantity	Amended Contract Amount	This Estimate Quantity	This Estimate Amount	Previous Quantity	Total Estimate To Date Quantity	Total Estimate To Date Amount	% Auth.
1	DUST ABATEMENT	LS	1	3,500.00	3,500.00			1.00	3,500.00	1.00	3,500.00		1.00	3,500.00	100%
2	WATER POLLUTION CONTROL	LS	1	2,000.00	2,000.00			1.00	2,000.00	1.00	2,000.00		1.00	2,000.00	100%
3	TRAFFIC CONTROL SYSTEM	LS	1	3,700.00	3,700.00			1.00	3,700.00	1.00	3,700.00		1.00	3,700.00	100%
4	CLEARING AND GRUBBING	LS	1	11,000.00	11,000.00			1.00	11,000.00	1.00	11,000.00		1.00	11,000.00	100%
5	DEVELOP WATER SUPPLY	LS	1	2,800.00	2,800.00			1.00	2,800.00	1.00	2,800.00		1.00	2,800.00	100%
6	ROADWAY EXCAVATION	CY	10	150.00	1,500.00			10.00	1,500.00	11.50	1,725.00		11.50	1,725.00	115%
7	HOT MIX ASPHALT - TYPE A	TON	20	190.00	3,800.00			20.00	3,800.00	25.00	4,750.00		25.00	4,750.00	125%
8	RELOCATE CHAIN LINK FENCE/GATE	LF	175	60.00	10,500.00			175.00	10,500.00	178.00	10,680.00		178.00	10,680.00	102%
9	REMOVE AND REPLACE MAILBOX NEW	EA	28	300.00	8,400.00			28.00	8,400.00	28.00	8,400.00		28.00	8,400.00	100%
10	MINOR CONCRETE (TYPE "C" CURB) (CRS 202)	LF	100	30.00	3,000.00			100.00	3,000.00	100.00	3,000.00		100.00	3,000.00	100%
11	MINOR CONCRETE (CURB TRANSITION) (CRS 211)	LF	60	30.00	1,800.00			60.00	1,800.00	75.00	2,250.00		75.00	2,250.00	125%
12	MINOR CONCRETE (CURB RAMP) (CRS 403)	EA	7	2,400.00	16,800.00			7.00	16,800.00	7.00	16,800.00		7.00	16,800.00	100%
13	MINOR CONCRETE (SIDEWALK)	SQFT	16,200	4.45	72,090.00			16,200.00	72,090.00	16,584.00	73,798.80		16,584.00	73,798.80	102%
14	MINOR CONCRETE (DRIVEWAY)	SQFT	6,400	6.30	40,320.00			6,400.00	40,320.00	6,528.00	41,126.40		6,528.00	41,126.40	102%
15	REMOVE TREE	EA	24	495.00	11,880.00			24.00	11,880.00	24.00	11,880.00		24.00	11,880.00	100%
16	REMOVE AND SALVAGE ROADSIDE SIGNS	EA	7	100.00	700.00			7.00	700.00	7.00	700.00		7.00	700.00	100%
17	ROADSIDE SIGN - ONE POST	EA	7	150.00	1,050.00			7.00	1,050.00	7.00	1,050.00		7.00	1,050.00	100%
18	MISCELLANEOUS WORK (AS DIRECTED)	FA	1	5,000.00	5,000.00			1.00	5,000.00	0.768198	3,840.99		0.768198	3,840.99	77%
19	DE-MOBILIZATION	LS	1	5,500.00	5,500.00			1.00	5,500.00	1.00	5,500.00		1.00	5,500.00	100%

PLEASE COMPLETE THIS INFORMATION
RECORDING REQUESTED BY:

KECIA HARPER-IHEM, CLERK OF THE BOARD
RIVERSIDE CO. CLERK OF THE BOARD
4080 LEMON STREET, 1ST FLOOR CAC
P O BOX 1147 - RIVERSIDE, CA 92502

MAIL STOP # 1010

AND WHEN RECORDED MAIL TO:

RETURN TO: STOP #1010
RIVERSIDE COUNTY CLERK OF THE BOARD
P. O. BOX 1147 - RIVERSIDE, CA 92502

2016-0487561

11/03/2016 10:44 AM

Customer Copy Label

The paper to which this label is affixed
has not been compared with the
filed/recorded document

Peter Aldana
County Of Riverside
Assessor-County Clerk-Recorder

THIS SPACE FOR RECORDERS USE ONLY

NOTICE OF COMPLETION

To be recorded with County Recorder
within 10 days after completion.
No recording fee.

Notice is hereby given by the undersigned owner, a public entity of the State of California, that a public work of
improvement has been completed, as follows:

Project title or description of work: Avenida Rambla and Camino Campesino Sidewalk Safety Project

Date of Completion: Date of this notice 10/25/16

Nature of owner: County of Riverside, public entity

Interest or estate of owner: Public Roadway

Address of owner: 4080 Lemon Street, 8th Floor, Riverside, CA 92501

Name of contractor: CT&T Concrete Paving, Inc.

Street or legal description of site: Avenida Rambla and Camino Campesino

Dated: October 25, 2016

Owner: County of Riverside
(Name of Public Entity)

By: John J. Benoit
Chairman, Board of Supervisors
John J. Benoit

STATE OF CALIFORNIA)

ss

COUNTY OF RIVERSIDE)

I am the Chairman of the governing board of the County of Riverside, the public entity which executed the
foregoing notice and on whose behalf I make this verification; I have read this notice, know its contents, and the same is
true. I certify under penalty of perjury that the foregoing is true and correct.

Executed at Riverside, California on 10/25/16 (Date)

John J. Benoit, Chairman of the Board of Supervisors
John J. Benoit

COPY

ATTEST:

KECIA HARPER-IHEM, Clerk

By: Kecia Harper-Ihem
DEPUTY

10.25.16 3-43

FORM APPROVED COUNTY COUNSEL

BY: Paola R. Victor 9/26/16
MARSHAL VICTOR DATE



PETER ALDANA
COUNTY OF RIVERSIDE
ASSESSOR-COUNTY CLERK-RECORDER

Recorder
P.O. Box 751
Riverside, CA 92502-0751
(951) 486-7000


www.riversideacr.com

CERTIFICATION

Pursuant to the provisions of Government Code 27361.7, I certify under the penalty of perjury that the following is a true copy of illegible wording found in the attached document:

(Print or type the page number(s) and wording below):

CLARIFICATION OF THE SEAL for the Riverside County Board of Supervisors
(embossed on document)



Date:

10-25-16

Signature:

Print Name:

Karen Barton, Board Assistant, Riverside County Clerk of the Board
