

**SUBMITTAL TO THE BOARD OF SUPERVISORS
COUNTY OF RIVERSIDE, STATE OF CALIFORNIA**



ITEM
3.57
(ID # 4469)

MEETING DATE:

Tuesday, July 25, 2017

FROM : TLMA-TRANSPORTATION:

SUBJECT: TRANSPORTATION AND LAND MANAGEMENT AGENCY/ TRANSPORTATION:

Notice of Completion – Emergency Storm Damage Repair Work, Mockingbird Canyon Road, Box Culvert South of Van Buren Boulevard, in the Community of Woodcrest. California Environmental Quality Act (CEQA) Exempt. 1st District. [\$282,580]; Local Funds 100%

RECOMMENDED MOTION: That the Board of Supervisors:

1. Accept Emergency Storm Damage Repair Work, Mockingbird Canyon Road, Box Culvert South of Van Buren Boulevard as completed; and
2. Authorize the Chairman of the Board to execute the Notice of Completion and the Clerk of the Board to record the Notice.


ACTION: Policy

MINUTES OF THE BOARD OF SUPERVISORS

On motion of Supervisor Jeffries, seconded by Supervisor Tavaglione and duly carried by unanimous vote, IT WAS ORDERED that the above matter is approved as recommended.

Ayes: Jeffries, Tavaglione, Washington, Perez and Ashley
Nays: None
Absent: None
Date: July 25, 2017
xc: Transp., Recorder

Kecia Harper-Ihem
Clerk of the Board

By: 
Deputy

**SUBMITTAL TO THE BOARD OF SUPERVISORS COUNTY OF RIVERSIDE,
STATE OF CALIFORNIA**

FINANCIAL DATA	Current Fiscal Year:	Next Fiscal Year:	Total Cost:	Ongoing Cost
COST	\$ 282,580	\$ 0	\$ 282,580	\$ 0
NET COUNTY COST	\$ 0	\$ 0	\$ 0	\$ 0
SOURCE OF FUNDS: Gax Tax (100%) There are no general funds used in this project.			Budget Adjustment:	N/A
			For Fiscal Year:	17/18

C.E.O. RECOMMENDATION: Approve

BACKGROUND:

Summary

On May 2, 2017, by Minute Order 3-34, the Board of Supervisors entered into a contract with Riverside Construction Company, Inc. of Riverside, CA for the Emergency Storm Damage Repair Work on the Mockingbird Canyon Road Box Culvert located south of Van Buren Boulevard, Woodcrest area. The originally authorized amount of the contract was \$350,000. The total amended contract is \$282,580 which is 19.3% less than the originally authorized amount. Due to the nature of the damage, the actual extent of erosion beneath the existing box culvert could not be fully determined at the time of award and the amount of material required to make the repairs was less than originally anticipated.

This work was completed at the direction of the County of Riverside Transportation Department (Transportation Department) on March 30, 2017, and was inspected by the Construction Engineering Section of the Transportation Department. Work Order Number 45-171101.

County Counsel has approved the Notice of Completion as to legal form.

Impact on Residents and Businesses

During initial stages of the emergency work, traffic control was utilized along with flagmen to keep the bridge open to public traffic. When no repair operations were taking place, the road was open to public traffic with the exception of large trucks.

SUPPLEMENTAL

Additional Fiscal Information

**SUBMITTAL TO THE BOARD OF SUPERVISORS COUNTY OF RIVERSIDE,
STATE OF CALIFORNIA**

Budget

Original Contract Amount		\$350,000
Total Change Orders Authorized	0.0%	\$0
Estimated Pending Change Orders	0.0%	\$0
Authorized Contract Amount		\$350,000
* Quantity Adjustments	-19.3%	(\$67,420)
+ CCO FA Adjustments	0.0%	\$0
Total Amended Contract Amount	80.7%	\$282,580

Expenditures

Total Progress Payments	\$282,580
Estimated Pending Payments	\$0
Total Expenditures	\$282,580

(Over)/Under Contract Amount \$0

+ Change Orders using the Force Account method of payment issued prior to the work being completed generally do not use the total authorized amount.

* CAL-Trans Standard Specifications 4-1.03B. Increases or decreases in the quantity of a contract item of work will be determined by comparing the total pay quantity of such item of work with the Engineer's Estimate. If the total pay quantity of any item of work required under the contract varies from the Engineer's Estimate by 25 percent or less, payment will be made for the quantity of work of said item performed at the contract unit price, unless eligible for adjustment pursuant to Section 4-1.03C, "Changes in Character of Work."

This project was funded with \$282,580 of Gas Tax funds.


Contract History and Price Reasonableness

N/A

ATTACHMENTS:

Vicinity Map
Progress Estimate Report
Notice of Completion


SUBMITTAL TO THE BOARD OF SUPERVISORS COUNTY OF RIVERSIDE,
STATE OF CALIFORNIA


Patricia Romo, Director of Transportation 6/27/2017


Marsha Victor, Chief Deputy County Counsel 6/28/2017


Gregory P. Priamos, Director County Counsel 6/28/2017



Tina Grande, Principal Management Analyst 7/17/2017


Gregory P. Priamos, Director County Counsel 6/28/2017

**County of Riverside
Transportation Department**

**Emergency Storm Damage Repair Work
Mockingbird Canyon Road
Box Culvert South of Van Buren Boulevard
Community of Woodcrest
Project No. 45-171101**

Vicinity Map

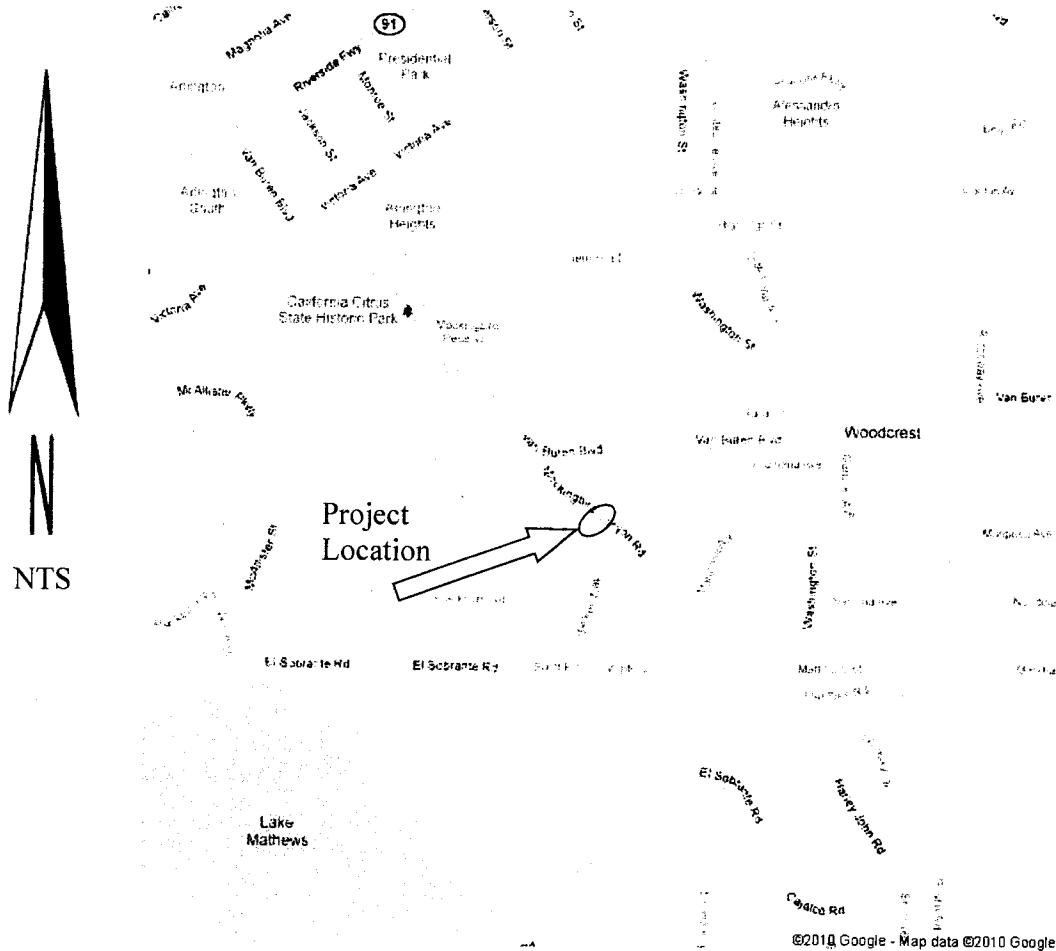

Township 3S Range 5W Section 27
County Road Book page No. 26

PROJECT: Mockingbird Canyon Emergency Storm Damage Repairs

County Project No.: 45-171101

Contract No. 17-03-002

Contractor: Riverside Construction Company, Inc.

Address: 4225 Garner Road

City, State, Zip: Riverside, CA 92502



Estimate No. 1 Final
From: March 15, 2017
To: March 30, 2017

Item No.	Item Description	Units	Quantity	Unit Price	Original Contract Amount	Change Authorized Quantity	Change Authorized Amount	Total Authorized Quantity	Total Authorized Amount	This Estimate Quantity	This Estimate Amount	Previous Quantity	Total Estimate To Date Quantity	Total Estimate To Date Amount	% Auth.
1	Emergency Culvert Repairs	FA	350,000	1.00	350,000.00			350,000.00	350,000.00	282,580.22	282,580.22		282,580.22	282,580.22	81%
PROJECT TOTAL					350,000.00		0.00		350,000.00		282,580.22			282,580.22	

Made by: Trai Nguyen

Checked by: MS 4-27-17OK Const. Supv. MS 4/27/17

Working Days: 10

Days Added: 0

Subtotal: 10

Days Used: 9

% Time Elapsed: 90%

Start Date: 3-15-17

End Date: 3-30-17

% \$ Complete: 81%

Original Contract: \$350,000.00

Amended Contract: \$350,000.00

TOTAL VALUE OF WORK TO DATE: \$282,580.22

LESS RETENTION: 0% 0.00

TOTAL DUE TO DATE: \$282,580.22

LESS PREVIOUSLY INVOICED:

LESS LABOR NON COMPLIANCE: 0.00

TOTAL DUE THIS PAYMENT: \$282,580.22

This Estimate Approved _____ Date: _____ for: \$282,580.22
Patricia Romo, Director of Transportation

Quantities on This Estimate Approved [Signature] Date: 5/18/17
Riverside Construction Company, Inc.
JASON MOORE

PAYMENT APPROVAL

Fund 20000

Received by Accounts Payable: _____

By: _____

Dept ID 31305Account 527980Project 245-171101EActivity ID 23500Resource Type CNTSignature [Signature]Date 5/19/17

PLEASE COMPLETE THIS INFORMATION
RECORDING REQUESTED BY:

KECIA HARPER-IHEM, CLERK OF THE BOARD
RIVERSIDE CO. CLERK OF THE BOARD
4080 LEMON STREET, 1ST FLOOR CAC
P O BOX 1147 - RIVERSIDE, CA 92502

MAIL STOP # 1010

AND WHEN RECORDED MAIL TO:

RETURN TO: STOP #1010
RIVERSIDE COUNTY CLERK OF THE BOARD
P. O. BOX 1147 - RIVERSIDE, CA 92502

2017-0309528

07/28/2017 12:04 PM Fee: \$ 0.00

Page 1 of 2

Recorded in Official Records
County of Riverside
Peter Aldana
Assessor-County Clerk-Recorder



126					R	A	Exam:	380	
Page	DA	PCOR	Misc	Long	RFD	1st Pg	Adtl Pg	Cert	CC
2	1								
SIZE	NCOR	SMF	NCHG	T:	NCLGcc				

NOTICE OF COMPLETION

To be recorded with County Recorder
within 10 days after completion.
No recording fee.

Notice is hereby given by the undersigned owner, a public entity of the State of California, that a public work of improvement has been completed, as follows:

Project title or description of work: Emergency Storm Damage Repair Work

Date of Completion: Date of this notice 07/25/17

Nature of owner: County of Riverside, public entity

Interest or estate of owner: Public Roadway

Address of owner: 4080 Lemon Street, 8th Floor, Riverside, CA 92501

Name of contractor: Riverside Construction Company, Inc.

Street or legal description of site: Mockingbird Canyon Road, Box Culvert South of Van Buren Boulevard and Greenview Drive, Woodcrest, Project No. 45-171101, Township 3S Range 5W Section 27, County Road Book Page No. 26

Dated: July 25, 2017

Owner: County of Riverside
(Name of Public Entity)

By:
Chairman, Board of Supervisors
John Tavaglione

STATE OF CALIFORNIA)

COUNTY OF RIVERSIDE)

ss

I am the Chairman of the governing board of the County of Riverside, the public entity which executed the foregoing notice and on whose behalf I make this verification; I have read this notice, know its contents, and the same is true. I certify under penalty of perjury that the foregoing is true and correct.

Executed at Riverside, California on 07/25/17 (Date)

Chairman of the Board of Supervisors

John Tavaglione

07.25.17 3.57

FORM APPROVED COUNTY COUNSEL

BY: Yousha R. Victor 6/28/17
MARSHAL VICTOR DATE

2017-8-136587

ATTEST:
KECIA HARPER-IHEM, Clerk
By:
DEPUTY



PETER ALDANA
COUNTY OF RIVERSIDE
ASSESSOR-COUNTY CLERK-RECORDER


Recorder
P.O. Box 751
Riverside, CA 92502-0751
(951) 486-7000
www.riversideacr.com

CERTIFICATION

Pursuant to the provisions of Government Code 27361.7, I certify under the penalty of perjury that the following is a true copy of illegible wording found in the attached document:

(Print or type the page number(s) and wording below):

CLARIFICATION OF THE SEAL for the Riverside County Board of Supervisors
(embossed on document)



Date:

7-25-17

Signature:

Karen Barton

Print Name:

Karen Barton, Board Assistant, Riverside County Clerk of the Board
