

**SUBMITTAL TO THE BOARD OF SUPERVISORS
COUNTY OF RIVERSIDE, STATE OF CALIFORNIA**



ITEM
3.23
(ID # 5100)

MEETING DATE:

Tuesday, October 17, 2017


FROM : TLMA-TRANSPORTATION:

SUBJECT: TRANSPORTATION AND LAND MANAGEMENT AGENCY/ TRANSPORTATION:
Notice of Completion – Van Buren Boulevard Pavement Rehabilitation Project
between Limonite Avenue and 56th Street Within the City of Jurupa Valley. 2nd
District. [487,906]; Federal Funds 72%, Local Funds 28%

RECOMMENDED MOTION: That the Board of Supervisors:

1. Accept Van Buren Boulevard Pavement Rehabilitation Project between Limonite Avenue and 56th Street Within the City of Jurupa Valley; and
2. Authorize the Chairman of the board to execute the Notice of Completion and the Clerk of the Board to record the Notice.

ACTION: Policy



Patricia Romo, Director of Transportation 10/8/2017

MINUTES OF THE BOARD OF SUPERVISORS

On motion of Supervisor Jeffries, seconded by Supervisor Washington and duly carried by unanimous vote, IT WAS ORDERED that the above matter is approved as recommended.

Ayes: Jeffries, Tavaglione, Washington, Perez and Ashley
Nays: None
Absent: None
Date: October 17, 2017
xc: Transp. , Recorder

Kecia Harper-Ihem
Clerk of the Board

By: 
Deputy

**SUBMITTAL TO THE BOARD OF SUPERVISORS COUNTY OF RIVERSIDE,
STATE OF CALIFORNIA**

FINANCIAL DATA	Current Fiscal Year:	Next Fiscal Year:	Total Cost:	Ongoing Cost
COST	\$ 487,906	\$ 0	\$ 487,906	\$ 0
NET COUNTY COST	\$ 0	\$ 0	\$ 0	\$ 0
SOURCE OF FUNDS: STP-Discretionary (72%), City of Jurupa Valley (28%) There are no General funds used in this Project.			Budget Adjustment: N/A	
			For Fiscal Year: 17/18	

C.E.O. RECOMMENDATION: Approve

BACKGROUND:

Summary

The originally authorized amount of the contract was \$535,065. The total amended contract is \$487,906 which is 8.8% less than the originally authorized amount. The decrease in the total contract price was the result of using less asphalt concrete required to perform the paving operations. The estimated quantity required to complete the work was less than the Engineer's Estimate due to a varying roadway width between the project limits.

The work was completed in conformance with the plans and specifications and the contractor was granted relief of maintenance on May 25, 2017. Work Order Number C6-0087, Federal Aid No. STPL-5956(255).

Impact on Residents and Businesses

The improvements have significantly improved the service life of the existing infrastructure.

SUPPLEMENTAL:

Additional Fiscal Information

Budget

Original Contract Amount		\$535,065
Total Change Orders Authorized	0.0%	\$0
Estimated Pending Change Orders	0.0%	\$0
Authorized Contract Amount		\$535,065
* Quantity Adjustments	-8.8%	(\$47,159)
+ CCO FA Adjustments	0.0%	\$0
Total Amended Contract Amount	91.2%	\$487,906

Expenditures

Total Progress Payments	\$487,906
Estimated Pending Payments	\$0
Total Expenditures	\$487,906

(Over)/Under Contract Amount \$0

+ Change Orders using the Force Account method of payment issued prior to the work being completed generally do not use the total authorized amount.

**SUBMITTAL TO THE BOARD OF SUPERVISORS COUNTY OF RIVERSIDE,
STATE OF CALIFORNIA**

* CAL-Trans Standard Specifications 4-1.03B. Increases or decreases in the quantity of a contract item of work will be determined by comparing the total pay quantity of such item of work with the Engineer's Estimate. If the total pay quantity of any item of work required under the contract varies from the Engineer's Estimate by 25 percent or less, payment will be made for the quantity of work of said item performed at the contract unit price, unless eligible for adjustment pursuant to Section 4-1.03C, "Changes in Character of Work."

This project was funded with \$351,292 of STP Discretionary Funds and \$136,614 of City of Jurupa Valley Funds.

Contract History and Price Reasonableness

Five bids were received on January 18, 2017 ranging from \$535,065 to \$686,686. The basis for the selection of a contractor is the lowest responsive and responsible bid. The lowest responsible bid was submitted by All American Asphalt in the amount of \$535,065, which is \$205,035 (27.7%) below the Engineer's Estimate.

ATTACHMENTS


Vicinity Map
Progress Estimate Report
Notice of Completion


Patricia Romo, Director of Transportation 9/8/2017


Marsha Victor, Chief Deputy County Counsel 9/25/2017


Gregory B. Priamos, Director County Counsel 9/25/2017


Tina Grande, Principal Management Analyst 10/8/2017


Gregory B. Priamos, Director County Counsel 9/25/2017

PLEASE COMPLETE THIS INFORMATION
RECORDING REQUESTED BY:

KECIA HARPER-IHEM, CLERK OF THE BOARD
RIVERSIDE CO. CLERK OF THE BOARD
4080 LEMON STREET, 1ST FLOOR CAC
P O BOX 1147 – RIVERSIDE, CA 92502

MAIL STOP # 1010

AND WHEN RECORDED MAIL TO:

RETURN TO: STOP #1010
RIVERSIDE COUNTY CLERK OF THE BOARD
P. O. BOX 1147 – RIVERSIDE, CA 92502

2017-0438993

10/23/2017 11:13 AM Fee: \$ 0.00

Page 1 of 3

Recorded in Official Records
County of Riverside
Peter Aldana
Assessor-County Clerk-Recorder



782

THIS SPACE FOR RECORDERS USE ONLY

NOTICE OF COMPLETION

To be recorded with County Recorder
within 10 days after completion.
No recording fee.

Notice is hereby given by the undersigned owner, a public entity of the State of California, that a public work of improvement has been completed, as follows:

Project title or description of work: Van Buren Boulevard Pavement Rehabilitation Phase 1A

Date of Completion: Date of this notice 10/17/17

Nature of owner: County of Riverside, public entity

Interest or estate of owner: Public Roadway

Address of owner: 4080 Lemon Street, 8th Floor, Riverside, CA 92501

Name of contractor: All American Asphalt

Street or legal description of site: Van Buren Boulevard, Limonite Avenue to 56th Street, City of Jurupa Valley, Project Number C6-0087, STPL-5956(255)

Dated: October 17, 2017

Owner: County of Riverside
(Name of Public Entity)

By: [Signature]
Chairman, Board of Supervisors
John Tavaglione

STATE OF CALIFORNIA)

ss

COUNTY OF RIVERSIDE)

I am the Chairman of the governing board of the County of Riverside, the public entity which executed the foregoing notice and on whose behalf I make this verification; I have read this notice, know its contents, and the same is true. I certify under penalty of perjury that the foregoing is true and correct.

Executed at Riverside, California on 10/17/17 (Date)

[Signature], Chairman of the Board of Supervisors
John Tavaglione

ATTEST:


KECIA HARPER-IHEM, Clerk

By: [Signature]
DEPUTY

10.17.17 3.23

FORM APPROVED COUNTY COUNSEL

BY: [Signature] 9/26/17
MARSHAL L. VICTOR DATE



PETER ALDANA
COUNTY OF RIVERSIDE
ASSESSOR-COUNTY CLERK-RECORDER

Recorder
P.O. Box 751
Riverside, CA 92502-0751
(951) 486-7000


www.riversideacr.com

CERTIFICATION

Pursuant to the provisions of Government Code 27361.7, I certify under the penalty of perjury that the following is a true copy of illegible wording found in the attached document:

(Print or type the page number(s) and wording below):

CLARIFICATION OF THE SEAL for the Riverside County Board of Supervisors
(embossed on document)



Date:

10-17-17

Signature:

Karen Barton



Print Name:

Karen Barton, Board Assistant, Riverside County Clerk of the Board

COUNTY OF RIVERSIDE
TRANSPORTATION DEPARTMENT

VAN BUREN BOULEVARD
PAVEMENT REHABILITATION PHASE 1A

LIMONITE AVENUE To 56TH STREET
CITY OF JURUPA VALLEY
PROJECT No. C6-0087
FEDERAL AID No. STPL 5956(255)

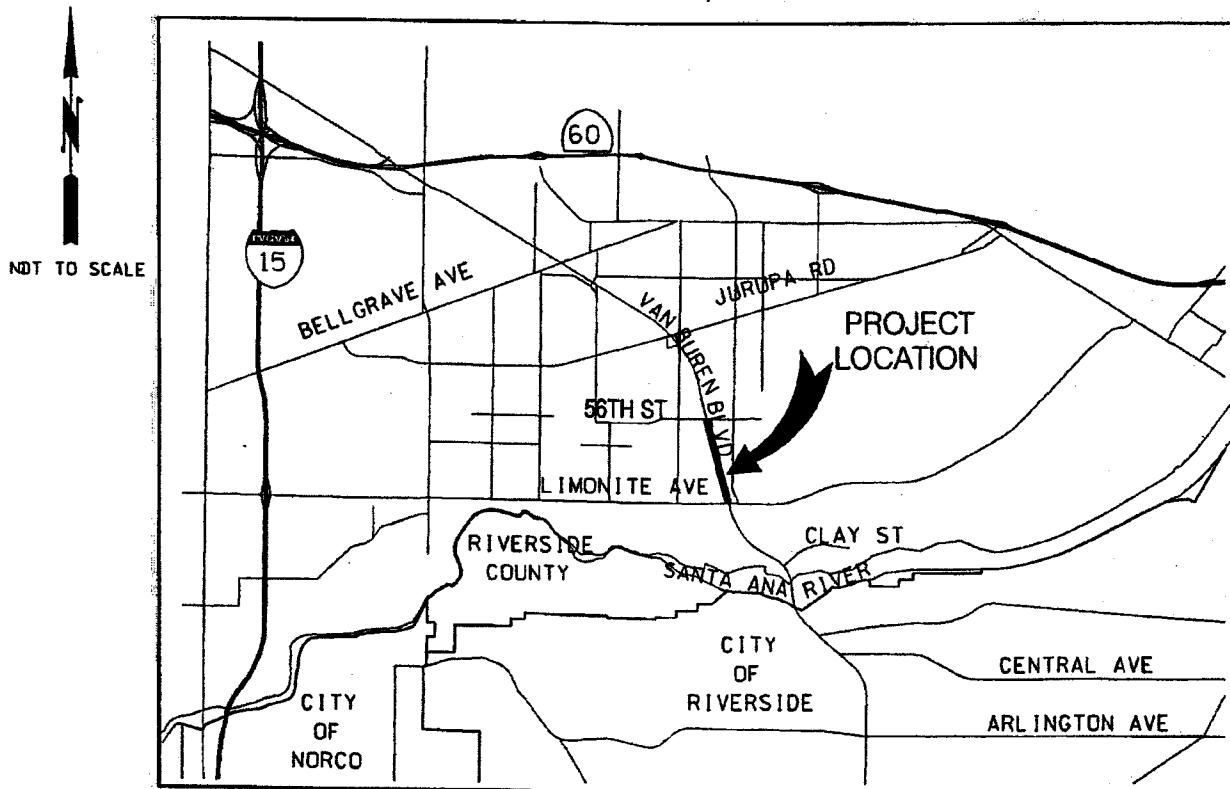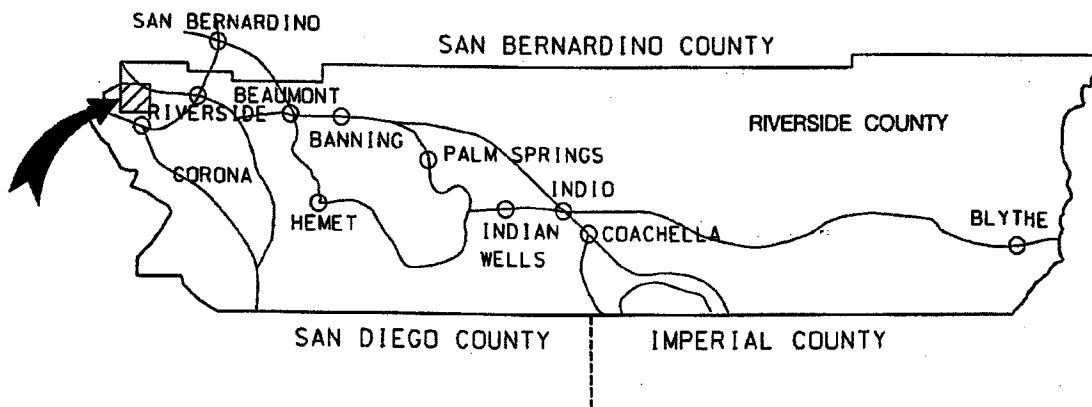

VICINITY MAP

PROGRESS ESTIMATE RECORD - COUNTY OF RIVERSIDE

PROJECT: Van Buren Blvd. Pavement Rehabilitation Phase 1A, Limonite Ave. to 56th St.

County Project No.: CE-0087, STPL-6966 (255)

Contract No. 17-03-003

SHEET 1 of 2

Processed Construction Inspection 7/11/2017



Contractor: All American Asphalt
Address: 400 E. Sixth Street
City, State, Zip: Corona, CA 92879

Item No.	Item Description	Units	Quantity	Unit Price	Original Contract		Change Orders		Amended Contract		This Estimate		Previous Quantity		Total Estimate To Date		% Auth.
					Amount	Quantity	Amount	Quantity	Quantity	Amount	Quantity	Amount	Quantity	Amount	Quantity	Amount	
1	DUST ABATEMENT	LS	1	1,545.50	1,545.50	1.00			1.00	1,545.50			1.00		1.00	1,545.50	100%
2	WATER POLLUTION CONTROL	LS	1	3,901.00	3,901.00	1.00			1.00	3,901.00			1.00		1.00	3,901.00	100%
3	TRAFFIC CONTROL SYSTEM	LS	1	24,000.00	24,000.00	1.00			1.00	24,000.00			1.00		1.00	24,000.00	100%
4	DEVELOP WATER SUPPLY	LS	1	515.00	515.00	1.00			1.00	515.00			1.00		1.00	515.00	100%
5	CLEARING AND GRUBBING	LS	1	1,236.50	1,236.50	1.00			1.00	1,236.50			1.00		1.00	1,236.50	100%
6	PROJECT FUNDING IDENTIFICATION SIGN	EA	2	1,030.50	2,061.00	2.00			2.00	2,061.00			2.00		2.00	2,061.00	100%
7	PORTABLE CHANGEABLE MESSAGE SIGNS	EA	4	1,236.50	4,946.00	4.00			4.00	4,946.00			4.00		4.00	4,946.00	100%
8	COLD PLANE ASPHALT PAVEMENT (2" MIN DEPTH)	SQYD	16,400	0.67	10,988.00	16,400.00			16,400.00	10,988.00			15,922.51		15,922.51	10,668.08	97%
9	COLD PLANE ASPHALT PAVEMENT (4" MIN DEPTH)	SQYD	17,300	1.63	28,199.00	17,300.00			17,300.00	28,199.00			16,392.00		16,392.00	26,718.96	95%
10	HOT MIX ASPHALT	TON	2,000	66.00	132,000.00	2,000.00			2,000.00	132,000.00			1,849.31		1,849.31	122,054.46	92%
11	RUBBERIZED HOT MIX ASPHALT (GAP GRADED)	TON	3,900	72.50	282,750.00	3,900.00			3,900.00	282,750.00			3,395.65		3,395.65	246,184.63	87%
12	PLACE HOT MIX ASPHALT DIKE (TYPE A)	LF	2,600	2.50	6,500.00	2,600.00			2,600.00	6,500.00			2,782.00		2,782.00	6,955.00	107%
13	SHOULDER BACKING	LF	4,500	1.13	5,085.00	4,500.00			4,500.00	5,085.00			4,633.00		4,633.00	5,235.29	103%
14	THERMOPLASTIC PAVEMENT MARKING	SQFT	100	7.00	700.00	100.00			100.00	700.00			75.00		75.00	525.00	75%
15	PAINT TRAFFIC STRIPE (2-COAT)	LF	25,000	0.16	4,000.00	25,000.00			25,000.00	4,000.00			27,169.00		27,169.00	4,347.04	109%
16	PAVEMENT MARKER (REFLECTIVE)	EA	300	5.00	1,500.00	300.00			300.00	1,500.00			375.00		375.00	1,875.00	125%
17	MOBILIZATION, DEMOBILIZATION, AND FINAL CLEAN	LS	1	25,138.00	25,138.00	1.00			1.00	25,138.00	0.50	12,569.00	0.50		1.00	25,138.00	100%

PROGRESS ESTIMATE RECORD - COUNTY OF RIVERSIDE

PROJECT: Van Buren Blvd. Pavement Rehabilitation Phase 1A, Limonte Ave. to 56th St.
County Project No.: CE-0087, STPL-5955 (255)
Contract No. 17-03-003

Contractor: All American Asphalt
Address: 400 E. Sixth Street
City, State, Zip: Corona, CA 92879

SHEET 2 of 2

Processed Construction Inspection 7/17/2017



Estimate No.

2 Final

From: May 26, 2017
To: June 25, 2017

Item No.	Item Description	Units	Quantity	Unit Price	Original Contract Amount	Change Orders Quantity	Change Orders Amount	Amended Contract Quantity	Amended Contract Amount	This Estimate Quantity	This Estimate Amount	Previous Quantity	Total Estimate To Date Quantity	Total Estimate To Date Amount	% Auth
					535,065.00		0.00		535,065.00		12,569.00			487,906.46	
PROJECT TOTAL															

Made by: Trai Nguyen

Checked by: *[Signature]* 7-11-17
OK Const. Supv. *[Signature]* 7-11-17

Working Days: 20
Days Added: 0
Subtotal: 20
Days Used: 10
% Time Elapsed: 50%

Start Date: 5-15-17
End Date: 5-25-17
% \$ Complete: 91%
Original Contract: \$535,065.00
Amended Contract: \$535,065.00

TOTAL VALUE OF WORK TO DATE: \$487,906.46
LESS RETENTION: 0%
TOTAL DUE TO DATE: \$487,906.46
LESS PREVIOUSLY INVOICED: 475,337.46
LESS LABOR NON COMPLIANCE: 0.00
TOTAL DUE THIS PAYMENT: \$12,569.00

This Estimate Approved _____ Date: _____ for: _____

Patricia Romo, Director of Transportation

Received by Accounts Payable: _____
By: _____

PAYMENT APPROVAL

Fund 20000

Dept ID 31305

Account 527480

Project 2006-0087E

Activity ID 23500

Resource Type CNT

Signature *[Signature]*

Date 7/20/17

7/26/17

Quantities on This Estimate Approved _____ Date: _____

All American Asphalt
