

SUBMITTAL TO THE BOARD OF SUPERVISORS
COUNTY OF RIVERSIDE, STATE OF CALIFORNIA



ITEM
3.26
(ID # 8087)

MEETING DATE:

Tuesday, October 16, 2018

FROM : TLMA-TRANSPORTATION:

SUBJECT: TRANSPORTATION AND LAND MANAGEMENT AGENCY/TRANSPORTATION:

Notice of Completion – Thousand Palms Canyon Road Widening, Turning Lane
and Resurfacing Project in the Community of Thousand Palms. 4th District. [\$0]

RECOMMENDED MOTION: That the Board of Supervisors:


1. Accept Thousand Palms Canyon Road Widening, Turning Lane and Resurfacing Project as completed; and
2. Authorize the Chairman of the board to execute the Notice of Completion and the Clerk of the Board to record the Notice.

ACTION: Policy

MINUTES OF THE BOARD OF SUPERVISORS

On motion of Supervisor Perez, seconded by Supervisor Ashley and duly carried by unanimous vote, IT WAS ORDERED that the above matter is approved as recommended.

Ayes: Jeffries, Tavaglione, Washington, Perez and Ashley
Nays: None
Absent: None
Date: October 16, 2018
xc: Transp., Recorder

Kecia Harper-Ihem
Clerk of the Board
By: 
Deputy

3.26

**SUBMITTAL TO THE BOARD OF SUPERVISORS COUNTY OF RIVERSIDE,
STATE OF CALIFORNIA**

| FINANCIAL DATA | Current Fiscal Year: | Next Fiscal Year: | Total Cost: | Ongoing Cost |
|-----------------------------|-----------------------------|--------------------------|---------------------------|---------------------|
| COST | \$ 0 | \$ 0 | \$ 0 | \$ 0 |
| NET COUNTY COST | \$ 0 | \$ 0 | \$ 0 | \$ 0 |
| SOURCE OF FUNDS: N/A | | | Budget Adjustment: | N/A |
| | | | For Fiscal Year: | 18/19 |

C.E.O. RECOMMENDATION: Approve

BACKGROUND:

Summary

By Minute Order 3-25 of May 1, 2018, the Board of Supervisors entered into a contract with Granite Construction Company of Indio, CA for the construction of Thousand Palms Canyon Road Widening, Turning Lane and Resurfacing Project in the Community of Thousand Palms.

The originally authorized amount of the contract was \$605,506. The total amended contract is \$527,529 which is 12.9% less than the originally authorized amount. The reduction in the total contract price was primarily the result of using less asphalt concrete required to reconstruct the pavement surface.

The work was completed in conformance with the plans and specifications and the contractor was granted relief of maintenance on June 21, 2018. Work Order Number C3-0087, Federal Aid No. HRRRL-5956(219).

Impact on Residents and Businesses

This project has improved traffic safety for travelers through this corridor.

Additional Fiscal Information

Budget

| | | |
|---------------------------------|--------|------------|
| Original Contract Amount | | \$605,506 |
| Total Change Orders Authorized | 0.0% | \$0 |
| Estimated Pending Change Orders | 0.0% | \$0 |
| Authorized Contract Amount | | \$605,506 |
| * Quantity Adjustments | -12.9% | (\$77,977) |
| + CCO FA Adjustments | 0.0% | \$0 |
| Total Amended Contract Amount | 87.1% | \$527,529 |

Expenditures

| | |
|----------------------------|-----------|
| Total Progress Payments | \$527,529 |
| Estimated Pending Payments | \$0 |
| Total Expenditures | \$527,529 |

| | |
|-------------------------------------|------------|
| (Over)/Under Contract Amount | \$0 |
|-------------------------------------|------------|

**SUBMITTAL TO THE BOARD OF SUPERVISORS COUNTY OF RIVERSIDE,
STATE OF CALIFORNIA**

+ Change Orders using the Force Account method of payment issued prior to the work being completed generally do not use the total authorized amount.

* CAL-Trans Standard Specifications 4-1.03B. Increases or decreases in the quantity of a contract item of work will be determined by comparing the total pay quantity of such item of work with the Engineer's Estimate. If the total pay quantity of any item of work required under the contract varies from the Engineer's Estimate by 25 percent or less, payment will be made for the quantity of work of said item performed at the contract unit price, unless eligible for adjustment pursuant to Section 4-1.03C, "Changes in Character of Work."


This project was funded with \$94,955 of Gas Tax/HUTA funds and \$432,574 of Highway Safety Improvement Program funds.

Contract History and Price Reasonableness

Four bids were received ranging from \$605,506 to \$888,000. The basis for the selection of a contractor is the lowest responsive and responsible bid. The lowest responsible bid was submitted by Granite Construction Company in the amount of \$605,506, which was \$59,164 (9%) lower than the Engineer's Estimate.

ATTACHMENTS:

Vicinity Map
Progress Estimate Report
Notice of Completion



Patricia Romo, Director of Transportation

10/2/2018



Scott Bruckner

10/8/2018

PLEASE COMPLETE THIS INFORMATION
RECORDING REQUESTED BY:

KECIA HARPER-IHEM, CLERK OF THE BOARD
RIVERSIDE CO. CLERK OF THE BOARD
4080 LEMON STREET, 1ST FLOOR CAC
P O BOX 1147 - RIVERSIDE, CA 92502

MAIL STOP # 1010

AND WHEN RECORDED MAIL TO:

RETURN TO: STOP #1010
RIVERSIDE COUNTY CLERK OF THE BOARD
P. O. BOX 1147 - RIVERSIDE, CA 92502

2018-0456087

11/20/2018 11:20 AM Fee: \$ 0.00

Page 1 of 2

Recorded in Official Records
County of Riverside
Peter Aldana
Assessor-County Clerk-Recorder



127

THIS SPACE FOR RECORDERS USE ONLY

NOTICE OF COMPLETION

To be recorded with County Recorder
within 10 days after completion.
No recording fee.

Notice is hereby given by the undersigned owner, a public entity of the State of California, that a public work of improvement has been completed, as follows:

Project title or description of work: Thousand Palms Canyon Road Widening, Turning Lane and Resurfacing Project,
Project. No. C3-0087, Federal Aid No. HRRL-5956(219)

Date of Completion: Date of this notice 10/16/18

Nature of owner: County of Riverside, public entity

Interest or estate of owner: Public Roadway

Address of owner: Clerk of the Board of Supervisors, County Administrative Center
4080 Lemon Street, 8th Floor, Riverside, CA 92501

Name of contractor: Granite Construction Company, 38000 Monroe St. Indio, CA 92203

Street or legal description of site: Thousand Palms Canyon Road, between Ramon Road, Washington Street and
Dillon Road, Thousand Palms Area, Township 4S Range 6E Section 12, County
Road Book Page No. 205

ATTEST: 10/16/18

KECIA HARPER-IHEM, Clerk

By: [Signature]
DEPUTY

STATE OF CALIFORNIA)

COUNTY OF RIVERSIDE)

ss

Owner: County of Riverside
(Name of Public Entity)

By: [Signature]
Chairman, Board of Supervisors
CHUCK WASHINGTON

I am the Chairman of the governing board of the County of Riverside, the public entity which executed the foregoing notice and on whose behalf I make this verification; I have read this notice, know its contents, and the same is true. I certify under penalty of perjury that the foregoing is true and correct.

Executed at Riverside, California on 10/16/18 (Date)

[Signature], Chairman of the Board of Supervisors
10.16.18 3,26

CHUCK WASHINGTON

FORM APPROVED COUNTY COUNSEL

BY [Signature] 11/13/18 DATE
KRISTINE BELL-VALDEZ



**PETER ALDANA
COUNTY OF RIVERSIDE
ASSESSOR-COUNTY CLERK-RECORDER**

Recorder
P.O. Box 751
Riverside, CA 92502-0751
(951) 486-7000

www.riversideacr.com

CERTIFICATION

Pursuant to the provisions of Government Code 27361.7, I certify under the penalty of perjury that the following is a true copy of illegible wording found in the attached document:

(Print or type the page number(s) and wording below):

Clarification of the Seal for the Riverside County Board of Supervisors
(embossed on the document)



Date:

10-16-13

Signature:

Karen Barton

Print Name:



Karen Barton, Board Assistant

COUNTY OF RIVERSIDE
TRANSPORTATION DEPARTMENT

THOUSAND PALMS CANYON ROAD
RESURFACING PROJECT
BETWEEN RAMON RD/WASHINGTON ST AND DILLON RD
THOUSAND PALMS AREA

PROJECT No. C3-0087

FEDERAL AID No. HRRRL-5956(219)

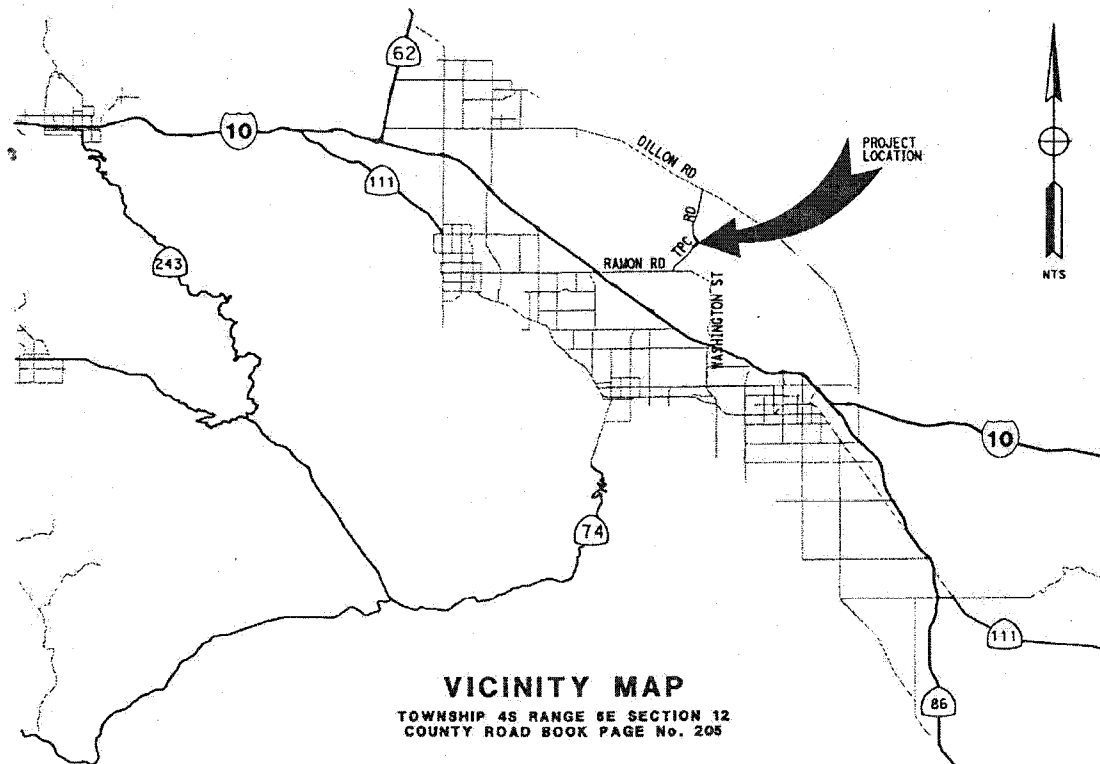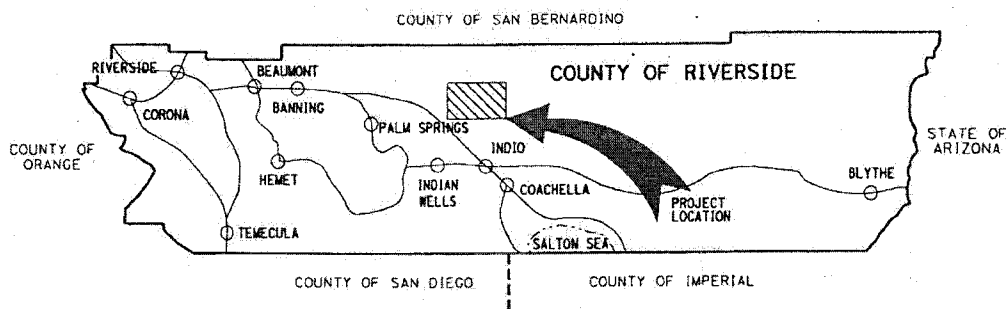

PROGRESS ESTIMATE RECORD - COUNTY OF RIVERSIDE
 PROJECT: Thousand Palms Canyon Road Widening, Turning Lane
 Contract No. 18-03-012
 Project No. C3-0087, Federal Aid NO. HRRRL-5956(219)

Contractor: Granite Construction Company
 Address: 38000 Monroe St.
 City, State, Zip: Indio, Ca 92203

Estimate No. 2 Final
 From: June 26, 2018
 To: September 25, 2018



| Item No. | Item Description | Units | Quantity | Unit Price | Original Contract Amount | Change Orders Quantity | Change Orders Amount | Amended Contract Quantity | Amended Contract Amount | This Estimate Quantity | This Estimate Amount | Previous Quantity | Total Estimate To Date Quantity | Total Estimate To Date Amount | % Auth. |
|----------------------|------------------|-------|----------|------------|--------------------------|------------------------|----------------------|---------------------------|-------------------------|------------------------|----------------------|-------------------|---------------------------------|-------------------------------|---------|
| | | | | | 605,506.00 | | 0.00 | | 605,506.00 | | 12,778.96 | | | 527,529.00 | |
| PROJECT TOTAL | | | | | | | | | | | | | | | |

Made by: Justin Robbins
 Checked by: *[Signature]*
 OK Const. Supv. *[Signature]*

Working Days: 30 Start Date: 5-31-18
 Days Added: 0 End Date: 6-21-18
 Subtotal: 30 % \$ Complete: 87%
 Days Used: 22 Original Contract: \$605,506.00
 % Time Elapsed: 73% Amended Contract: \$605,506.00

TOTAL VALUE OF WORK TO DATE: \$527,529.00
 LESS RETENTION: 0% 0.00
 TOTAL DUE TO DATE: \$527,529.00
 LESS PREVIOUSLY INVOICED: 514,750.04
 LESS LABOR NON COMPLIANCE: 0.00
 TOTAL DUE THIS PAYMENT: \$12,778.96

This Estimate Approved _____ Date: _____ for: _____

Patricia Romo, Director of Transportation

Received by Accounts Payable: _____
 By: _____

Quantities on This Estimate Approved _____ Date: _____
 Granite Construction Company

| PROGRESS ESTIMATE RECORD - COUNTY OF RIVERSIDE | | | | | | | | | | | | | | | |
|--|---|-------|----------|------------|--------------------------|------------------------|----------------------|---------------------------|-------------------------|------------------------|----------------------|-------------------|---------------------------------|-------------------------------|---------|
| PROJECT: Thousand Palms Canyon Road Widening, Turning Lane | | | | | | | | | | | | | | | |
| Contract No. 18-03-012 | | | | | | | | | | | | | | | |
| Project No. C3-0087, Federal Aid No. HRRRL-5956(219) | | | | | | | | | | | | | | | |
| Contractor: Granite Construction Company | | | | | | | | | | | | | | | |
| Address: 38000 Monroe St. | | | | | | | | | | | | | | | |
| City, State, Zip: Indio, Ca 92203 | | | | | | | | | | | | | | | |
| Estimate No. From: June 26, 2018 To: September 25, 2018 | | | | | | | | | | | | | | | |
| SHEET 1 of 2 Processed Construction 9/12/2018 | | | | | | | | | | | | | | | |
| Item No. | Item Description | Units | Quantity | Unit Price | Original Contract Amount | Change Orders Quantity | Change Orders Amount | Amended Contract Quantity | Amended Contract Amount | This Estimate Quantity | This Estimate Amount | Previous Quantity | Total Estimate To Date Quantity | Total Estimate To Date Amount | % Auth. |
| 1 | FUNDING AWARENESS SIGN | EA | 2 | 1,500.00 | 3,000.00 | | | 2.00 | 3,000.00 | | | 1.00 | 1.00 | 1,500.00 | 50% |
| 2 | COLD PLANE ASPHALT CONCRETE PAVEMENT | SQYD | 100 | 75.00 | 7,500.00 | | | 100.00 | 7,500.00 | | | 98.00 | 98.00 | 7,350.00 | 98% |
| 3 | SHOULDER BACKING | LF | 7,500 | 5.00 | 37,500.00 | | | 7,500.00 | 37,500.00 | | | 7,526.00 | 7,526.00 | 37,630.00 | 100% |
| 4 | HOT MIX ASPHALT (TYPE A) | TON | 4,300 | 73.00 | 313,900.00 | | | 4,300.00 | 313,900.00 | | | 3,696.22 | 3,696.22 | 269,824.06 | 86% |
| 5 | RUMBLE STRIP AND STRIPE | LF | 3,750 | 4.00 | 15,000.00 | | | 3,750.00 | 15,000.00 | | | 3,763.35 | 3,763.35 | 15,053.40 | 100% |
| 6 | THERMOPLASTIC TRAFFIC STRIPE | SQFT | 12,000 | 0.95 | 11,400.00 | | | 12,000.00 | 11,400.00 | | | 12,102.00 | 12,102.00 | 11,496.90 | 101% |
| 7 | THERMOPLASTIC PAVEMENT MARKING | SQFT | 40 | 6.50 | 260.00 | | | 40.00 | 260.00 | | | 40.00 | 40.00 | 260.00 | 100% |
| 8 | PAVEMENT MARKER (RETROREFLECTIVE) | EA | 500 | 3.50 | 1,750.00 | | | 500.00 | 1,750.00 | | | 500.00 | 500.00 | 1,750.00 | 100% |
| 9 | PULVERIZE EXISTING ASPHALT | SQYD | 15,000 | 0.90 | 13,500.00 | | | 15,000.00 | 13,500.00 | | | 14,846.98 | 14,846.98 | 13,362.28 | 99% |
| 10 | ITEM DELETED BY ADDENDUM | | | | 0.00 | | | | | | | | | | N/A |
| 11 | SAFETY EDGE | LF | 7,500 | 1.00 | 7,500.00 | | | 7,500.00 | 7,500.00 | | | 7,526.00 | 7,526.00 | 7,526.00 | 100% |
| 12 | DUST CONTROL | LS | 1 | 7,000.00 | 7,000.00 | | | 1.00 | 7,000.00 | | | 1.00 | 1.00 | 7,000.00 | 100% |
| 13 | TRAFFIC CONTROL SYSTEM | LS | 1 | 89,396.00 | 89,396.00 | | | 1.00 | 89,396.00 | | | 1.00 | 1.00 | 89,396.00 | 100% |
| 14 | PREPARE WATER POLLUTION CONTROL PROGRAM | LS | 1 | 5,000.00 | 5,000.00 | | | 1.00 | 5,000.00 | | | 1.00 | 1.00 | 5,000.00 | 100% |
| 15 | RELOCATE ROADSIDE SIGN-ONE POST | EA | 3 | 100.00 | 300.00 | | | 3.00 | 300.00 | | | 3.00 | 3.00 | 300.00 | 100% |
| 16 | ROADSIDE SIGN - ONE POST | EA | 5 | 250.00 | 1,250.00 | | | 5.00 | 1,250.00 | | | 5.00 | 5.00 | 1,250.00 | 100% |
| 17 | CLEARING AND GRUBBING | LS | 1 | 3,000.00 | 3,000.00 | | | 1.00 | 3,000.00 | | | 1.00 | 1.00 | 3,000.00 | 100% |
| 18 | DEVELOP WATER SUPPLY | LS | 1 | 3,000.00 | 3,000.00 | | | 1.00 | 3,000.00 | | | 1.00 | 1.00 | 3,000.00 | 100% |
| 19 | TEMPORARY FENCE (TYPE ESA) | LF | 7,500 | 3.90 | 29,250.00 | | | 7,500.00 | 29,250.00 | | | 7,526.00 | 7,526.00 | 29,351.40 | 100% |
| 20 | MOBILIZATION, DEMOBILIZATION, AND FINAL CLEAN | LS | 1 | 3,000.00 | 3,000.00 | | | 1.00 | 3,000.00 | 0.10 | 300.00 | 0.90 | 1.00 | 3,000.00 | 100% |
| 21 | CONSTRUCT 80' LONG PAVEMENT TRANSITION PER | LS | 1 | 8,000.00 | 8,000.00 | | | 1.00 | 8,000.00 | | | 1.00 | 1.00 | 8,000.00 | 100% |
| 22 | MISCELLANEOUS WORK (AS DIRECTED) | FA | 1 | 45,000.00 | 45,000.00 | | | 1.00 | 45,000.00 | 0.2773102 | 12,478.96 | | 0.2773102 | 12,478.96 | 28% |
