

SUBMITTAL TO THE BOARD OF SUPERVISORS
COUNTY OF RIVERSIDE, STATE OF CALIFORNIA



ITEM
3.45
(ID # 9877)

MEETING DATE:

Tuesday, June 25, 2019


FROM : TLMA-TRANSPORTATION:

SUBJECT: TRANSPORTATION AND LAND MANAGEMENT AGENCY/TRANSPORTATION:
Notice of Completion – Borel Road Resurfacing Project in the French Valley area
and Rancho California Road Resurfacing Project in the Rancho California Area.
District 3. [\$0]

RECOMMENDED MOTION: That the Board of Supervisors:

1. Accept as complete the Construction of Borel Road Resurfacing Project, from Auld Road to Buck Road in the French Valley area and Rancho California Road from Monte De Oro to Buck Road in the Rancho California area;
2. Authorize the Chairman of the Board to execute the Notice of Completion on behalf of the County; and
3. Direct the Clerk of the Board to record the Notice of Completion.


ACTION:Policy


Patricia Romo, Director of Transportation 5/22/2019

MINUTES OF THE BOARD OF SUPERVISORS

On motion of Supervisor Perez, seconded by Supervisor Hewitt and duly carried by unanimous vote, IT WAS ORDERED that the above matter is approved as recommended.

Ayes: Jeffries, Spiegel, Washington, Perez and Hewitt
Nays: None
Absent: None
Date: June 25, 2019
xc: Transp., Recorder

Kecia Harper
Clerk of the Board
By: 
Deputy

**SUBMITTAL TO THE BOARD OF SUPERVISORS COUNTY OF RIVERSIDE,
STATE OF CALIFORNIA**

FINANCIAL DATA	Current Fiscal Year:	Next Fiscal Year:	Total Cost:	Ongoing Cost
COST	\$ 0	\$ 0	\$ 0	\$ 0
NET COUNTY COST	\$ 0	\$ 0	\$ 0	\$ 0
SOURCE OF FUNDS: N/A			Budget Adjustment: N/A	
			For Fiscal Year: 18/19	

C.E.O. RECOMMENDATION: Approve

BACKGROUND:

Summary

By Minute Order 3-70 of August 28, 2018, the Board of Supervisors entered into a contract with All American Asphalt of Corona, California for the construction of Borel Road Resurfacing Project, from Auld Road to Buck Road in the French Valley area and Rancho California Road from Monte De Oro to Buck Road in the Rancho California area.

The original authorized amount of the contract was \$2,137,395. The total price of the contract came in at \$1,740,163 which is 18.6% less than the original authorized amount. The reduction of the total cost was the result of using less quantities than anticipated to complete the work.

The work was completed in conformance with the plans and specifications and the contractor was granted relief of maintenance on February 5, 2019.

Project No. C6-0013 (Borel Road)

Project No. C8-0046 (Rancho California Road)

Impact on Residents and Businesses

The improvements have provided a smooth paved roadway that has improved the safety and efficiency of vehicular traffic.

Additional Fiscal Information

**SUBMITTAL TO THE BOARD OF SUPERVISORS COUNTY OF RIVERSIDE,
STATE OF CALIFORNIA**

Budget

Original Contract Amount		\$2,137,395
Total Change Orders Authorized	0.0%	\$0
Estimated Pending Change Orders	0.0%	\$0
Authorized Contract Amount		\$2,137,395
* Quantity Adjustments	-18.6%	(\$397,232)
+ CCO FA Adjustments	0.0%	\$0
Total Amended Contract Amount	81.4%	\$1,740,163

Expenditures

Total Progress Payments	\$1,740,163
Estimated Pending Payments	\$0
Total Expenditures	\$1,740,163

(Over)/Under Contract Amount \$0

+ Change Orders using the Force Account method of payment issued prior to the work being completed generally do not use the total authorized amount.

* Caltrans Standard Specifications 4-1.03B. Increases or decreases in the quantity of a contract item of work will be determined by comparing the total pay quantity of such item of work with the Engineer's Estimate. If the total pay quantity of any item of work required under the contract varies from the Engineer's Estimate by 25 percent or less, payment will be made for the quantity of work of said item performed at the contract unit price, unless eligible for adjustment pursuant to Section 4-1.03C, "Changes in Character of Work."

This project was funded with \$1,740,163 of Gas Tax / SB-1 funds.



Contract History and Price Reasonableness

Five bids were received ranging from \$2,139,495 to \$2,403,643. The basis for the selection of a contractor is the lowest responsive and responsible bid. The lowest responsible bid was submitted by All American Asphalt in the amount of \$2,139,495, which was \$124,772 (5.5%) below the Engineer's Estimate.

ATTACHMENTS:

Vicinity Map
Progress Estimate Report
Notice of Completion

SUBMITTAL TO THE BOARD OF SUPERVISORS COUNTY OF RIVERSIDE,
STATE OF CALIFORNIA

 Jason Farin, Senior Management Analyst 6/19/2019  Gregory V. Priaplos, Director County Counsel 5/28/2019

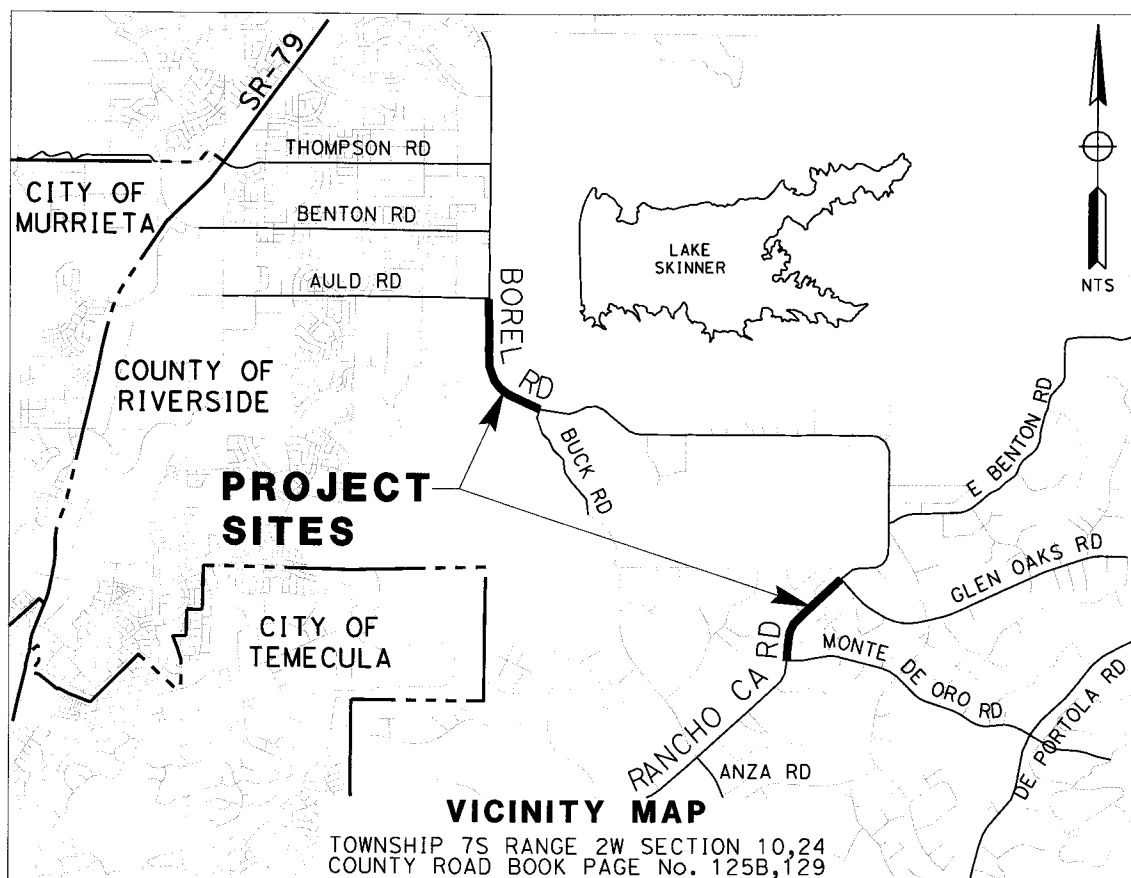
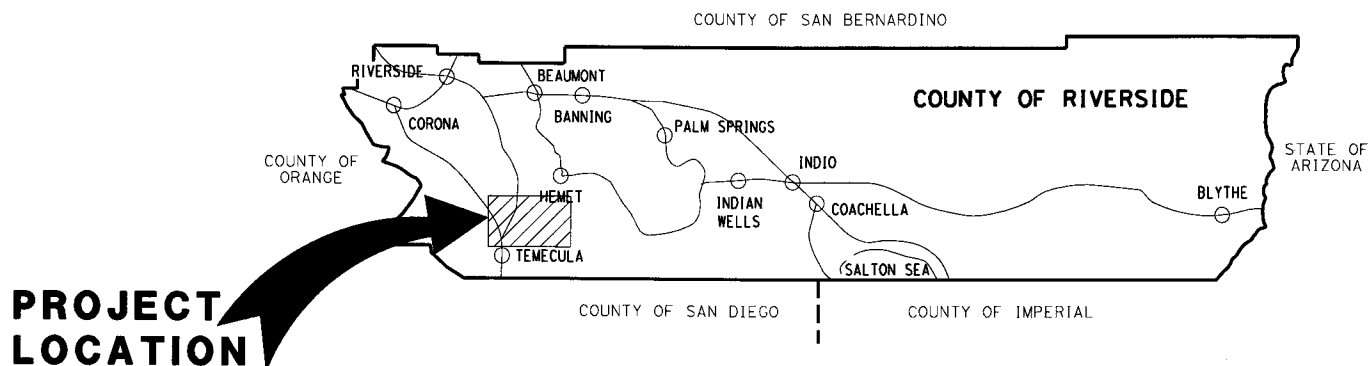
COUNTY OF RIVERSIDE
TRANSPORTATION DEPARTMENT

BOREL RD & RANCHO CA RD RESURFACING PROJECT

200' NORTH OF BUCK ROAD TO AULD ROAD,
MONTE DE ORO RD TO BUCK RD

COMMUNITIES OF FRENCH VALLEY & RANCHO CALIFORNIA

W.O. No. C6-0013, C8-0046



PROJECT: Borel Rd. Resurfacing Project, Auld Rd. to Buck Rd. & Rancho California Rd. Resurfacing Project, Mantia Da Oro to Buck Rd.
County Project No.: CR-0013 & CR-0046
Contract No. 18-07-003

Item No.	Item Description	Units	Quantity	Unit Price	Original Contract		Change Orders		Amended Contract		This Estimate		Previous		Total Estimate To Date		% Auth.
					Amount	Quantity	Amount	Quantity	Amount	Quantity	Amount	Quantity	Amount	Quantity			
	BASE BID SCH. 1 - BORAL ROAD RESURFACING - CS-0013				0.00			982,085.50			0.00					768,854.90	
	BASE BID SCH. 2 - RANCHO CALIFORNIA ROAD RESURFACING - CR-0046				0.00			1,175,308.50			1,600.00					971,307.60	
PROJECT TOTAL								2,137,395.00			1,600.00					1,740,182.50	

Made by: Steven Viano
Checked by: TLAR
OK Const. Supv. TLAR

Working Days: 10-29-18
Days Added: 2-5-19
Subtotal: 81%
Days Used: \$2,137,395.00
% Time Elapsed: \$2,137,395.00

Start Date: 10-29-18
End Date: 2-5-19
% \$ Complete: 81%
Original Contract: \$2,137,395.00
Amended Contract: \$2,137,395.00

TOTAL VALUE OF WORK TO DATE: \$1,740,182.50
LESS RETENTION: 5% 87,008.14
TOTAL DUE TO DATE: \$1,653,154.38
LESS PREVIOUSLY INVOICED: 1,651,834.38
LESS LABOR NON COMPLIANCE: 0.00
TOTAL DUE THIS PAYMENT: \$1,520.00

This Estimate Approved [Signature] Date: 4/9/19 for: Patricia Rorfo, Director of Transportation

Received by Accounts Payable: By:

PAYMENT APPROVAL

Fund 20000
Dept ID 31305
Account 527980
Project 208-00466
Activity ID 23500
Resource Type CNT
Signature [Signature]
Date 4/9/19

TRANSCAL APPROVED
By: Lori Conrad 5-3461
APR 10 2019

RECEIVED
APR 10 2019

PROJECT: Royal Rd. Resurfacing Project, Audit Rd. to Buck Rd. & Rancho California Rd. Resurfacing
 Project: Monte De Oro to Buck Rd.
 County Project No.: CR-0013 & CR-0048
 Contract No. 19-07-003

Contractor: All American Asphalt
 Address: P.O. Box 2229
 City, State, Zip: Corona, CA 92601



Estimate No. 5 Final
 From: February 28, 2019
 To: March 28, 2019

Item No.	Item Description	Units	Quantity	Unit Price	Original Contract Amount	Change Orders Quantity	Change Orders Amount	Amended Contract Quantity	Amended Contract Amount	This Estimate Quantity	This Estimate Amount	Previous Quantity	Total Estimate To Date Quantity	Total Estimate To Date Amount	% Auth.
1	BASE BID SCH. 1 - BORAL ROAD RESURFACING - CR-0013	LF	11,060	3.00	33,180.00			11,060.00	33,180.00			11,048.00	11,048.00	33,144.00	100%
2	SHOULDER BACKING	EA	1	1,600.00	1,600.00			1.00	1,600.00			1.00	1.00	1,600.00	100%
3	ASPHALT CONCRETE OVERSIDE DRAIN (CRS 306)	LF	1,840	5.20	9,568.00			1,840.00	9,568.00			1,865.00	1,865.00	9,698.00	101%
4	PLACE ASPHALT CONCRETE DIKE (CRS 212) (6")	TON	9,410	69.80	656,818.00			9,410.00	656,818.00			8,180.50	8,180.50	570,998.90	87%
5	HOT MIX ASPHALT (TYPE A)	EA	579	4.50	2,605.50			579.00	2,605.50			478.00	478.00	2,151.00	83%
6	PAVEMENT MARKER (RETROREFLECTIVE)	EA	6	63.00	378.00			6.00	378.00			6.00	6.00	378.00	100%
7	SALVAGE ROADSIDE SIGN	EA	8	313.00	2,504.00			8.00	2,504.00			8.00	8.00	2,504.00	100%
8	ROADSIDE SIGN - ONE POST	EA	8	313.00	2,504.00			8.00	2,504.00			8.00	8.00	2,504.00	100%
9	THERMOPLASTIC PAVEMENT MARKING	SQFT	510	6.00	3,060.00			510.00	3,060.00			554.00	554.00	3,324.00	108%
10	PAINT TRAFFIC STRIPE (2-COAT)	LF	17,775	0.50	8,887.50			17,775.00	8,887.50			17,216.00	17,216.00	8,608.00	97%
11	DEVELOP WATER SUPPLY	LS	1	2,000.00	2,000.00			1.00	2,000.00			1.00	1.00	2,000.00	100%
12	TRAFFIC CONTROL SYSTEM	LS	1	48,800.00	48,800.00			1.00	48,800.00			1.00	1.00	48,800.00	100%
13	PREPARE WATER POLLUTION CONTROL PROGRAM	LS	1	1,040.00	1,040.00			1.00	1,040.00			1.00	1.00	1,040.00	100%
14	CLEARING AND GRUBBING (LS)	LS	1	10,250.00	10,250.00			1.00	10,250.00			1.00	1.00	10,250.00	100%
15	DUST ABATEMENT	LS	1	2,800.00	2,800.00			1.00	2,800.00			1.00	1.00	2,800.00	100%
16	GRINDING ASPHALT CONCRETE IN PLACE	SOYD	29,470	1.75	51,572.50			29,470.00	51,572.50			28,444.00	28,444.00	46,277.00	90%
17	CATCH BASIN (COMBINATION INLET) (CRS 301 - NO. 1)	EA	1	12,522.00	12,522.00			1.00	12,522.00			1.00	1.00	12,522.00	100%
18	MINOR CONCRETE (DRIVEWAY APPROACH WITH ASPHALT CONCRETE DIKE) (CRS 206)	SOFT	250	58.00	14,500.00			250.00	14,500.00			220.00	220.00	12,780.00	88%
19	MISCELLANEOUS WORK (AS DIRECTED)	FA	1	100,000.00	100,000.00			1.00	100,000.00						0%

PROJECT: Beryl Rd. Resurfacing Project, Add Rd. to Buck Rd. & Rancho California Rd. Resurfacing
 Project, Monte De Oro to Buck Rd.
 County Project No.: C6-0613 & C6-0046
 Contract No. 18-07-003

Contractor: Ali American Asphalt
 Address: P.O. Box 2229
 City, State, Zip: Corona, CA 92604

Estimate No. 5 Final
 From: February 28, 2019
 To: March 28, 2019



Item No.	Item Description	Units	Quantity	Unit Price	Original Contract Amount	Changes Orders Quantity	Amended Contract Quantity	Amount	This Estimate Quantity	Amount	Previous Quantity	Total Estimate To Date Quantity	Amount	% Auth.
19	BASE BID SCH. 2 - RANCHO CALIFORNIA ROAD RESURFACING - C6-0046	LF	9,800	3.00	28,700.00		9,800.00	28,700.00			9,440.00	9,440.00	28,320.00	95%
20	SHOULDER BACKING	EA	1	1,600.00	1,600.00		1.00	1,600.00	1.00	1,600.00		1.00	1,600.00	100%
21	ASPHALT CONCRETE OVERSIDE DRAIN (CRS 306)	LF	710	5.20	3,692.00		710.00	3,692.00			720.00	720.00	3,744.00	101%
22	PLACE ASPHALT CONCRETE DIKE (CRS 212) (6")	TON	6,220	69.80	434,156.00		6,220.00	434,156.00			5,812.47	5,812.47	391,750.41	90%
23	HOT MIX ASPHALT (TYPE A)	EA	620	4.50	2,790.00		620.00	2,790.00			528.00	528.00	2,376.00	85%
24	PAVEMENT MARKER (RETROREFLECTIVE)	EA	18	63.00	1,134.00		18.00	1,134.00			21.00	21.00	1,323.00	117%
25	SALVAGE ROADSIDE SIGN	EA	18	313.00	5,634.00		18.00	5,634.00			17.00	17.00	5,321.00	94%
26	ROADSIDE SIGN - ONE POST	SQFT	875	6.00	5,250.00		875.00	5,250.00			755.00	755.00	4,530.00	86%
27	THERMOPLASTIC PAVEMENT MARKING	LF	18,400	0.50	9,200.00		18,400.00	9,200.00			15,880.00	15,880.00	7,940.00	86%
28	PAINT TRAFFIC STRIPE (2-COAT)	LS	1	2,000.00	2,000.00		1.00	2,000.00			1.00	1.00	2,000.00	100%
29	DEVELOP WATER SUPPLY	LS	1	46,800.00	46,800.00		1.00	46,800.00			1.00	1.00	46,800.00	100%
30	TRAFFIC CONTROL SYSTEM	LS	1	1,040.00	1,040.00		1.00	1,040.00			1.00	1.00	1,040.00	100%
31	PREPARE WATER POLLUTION CONTROL PROGRAM	LS	1	10,250.00	10,250.00		1.00	10,250.00			1.00	1.00	10,250.00	100%
32	CLEARING AND GRUBBING (LS)	LS	1	2,800.00	2,800.00		1.00	2,800.00			1.00	1.00	2,800.00	100%
33	DUST ABATEMENT	SOYD	25,100	5.96	149,596.00		25,100.00	149,596.00			24,551.00	24,551.00	146,323.96	98%
34	PULVERIZE EXISTING ASPHALT	TON	3,020	86.55	261,381.00		3,020.00	261,381.00			3,086.49	3,086.49	267,135.71	102%
35	RUBBERIZED HOT MIX ASPHALT (GAP GRADED)	SOYD	1,600	53.00	84,800.00		1,600.00	84,800.00			404.44	404.44	21,435.32	25%
36	PLACE HOT MIX ASPHALT (MISCELLANEOUS AREA)	SQFT	835	21.90	18,286.50		835.00	18,286.50			978.00	978.00	21,418.20	117%
37	MINOR CONCRETE (CROSS-GUTTER AND SPANDREL)	FA	1	100,000.00	100,000.00		1.00	100,000.00						0%
37A	MISCELLANEOUS WORK (AS DIRECTED)	EA	2	2,600.00	5,200.00		2.00	5,200.00			2.00	2.00	5,200.00	100%

PLEASE COMPLETE THIS INFORMATION
RECORDING REQUESTED BY:

KECIA R. HARPER, CLERK OF THE BOARD
RIVERSIDE CO. CLERK OF THE BOARD
4080 LEMON STREET, 1ST FLOOR CAC
P O BOX 1147 – RIVERSIDE, CA 92502

MAIL STOP # 1010

AND WHEN RECORDED MAIL TO:

RETURN TO: STOP #1010
RIVERSIDE COUNTY CLERK OF THE BOARD
P. O. BOX 1147 – RIVERSIDE, CA 92502

2019-0231829

06/26/2019 12:37 PM Fee: \$ 0.00

Page 1 of 2

Recorded in Official Records
County of Riverside
Peter Aldana
Assessor-County Clerk-Recorder



6080

NOTICE OF COMPLETION

To be recorded with County Recorder
within 10 days after completion.
No recording fee.

Notice is hereby given by the undersigned owner, a public entity of the State of California, that a public work of improvement has been completed, as follows:

Project title or description of work: Borel Road Resurfacing Project and Rancho California Road Resurfacing Project, Project Nos. C6-0013 & C8-0046

Date of Completion: Date Hereof 06/25/19

Nature of owner: County of Riverside, public entity

Interest or estate of owner: Public Road Right-of-Way

Address of owner: Clerk of the Board of Supervisors, County Administrative Center
4080 Lemon Street, 8th Floor, Riverside, CA 92501


Name and Address of contractor: All American Asphalt, 400 East 6th Street, Corona, CA 92879

Street or legal description of site: Borel Road from Auld Road to Buck Road, Community of French Valley and Rancho California Road from Monte De Oro to Buck Road, Community of Rancho California

Dated: June 25, 2019

Owner: County of Riverside
(Name of Public Entity)

By:


Chairman, Board of Supervisors
Kevin Jeffries

STATE OF CALIFORNIA)

ss

COUNTY OF RIVERSIDE)

I am the Chairman of the governing board of the County of Riverside, the public entity which executed the foregoing notice and on whose behalf I make this verification; I have read this notice, know its contents, and the same is true. I certify under penalty of perjury that the foregoing is true and correct.

Executed at Riverside, California on 06/25/19 (Date)




, Chairman of the Board of Supervisors

Kevin Jeffries

FORM APPROVED COUNTY COUNSEL

06.25.19 3.45

BY


KRISTINE BELL-VALDEZ

DATE



**PETER ALDANA
COUNTY OF RIVERSIDE
ASSESSOR-COUNTY CLERK-RECORDER**

Recorder
P.O. Box 751
Riverside, CA 92502-0751
(951) 486-7000

www.riversideacr.com

CERTIFICATION

Pursuant to the provisions of Government Code 27361.7, I certify under the penalty of perjury that the following is a true copy of illegible wording found in the attached document:

(Print or type the page number(s) and wording below):

Clarification of the Seal for the Riverside County Board of Supervisors
(embossed on the document)



Date:

6-25-19

Signature:

Karen Barton

Print Name:

Karen Barton, Board Assistant
