# SUBMITTAL TO THE BOARD OF SUPERVISORS COUNTY OF RIVERSIDE, STATE OF CALIFORNIA



**MEETING DATE:** 

Tuesday, August 27, 2019

FROM: TLMA-TRANSPORTATION:

SUBJECT: TRANSPORTATION AND LAND MANAGEMENT AGENCY/TRANSPORTATION:

Notice of Completion - Santa Ana River Trail, Multipurpose Trail and Bike Lane,

in the Chino Hills State Park. District 2. [\$0]

#### **RECOMMENDED MOTION:** That the Board of Supervisors:

- 1. Accept as complete the Construction of the Santa Ana River Trail, Multipurpose Trail and Bike Lane, in Chino Hill State Park by Riverside Construction Company, Inc.;
- 2. Authorize the Chairman of the Board to execute the Notice of Completion on behalf of the County; and
- 3. Direct the Clerk of the Board to record the Notice of Completion.

**ACTION:Policy** 

MINUTES OF THE BOARD OF SUPERVISORS

On motion of Supervisor Washington, seconded by Supervisor Spiegel and duly carried by unanimous vote, IT WAS ORDERED that the above matter is approved as recommended.

Ayes:

Jeffries, Spiegel, Washington, Perez and Hewitt

Nays:

None

Absent:

None

Date:

August 27, 2019

XC:

Transp.

3.39

Kecia R. Harper

## SUBMITTAL TO THE BOARD OF SUPERVISORS COUNTY OF RIVERSIDE, STATE OF CALIFORNIA

FINANCIAL DATA	Current Fiscal Year: Next Fiscal Year: Total Cost			Total Cost:		Ongoi	ng Cost	<b>7</b>	
COST	\$	0	\$	0	\$	0	7.40 M	\$	0
NET COUNTY COST	\$	0	\$	0	\$	0		\$	0
SOURCE OF FUNDS	5: N/A	· · · · · · · · · · · · · · · · · · ·					ustment:	No	
					For Fis	cal Y	<b>/ear:</b> 19	/20	

C.E.O. RECOMMENDATION: Approve

#### **BACKGROUND:**

#### **Summary**

By Minute Order 3-53 of December 4, 2018, the Board of Supervisors entered into a contract with Riverside Construction Company, Inc. of Riverside, California for the improvements on approximately a one mile segment of the existing Santa Ana River dirt trail within the Chino Hills State Park. The project limits are from approximately one mile easterly of the Green River Golf Course to approximately one third of a mile west of the Prado Basin.

The original authorized amount of the contract was \$979,241. The total price of the contract came in at \$849,899 which is 13.2% less than the original authorized amount. The reduction of the total cost was the result of using less quantities than anticipated to complete the work.

The work was completed in conformance with the plans and specifications and the contractor was granted relief of maintenance on April 13, 2019.

Project No. C1-0642

#### Impact on Residents and Businesses

The improved trail provides a defined usable and safe bike lane and multipurpose trail for multiple users (hikers, bicyclists and equestrians) and contributes to the 110 mile Santa Ana River Trail.

#### **Additional Fiscal Information**

### SUBMITTAL TO THE BOARD OF SUPERVISORS COUNTY OF RIVERSIDE, STATE OF CALIFORNIA

Budget		
Original Contract Amount		\$979,241
Total Change Orders Authorized	0.0%	\$0
Estimated Pending Change Orders	0.0%	\$0
Authorized Contract Amount		\$979,241
* Quantity Adjustments	-13.2%	(\$129,342)
+ CCO FA Adjustments	0.0%	\$0
Total Amended Contract Amount	86.8%	\$849,899
Expenditures		
Total Progress Payments		\$849,899
Estimated Pending Payments		\$0
Total Expenditures	***************************************	\$849,899
(Over)/Under Contract Amount	· · · · · · · · · · · · · · · · · · ·	\$0

- + Change Orders using the Force Account method of payment issued prior to the work being completed generally do not use the total authorized amount.
- \* <u>CAL-Trans Standard Specifications 4-1.03B</u>. Increases or decreases in the quantity of a contract item of work will be determined by comparing the total pay quantity of such item of work with the Engineer's Estimate. If the total pay quantity of any item of work required under the contract varies from the Engineer's Estimate by 25 percent or less, payment will be made for the quantity of work of said item performed at the contract unit price, unless eligible for adjustment pursuant to Section 4-1.03C, "Changes in Character of Work."

This project was funded with \$849,899 of County Parks District funds.

#### **Contract History and Price Reasonableness**

Eight bids were received ranging from \$979,241 to \$2,738,107. The basis for the selection of a contractor is the lowest responsive and responsible bid. The lowest responsible bid was submitted by Riverside Construction Company, Inc. in the amount of \$979,241, which was \$382,774 (28%) below the Engineer's Estimate.

#### **ATTACHMENTS:**

Vicinity Map
Progress Estimate Report
Notice of Completion

Jason Farin Senior Management Analyst

8/20/2019

Gregory . Priaryos, Director County Counse

8/14/2019


# COUNTY OF RIVERSIDE

# TRANSPORTATION DEPARTMENT

# SANTA ANA RIVER TRAIL

# MULTIPURPOSE TRAIL AND BIKE LANE IN THE CHINO HILLS STATE PARK

PROJECT No. C1-0642

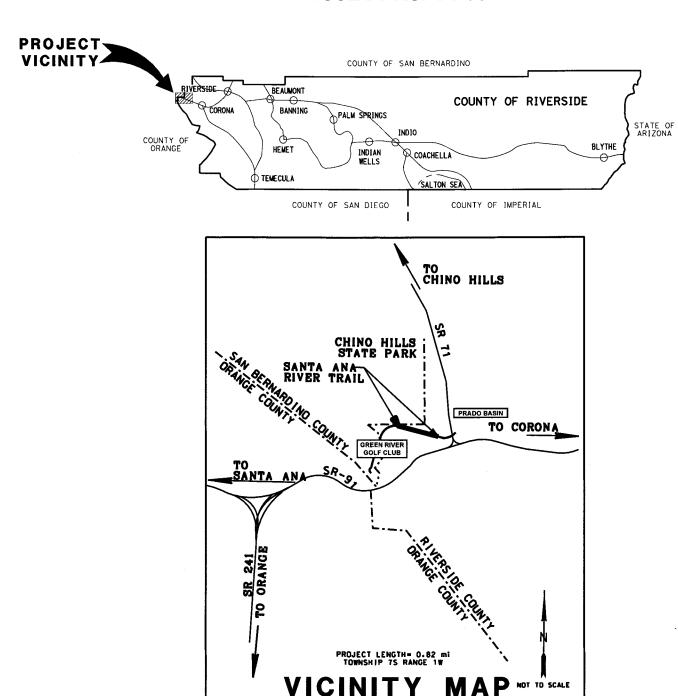

98hLb

1,338.75 125% % March 26, 2019 Processed Construction Inspection 5/3/2019 April 25, 2019 0.00 849,898.89 \$409,229.69 \$849,898.89 \$807,403.95 398,174.26 42,494.94 Total Estimate To Date
Quantity Amount 78.75 2% From: ق Received by Accounts Payable: TOTAL DUE TO DATE: LESS PREVIOUSLY INVOICED: TOTAL VALUE OF WORK TO DATE: LESS RETENTION: LESS LABOR NON COMPLIANCE: TOTAL DUE THIS PAYMENT: Previous Quantity SHEET 2 of 2 1,338.75 430,768.09 Amount Account 521780 78.75 THOUGH THE PAYMENT APPROVAL 31305 Fund 2000D 1,071.00 25,000,00 979,241.00 Sa Amended Contract Carl Dept ID\_ \$979,241.00 \$979,241.00 Validities No. 63.00 8 4-13-19 2-18-19 87% 0.00 Original Contract: Start Date: End Date: % \$ Complete: Amended Contract: Contractor: Riverside Construction Comp. Original Contract Change Orders
Amount Quantity Ar \$409,229.69 Address: 4225 Gerner Road City, State, Zip: Riverside, CA 92501 1,071.00 25,000.00 979,241.00 30 30 80 Working Days: Days Added: 17.00 25,000.00 Days Used: % Time Elapsed: Subtotal: Unit Price PROGRESS ESTIMATE RECORD - COUNTY OF RIVERSIDE PROJECT: Santa Ana River Trail Multipurpose Trail and Bike Lane in the Chino Hills State Park County Project No.: C1-0842 Quantity 8 SOFT Units CONSTRUCTION ZONE ENHANCED ENFORCEMENT | FA THERMOPLASTIC PAVEMENT MARKING flem Description Quantities on This Estimate Approved This Estimate Approved Mac PROJECT TOTAL Made by: Trai Ngu OK Const. Sup Checked by \_\_ ontract No. 18-10-004 25 24

TRANSFISCAL APPROVED By: Lori Conrad 5-3461

Project 201-06426 Activity ID Z3500 Resource Type,

Signature (

Date

PROJE Sounty	PROJECT: Santa Ana River Trail Multipurpose Trail and Bike Lane in the Chino Hills State Park County Project No.: C1-0642 Contract No. 18-10-004	Hino Hill	Ils State Pa		Contractor: Riverside Construction Address: 4226 Garner Road City, State, Zip: Riverside, CA 92501	Contractor: Riverside Construction Company Address: 4225 Gamer Road City, State, Zip: Riverside, CA 92501	ompany						Estimate No. 3 Final From: March 26, 2019	3 Final March 26, 2019 April 25, 2019
E o	item Description	sile5	Quantity	Unit Price	Original Contract Amount	Change Orders Quantity Amount		Amended Contract Quantity	act Amount	This Estimate Quantity	Amount	Previous Quantity	Total Estimate To Date Quantity A	Date
•	DUST ABATEMENT	2	***	24,000.00	24,000.00		***************************************	00.1	24,000.00	0:20	12,000.00	0.50	1.00	24,000.00
~	PREPARE STORM WATER POLLUTION PREVENTION	S	-	9,100.00	9,100.00			1,00	9,100.00	0.25	2,275.00	0.75	1.00	9,100.00 100%
ю	TEMPORARY HIGH-VISIBILITY FENCE (TYPE ESA)	<b>5</b>	4,100	5.50	22,550.00			4,100.00	22,550.00	1,025.00	5,637.50	3,075.00	4,100.00	22,550.00 100%
4	TEMPORARY FENCE (CHAINLINK WITH ACOUSTIFEN	<u>"</u>	4,110	40.00	164,400.00		<u>;</u> ;;,	4,110.00	164,400.00	1,111.00	44,440.00	3,075.00	4,186.00	167,440.00 102%
Ŋ	TRAFFIC CONTROL SYSTEM(INCLUDING CONSTRUC	S	-	54,000.00	54,000.00		***************************************	1.00	54,000.00	0.5370370370	29,000 00	0.4629629630	1.00	54,000.00 100%
Ф	CLEARING AND GRUBBING	รา	-	38,400.00	38,400.00		ygas vil <b>sam</b> iyali	9.	38,400.00	0.05	1,920.00	0.95	1.00	38,400.00 100%
~	DEVELOP WATER SUPPLY	ည	<del>-</del>	8,500.00	8,500.00	imicanyiin	ing to reason and a second	1.00	8,500.00	0.5588824000	4,750.50	0.4411176000	1.00	8,500.00 100%
œ	ROADWAY EXCAVATION AND EARTHWORK (INCLUD	ថ	2,700	39.00	105,300.00	andin della	-1-15-18	2,700.00	105,300.00	898.33	35,034.87	1,801.67	2,700.00	105,300.00 100%
o	EROSION CONTROL (TYPE BONDED FIBER MATRIX ( Acre	Acre	m	3,700.00	11,100.00	<b></b>	·····	3.00	11,100.00	3.00	11,100.00	ejaran en en e	3.00	11,100.00 100%
6	CLASS 2 AGGREGATE BASE	ঠ	006	57.00	51,300.00		nave provide	900.00	51,300,00	00.006	51,300.00	ericka kitoka	00.006	51,300.00 100%
Ŧ	CONSTRUCT TRAIL (DECOMPOSED GRANITE (THICK	გ	320	185.00	64,750.00	<del>- New de jeur</del>		350.00	64,750.00	350.00	64,750.00		350.00	64,750.00 100%
5	HOT MIX ASPHALT (TYPE A)	Ιο	006	89.00	80,100.00			900.00	80,100.00	804.60	71,609.40	o internet e quanti	804.60	71,609.40
5	MINOR CONCRETE (DIP SECTION) (CRS 307)	Շ	130	345.00	44,850.00		, , , , , , , , , , , , , , , , , , ,	130.00	44,850.00	130.00	44,850.00	ang tabiling	130.00	44,850.00 100%
*	PRECAST REINFORCED CONCRETE BOX (5'X2')	4	99	620.00	36,580.00		• · · · · · · · · · · · · · · · · · · ·	29.00	36,580.00	<b>**********</b> **************************		59.00	29.00	36,580.00 100%
5	STRUCTURAL CONCRETE, CUTOFF WALL PER DETA	ঠ	œ	953.00	7,624.00	ereyesinepre	nig <del>ino, e</del> 174.	8:00	7,624.00	restroj čas ne	and the state of t	8.00	8.00	7,624.00 100%
9	MINOR CONCRETE (MINOR STRUCTURES) IWINGWAL	₹	78	1,192.00	33,376.00	Q.Vierge gradine	mo-relivie	28.00	33,376.00			28.00	28.00	33,376.00
11	ROADSIDE SIGN - ONE STEEL POST	ā	82	375.00	6,750.00	÷ 2011-1-1-1-1-1-1-1-1-1-1-1-1-1-1-1-1-1-1	-mujous	18.00	6,750.00	16.00	6,000.00	general (* )	16.00	6,000.00
\$	ROADSIDE SIGN - TWO STEEL POST	2	4	750.00	3,000.00	************	ndagarini d	4.00	3,000.00	4.00	3,000.00	ni aku made (firend	4.00	3,000.00
<b>5</b>	ROCK SLOPE PROTECTION (1 TON, METHOD B) (INC	გ	8	162.00	12,960.00		<u> </u>	80.00	12,960.00	80.00	12,960.00		80.00	12,980.00 100%
8	THERMOPLASTIC TRAFFIC STRIPE	4	3,900	2,70	10,530.00	idis	<b>0</b> 77477 <b>3</b> 183	3,900.00	10,530.00	4,197.00	11,331.90	de tile må Hanny i	4,197.00	11,331.90
2	MOBILIZATION, DEMOBILIZATION AND FINAL CLEAN	SI	*	54,000.00	54,000.00		,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,	1,00	54,000.00	0.25	13,500.00	0.75	99.1	54,000.00
22	OBTAIN ENCROACHMENT PERMITS [CALTRANS, CHI	¥		10,000.00	10,000.00	ngan a ti lakunda nda	omandir met	1.00	10,000.00	0.0000		0.0820	0,0820	820.00
ş		×		000000		igani wan			24 3000	3000	1	1	2	- realiza

PLEASE COMPLETE THIS INFORMATION RECORDING REQUESTED BY:

KECIAR. HARPER, CLERK OF THE BOARD RIVERSIDE CO. CLERK OF THE BOARD 4080 LEMON STREET, 1ST FLOOR CAC P O BOX 1147 - RIVERSIDE, CA 92502

**MAIL STOP # 1010** 

AND WHEN RECORDED MAIL TO:

**RETURN TO: STOP #1010** RIVERSIDE COUNTY CLERK OF THE BOARD P. O. BOX 1147 - RIVERSIDE, CA 92502

09/03/2019 11:34 AM Fee: \$ 0.00

Page 1 of 2

Recorded in Official Records County of Riverside

Aldana Assessor-County Clerk-Recorder





THIS SPACE FOR RECORDERS USE ONLY

## NOTICE OF COMPLETION

To be recorded with County Recorder within 10 days after completion. No recording fee.

Notice is hereby given by the undersigned owner, a public entity of the State of California, that a public work of improvement has been completed, as follows:

Project title or description of work:

Santa Ana River Trail, Multipurpose Trail and Bike Lane, Chino

Hills State Park

**Date of Completion:** 

Date Hereof

08/27/19

Nature of owner:

County of Riverside, public entity

**Interest or estate of owner:** 

Public Road Right-of-Way

Address of owner:

Clerk of the Board of Supervisors, County Administrative Center

4080 Lemon Street, 8th Floor, Riverside, CA 92501

Name and Address of contractor:

Riverside Construction Company, Inc., 4225 Garner Road, Riverside, CA 92501

Street or legal description of site:

Santa Ana River dirt trail from approximately one mile easterly of Green River

Golf Course to approximately one third mile west of Prado Basin, Chino Hills

State Park

Dated: August 27, 2019

County of Riverside

(Name of Public Entity)

Chairman, Board of Supervisors

Kevin Jeffries

STATE OF CALIFORNIA )

**COUNTY OF RIVERSIDE)** 

I am the <u>Chairman</u> of the governing board of the <u>County of Riverside</u>, the public entity which executed the foregoing notice and on whose behalf I make this verification; I have read this notice, know its contents, and the same is true. I certify under penalty of perjury that the foregoing is true and correct.

ATTEST: Kecia R. Harper, Clerk

Executed at

Riverside , California on 08/27/19

Deputy

Chairman of the Board of Supervisors

በጹ 27 19 2 20



## PETER ALDANA COUNTY OF RIVERSIDE ASSESSOR-COUNTY CLERK-RECORDER

Recorder P.O. Box 751 Riverside, CA 92502-0751 (951) 486-7000

www.riversideacr.com

# **CERTIFICATION**

Pursuant to the provisions of Government Code 27361.7, I certify under the penalty of perjury that the following is a true copy of illegible wording found in the attached document:

(Print or type the page number(s) and wording below):

Clarification of the Seal for the Riverside County Board of Supervisors (embossed on the document)



the	
15	

Date:

8-27-19

Signature:

Print Name:

Karen Barton, Board Assistant
