

SUBMITTAL TO THE BOARD OF SUPERVISORS  
COUNTY OF RIVERSIDE, STATE OF CALIFORNIA



ITEM: 3.29  
(ID # 11182)

**MEETING DATE:**

Tuesday, February 11, 2020


**FROM :** TLMA-TRANSPORTATION:

**SUBJECT:** TRANSPORTATION AND LAND MANAGEMENT AGENCY/TRANSPORTATION:  
Notice of Completion – Clinton Keith Road Construction Project Phase 4,  
Community of French Valley and City of Murrieta. District 3. [\$0]

**RECOMMENDED MOTION:** That the Board of Supervisors:

1. Accept as complete the construction of Clinton Keith Road Construction Project Phase 4, Community of French Valley and City of Murrieta;
2. Authorize the Chairman of the Board to execute the Notice of Completion on behalf of the County; and
3. Direct the Clerk of the Board to record the Notice of Completion.

**ACTION:** Policy


  
Patricia Romo, Director of Transportation 1/26/2020

---

**MINUTES OF THE BOARD OF SUPERVISORS**

On motion of Supervisor Jeffries, seconded by Supervisor Spiegel and duly carried by unanimous vote, IT WAS ORDERED that the above matter is approved as recommended.

Ayes: Jeffries, Spiegel, Washington, Perez and Hewitt  
Nays: None  
Absent: None  
Date: February 11, 2020  
xc: Transp.

Kecia R. Harper  
Clerk of the Board  
By:   
Deputy

**SUBMITTAL TO THE BOARD OF SUPERVISORS COUNTY OF RIVERSIDE,  
STATE OF CALIFORNIA**

<b>FINANCIAL DATA</b>	<b>Current Fiscal Year:</b>	<b>Next Fiscal Year:</b>	<b>Total Cost:</b>	<b>Ongoing Cost</b>
<b>COST</b>	\$ 0	\$ 0	\$ 0	\$ 0
<b>NET COUNTY COST</b>	\$ 0	\$ 0	\$ 0	\$ 0
<b>SOURCE OF FUNDS: N/A</b>			<b>Budget Adjustment:</b>	N/A
			<b>For Fiscal Year:</b>	19/20

**C.E.O. RECOMMENDATION:** Approve

**BACKGROUND:**

**Summary**

By Minute Order 3.52 of February 27, 2018, the Board of Supervisors entered into a contract with Sukut Construction, LLC. of Santa Ana, California for the construction of Clinton Keith Road, from Whitewood Road to Leon Road, in the Community of French Valley and the City of Murrieta. The original authorized amount of the contract was \$4,987,654. The total revised contract amount is \$4,792,246 which is 3.9% less than the original authorized amount. The reduction of the total contract price was primarily the result of a Value Engineering contract change order which provided a \$150,000 credit to the County for allowing the Contractor to combine the roadway construction for this project with the Clinton Keith Road Project Phase 2 project. Combining the work of the two projects provided cost and time saving to both the Contractor and the County.

The work was completed in conformance with the plans and specifications and the contractor was granted relief of maintenance on September 2, 2018.

Work Order Number B2-04274

**Impact on Residents and Businesses**

The 4 lane extension of Clinton Keith Road has provided an additional east-west connection between Interstate 15 and State Route 79, thus reducing traffic volumes on Los Alamos Road.

**Additional Fiscal Information**

**SUBMITTAL TO THE BOARD OF SUPERVISORS COUNTY OF RIVERSIDE,  
STATE OF CALIFORNIA**

**Budget**

Original Contract Amount		\$4,987,654
Total Change Orders Authorized	-3.0%	(\$150,000)
Estimated Pending Change Orders	0.0%	\$0
Authorized Contract Amount		\$4,837,654
* Quantity Adjustments	-0.9%	(\$45,408)
+ CCO FA Adjustments	0.0%	\$0
Total Amended Contract Amount	96.1%	<u>\$4,792,246</u>

**Expenditures**

Total Progress Payments		\$4,792,246
Estimated Pending Payments		<u>\$0</u>
Total Expenditures		<u>\$4,792,246</u>

**(Over)/Under Contract Amount** \$0

+ Change Orders using the Force Account method of payment issued prior to the work being completed generally do not use the total authorized amount.

\* CAL-Trans Standard Specifications 4-1.03B. Increases or decreases in the quantity of a contract item of work will be determined by comparing the total pay quantity of such item of work with the Engineer's Estimate. If the total pay quantity of any item of work required under the contract varies from the Engineer's Estimate by 25 percent or less, payment will be made for the quantity of work of said item performed at the contract unit price, unless eligible for adjustment pursuant to Section 4-1.03C, "Changes in Character of Work."

This project was funded with \$2,003,159 of RCTC Measure A – Discretionary funds and \$2,789,087 of CFD 07-2 Clinton Keith Road funds.

**Contract History and Price Reasonableness**

Three bids were received ranging from \$4,987,654 to \$5,597,324. The basis for the selection of a contractor is the lowest responsive and responsible bid. The lowest responsive and responsible bid was submitted by Sukut Construction, LLC, in the amount of \$4,987,654 which is \$350,000 (6.6%) lower than the Engineer's Estimate.

**ATTACHMENTS:**

- Change Order Report
- Vicinity Map
- Progress Estimate Report
- Notice of Completion

SUBMITTAL TO THE BOARD OF SUPERVISORS COUNTY OF RIVERSIDE,  
STATE OF CALIFORNIA



Jason Farin, Senior Management Analyst

2/4/2020



Gregory V. Priaplos, Director County Counsel


1/29/2020

COUNTY OF RIVERSIDE  
TRANSPORTATION DEPARTMENT

CLINTON KEITH ROAD CONSTRUCTION PROJECT – PHASE 4

FROM WHITEWOOD ROAD TO LEON ROAD  
IN THE CITY OF MURRIETA AND FRENCH VALLEY AREA

PROJECT No. B2-04724

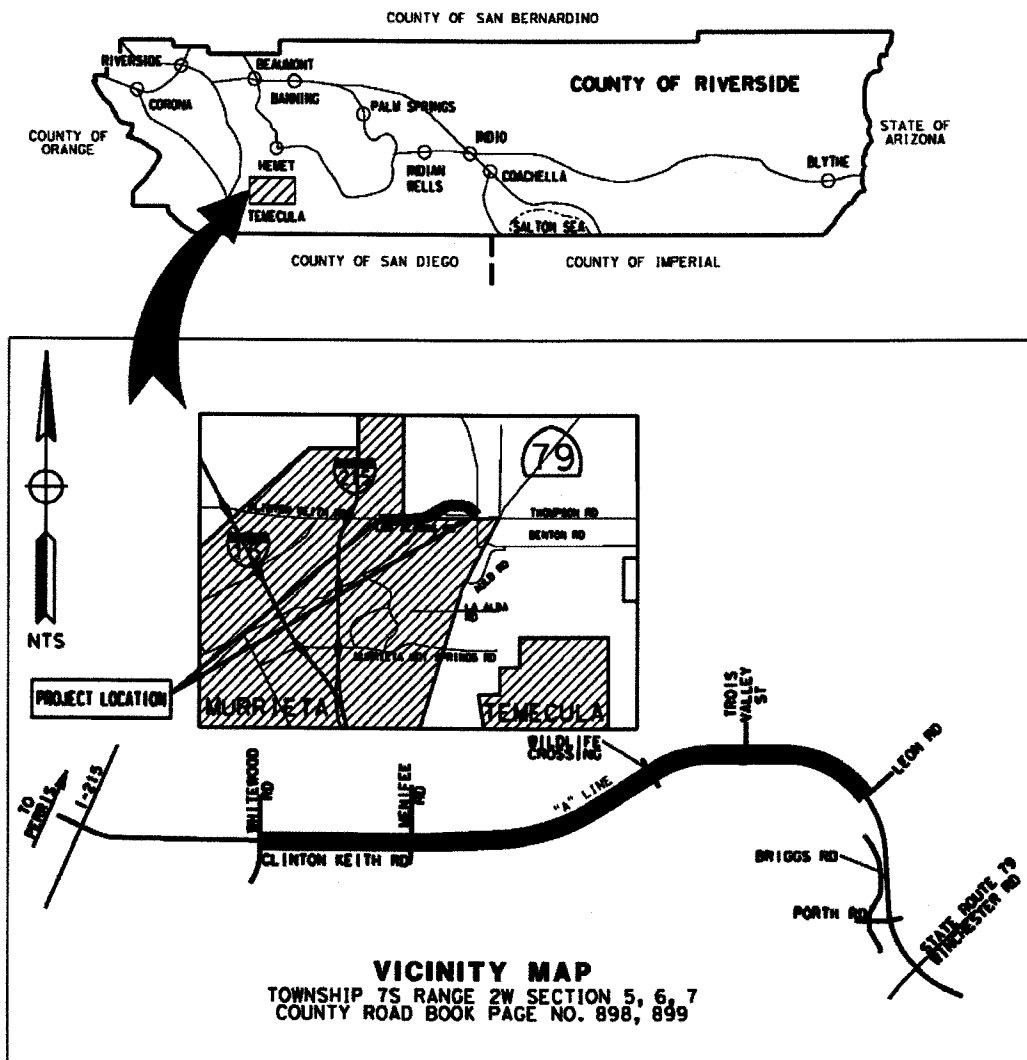

**CHANGE ORDER REPORT**  
**(Clinton Keith Road Construction Phase 4)**

<b>CCO #</b>	<b>Amount</b>	<b>Percent</b>	<b>Description</b>
	Original Contract Amount \$4,987,654		
1	(\$150,000)	(3.0%)	
Quantity Adjustments	(\$45,408)	(0.9%)	
Change Order Total and New Contract Total	\$4,792,246		

Item No.	Item Description	Units	Quantity	Unit Price	Original Contract Amount	Change Orders Quantity	Change Orders Amount	Amended Contract Quantity	Amended Contract Amount	This Estimate Quantity	This Estimate Amount	Previous Quantity	Previous Amount	Total Estimate To Date Quantity	Total Estimate To Date Amount	% Auth.
					4,987,654.00		(150,000.00)		4,837,654.00		185,908.07				4,792,246.48	
<b>PROJECT TOTAL</b>																

Contractor: Sultut Construction, LLC  
 Address: 4010 W Chandler Ave.  
 City, State, Zip: Santa Ana CA 92704

Working Days: 80  
 Days Added: 14  
 Subtotal: 94  
 Days Used: 94  
 % Time Elapsed: 100%

Start Date: 3-23-18  
 End Date: 8-3-18  
 % \$ Complete: 99%  
 Original Contract: \$4,987,654.00  
 Amended Contract: \$4,837,654.00

TOTAL VALUE OF WORK TO DATE: \$4,792,246.48  
 LESS RETENTION TO ESCROW: 2% 95,844.95  
 TOTAL DUE TO DATE: \$4,696,401.53  
 LESS PREVIOUSLY INVOICED: 4,376,021.47  
 RELEASE RETENTION FROM ESCROW 138,190.15  
 TOTAL DUE THIS PAYMENT: \$182,189.91

Made by: Eric Lohr  
 Checked by: [Signature] 9/10/19  
 OK Const. Supv. [Signature]

This Estimate Approved: [Signature]  
 Patricia Rorho, Director of Transportation  
 Date: 9/23/19

Received by Accounts Payable: \_\_\_\_\_  
 By: \_\_\_\_\_

Quantities on This Estimate Approved  
 [Signature]  
 Sultut Construction, LLC

**PAYMENT APPROVAL**  
 Fund 20000  
 Dept ID 31305  
 Account 527980

Project Z B2-04724E  
 Activity ID Z5500  
 Resource Type CNT  
 Signature [Signature]  
 Date 9/19/19

THANATOPICAL PROJECT  
 By Lon Conrad 8-3-18

SEP 23 2019

SEP 25 2019

459005

Item No.	Item Description	Units	Quantity	Unit Price	Original Contract Amount	Change Orders Quantity	Change Orders Amount	Amended Contract Quantity	Amended Contract Amount	This Estimate Quantity	This Estimate Amount	Previous Quantity	Total Estimate To Date Quantity	Total Estimate To Date Amount	% Auth.
1	OBTAIN ENCROACHMENT PERMIT	FA	1	5,000.00	5,000.00			1.00	5,000.00				1.00	5,000.00	0%
2	DUST ABATEMENT	LS	1	67,000.00	67,000.00			1.00	67,000.00			1.00	1.00	67,000.00	100%
3	PROGRESS SCHEDULE (CRITICAL PATH)	LS	1	10,000.00	10,000.00			1.00	10,000.00			1.00	1.00	10,000.00	100%
4	LEAD COMPLIANCE PLAN	LS	1	6,700.00	6,700.00			1.00	6,700.00						0%
5	CONSTRUCTION AREA SIGNS	LS	1	45,500.00	45,500.00			1.00	45,500.00			1.00	1.00	45,500.00	100%
6	PREPARE STORM WATER POLLUTION PREVENTION PLAN	LS	1	154,000.00	154,000.00			1.00	154,000.00			1.00	1.00	154,000.00	100%
7	REMOVE PAINTED TRAFFIC STRIPE	LF	7,913	0.85	6,726.05			7,913.00	6,726.05			5,368.00	5,368.00	4,562.80	68%
8	REMOVE PAINTED PAVEMENT MARKING	SQFT	1,104	1.50	1,656.00			1,104.00	1,656.00			705.00	705.00	1,057.50	64%
9	REMOVE ROADSIDE SIGN	EA	11	58.00	616.00			11.00	616.00			12.00	12.00	672.00	109%
10	RELOCATE ROADSIDE SIGN	EA	3	84.00	252.00			3.00	252.00			3.00	3.00	252.00	100%
11	CLEARING AND GRUBBING	LS	1	500.00	500.00			1.00	500.00			1.00	1.00	500.00	100%
12	DEVELOP WATER SUPPLY	LS	1	11,000.00	11,000.00			1.00	11,000.00			1.00	1.00	11,000.00	100%
13	COLD PLANE AND ASPHALT CONCRETE PAVEMENT	SQYD	4,510	7.70	34,727.00			4,510.00	34,727.00			3,966.00	3,966.00	30,538.20	88%
14	ROADWAY EXCAVATION	CY	13,310	24.05	320,105.50			13,310.00	320,105.50			13,310.00	13,310.00	320,105.50	100%
15	ROCK EXCAVATION	CY	5,000	7.98	39,900.00			5,000.00	39,900.00			5,000.00	5,000.00	39,900.00	100%
16	STRUCTURE BACKFILL (SLURRY CEMENT)	CY	45	120.00	5,400.00			45.00	5,400.00						0%
17	SUBGRADE ENHANCEMENT GEOTEXTILE (MULTI-AXIAL)	SQYD	19,680	6.55	128,904.00			19,680.00	128,904.00			23,707.00	23,707.00	155,280.85	120%
18	DECOMPOSED GRANITE (MISCELLANEOUS AREAS)	SQFT	100,711	3.65	367,595.15			100,711.00	367,595.15			84,738.00	84,738.00	309,293.70	84%
19	EROSION CONTROL (TYPE D)	SQFT	22,486	0.12	2,698.32			22,486.00	2,698.32						0%
20	HYDROSEED [WILDLIFE OVERCROSSING]	SQFT	137,692	0.16	22,030.72			137,692.00	22,030.72	63,818.00	10,210.88		63,818.00	10,210.88	46%
21	CLASS 2 AGGREGATE BASE	CY	5,250	40.00	210,000.00			5,250.00	210,000.00			6,343.00	6,343.00	253,720.00	121%
22	HOT MIX ASPHALT (TYPE C)	TON	3,990	80.00	319,200.00			3,990.00	319,200.00			4,193.00	4,193.00	335,440.00	105%
23	HOT MIX ASPHALT (TYPE A)	TON	12,779	92.00	1,175,668.00			12,779.00	1,175,668.00			12,472.00	12,472.00	1,147,424.00	98%



PROJECT: Clinton Keith Road Project Phase 4  
 County Project No.: B2-04724  
 Contract No. 18-03-002

Contractor: Sukut Construction, LLC  
 Address: 4010 W Chandler Ave.  
 City, State, Zip: Santa Ana CA 92704

Estimate No. 8 Final  
 From: March 26, 2019  
 To: July 25, 2019

Item No.	Item Description	Units	Quantity	Unit Price	Original Contract Amount	Change Orders Quantity	Change Orders Amount	Amended Contract Quantity	Amended Contract Amount	This Estimate Quantity	This Estimate Amount	Previous Quantity	Total Estimate To Date Quantity	Total Estimate To Date Amount	% Auth.
24	MINOR CONCRETE (MINOR STRUCTURE) (CONCRETE BANDING)	CY	190	360.00	68,400.00			190.00	68,400.00			190.00	190.00	68,400.00	100%
25	FURNISH SINGLE SHEET ALUMINUM SIGN (0.63" UNFRAMED)	SQFT	726	18.00	13,068.00			726.00	13,068.00			484.00	484.00	8,712.00	67%
26	ROADSIDE SIGN - ONE POST	EA	84	112.00	9,408.00			84.00	9,408.00			84.00	84.00	9,408.00	100%
27	INSTALL SIGN (STRAP AND SADDLE BRACKET METHOD)	EA	9	55.00	495.00			9.00	495.00			8.00	8.00	440.00	89%
28	18" REINFORCED CONCRETE PIPE (CLASS IV)	LF	80	425.00	34,000.00			80.00	34,000.00			90.60	90.60	38,505.00	113%
29	GRATED LINE DRAIN	LF	2,630	95.00	249,850.00			2,630.00	249,850.00			2,637.00	2,637.00	250,515.00	100%
30	MINOR CONCRETE (TYPE A-8 CURB) (CRS 201)	LF	3,438	33.00	113,454.00			3,438.00	113,454.00			3,787.00	3,787.00	124,971.00	110%
31	MINOR CONCRETE (TYPE "C" CURB) (CRS 202)(MOD)	LF	781	40.00	31,240.00			781.00	31,240.00			585.00	585.00	23,400.00	75%
32	MINOR CONCRETE (TYPE "D" CURB) (CRS 204)	LF	11,230	17.00	190,910.00			11,230.00	190,910.00			10,969.00	10,969.00	186,473.00	98%
33	DETECTABLE WARNING SURFACE	SQFT	20	81.00	1,620.00			20.00	1,620.00			24.00	24.00	1,944.00	120%
34	MINOR CONCRETE (MISCELLANEOUS CONSTRUCTION-PASSAGEWAY)	CY	1	2,160.00	2,160.00			1.00	2,160.00			1.00	1.00	2,160.00	100%
35	MINOR CONCRETE (ISLAND PAVING)	CY	58	618.00	35,844.00			58.00	35,844.00			666.85	666.85	313,419.50	93%
36	MINOR CONCRETE (SIDEWALK)	CY	714	470.00	335,580.00			714.00	335,580.00			28.00	28.00	95,200.00	104%
37	MINOR DRAINAGE STRUCTURE (TYPE G1 INLET)	EA	27	3,400.00	91,800.00			27.00	91,800.00			48,100.00	48,100.00	12,025.00	100%
38	MISCELLANEOUS IRON AND STEEL	LB	48,100	0.25	12,025.00			48,100.00	12,025.00			50.00	50.00	2,350.00	100%
39	MIDWEST GUARD RAIL SYSTEM	LF	50	47.00	2,350.00			50.00	2,350.00			1.00	1.00	907.00	0%
40	END ANCHOR ASSEMBLY (TYPE SFT)	EA	1	907.00	907.00			1.00	907.00			1.00	1.00	4,620.00	0%
41	SOFTSTOP IN-LINE TERMINAL SYSTEM	EA	1	4,620.00	4,620.00			1.00	4,620.00			3,852.00	3,852.00	258,084.00	102%
42	CONCRETE BARRIER (TYPE 60)	LF	3,780	67.00	253,260.00			3,780.00	253,260.00			45,316.00	45,316.00	20,392.20	101%
43	4" THERMOPLASTIC TRAFFIC STRIPE	LF	44,680	0.45	20,106.00			44,680.00	20,106.00			43,142.00	43,142.00	23,728.10	107%
44	6" THERMOPLASTIC TRAFFIC STRIPE	LF	40,195	0.55	22,107.25			40,195.00	22,107.25			4,441.00	4,441.00	2,886.65	100%
45	8" THERMOPLASTIC TRAFFIC STRIPE	LF	4,441	0.65	2,886.65			4,441.00	2,886.65			5,232.00	5,232.00	26,160.00	120%
46	THERMOPLASTIC CROSSWALK AND PAVEMENT MARKING	SQFT	4,347	5.00	21,735.00			4,347.00	21,735.00						

PROJECT: Clinton Keith Road Project Phase 4  
 County Project No.: B2-94724  
 Contract No.: 18-03-002

Contractor: Sukut Construction, LLC  
 Address: 4010 W Chandler Ave.  
 City, State, Zip: Santa Ana CA 92704

Estimate No. 8 Final  
 From: March 26, 2019  
 To: July 26, 2019

Item No.	Item Description	Units	Quantity	Unit Price	Original Contract		Change Orders		Amended Contract		This Estimate		Previous		Total Estimate To Date		% Auth
					Quantity	Amount	Quantity	Amount	Quantity	Amount	Quantity	Amount	Quantity	Amount	Quantity	Amount	
47	PAVEMENT MARKER (RETROREFLECTIVE)	EA	1,559	3.00	4,677.00			1,559.00	4,677.00			1,651.00	4,953.00	106%		4,953.00	106%
48	INDUCTIVE LOOP DETECTOR	EA	45	257.00	11,565.00			45.00	11,565.00			49.00	12,593.00	109%		12,593.00	109%
49	MOBILIZATION, DEMOBILIZATION AND FINAL CLEANUP	LS	1	179,157.36	179,157.36			1.00	179,157.36			1.00	179,157.36	100%		179,157.36	100%
50	MISCELLANEOUS WORK (AS DIRECTED)	FA	1	300,000.00	300,000.00			1.00	300,000.00	0.58565730	175,697.19	0.5523423	341,399.89	114%		341,399.89	114%
51	DELINEATOR (CLASS 1)	EA	8	50.00	400.00			8.00	400.00			10.00	500.00	125%		500.00	125%
52	CHANNELIZER (SURFACE MOUNTED)	EA	17	50.00	850.00			17.00	850.00			1.00	38,000.00	100%		38,000.00	100%
53	RESIDENT ENGINEERS OFFICE	LS	1	38,000.00	38,000.00			1.00	38,000.00			1.00	38,000.00	100%		38,000.00	100%
CCO 1	VALUED ENGINEERING	LS	0	1.00	0.00	-150,000.00	-150,000.00	-150,000.00	-150,000.00			-150,000.00	-150,000.00	100%		-150,000.00	100%





# COUNTY OF RIVERSIDE

Purchasing and Fleet Services Department  
2980 Washington St  
Riverside, CA 92504  
Phone: (951) 955-4937  
Fax: (951) 955-3730

## PURCHASE ORDER

### Vendor Instructions

1. Packaging Slip showing P.O. number and contents must accompany each shipment.
2. No charge for packaging or drayage will be allowed except when specified in order.
3. No partial billings except when specified in the order.
4. THIS ORDER EXPRESSLY LIMITS ACCEPTANCE TO THE TERMS OF THIS ORDER. ANY ADDITIONAL OR DIFFERENT TERMS PROPOSED BY THE SELLER ARE REJECTED UNLESS EXPRESSLY ASSENTED TO IN WRITING BY THE BUYER.
5. MAIL INVOICE TO THE ADDRESS SHOWN BELOW. SHOW PURCHASE ORDER NUMBER AND ORDERING DEPARTMENT.
6. Out of state vendors MUST show CA Board of Equilization Permit Number. Otherwise, sales tax will be deducted.
7. IMPORTANT: Seller shall provide material safety data sheets for each product containing hazardous substances as listed by CA Dir. Ind. Rel. in CA Adm. Code, Title 8, Section 5194 and labor codes
8. If work is to be carried out on county property, vendor shall call purchasing and ascertain amounts and types of insurance required and provide proof of insurance before beginning work

### TLMA AGENCY

County of Riverside  
TLMA Administration  
PO Box 1605  
Riverside CA 92502  
United States

Dispatch Via Email		
<b>Purchase Order</b> TLARC-0000098756	<b>Date</b> 2019-10-02	<b>Revision</b>
<b>Payment Terms</b> Net 30	<b>Freight Terms</b> FOB Destination, Freight Paid	<b>Ship Via</b> BEST WAY
<b>Buyer</b> Henry Robles	<b>Phone</b>	<b>Currency</b> USD

**Vendor:** 0000222131  
Sukut Construction LLC  
4010 W Chandler Ave  
Santa Ana CA 92704  
United States

**Ship To:** 6392-10830  
County of Riverside  
TLMA Administration  
PO Box 1605  
Riverside CA 92502  
United States

**Attention:** Not Specified

**Bill To:** County of Riverside  
TLMA Administration  
PO Box 1605  
Riverside CA 92502  
United States

Line-Sch	Item/Description	Mfg ID	Quantity	UOM	PO Price	Extended Amt	Due Date
----------	------------------	--------	----------	-----	----------	--------------	----------

1 - 1	CLINTON KEITH RD EXTENSION. PHASE 4 PROJECT BOS 2/27/2018 3.52 EST 8 FINAL		1.00	HR	182189.91	182189.91	11/16/2019
-------	--	--	------	----	-----------	-----------	------------

Contract ID: TLARC-91396-00046-06/19  
Total Amount: 0.000  
Total Quantity: 0.00

**Schedule Total** 182189.91  
Contract Line: 1 Release: 9  
Amount Open: 0.000  
Quantity Open: 0.0000

**Item Total TL91396-00046** 182189.91

CLINTON KEITH ROAD EXTENSION, PHASE 4 PROJECT, COMMUNITY OF FRENCH VALLEY AND CITY OF MURRIETA  
BOS APPROVAL 2/27/2018

THIS CONTRACT REPLACES CONTRACT # TLARC-91396-044-06/19

Maximum Amount: \$4,987,654.00  
Total Released Amount: \$4,128,545.71  
Remaining Amount: \$859,108.29

Added \$1,834,521.23 to this contract due to closing PO in old contract prior to encumbrance. Had to create new contract since vendor changed its TIN number.

\$859108.29 + 1,834,521.29 = \$2,693,629.40

**Total PO Amount** 182189.91

Authorized Signature

PLEASE COMPLETE THIS INFORMATION  
RECORDING REQUESTED BY:

**KECIA R. HARPER, CLERK OF THE BOARD  
RIVERSIDE CO. CLERK OF THE BOARD  
4080 LEMON STREET, 1<sup>ST</sup> FLOOR CAC  
P O BOX 1147 – RIVERSIDE, CA 92502**

**MAIL STOP # 1010**

AND WHEN RECORDED MAIL TO:

**RETURN TO: STOP #1010  
RIVERSIDE COUNTY CLERK OF THE BOARD  
P. O. BOX 1147 – RIVERSIDE, CA 92502**

**2020-0072056**

02/18/2020 12:41 PM Fee: \$ 0.00

Page 1 of 2

Recorded in Official Records  
County of Riverside  
Peter Aldana  
Assessor-County Clerk-Recorder



6080

THIS SPACE FOR RECORDERS USE ONLY

**NOTICE OF COMPLETION**

To be recorded with County Recorder  
within 10 days after completion.  
No recording fee.

Notice is hereby given by the undersigned owner, a public entity of the State of California, that a public work of improvement has been completed, as follows:

**Project title or description of work:** Clinton Keith Road Construction Project Phase 4, Project No. B2-04724

**Date of Completion:** Date Hereof 02/11/2020

**Nature of owner:** County of Riverside, public entity

**Interest or estate of owner:** Public Road Right-of-Way

**Address of owner:** Clerk of the Board of Supervisors, County Administrative Center  
4080 Lemon Street, 8th Floor, Riverside, CA 92501

**Name and Address of contractor:** Sukut Construction, LLC. 4010 W Chandler Avenue, Santa Ana, CA 92704

**Street or legal description of site:** Clinton Keith Road, from Whitewood Road to Leon Road, City of Murrieta and Community of French Valley

Dated: February 11, 2020

Owner: County of Riverside  
(Name of Public Entity)

By: V. Manuel Perez  
Chairman, Board of Supervisors  
V. Manuel Perez

STATE OF CALIFORNIA )

ss

COUNTY OF RIVERSIDE )

I am the Chairman of the governing board of the County of Riverside, the public entity which executed the foregoing notice and on whose behalf I make this verification; I have read this notice, know its contents, and the same is true. I certify under penalty of perjury that the foregoing is true and correct.

Executed at Riverside, California on 02/11/2020 (Date)

V. Manuel Perez, Chairman of the Board of Supervisors  
V. Manuel Perez

ATTEST:

KECIA R. HARPER, Clerk

[Signature]  
DEPUTY

FORM APPROVED COUNTY COUNSEL

BY [Signature] 02.11.2020 3.29  
KRISTINE BELL-VALDEZ 1/29/2022 DATE



**PETER ALDANA  
COUNTY OF RIVERSIDE  
ASSESSOR-COUNTY CLERK-RECORDER**

**Recorder**  
P.O. Box 751  
Riverside, CA 92502-0751  
(951) 486-7000

www.riversideacr.com

**CERTIFICATION**

Pursuant to the provisions of Government Code 27361.7, I certify under the penalty of perjury that the following is a true copy of illegible wording found in the attached document:

(Print or type the page number(s) and wording below):

CLARIFICATION FOR SEAL for the Riverside County Board of Supervisors  
(EMBOSSSED ON DOCUMENT)



Date:

2-11-2020

Signature:

Karen Barton

Print Name: Karen Barton, Deputy Clerk of the Board
