

SUBMITTAL TO THE BOARD OF SUPERVISORS
COUNTY OF RIVERSIDE, STATE OF CALIFORNIA



ITEM: 3.41
(ID # 11684)

MEETING DATE:
Tuesday, March 10, 2020

FROM : TLMA-TRANSPORTATION:

SUBJECT: TRANSPORTATION AND LAND MANAGEMENT AGENCY/TRANSPORTATION:
Notice of Completion – La Sierra Avenue Guardrail Reconstruction Project, in the Communities of Lake Hills and Lake Mathews; and Reche Vista Drive and Reche Canyon Road Guardrail Reconstruction Project, in the Community of Reche Canyon. Districts 1 and 5. [\$0]

RECOMMENDED MOTION: That the Board of Supervisors:

1. Accept as complete the La Sierra Avenue Guardrail Reconstruction Project, in the Communities of Lake Hills and Lake Mathews; and the Reche Vista Drive and Reche Canyon Road Guardrail Reconstruction Project, in the Community of Reche Canyon;
2. Authorize the Chairman of the Board to execute the Notice of Completion on behalf of the County; and
3. Direct the Clerk of the Board to record the Notice of Completion.

ACTION:Policy


Patricia Romo, Director of Transportation 2/8/2020

MINUTES OF THE BOARD OF SUPERVISORS

On motion of Supervisor Perez, seconded by Supervisor Hewitt and duly carried by unanimous vote, IT WAS ORDERED that the above matter is approved as recommended.

Ayes: Jeffries, Spiegel, Washington, Perez and Hewitt
Nays: None
Absent: None
Date: March 10, 2020
xc: Transp.

Kecia R. Harper
Clerk of the Board

By: 
Deputy

**SUBMITTAL TO THE BOARD OF SUPERVISORS COUNTY OF RIVERSIDE,
STATE OF CALIFORNIA**

FINANCIAL DATA	Current Fiscal Year:	Next Fiscal Year:	Total Cost:	Ongoing Cost
COST	\$ 0	\$ 0	\$ 0	\$ 0
NET COUNTY COST	\$ 0	\$ 0	\$ 0	\$ 0
SOURCE OF FUNDS: N/A			Budget Adjustment:	N/A
			For Fiscal Year:	19/20

C.E.O. RECOMMENDATION: Approve

BACKGROUND:

Summary

By Minute Order 3.46 of August 27, 2019, the Board of Supervisors entered into a contract with Alcorn Fence Company of Riverside, California for the construction of the La Sierra Avenue Guardrail Reconstruction Project in the Communities of Lake Hills and Lake Mathews; and the Reche Vista Drive and Reche Canyon Road Guardrail Reconstruction Project in the Community of Reche Canyon.

The original authorized amount of the contract was \$647,670. The total price of the contract came in at \$629,364.92 which is 4.1% less than the originally authorized amount. The reduction of the total cost was the result of using less quantities than anticipated to complete the work.

The work was completed in conformance with the plans and specifications and the contractor was granted relief of maintenance on November 8, 2019.

Project Number C7-0046, Federal Aid No. HSIPL-5956(264)

Impact on Residents and Businesses

The improvements enhance roadway safety within the project limits by providing a safety barrier intended to protect motorists who leave the roadway.

Additional Fiscal Information

**SUBMITTAL TO THE BOARD OF SUPERVISORS COUNTY OF RIVERSIDE,
STATE OF CALIFORNIA**

Budget

Original Contract Amount		\$647,670
Total Change Orders Authorized	1.3%	\$8,380
Estimated Pending Change Orders	0.0%	\$0
Authorized Contract Amount		\$656,050
* Quantity Adjustments	-4.1%	(\$26,685)
+ CCO FA Adjustments	0.0%	\$0
Total Amended Contract Amount	97.2%	\$629,365

Expenditures

Total Progress Payments		\$629,365
Estimated Pending Payments		\$0
Total Expenditures		\$629,365

(Over)/Under Contract Amount \$0

+ Change Orders using the Force Account method of payment issued prior to the work being completed generally do not use the total authorized amount.

* Caltrans Standard Specifications 9-1.06 (Changed Quantity Payment Adjustments). Increases or decreases in the quantity of a contract item of work will be determined by comparing the total pay quantity of such item of work with the Engineer's Estimate. If the total pay quantity of any item of work required under the contract varies from the Engineer's Estimate by 25 percent or less, payment will be made for the quantity of work of said item performed at the contract unit price, unless eligible for adjustment pursuant to Section 9-1.15, "Work-Character Changes."

This project was funded with HSIP Highway Safety Improvement Program funds.

Contract History and Price Reasonableness

Two bids were received on June 26, 2019 ranging from \$647,670 to \$739,014. The basis for the selection of a contractor is the lowest responsive and responsible bid. The lowest responsible bid was submitted by Alcorn Fence Company in the amount of \$647,670, which is \$134,729 (17%) lower than the Engineer's Estimate.

ATTACHMENTS:

- Change Order Report
- Vicinity Map
- Progress Estimate Report
- Notice of Completion

SUBMITTAL TO THE BOARD OF SUPERVISORS COUNTY OF RIVERSIDE,
STATE OF CALIFORNIA



Jason Farin, Senior Management Analyst

3/4/2020



Gregory V. Priamos, Director County Counsel

2/24/2020

PLEASE COMPLETE THIS INFORMATION
RECORDING REQUESTED BY:

**KECIA R. HARPER, CLERK OF THE BOARD
RIVERSIDE CO. CLERK OF THE BOARD
4080 LEMON STREET, 1ST FLOOR CAC
P O BOX 1147 – RIVERSIDE, CA 92502**

MAIL STOP # 1010

AND WHEN RECORDED MAIL TO:

**RETURN TO: STOP #1010
RIVERSIDE COUNTY CLERK OF THE BOARD
P. O. BOX 1147 – RIVERSIDE, CA 92502**

2020-0115697

03/12/2020 12:39 PM Fee: \$ 0.00

Page 1 of 2

Recorded in Official Records
County of Riverside
Peter Aldana
Assessor-County Clerk-Recorder



001

THIS SPACE FOR RECORDERS USE ONLY

NOTICE OF COMPLETION

To be recorded with County Recorder
within 10 days after completion.
No recording fee.

Notice is hereby given by the undersigned owner, a public entity of the State of California, that a public work of improvement has been completed, as follows:

Project title or description of work: La Sierra Avenue Guardrail Reconstruction Project and Reche Vista Drive and Reche Canyon Road Guardrail Reconstruction Project, Communities of Lake Hills, Lake Mathews and Reche Canyon, Project No. C7-0046, Federal Aid No. HSIPL-5956(264)

Date of Completion: Date Hereof 03/10/2020

Nature of owner: County of Riverside, public entity

Interest or estate of owner: Public Road Right-of-Way

Address of owner: Clerk of the Board of Supervisors, County Administrative Center
4080 Lemon Street, 8th Floor, Riverside, CA 92501

Name and Address of contractor: Alcorn Fence Company, 6445 Pedley Road, Riverside, CA 92509

Street or legal description of site: La Sierra Avenue, El Sobrante Road to Orchard View Lane and Reche Vista Drive and Reche Canyon Drive, Hill Court to 0.1 Mile North of Woodson Road

Dated: March 10, 2020

Owner: County of Riverside
(Name of Public Entity)

By: *V. Manuel Perez*
Chairman, Board of Supervisors
V. Manuel Perez



ATTEST:
KECIA R. HARPER, Clerk
[Signature]
DEPUTY

STATE OF CALIFORNIA)
 ss
COUNTY OF RIVERSIDE)

I am the Chairman of the governing board of the County of Riverside, the public entity which executed the foregoing notice and on whose behalf I make this verification; I have read this notice, know its contents, and the same is true. I certify under penalty of perjury that the foregoing is true and correct.

Executed at Riverside, California on 03/10/2020 (Date)

V. Manuel Perez, Chairman of the Board of Supervisors
V. Manuel Perez

03.10.2020 3.41 BY *Kristine Bell-Valdez* **APPROVED COUNTY COUNSEL**
DATE 2/19/20



**PETER ALDANA
COUNTY OF RIVERSIDE
ASSESSOR-COUNTY CLERK-RECORDER**

Recorder
P.O. Box 751
Riverside, CA 92502-0751
(951) 486-7000

www.riversideacr.com

CERTIFICATION

Pursuant to the provisions of Government Code 27361.7, I certify under the penalty of perjury that the following is a true copy of illegible wording found in the attached document:

(Print or type the page number(s) and wording below):

CLARIFICATION FOR SEAL for the Riverside County Board of Supervisors
(EMBOSSSED ON DOCUMENT)



Supervisors

Date:

3-10-2020

Signature:

Karen Barton

Print Name: Karen Barton, Deputy Clerk of the Board

COUNTY OF RIVERSIDE
TRANSPORTATION DEPARTMENT



**RECHE VISTA DR AND
RECHE CANYON RD**

GUARDRAIL RECONSTRUCTION
HILL CT TO 0.1 MILE NORTH OF WOODSON RD

COMMUNITY OF RECHE CANYON

WO No. C7-0046

FEDERAL AID No. HSIPL-5956 (264)

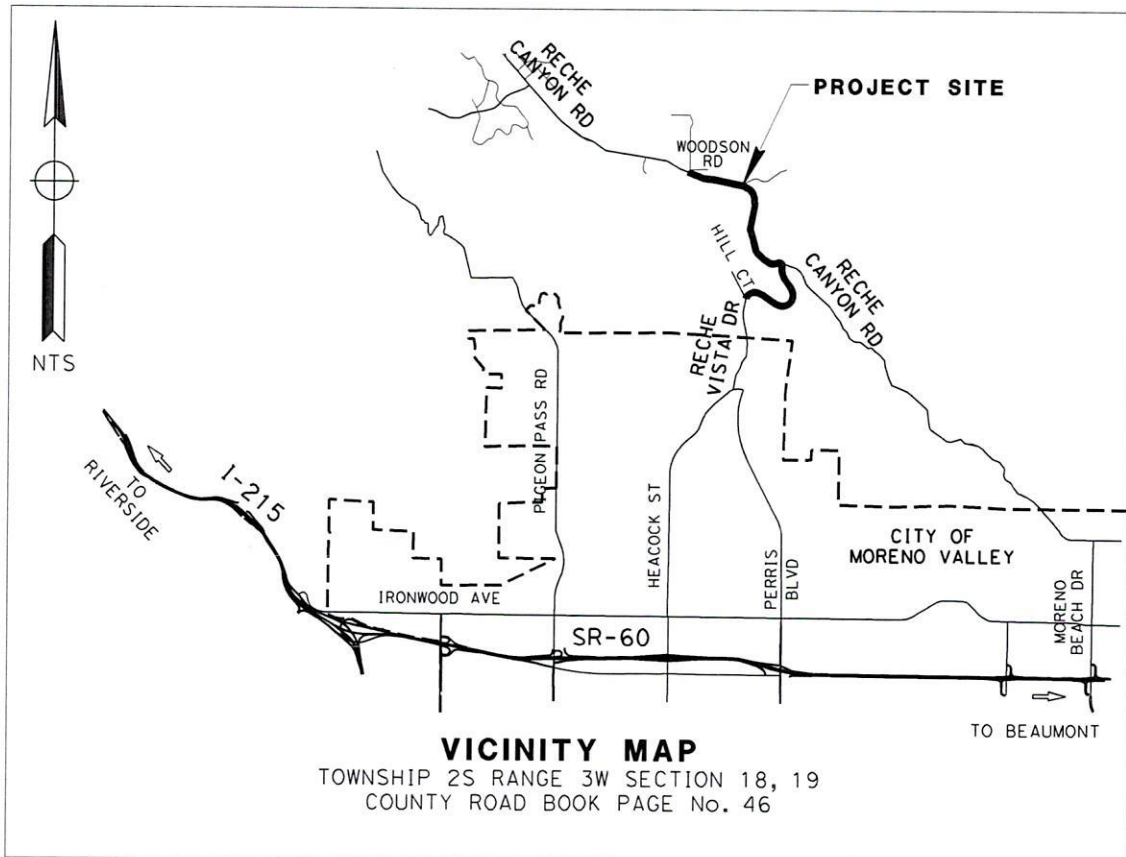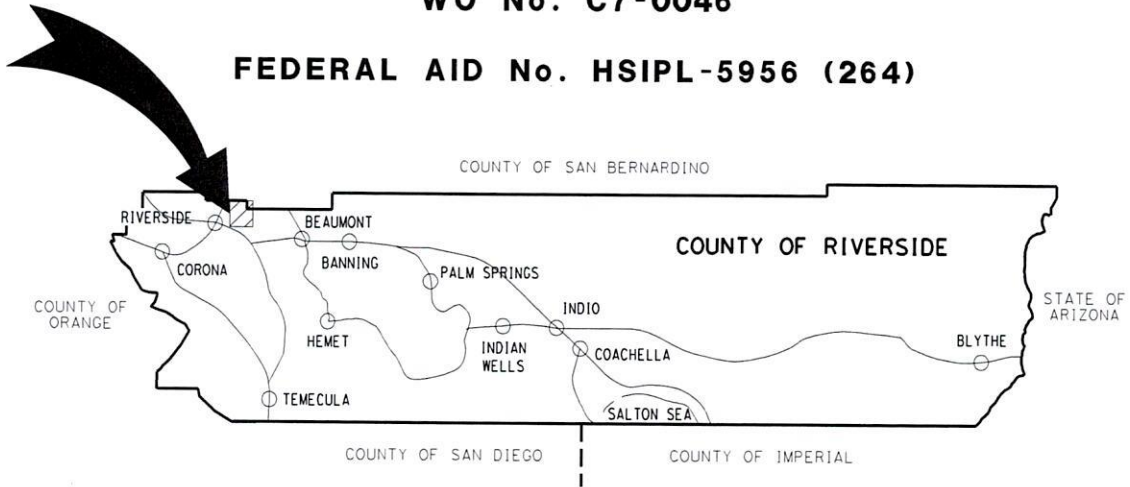

COUNTY OF RIVERSIDE
TRANSPORTATION DEPARTMENT



LA SIERRA AVE

GUARDRAIL RECONSTRUCTION
EL SOBRANTE RD TO ORCHARD VIEW LN

COMMUNITIES OF LAKE HILLS AND LAKE MATHEWS

WO No. C7-0046

FEDERAL AID No. HSIPL-5956 (264)

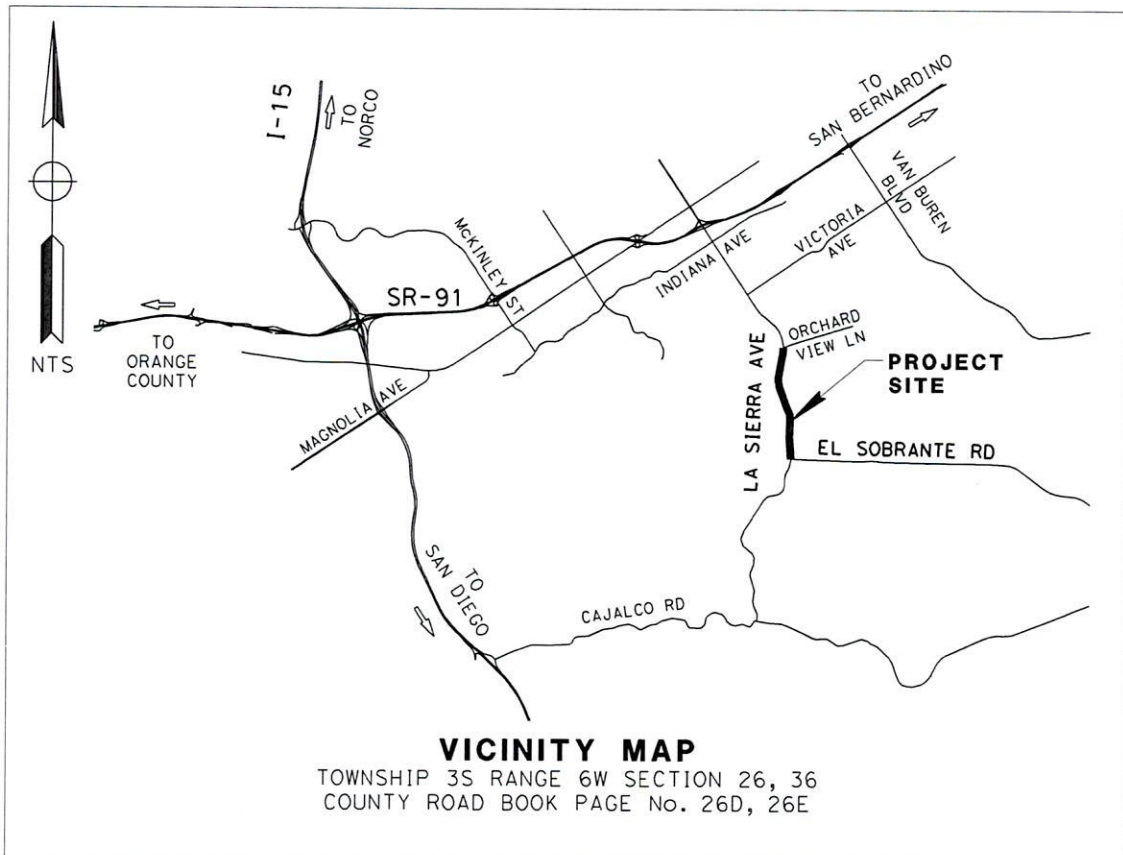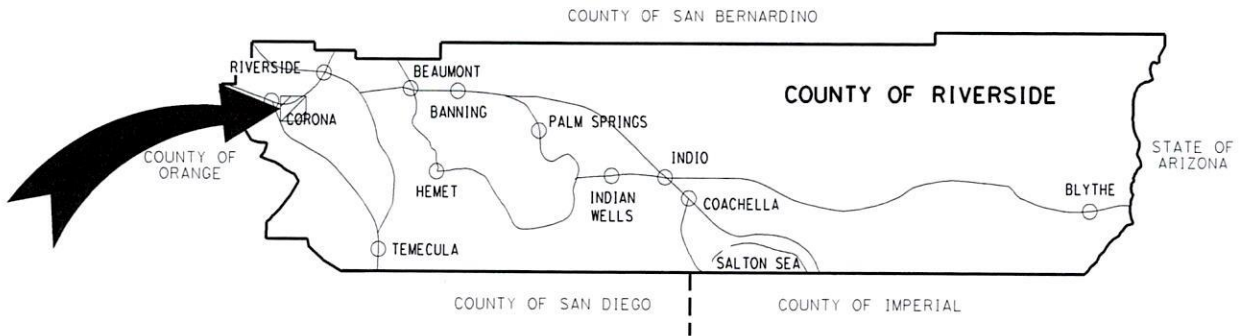



PROJECT: La Sierra Ave. Guardrail Reconstruction and Reche Vista Dr. and Reche Canyon Rd. Guardrail Reconstruction Projects
 County Project No.: C7-0046, HSPL-5956(264)
 Contract No. 19-07-008

Contractor: Alcorn Fence Company
 Address: 6445 Pedley Road
 City, State, Zip: Riverside, CA 92509

Estimate No. 2 Final
 From: October 26, 2019
 To: November 25, 2019

Item No.	Item Description	Units	Quantity	Unit Price	Original Contract Amount	Change Orders		Amended Contract		This Estimate		Previous Quantity	Total Estimate To Date		% Auth.
						Quantity	Amount	Quantity	Amount	Quantity	Amount		Quantity	Amount	
PROJECT TOTAL					647,670.48		8,380.00		656,050.48		284,742.35			629,364.92	

Made by: Paul Castillo/Andrew Potter

Checked by: DR

OK Const. Supv. [Signature]

Working Days: 30
 Days Added: 0
 Subtotal: 30
 Days Used: 19
 % Time Elapsed: 63%

Start Date: 10-15-19
 End Date: 11-8-19
 % Complete: 96%
 Original Contract: \$647,670.48
 Amended Contract: \$656,050.48

TOTAL VALUE OF WORK TO DATE: \$629,364.92
 LESS RETENTION: 0% 0.00
 TOTAL DUE TO DATE: \$629,364.92
 LESS PREVIOUSLY INVOICED: 327,391.44
 LESS LABOR NON COMPLIANCE: 0.00
 TOTAL DUE THIS PAYMENT: \$301,973.48

This Estimate Approved _____ Date: _____ for: \$301,973.48
 Patricia Romo, Director of Transportation

Received by Accounts Payable: _____
 By: _____

Quantities on This Estimate Approved [Signature] Date: 12.20.19
 Alcorn Fence Company

PAYMENT APPROVAL

Fund 20000
 Dept ID 31305
 Account 527980
 Project 207-0046G
 Activity ID 23500
 Resource Type CNT
 Signature [Signature]
 Date 12/31/19

TRANSFISCAL APPROVED
 By: Lori Conrad 5-3461
 JAN 09 2020

YG
12/31/19



PROGRESS ESTIMATE RECORD - COUNTY OF RIVERSIDE

PROJECT: La Sierra Ave. Guardrail Reconstruction and Reche Vista Dr. and Reche Canyon Rd. Guardrail Reconstruction Projects
 County Project No.: C7-0046, HSP/L-5956(264)
 Contract No. 19-07-008

Contractor: Alcorn Fence Company
 Address: 6445 Pedley Road
 City, State, Zip: Riverside, CA 92509

SHEET 1 of 2

Processed Construction Inspection 12/19/2019



Estimate No. 2 Final
 From: October 26, 2019
 To: November 25, 2019

Item No.	Item Description	Units	Quantity	Unit Price	Original Contract Amount	Change Orders		Amended Contract		This Estimate		Previous Quantity	Total Estimate To Date		% Auth.
						Quantity	Amount	Quantity	Amount	Quantity	Amount		Quantity	Amount	
1	DEVELOP WATER SUPPLY	LS	1	2,400.00	2,400.00			1.00	2,400.00	0.70	1,680.00	0.30	1.00	2,400.00	100%
2	TRAFFIC CONTROL SYSTEM	LS	1	131,990.00	131,990.00			1.00	131,990.00	0.70	92,393.00	0.30	1.00	131,990.00	100%
3	PREPARE WATER POLLUTION CONTROL PROGRAM	LS	1	5,500.00	5,500.00			1.00	5,500.00	0.70	3,850.00	0.30	1.00	5,500.00	100%
4	CLEARING AND GRUBBING	LS	1	16,260.00	16,260.00			1.00	16,260.00	0.70	11,382.00	0.30	1.00	16,260.00	100%
5	MOBILIZATION, DEMOBILIZATION, AND FINAL CLEANUP	LS	1	51,660.00	51,660.00			1.00	51,660.00	0.854820	44,160.00	0.15	1.00	51,660.00	100%
6	DUST ABATEMENT	LS	1	35,520.00	35,520.00			1.00	35,520.00	0.70	24,864.00	0.30	1.00	35,520.00	100%
7	PLACE ASPHALT CONCRETE DIKE (CRS 212) (6) "	LF	200	24.50	4,900.00			200.00	4,900.00						0%
8	RELOCATE MAILBOX	EA	4	977.50	3,910.00			4.00	3,910.00			4.00	4.00	3,910.00	100%
9	GUARD RAILING DELINEATOR	EA	300	16.73	5,019.00			300.00	5,019.00	242.00	4,048.66	107.00	349.00	5,838.77	116%
10	MIDWEST GUARDRAIL SYSTEM (STEEL POST)	LF	3,550	32.06	113,813.00			3,550.00	113,813.00	569.712414223	18,264.98	2,705.00	3,274.712414223	104,987.28	92%
11	MIDWEST GUARDRAIL SYSTEM (WOOD POST)	LF	3,800	28.18	107,084.00			3,800.00	107,084.00	748.00	21,078.64	2,814.00	3,562.00	100,377.16	94%
12	END ANCHOR ASSEMBLY (TYPE SFT)	EA	19	888.42	16,879.98			19.00	16,879.98	12.00	10,661.04	9.00	21.00	18,656.82	111%
13	ALTERNATIVE IN-LINE TERMINAL SYSTEM	EA	16	3,948.75	63,180.00			16.00	63,180.00	6.00	23,692.50	9.00	15.00	59,231.25	94%
14	ITEM DELETED PER ADDENDUM No. 1		0	0.00	0.00										N/A
15	REMOVE GUARDRAIL (WOOD POST)	LF	4,120	10.35	42,642.00			4,120.00	42,642.00	1,189.00	12,306.15	2,640.00	3,829.00	39,630.15	93%
16	REMOVE GUARDRAIL (STEEL POST)	LF	3,750	12.51	46,912.50			3,750.00	46,912.50	638.00	7,981.38	2,961.00	3,599.00	45,023.49	96%
CCO 1	PROJECT FUNDING SIGNS	LS	0	1.00	0.00	8,380.00	8,380.00	8,380.00	8,380.00	8,380.00	8,380.00		8,380.00	8,380.00	100%

La Sierra Ave./Reche Canyon Guardrails

	Total This Estimate
Total This Estimate	\$284,742.35
*Retention from Estimate 1	\$17,231.13
Total Due This Payment	\$301,973.48

*Release Retention - We don't hold retention for Federal Projects

CHANGE ORDER REPORT

(La Sierra Avenue Guardrail Project and Reche Vista Drive and Reche Canyon Road Guardrail Reconstruction Project)

CCO #	Amount	Percent	Description
	Original Contract Amount \$647,670		
1	\$8,380	1.29%	Furnish and install four (4) project funding signs.
Quantity Adjustments	(\$26,685)	(4.1%)	
Change Order Total and New Contract Total	\$629,365		
