

SUBMITTAL TO THE BOARD OF SUPERVISORS
COUNTY OF RIVERSIDE, STATE OF CALIFORNIA



ITEM: 3.31
(ID # 12162)

MEETING DATE:
Tuesday, April 21, 2020

FROM : TLMA-TRANSPORTATION:

SUBJECT: TRANSPORTATION AND LAND MANAGEMENT AGENCY/TRANSPORTATION:
Notice of Completion – De Portola Equestrian Crossings Improvements, in the
Community of Temecula Valley. District 3. [\$0]

RECOMMENDED MOTION: That the Board of Supervisors:

1. Accept as complete the De Portola Equestrian Crossings Improvements in the Community of Temecula Valley;
2. Authorize the Chairman of the Board to execute the Notice of Completion on behalf of the County; and
3. Direct the Clerk of the Board to record the Notice of Completion.

ACTION:Policy


Patricia Romo, Director of Transportation 3/18/2020

MINUTES OF THE BOARD OF SUPERVISORS

On motion of Supervisor Jeffries, seconded by Supervisor Washington and duly carried by unanimous vote, IT WAS ORDERED that the above matter is approved as recommended.

Ayes: Jeffries, Spiegel, Washington, Perez and Hewitt
Nays: None
Absent: None
Date: April 21, 2020
xc: Transp.

Kecia R. Harper
Clerk of the Board

By: 
Deputy

**SUBMITTAL TO THE BOARD OF SUPERVISORS COUNTY OF RIVERSIDE,
STATE OF CALIFORNIA**

FINANCIAL DATA	Current Fiscal Year:	Next Fiscal Year:	Total Cost:	Ongoing Cost
COST	\$ 0	\$ 0	\$ 0	\$ 0
NET COUNTY COST	\$ 0	\$ 0	\$ 0	\$ 0
SOURCE OF FUNDS: N/A			Budget Adjustment:	N/A
			For Fiscal Year:	19/20

C.E.O. RECOMMENDATION: Approve

BACKGROUND:

Summary

By Minute Order 3.20 of June 11, 2019, the Board of Supervisors entered into a contract with Global Road Sealing, Inc. of Garden Grove, California for the construction of De Portola Equestrian Crossings Improvements in the Community of Temecula Valley Wine Country.

The original authorized amount of the contract was \$240,345. The total price of the contract came in at \$217,356 which is 9.6% less than the originally authorized amount. The reduction of the total cost was the result of using less quantities than anticipated to complete the work.

The work was completed in conformance with the plans and specifications and the contractor was granted relief of maintenance on December 13, 2019.

Project Number C7-0036.

Impact on Residents and Businesses

The equestrian crossing improvements enhance safety and protect the community's equestrian rural lifestyle by providing signs, signals, and pavement markings that alert motorists to the presence of equestrian crossing.

Additional Fiscal Information

**SUBMITTAL TO THE BOARD OF SUPERVISORS COUNTY OF RIVERSIDE,
STATE OF CALIFORNIA**

Budget

Original Contract Amount		\$240,345
Total Change Orders Authorized	0.0%	\$0
Estimated Pending Change Orders	0.0%	\$0
Authorized Contract Amount		\$240,345
* Quantity Adjustments	-9.6%	(\$22,989)
+ CCO FA Adjustments	0.0%	\$0
Total Amended Contract Amount	90.4%	<u>\$217,356</u>

Expenditures

Total Progress Payments		\$217,356
Estimated Pending Payments		<u>\$0</u>
Total Expenditures		<u>\$217,356</u>

(Over)/Under Contract Amount \$0

+ Change Orders using the Force Account method of payment issued prior to the work being completed generally do not use the total authorized amount.

* Caltrans Standard Specifications 9-1.06 (Changed Quantity Payment Adjustments). Increases or decreases in the quantity of a contract item of work will be determined by comparing the total pay quantity of such item of work with the Engineer's Estimate. If the total pay quantity of any item of work required under the contract varies from the Engineer's Estimate by 25 percent or less, payment will be made for the quantity of work of said item performed at the contract unit price, unless eligible for adjustment pursuant to Section 9-1.15, "Work-Character Changes."



This project was funded with West County DIF Signal Mitigation fund.

Contract History and Price Reasonableness

Five bids were received on Wednesday, April 3, 2019 ranging from \$240,345 to \$280,335. The basis for the selection of a contractor is the lowest responsive and responsible bid. The lowest responsible bid was submitted by Global Road Sealing, Inc. in the amount of \$240,345, which is \$32,630 (12%) lower than the Engineer's Estimate.

ATTACHMENTS:



- Vicinity Map
- Progress Estimate Report
- Notice of Completion

		
Jason Farin, Senior Management Analyst	Gregory L. Priamos, Director County Counsel	
4/14/2020	3/27/2020	

COUNTY OF RIVERSIDE
TRANSPORTATION DEPARTMENT

DE PORTOLA ROAD

EQUESTRIAN CROSSING IMPROVEMENT PROJECT
TEMECULA VALLEY AREA
PROJECT No. C7-0036

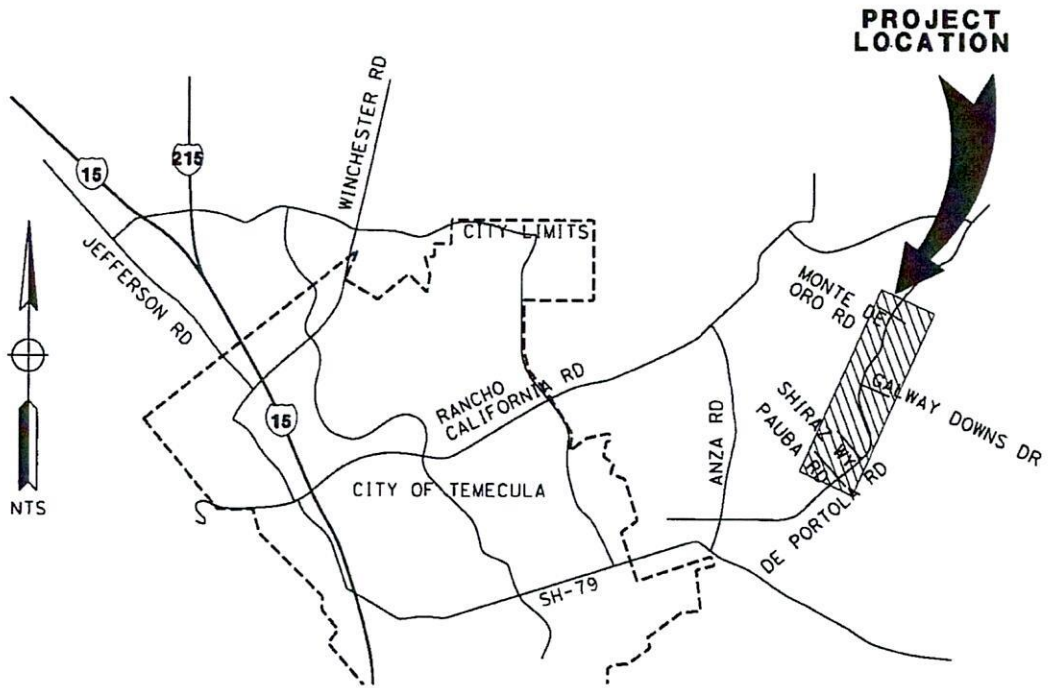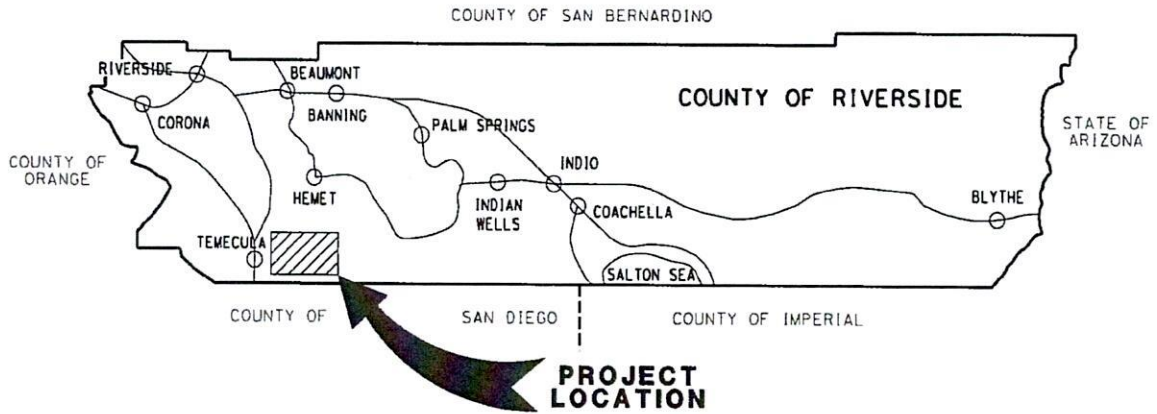

TOWNSHIP 6S RANGE 2W SECTION 30
COUNTY ROAD BOOK No. 121-B

VICINITY MAP

PROJECT: De Portola Road Equestrian Crossing Improvement Project Temecula Valley Area
 County Project No.: C7-0036
 Contract No. 19-05-004

Contractor: Global Road Sealing, Inc.
 Address: 10832 Dorothy Avenue
 City, State, Zip: Garden Grove, CA 92843



Estimate No. 4 Final
 From: December 26, 2019
 To: January 25, 2020

Item No.	Item Description	Units	Quantity	Unit Price	Original Contract Amount	Change Orders		Amended Contract		This Estimate		Previous Quantity	Total Estimate To Date		% Auth.
						Quantity	Amount	Quantity	Amount	Quantity	Amount		Quantity	Amount	
PROJECT TOTAL					240,345.00						3,100.00			217,355.85	

Made by: Ivan Mendoza
 Checked by: [Signature]
 OK Const. Supv. [Signature]

Working Days: 30
 Days Added: 0
 Subtotal: 30
 Days Used: 30
 % Time Elapsed: 100%

Start Date: 9-9-19
 End Date: 12-13-19
 % \$ Complete: 90%
 Original Contract: \$240,345.00
 Amended Contract: \$240,345.00

TOTAL VALUE OF WORK TO DATE: \$217,355.85
 LESS RETENTION: 5% 10,867.79
 TOTAL DUE TO DATE: \$206,488.06
 LESS PREVIOUSLY INVOICED: 203,543.06
 LESS LABOR NON COMPLIANCE: 0.00
 TOTAL DUE THIS PAYMENT: \$2,945.00

This Estimate Approved _____ Date: _____ for: \$2,945.00
 Patricia Romo, Director of Transportation

Received by Accounts Payable: _____
 By: _____

Quantities on This Estimate Approved [Signature] Date: 2-24-2020
 Global Road Sealing Inc.

PAYMENT APPROVAL

Fund 20000
 Dept ID 31305
 Account 5200007980
 Project 20700368E
 Activity ID 23500
 Resource Type CNT
 Signature [Signature]
 Date 3/4/20

PROGRESS ESTIMATE RECORD - COUNTY OF RIVERSIDE

SHEET 1 of 2

Processed Construction Inspection 2/5/2020

PROJECT: De Portola Road Equestrian Crossing Improvement Project Temecula Valley Area
 County Project No.: C7-0036
 Contract No. 19-05-004

Contractor: Global Road Sealing, Inc.
 Address: 10832 Dorothy Avenue
 City, State, Zip: Garden Grove, CA 92843



Estimate No. 4 Final
 From: December 26, 2019
 To: January 25, 2020

Item No.	Item Description	Units	Quantity	Unit Price	Original Contract Amount	Change Orders		Amended Contract		This Estimate		Previous Quantity	Total Estimate To Date		% Auth.
						Quantity	Amount	Quantity	Amount	Quantity	Amount		Quantity	Amount	
1	DUST CONTROL	LS	1	2,500.00	2,500.00			1.00	2,500.00			1.00	1.00	2,500.00	100%
2	DEVELOP WATER SUPPLY	LS	1	2,500.00	2,500.00			1.00	2,500.00			1.00	1.00	2,500.00	100%
3	TRAFFIC CONTROL SYSTEM	LS	1	7,000.00	7,000.00			1.00	7,000.00			1.00	1.00	7,000.00	100%
4	PREPARE WATER POLLUTION CONTROL PROGRAM	LS	1	3,000.00	3,000.00			1.00	3,000.00			1.00	1.00	3,000.00	100%
5	CLEARING AND GRUBBING [CONSTRUCTION NOTE 4 & 9]	LS	1	3,000.00	3,000.00			1.00	3,000.00			1.00	1.00	3,000.00	100%
6	STRUCTURE EXCAVATION (CULVERT) [CONSTRUCTION NOTE 1]	CY	50	150.00	7,500.00			50.00	7,500.00			50.00	50.00	7,500.00	100%
7	10" PLASTIC PIPE [HIGH DENSITY POLYETHYLENE PIPE]	LF	30	90.00	2,700.00			30.00	2,700.00			29.00	29.00	2,610.00	97%
8	24" PLASTIC PIPE [HIGH DENSITY POLYETHYLENE PIPE]	LF	230	140.00	32,200.00			230.00	32,200.00			211.00	211.00	29,540.00	92%
9	IMPORTED BORROW	CY	200	15.00	3,000.00			200.00	3,000.00			234.27	234.27	3,514.05	117%
10	STRUCTURE BACKFILL (SLURRY CEMENT)	CY	100	130.00	13,000.00			100.00	13,000.00			70.00	70.00	9,100.00	70%
11	REPLACE CONCRETE PAVEMENT	CY	15	280.00	4,200.00			15.00	4,200.00			5.00	5.00	1,400.00	33%
12	ROCK SLOPE PROTECTION (LIGHT, METHOD B)	CY	20	200.00	4,000.00			20.00	4,000.00			21.00	21.00	4,200.00	105%
13	FLASHING BEACON SYSTEM (SOLAR POWERED)	LS	1	126,750.00	126,750.00			1.00	126,750.00			1.00	1.00	126,750.00	100%
14	INSTALL SIGN (STRAP AND SADDLE BRACKET METHOD)	EA	12	130.00	1,560.00			12.00	1,560.00			13.00	13.00	1,690.00	108%
15	REMOVE ROADSIDE SIGN [AND POST]	EA	6	55.00	330.00			6.00	330.00			6.00	6.00	330.00	100%
16	RELOCATE ROADSIDE SIGN-ONE POST	EA	1	105.00	105.00			1.00	105.00			1.00	1.00	105.00	100%
17	PAINT TRAFFIC STRIPE (2-COAT)	LF	600	0.90	540.00			600.00	540.00			725.00	725.00	652.50	121%
18	THERMOPLASTIC PAVEMENT MARKING	SQFT	1,300	5.50	7,150.00			1,300.00	7,150.00			1,115.00	1,115.00	6,132.50	86%
19	REMOVE TRAFFIC STRIPE AND PAVEMENT MARKING	SQFT	1,650	1.40	2,310.00			1,650.00	2,310.00			1,237.00	1,237.00	1,731.80	75%
20	MOBILIZATION, DEMOBILIZATION, AND FINAL CLEANUP	LS	1	2,000.00	2,000.00			1.00	2,000.00	0.50	1,000.00	0.50	1.00	2,000.00	100%
21	MISCELLANEOUS WORK (AS DIRECTED)	FA	1	15,000.00	15,000.00			1.00	15,000.00	0.14	2,100.00		0.14	2,100.00	14%

PLEASE COMPLETE THIS INFORMATION
 RECORDING REQUESTED BY:

KECIA R. HARPER, CLERK OF THE BOARD
 RIVERSIDE CO. CLERK OF THE BOARD
 4080 LEMON STREET, 1ST FLOOR CAC
 P O BOX 1147 – RIVERSIDE, CA 92502

MAIL STOP # 1010

AND WHEN RECORDED MAIL TO:

RETURN TO: STOP #1010
RIVERSIDE COUNTY CLERK OF THE BOARD
P. O. BOX 1147 – RIVERSIDE, CA 92502

2020-0177822

04/23/2020 12:42 PM Fee: \$ 0.00

Page 1 of 2

Recorded in Official Records
 County of Riverside
 Peter Aidana
 Assessor-County Clerk-Recorder



782

THIS SPACE FOR RECORDERS USE ONLY

NOTICE OF COMPLETION

To be recorded with County Recorder
 within 10 days after completion.
 No recording fee.

Notice is hereby given by the undersigned owner, a public entity of the State of California, that a public work of improvement has been completed, as follows:

Project title or description of work: De Portola Road Equestrian Crossings Improvements, Project No. C7-0036

Date of Completion: Date Hereof 04/21/2020

Nature of owner: County of Riverside, public entity

Interest or estate of owner: Public Road Right-of-Way

Address of owner: Clerk of the Board of Supervisors, County Administrative Center
 4080 Lemon Street, 8th Floor, Riverside, CA 92501

Name and Address of contractor: Global Sealing, Inc., 10832 Dorothy Avenue, Garden Grove, CA 92843

Street or legal description of site: De Portola Road, from Shiraz Way 1,700 feet east of Pauba Road, at Galway Drive and at Monte De Oro Road, Community of Temecula Valley Wine Country

Dated: April 21, 2020

Owner: County of Riverside
 (Name of Public Entity)

By: V. Manuel Perez
 Chairman, Board of Supervisors
 V. Manuel Perez

STATE OF CALIFORNIA)
)
 COUNTY OF RIVERSIDE)

I am the Chairman of the governing board of the County of Riverside, the public entity which executed the foregoing notice and on whose behalf I make this verification; I have read this notice, know its contents, and the same is true. I certify under penalty of perjury that the foregoing is true and correct.

Executed at Riverside, California on 04/21/2020 (Date)

V. Manuel Perez, Chairman of the Board of Supervisors
 V. Manuel Perez

ATTEST:
 KECIA R. HARPER, Clerk
 By: Kristine Bell-Valdez
 DEPUTY

FORM APPROVED COUNTY COUNSEL
 BY Kristine Bell-Valdez 3/25/2020 DATE

04.21.2020 3.31



**PETER ALDANA
COUNTY OF RIVERSIDE
ASSESSOR-COUNTY CLERK-RECORDER**

Recorder
P.O. Box 751
Riverside, CA 92502-0751
(951) 486-7000

www.riversideacr.com

CERTIFICATION

Pursuant to the provisions of Government Code 27361.7, I certify under the penalty of perjury that the following is a true copy of illegible wording found in the attached document:

(Print or type the page number(s) and wording below):

CLARIFICATION FOR SEAL for the Riverside County Board of Supervisors
(EMBOSSSED ON DOCUMENT)



Date:

4-21-2020

Signature:

Karen Barton

Print Name: Karen Barton, Deputy Clerk of the Board
