

SUBMITTAL TO THE BOARD OF SUPERVISORS  
COUNTY OF RIVERSIDE, STATE OF CALIFORNIA



ITEM: 3.20  
(ID # 13114)

MEETING DATE:

Tuesday, October 20, 2020

FROM : TLMA-TRANSPORTATION:

SUBJECT: TRANSPORTATION AND LAND MANAGEMENT AGENCY/TRANSPORTATION:  
Notice of Completion – Whittier Avenue Resurfacing Project in the Community of  
East Hemet, District 3. [\$0]

RECOMMENDED MOTION: That the Board of Supervisors:

1. Accept as complete the Construction of Whittier Avenue Resurfacing Project in the Community of East Hemet;
2. Authorize the Chairman of the Board to execute the Notice of Completion on behalf of the County; and
3. Direct the Clerk of the Board to record the Notice of Completion.

ACTION: Policy

Patricia Romo, Director of Transportation 9/17/2020

---

MINUTES OF THE BOARD OF SUPERVISORS

On motion of Supervisor Hewitt, seconded by Supervisor Jeffries and duly carried by unanimous vote, IT WAS ORDERED that the above matter is approved as recommended.

Ayes: Jeffries, Spiegel, Washington, Perez and Hewitt  
Nays: None  
Abstain: None  
Date: October 20, 2020  
xc: Transp.

Kecia R. Harper  
Clerk of the Board  
By:   
Deputy

**SUBMITTAL TO THE BOARD OF SUPERVISORS COUNTY OF RIVERSIDE,  
STATE OF CALIFORNIA**

<b>FINANCIAL DATA</b>	<b>Current Fiscal Year:</b>	<b>Next Fiscal Year:</b>	<b>Total Cost:</b>	<b>Ongoing Cost</b>
<b>COST</b>	\$ 0	\$ 0	\$ 0	\$ 0
<b>NET COUNTY COST</b>	\$ 0	\$ 0	\$ 0	\$ 0
<b>SOURCE OF FUNDS:</b>			<b>Budget Adjustment:</b>	N/A
			<b>For Fiscal Year:</b>	20/21

**C.E.O. RECOMMENDATION:** Approve

**BACKGROUND:**

**Summary**

On October 1, 2019, agenda item 3.21, the Board of Supervisors entered into a contract with Hardy & Harper, Inc. of Lake Forest, California for the Whittier Avenue Resurfacing Project in the Community of East Hemet.

The original authorized amount of the contract was \$2,571,000. The total price of the contract came in at \$2,488,202 which is 3.2% less than the originally authorized amount. The reduction of the total cost was the result of using less quantities than anticipated to complete the work.

The work was completed in conformance with the plans and specifications and the contractor was granted relief of maintenance on March 18, 2020.

Project Number C5-0027.

**Impact on Residents and Businesses**

The project provides the public with a smooth paved roadway that has improved the safety and efficiency of vehicular traffic.

**Additional Fiscal Information**

<b>Budget</b>		
Original Contract Amount		\$2,571,000
Total Change Orders Authorized	0.0%	\$0
Estimated Pending Change Orders	0.0%	\$0
Authorized Contract Amount		\$2,571,000
* Quantity Adjustments	-3.2%	(\$82,798)
+ CCO FA Adjustments	0.0%	\$0
Total Amended Contract Amount	96.8%	\$2,488,202
<b>Expenditures</b>		
Total Progress Payments		\$2,488,202
Estimated Pending Payments		\$0
Total Expenditures		\$2,488,202
<b>(Over)/Under Contract Amount</b>		<u>\$0</u>

**SUBMITTAL TO THE BOARD OF SUPERVISORS COUNTY OF RIVERSIDE,  
STATE OF CALIFORNIA**

+ Change Orders using the Force Account method of payment issued prior to the work being completed generally do not use the total authorized amount.

\* Caltrans Standard Specifications 9-1.06 (Changed Quantity Payment Adjustments). Increases or decreases in the quantity of a contract item of work will be determined by comparing the total pay quantity of such item of work with the Engineer's Estimate. If the total pay quantity of any item of work required under the contract varies from the Engineer's Estimate by 25 percent or less, payment will be made for the quantity of work of said item performed at the contract unit price, unless eligible for adjustment pursuant to Section 9-1.15, "Work-Character Changes."

This project was funded with \$2,438,438 of Gas Tax funds and \$49,764 of City of Hemet.

**Contract History and Price Reasonableness**

Eight bids were received ranging from \$2,571,000 to \$3,540,700. The basis for the selection of a contractor is the lowest responsive and responsible bid. All received bids were responsive to the bidding requirements set forth for the project. The lowest responsible bid was submitted by Hardy & Harper, Inc. in the amount of \$2,571,000 which is \$44,690 (1.7%) below the Engineer's Estimate.

**ATTACHMENTS:**

Vicinity Map  
Progress Estimate Report  
Notice of Completion



Jason Farin, Principal Management Analyst 10/13/2020



Gregory E. Priarios, Director County Counsel 10/5/2020

PLEASE COMPLETE THIS INFORMATION  
RECORDING REQUESTED BY:

KECIA R. HARPER, CLERK OF THE BOARD  
RIVERSIDE CO. CLERK OF THE BOARD  
4080 LEMON STREET, 1<sup>ST</sup> FLOOR CAC  
P O BOX 1147 - RIVERSIDE, CA 92502

MAIL STOP # 1010

AND WHEN RECORDED MAIL TO:

RETURN TO: **STOP #1010**  
RIVERSIDE COUNTY CLERK OF THE BOARD  
P. O. BOX 1147 - RIVERSIDE, CA 92502

**2020-0512924**

10/23/2020 12:35 PM Fee: \$ 0.00

Page 1 of 1

Recorded in Official Records  
County of Riverside  
Peter Aldana  
Assessor-County Clerk-Recorder



THIS SPACE FOR RECORDERS USE ONLY *1628*

**NOTICE OF COMPLETION**

To be recorded with County Recorder  
within 10 days after completion.  
No recording fee.

Notice is hereby given by the undersigned owner, a public entity of the State of California, that a public work of improvement has been completed, as follows:

Project title or description of work: Whittier Ave. Resurfacing Project  
Project No. C5-0027

Date of Completion: Date Hereof **OCT 20 2020**

Nature of owner: County of Riverside, public entity

Interest or estate of owner: Public Road Right-of-Way

Address of owner: Clerk of the Board of Supervisors, County Administrative Center  
4080 Lemon Street, 8th Floor, Riverside, CA 92501

Name and Address of contractor: Hardy & Harper, Inc.,  
32 Rancho Circle, Lake Forest, CA 92630

Street or legal description of site: 200 Feet East of San Jacinto Street to 500 Feet East of Old Agency Road in  
the Community of East Hemet

Dated: **OCT 20 2020**

Owner: County of Riverside  
(Name of Public Entity)

By: *P. M. [Signature]*  
Chairman, Board of Supervisors

STATE OF CALIFORNIA )  
                                  )  
                                  ss  
COUNTY OF RIVERSIDE )

I am the Chairman of the governing board of the County of Riverside, the public entity which executed the foregoing notice and on whose behalf I make this verification; I have read this notice, know its contents, and the same is true. I certify under penalty of perjury that the foregoing is true and correct.

Executed at Riverside, California on **OCT 20 2020** (Date)

*P. M. [Signature]*, Chairman of the Board of Supervisors

BY *[Signature]* APPROVED COUNTY COUNSEL  
BY KRISTINE BELL-VALDEZ DATE 9/29/2020  
OCT 20 2020 **3.20**

ATTEST:  
**KECIA R. HARPER, Clerk**  
By *[Signature]*  
DEPUTY



COUNTY OF RIVERSIDE  
TRANSPORTATION DEPARTMENT

**Whittier Avenue  
Resurfacing Project**

**200 Feet East of San Jacinto Street  
to 500 Feet East of Old Agency Road**


**In the Community of East Hemet**

**Project No. C5-0027**

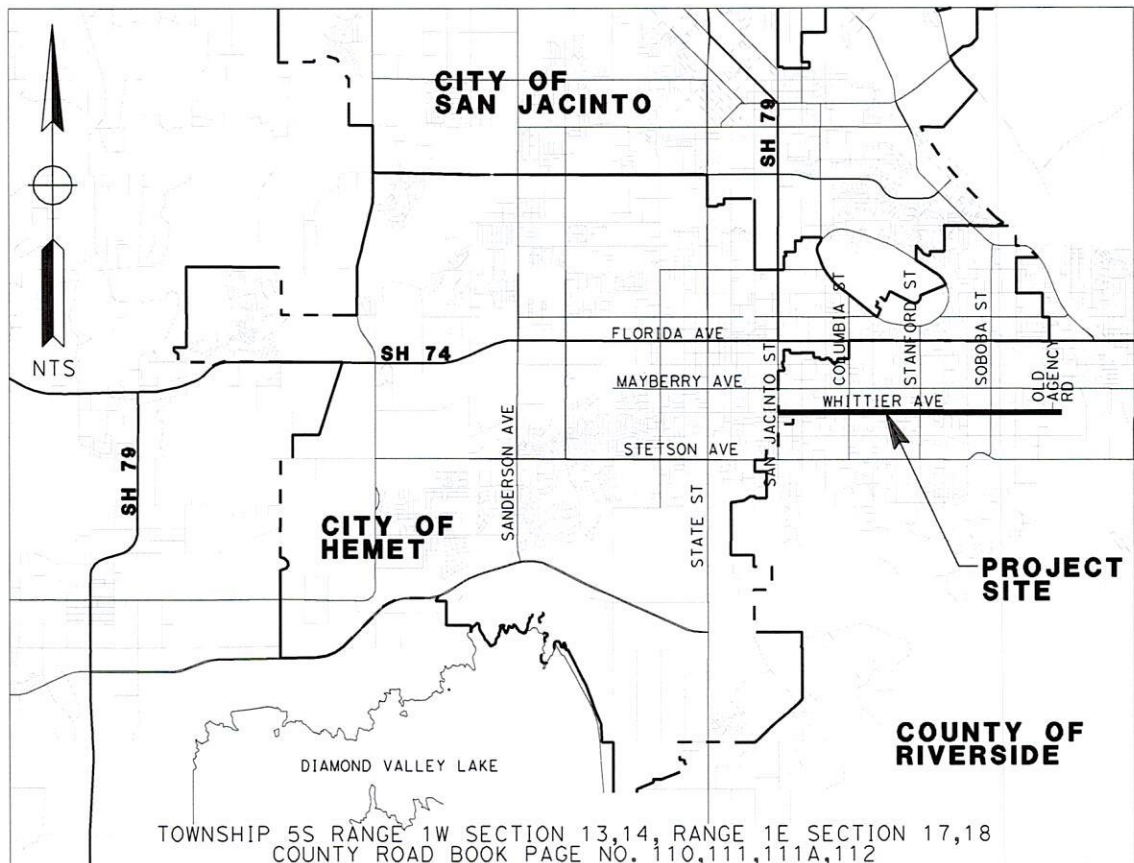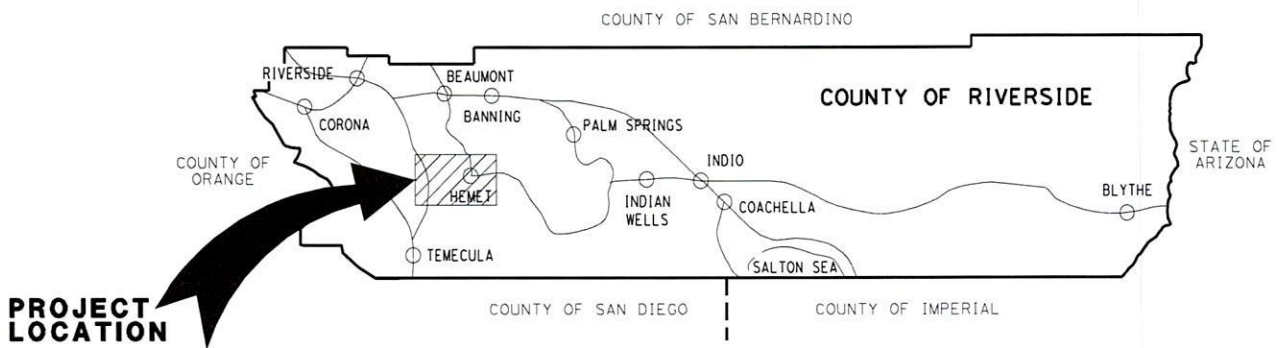

PROJECT: Whittier Avenue Resurfacing Project, 200 Feet East of San Jacinto Street to 800 Feet East of Old Agency Road in the Community of East Hemet  
 County Project No.: C5-0027  
 Contract No. 19-09-001

Contractor: Hardy & Harper, Inc.  
 Address: 32 Rancho Circle  
 City, State, Zip: Lake Forest, CA 92630



Estimate No. 6 Final  
 From: March 26, 2020  
 To: June 3, 2020

Item No.	Item Description	Units	Quantity	Unit Price	Original Contract Amount	Change Orders		Amended Contract		This Estimate		Previous Quantity	Total Estimate To Date		% Auth.
						Quantity	Amount	Quantity	Amount	Quantity	Amount		Quantity	Amount	
<b>PROJECT TOTAL</b>					2,571,000.00		0.00		2,571,000.00		135,712.76			2,488,202.44	

Made by: <u>George Saliba/Trai Nguyen</u>	Working Days: 60	Start Date: 11-13-19	TOTAL VALUE OF WORK TO DATE: \$2,488,202.44
Checked by: _____ TN _____	Days Added: 0	End Date: 3-18-20	LESS RETENTION: 5% 124,410.13
OK Const. Supv. _____ HD _____	Subtotal: 60	% \$ Complete: 97%	TOTAL DUE TO DATE: \$2,363,792.31
	Days Used: 60	Original Contract: \$2,571,000.00	LESS PREVIOUSLY INVOICED: 2,234,865.19
	% Time Elapsed: 100%	Amended Contract: \$2,571,000.00	LESS LABOR NON COMPLIANCE: 0.00
			TOTAL DUE THIS PAYMENT: \$128,927.12

This Estimate Approved \_\_\_\_\_ Date: \_\_\_\_\_ for: \$128,927.12  
 Patricia Romo, Director of Transportation

Quantities on This Estimate Approved *Anthony Lopez* Date: 6/23/2020  
 Hardy & Harper, Inc.

Received by Accounts Payable: \_\_\_\_\_  
By: \_\_\_\_\_

## Payment Approval

FUND: 20000

DEPT. ID.: 31305

ACCOUNT: 527980

PROJECT: ZC5-0027E

ACTIVITY ID.: Z3500

RESOURCE CNT

SIGNATURE: *Cindia Wachter*

DATE: 6/23/2020

PROJECT: Whittier Avenue Resurfacing Project, 200 Feet East of San Jacinto Street to 500 Feet East of Old Agency Road in the Community of East Hemet  
 County Project No.: CS-0027  
 Contract No. 19-09-001

Contractor: Hardy & Harper, Inc.  
 Address: 32 Rancho Circle  
 City, State, Zip: Lake Forest, CA 92630



Estimate No. 6 Final  
 From: March 26, 2020  
 To: June 3, 2020

Item No.	Item Description	Units	Quantity	Unit Price	Original Contract Amount	Change Orders		Amended Contract		This Estimate		Previous Quantity	Total Estimate To Date		% Auth.
						Quantity	Amount	Quantity	Amount	Quantity	Amount		Quantity	Amount	
1	DEVELOP WATER SUPPLY	LS	1	5,000.00	5,000.00			1.00	5,000.00			1.00	1.00	5,000.00	100%
2	TRAFFIC CONTROL SYSTEM	LS	1	75,000.00	75,000.00			1.00	75,000.00			1.00	1.00	75,000.00	100%
3	PREPARE STORM WATER POLLUTION PREVENTION PLAN	LS	1	5,000.00	5,000.00			1.00	5,000.00			1.00	1.00	5,000.00	100%
4	CLEARING AND GRUBBING	LS	1	15,000.00	15,000.00			1.00	15,000.00			1.00	1.00	15,000.00	100%
5	DUST ABATEMENT	LS	1	70,897.95	70,897.95			1.00	70,897.95			1.00	1.00	70,897.95	100%
6	ASPHALT CONCRETE ROLLED BERM	LF	2,240	5.54	12,409.60			2,240.00	12,409.60			2,007.00	2,007.00	11,118.78	90%
7	GRINDING ASPHALT CONCRETE IN PLACE	SQYD	16,900	1.10	18,590.00			16,900.00	18,590.00	1,308.00	1,438.80	16,578.44	17,886.44	19,675.08	108%
8	ROADWAY EXCAVATION	CY	5,190	32.00	166,080.00			5,190.00	166,080.00	226.22	7,239.04	5,012.97	5,239.19	167,654.08	101%
9	SHOULDER BACKING	LF	9,580	2.50	23,950.00			9,580.00	23,950.00			9,520.00	9,520.00	23,800.00	99%
10	PLACE ASPHALT CONCRETE DIKE (CRS 212) (6")	LF	2,590	5.54	14,348.80			2,590.00	14,348.80			3,237.50	3,237.50	17,935.75	125%
11	ASPHALT CONCRETE DRIVEWAY	SQFT	17,030	3.25	55,347.50			17,030.00	55,347.50	2,561.00	8,323.25	17,291.00	19,852.00	64,519.00	117%
12	HOT MIX ASPHALT (TYPE A)	TON	10,150	74.00	751,100.00			10,150.00	751,100.00			9,132.15	9,132.15	675,779.10	90%
13	RUBBERIZED HOT MIX ASPHALT (GAP GRADED)	TON	6,040	95.00	573,800.00			6,040.00	573,800.00			6,745.19	6,745.19	640,793.05	112%
14	PLACE HOT MIX ASPHALT DIKE (TYPE E)	LF	1,340	5.54	7,423.60			1,340.00	7,423.60	529.00	2,930.66	1,146.00	1,675.00	9,279.50	125%
15	ADJUST MANHOLE	EA	29	919.00	26,651.00			29.00	26,651.00			31.00	31.00	28,469.00	107%
16	MINOR CONCRETE (CURB AND GUTTER) (CRS 200)	LF	1,500	65.00	97,500.00			1,500.00	97,500.00			1,875.00	1,875.00	121,875.00	125%
17	MINOR CONCRETE (DRIVEWAY APPROACH) (CRS 207)	SQFT	250	12.00	3,000.00			250.00	3,000.00			250.00	250.00	3,000.00	100%
18	MINOR CONCRETE (CURB RAMP) (CRS 403 - CASE A)	EA	6	4,500.00	27,000.00			6.00	27,000.00			5.00	5.00	22,500.00	83%
19	MINOR CONCRETE (CURB RAMP) (CRS 403 - CASE B)	EA	3	4,000.00	12,000.00			3.00	12,000.00			1.00	1.00	4,000.00	33%
20	MINOR CONCRETE (CROSS-GUTTER AND SPANDREL)	SQFT	21,430	14.00	300,020.00			21,430.00	300,020.00	655.00	9,170.00	20,888.33	21,543.33	301,606.62	101%
21	MINOR CONCRETE (DRIVEWAY)	SQFT	1,667	12.00	20,004.00			1,667.00	20,004.00			2,083.75	2,083.75	25,005.00	125%
22	MINOR CONCRETE (SIDEWALK)	SQFT	800	12.00	9,600.00			800.00	9,600.00	25.00	300.00		25.00	300.00	3%
23	RELOCATE MAILBOX	EA	3	500.00	1,500.00			3.00	1,500.00	3.00	1,500.00		3.00	1,500.00	100%
24	PAVEMENT MARKER (RETROREFLECTIVE)	EA	1,070	5.25	5,617.50			1,070.00	5,617.50	34.00	178.50	924.00	958.00	5,029.50	90%

PROJECT: Whittier Avenue Resurfacing Project, 200 Feet East of San Jacinto Street to 500 Feet East of Old Agency Road in the Community of East Hemet  
 County Project No.: CS-0027  
 Contract No. 19-09-001

Contractor: Hardy & Harper, Inc.  
 Address: 32 Rancho Circle  
 City, State, Zip: Lake Forest, CA 92630



Estimate No. 6 Final  
 From: March 26, 2020  
 To: June 3, 2020

Item No.	Item Description	Units	Quantity	Unit Price	Original Contract Amount	Change Orders		Amended Contract		This Estimate		Previous Quantity	Total Estimate To Date		% Auth.
						Quantity	Amount	Quantity	Amount	Quantity	Amount		Quantity	Amount	
25	SALVAGE ROADSIDE SIGN	EA	35	36.75	1,286.25			35.00	1,286.25	35.00	1,286.25		35.00	1,286.25	100%
26	ROADSIDE SIGN - ONE POST	EA	44	341.00	15,004.00			44.00	15,004.00	51.00	17,391.00		51.00	17,391.00	118%
27	THERMOPLASTIC PAVEMENT MARKING	SQFT	2,820	4.50	12,690.00			2,820.00	12,690.00	2,415.00	10,867.50		2,415.00	10,867.50	86%
28	PAINT TRAFFIC STRIPE (2-COAT)	LF	18,190	0.53	9,640.70			18,190.00	9,640.70	310.00	164.30	16,865.00	17,175.00	9,102.75	94%
28	REMOVE THERMOPLASTIC PAVEMENT MARKING	SQFT	760	3.70	2,812.00			760.00	2,812.00			760.00	760.00	2,812.00	100%
30	MISCELLANEOUS WORK (AS DIRECTED)	FA	1	180,000.00	180,000.00			1.00	180,000.00	0.4162414667	74,923.46	0.0511487	0.4673901667	84,130.23	47%
31	TRAFFIC CONTROL SYSTEM	LS	1	5,000.00	5,000.00			1.00	5,000.00			1.00	1.00	5,000.00	100%
32	ROADWAY EXCAVATION	CY	190	32.00	6,080.00			190.00	6,080.00			194.00	194.00	6,208.00	102%
33	HOT MIX ASPHALT (TYPE A)	TON	260	74.00	19,240.00			260.00	19,240.00			260.00	260.00	19,240.00	100%
34	RUBBERIZED HOT MIX ASPHALT (GAP GRADED)	TON	160	95.00	15,200.00			160.00	15,200.00			160.00	160.00	15,200.00	100%
35	ADJUST MANHOLE	EA	2	919.00	1,838.00			2.00	1,838.00			2.00	2.00	1,838.00	100%
36	PAVEMENT MARKER (RETROREFLECTIVE)	EA	34	5.25	178.50			34.00	178.50			34.00	34.00	178.50	100%
37	PAINT TRAFFIC STRIPE (2-COAT)	LF	360	0.53	190.80			360.00	190.80			360.00	360.00	190.80	100%
38	MISCELLANEOUS WORK (AS DIRECTED)	FA	1	5,000.00	5,000.00			1.00	5,000.00						0%
