

SUBMITTAL TO THE BOARD OF SUPERVISORS
COUNTY OF RIVERSIDE, STATE OF CALIFORNIA



ITEM: 3.26
(ID # 13459)

MEETING DATE:
Tuesday, December 08, 2020

FROM : TLMA-TRANSPORTATION:

SUBJECT: TRANSPORTATION AND LAND MANAGEMENT AGENCY/TRANSPORTATION:
Notice of Completion – Datil Road and Sierra Del Sol Avenue Resurfacing
Projects, in the Community of Thousand Palms. District 4. [\$0]

RECOMMENDED MOTION: That the Board of Supervisors:

1. Accept as complete, the Construction of Datil Road and Sierra Del Sol Avenue Resurfacing Projects, in the Community of Thousand Palms, Districts 4;
2. Authorize the Chairman of the Board to execute the Notice of Completion on behalf of the County; and
3. Direct the Clerk of the Board to record the Notice of Completion.


ACTION:Policy


Patricia Romo, Director of Transportation 10/19/2020

MINUTES OF THE BOARD OF SUPERVISORS

On motion of Supervisor Spiegel, seconded by Supervisor Perez and duly carried by unanimous vote, IT WAS ORDERED that the above matter is approved as recommended.

Ayes: Jeffries, Spiegel, Washington, Perez and Hewitt
Nays: None
Absent: None
Date: December 8, 2020
xc: Transp., Record

Kecia R. Harper
Clerk of the Board
By: 
Deputy

**SUBMITTAL TO THE BOARD OF SUPERVISORS COUNTY OF RIVERSIDE,
STATE OF CALIFORNIA**

FINANCIAL DATA	Current Fiscal Year:	Next Fiscal Year:	Total Cost:	Ongoing Cost
COST	\$ 0	\$ 0	\$ 0	\$ 0
NET COUNTY COST	\$ 0	\$ 0	\$ 0	\$ 0
SOURCE OF FUNDS: NA.			Budget Adjustment:	N/A
			For Fiscal Year:	20/21

C.E.O. RECOMMENDATION: Approve

BACKGROUND:

Summary

By Minute Order 3.35 of May 5, 2020, the Board of Supervisors entered into a contract with Hardy & Harper, Inc. of Lake Forest, California for the resurfacing of Datil Road, from Thelma Avenue to San Miguelito Drive and Sierra Del Sol Resurfacing, from Ramon Road to La Canada Way, in the Community of Thousand Palms.

The original authorized amount of the contract was \$650,000. The total price of the contract was \$572,490, which is 11.9% less than the originally authorized amount. The reduction of the total cost was the result of using less quantities than anticipated to complete the work.

The work was completed in conformance with the plans and specifications and the contractor was granted relief of maintenance on July 2, 2020.

Datil Road, C9-0053
Sierra Del Sol, C9-0054

Impact on Residents and Businesses

The improvements have provided the public with a smooth paved roadway that has, Improving the safety and efficiency of vehicular traffic.

Additional Fiscal Information

**SUBMITTAL TO THE BOARD OF SUPERVISORS COUNTY OF RIVERSIDE,
STATE OF CALIFORNIA**

Budget

Original Contract Amount		\$650,000
Total Change Orders Authorized	0.0%	\$0
Estimated Pending Change Orders	0.0%	\$0
Authorized Contract Amount		\$650,000
* Quantity Adjustments	-11.9%	(\$77,510)
+ CCO FA Adjustments	0.0%	\$0
Total Amended Contract Amount	88.1%	\$572,490

Expenditures

Total Progress Payments		\$572,490
Estimated Pending Payments		\$0
Total Expenditures		\$572,490

(Over)/Under Contract Amount \$0

+ Change Orders using the Force Account method of payment issued prior to the work being completed generally do not use the total authorized amount.

* Caltrans Standard Specifications 9-1.06 (Changed Quantity Payment Adjustments). Increases or decreases in the quantity of a contract item of work will be determined by comparing the total pay quantity of such item of work with the Engineer's Estimate. If the total pay quantity of any item of work required under the contract varies from the Engineer's Estimate by 25 percent or less, payment will be made for the quantity of work of said item performed at the contract unit price, unless eligible for adjustment pursuant to Section 9-1.15, "Work-Character Changes."

This project was funded with \$572,490 of Gas Tax/SB1 funds.

Contract History and Price Reasonableness

Nine bids were received, ranging from \$650,000 to \$857,368. The basis for the selection of a contractor is the lowest responsive and responsible bid. The lowest responsible bid was submitted by Hardy & Harper, Inc. in the amount of \$650,000, which is \$200,285 (23.5%) lower than the Engineer's Estimate.

ATTACHMENTS:

- Vicinity Map
- Progress Estimate Report
- Notice of Completion


Jason Farin, Principal Management Analyst 11/30/2020


Gregory V. Priamos, Director County Counsel 11/5/2020

PLEASE COMPLETE THIS INFORMATION
RECORDING REQUESTED BY:

KECIA R. HARPER, CLERK OF THE BOARD
RIVERSIDE CO. CLERK OF THE BOARD
4080 LEMON STREET, 1ST FLOOR CAC
P O BOX 1147 – RIVERSIDE, CA 92502

MAIL STOP # 1010

AND WHEN RECORDED MAIL TO:

RETURN TO: **STOP #1010**
RIVERSIDE COUNTY CLERK OF THE BOARD
P. O. BOX 1147 – RIVERSIDE, CA 92502

2020-0631226

12/11/2020 03:09 PM Fee: \$ 0.00

Page 1 of 2

Recorded in Official Records
County of Riverside
Peter Aldana
Assessor-County Clerk-Recorder



6080

THIS SPACE FOR RECORDERS USE ONLY

NOTICE OF COMPLETION

To be recorded with County Recorder
within 10 days after completion.
No recording fee.

Notice is hereby given by the undersigned owner, a public entity of the State of California, that a public work of improvement has been completed, as follows:

Project title or description of work: Datil Road Resurfacing Project and Sierra Del Sol Avenue Resurfacing Project, Project Nos. C9-0053 and C9-0054

Date of Completion: Date Hereof **DEC 08 2020**

Nature of owner: County of Riverside, public entity

Interest or estate of owner: Public Road Right-of-Way

Address of owner: Clerk of the Board of Supervisors, County Administrative Center
4080 Lemon Street, 8th Floor, Riverside, CA 92501

Name and Address of contractor: Hardy & Harper, Inc., 32 Rancho Circle, Lake Forest, CA 92630

Street or legal description of site: Datil Road, from Thelma Avenue to San Miguelito Drive and Sierra Del Sol, from Ramon Road to La Canada Way

Dated: **DEC 08 2020**

Owner: County of Riverside
(Name of Public Entity)

By: *V. M. Perez*
Chairman, Board of Supervisors

STATE OF CALIFORNIA)
 ss
COUNTY OF RIVERSIDE)

I am the Chairman of the governing board of the County of Riverside, the public entity which executed the foregoing notice and on whose behalf I make this verification; I have read this notice, know its contents, and the same is true. I certify under penalty of perjury that the foregoing is true and correct.

Executed at Riverside California on **DEC 08 2020** (Date)

V. M. Perez, Chairman of the Board of Supervisors
V. Manuel Perez

FORM APPROVED COUNTY COUNSEL
BY *Kristine Bell-Valdez* 11/4/2020
KRISTINE BELL-VALDEZ DATE

ATTEST:
KECIA R. HARPER, Clerk
By *Paisella Ross*
DEPUTY

DEC 08 2020 3.26

**PETER ALDANA
COUNTY OF RIVERSIDE
ASSESSOR-COUNTY CLERK-RECORDER**

Recorder
P.O. Box 751
Riverside, CA 92502-0751
(951) 486-7000

www.riversideacr.com

CERTIFICATION

Pursuant to the provisions of Government Code 27361.7, I certify under the penalty of perjury that the following is a true copy of illegible wording found in the attached document:

(Print or type the page number(s) and wording below):

CLARIFICATION FOR SEAL for the Riverside County Board of Supervisors
(EMBOSSSED ON DOCUMENT)



Date:

December 8, 2020



Signature:

Priscilla Rasso

Print Name: Priscilla Rasso, Board Assistant

COUNTY OF RIVERSIDE
TRANSPORTATION DEPARTMENT

**Datil Road Resurfacing Project
Thelma Avenue to San Miguelito Drive, and
Sierra Del Sol Resurfacing Project
Ramon Road to La Canada Way
Community of Thousand Palms
Project No. C9-0053, C9-0054**

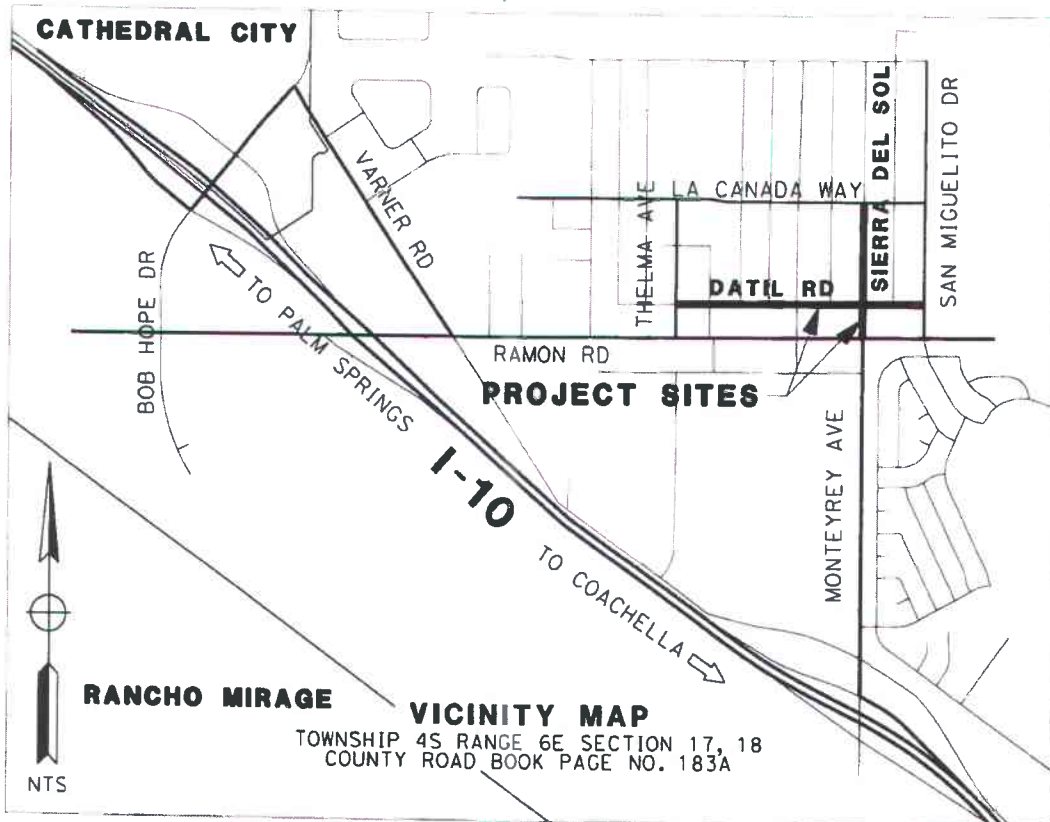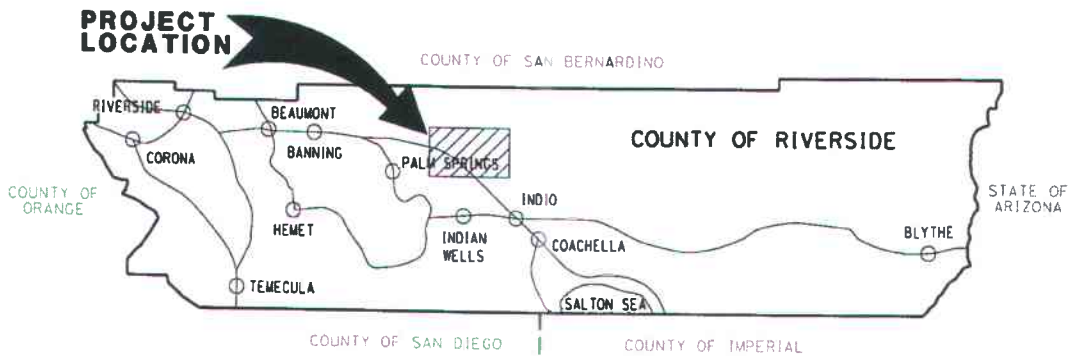

PROJECT: Detill Road Resurfacing Project and Sierra Del Sol Resurfacing Project
 County Project No: CR-0053 and CR-0054
 Contract No. 20-04-001

Contractor: Hardy & Harper, Inc.
 Address: 32 Rancho Circle
 City, State, Zip: Lake Forest, CA 92630

Estimate No. 2 Final
 From: July 7, 2019
 To: August 25, 2019

Item No.	Units	Item Description	Quantity	Unit Price	Original Contract Amount	Change Authorized Quantity	Change Authorized Amount	Total Authorized Quantity	Total Authorized Amount	The Estimate Quantity	Amount	Previous Quantity	Total Estimate To Date Quantity	Amount	% Arith.
1	LS	DEVELOP WATER SUPPLY	1.0	3,200.00	3,200.00	1.00	3,200.00	1.00	3,200.00	1.00	3,200.00	1.00	1.00	3,200.00	100%
		Detill Road Resurfacing - CR-0053	0.5	3,200.00	1,600.00	0.50	1,600.00	0.50	1,600.00	0.50	1,600.00	0.50	0.50	1,600.00	100%
		Sierra Del Sol Resurfacing - CR-0054	0.5	3,200.00	1,600.00	0.50	1,600.00	0.50	1,600.00	0.50	1,600.00	0.50	0.50	1,600.00	100%
2	LS	TRAFFIC CONTROL SYSTEM	1.0	48,000.00	48,000.00	1.00	48,000.00	1.00	48,000.00	1.00	48,000.00	1.00	1.00	48,000.00	100%
		Detill Road Resurfacing - CR-0053	0.5	48,000.00	24,000.00	0.50	24,000.00	0.50	24,000.00	0.50	24,000.00	0.50	0.50	24,000.00	100%
		Sierra Del Sol Resurfacing - CR-0054	0.5	48,000.00	24,000.00	0.50	24,000.00	0.50	24,000.00	0.50	24,000.00	0.50	0.50	24,000.00	100%
3	LS	PREPARE WATER POLLUTION CONTROL PLAN	1.0	3,000.00	3,000.00	1.00	3,000.00	1.00	3,000.00	1.00	3,000.00	1.00	1.00	3,000.00	100%
		Detill Road Resurfacing - CR-0053	0.5	3,000.00	1,500.00	0.50	1,500.00	0.50	1,500.00	0.50	1,500.00	0.50	0.50	1,500.00	100%
		Sierra Del Sol Resurfacing - CR-0054	0.5	3,000.00	1,500.00	0.50	1,500.00	0.50	1,500.00	0.50	1,500.00	0.50	0.50	1,500.00	100%
4	LS	CLEARING AND GRUBBING	1.0	9,500.00	9,500.00	1.00	9,500.00	1.00	9,500.00	1.00	9,500.00	1.00	1.00	9,500.00	100%
		Detill Road Resurfacing - CR-0053	0.5	9,500.00	4,750.00	0.50	4,750.00	0.50	4,750.00	0.50	4,750.00	0.50	0.50	4,750.00	100%
		Sierra Del Sol Resurfacing - CR-0054	0.5	9,500.00	4,750.00	0.50	4,750.00	0.50	4,750.00	0.50	4,750.00	0.50	0.50	4,750.00	100%
5	LS	DUST ABATEMENT	1.0	50,206.50	50,206.50	1.00	50,206.50	1.00	50,206.50	0.10	5,020.66	0.90	1.00	50,206.50	100%
		Detill Road Resurfacing - CR-0053	0.5	50,206.50	25,103.25	0.50	25,103.25	0.05	2,510.33	0.05	2,510.33	0.45	0.50	25,103.25	96%
		Sierra Del Sol Resurfacing - CR-0054	0.5	50,206.50	25,103.25	0.50	25,103.25	0.05	2,510.33	0.05	2,510.33	0.45	0.50	25,103.25	96%
6	SOYD	GRINDING ASPHALT CONCRETE IN PLACE	14,810	2.00	29,620.00	14,810.00	29,620.00	14,810.00	29,620.00	14,167.54	28,335.08	14,167.54	14,167.54	28,335.08	96%
		Detill Road Resurfacing - CR-0053	11,000	2.00	22,000.00	11,000.00	22,000.00	11,000.00	22,000.00	10,311.50	20,623.00	10,311.50	10,311.50	20,623.00	96%
		Sierra Del Sol Resurfacing - CR-0054	3,810	2.00	7,620.00	3,810.00	7,620.00	3,810.00	7,620.00	3,856.04	7,712.08	3,856.04	3,856.04	7,712.08	93%
7	CY	ROADWAY EXCAVATION	235	71.00	16,665.00	235.00	16,665.00	235.00	16,665.00	219.71	15,599.41	88.13	219.71	15,599.41	93%
		Detill Road Resurfacing - CR-0053	90	71.00	6,390.00	90.00	6,390.00	90.00	6,390.00	88.13	6,257.23	88.13	88.13	6,257.23	93%
		Sierra Del Sol Resurfacing - CR-0054	145	71.00	10,275.00	145.00	10,275.00	145.00	10,275.00	131.58	9,342.18	131.58	131.58	9,342.18	93%
8	LF	SHOULDER BACKING	6,900	3.41	23,529.00	6,900.00	23,529.00	6,900.00	23,529.00	6,840.00	23,324.40	6,840.00	6,840.00	23,324.40	99%
		Detill Road Resurfacing - CR-0053	4,920	3.41	16,777.20	4,920.00	16,777.20	4,920.00	16,777.20	4,914.00	16,756.74	4,914.00	4,914.00	16,756.74	99%
		Sierra Del Sol Resurfacing - CR-0054	1,980	3.41	6,751.80	1,980.00	6,751.80	1,980.00	6,751.80	1,926.00	6,567.66	1,926.00	1,926.00	6,567.66	99%
9	LF	PLACE ASPHALT CONCRETE ONE (CRS 212) (6) -	65	16.50	1,072.50	65.00	1,072.50	65.00	1,072.50	65.00	1,072.50	65.00	65.00	1,072.50	100%
		Detill Road Resurfacing - CR-0053	65	16.50	1,072.50	65.00	1,072.50	65.00	1,072.50	65.00	1,072.50	65.00	65.00	1,072.50	100%
		Sierra Del Sol Resurfacing - CR-0054	65	16.50	1,072.50	65.00	1,072.50	65.00	1,072.50	65.00	1,072.50	65.00	65.00	1,072.50	100%
10	SFT	ASPHALT CONCRETE DRIVEWAY	12,870	2.30	29,601.00	12,870.00	29,601.00	12,870.00	29,601.00	13,148.50	30,241.56	13,148.50	13,148.50	30,241.56	102%
		Detill Road Resurfacing - CR-0053	4,820	2.30	11,086.00	4,820.00	11,086.00	4,820.00	11,086.00	5,214.00	11,862.20	5,214.00	5,214.00	11,862.20	102%
		Sierra Del Sol Resurfacing - CR-0054	8,050	2.30	18,515.00	8,050.00	18,515.00	8,050.00	18,515.00	7,934.50	18,249.35	7,934.50	7,934.50	18,249.35	98%
11	TON	HOT MIX ASPHALT TYPE A	4,120	75.00	309,000.00	4,120.00	309,000.00	4,120.00	309,000.00	4,056.71	304,253.25	4,056.71	4,056.71	304,253.25	98%
		Detill Road Resurfacing - CR-0053	2,870	75.00	215,250.00	2,870.00	215,250.00	2,870.00	215,250.00	2,690.88	201,816.00	2,690.88	2,690.88	201,816.00	98%
		Sierra Del Sol Resurfacing - CR-0054	1,250	75.00	93,750.00	1,250.00	93,750.00	1,250.00	93,750.00	1,365.83	102,437.25	1,365.83	1,365.83	102,437.25	98%
12	LF	PLACE HOT MIX ASPHALT ONE TYPE E	635	10.00	6,350.00	635.00	6,350.00	635.00	6,350.00	635.00	6,350.00	635.00	635.00	6,350.00	100%
		Detill Road Resurfacing - CR-0053	635	10.00	6,350.00	635.00	6,350.00	635.00	6,350.00	635.00	6,350.00	635.00	635.00	6,350.00	100%
		Sierra Del Sol Resurfacing - CR-0054	635	10.00	6,350.00	635.00	6,350.00	635.00	6,350.00	635.00	6,350.00	635.00	635.00	6,350.00	100%
13	SOFT	PLACE HOT MIX ASPHALT (MISCELLANEOUS AREA)	210	3.50	735.00	210.00	735.00	210.00	735.00	210.00	735.00	210.00	210.00	735.00	100%
		Detill Road Resurfacing - CR-0053	210	3.50	735.00	210.00	735.00	210.00	735.00	210.00	735.00	210.00	210.00	735.00	100%
		Sierra Del Sol Resurfacing - CR-0054	210	3.50	735.00	210.00	735.00	210.00	735.00	210.00	735.00	210.00	210.00	735.00	100%
14	EA	MINOR CONCRETE (CURB RAMP) (CRS 403 - CASE A)	1	9,200.00	9,200.00	1.00	9,200.00	1.00	9,200.00	1.00	9,200.00	1.00	1.00	9,200.00	100%

PROJECT: Ditch Road Resurfacing Project and Sierra Del Sol Resurfacing Project
 County Project No. C9-0053 and C9-0054
 Contract No. 20-04-001

Contractor: Herdy & Harper, Inc.
 Address: 32 Rancho Circle
 City, State, Zip: Lake Forest, CA 92630

Estimate No. 2 Final
 From: July 7, 2019
 To: August 25, 2019



Item No.	Units	Item Description	Quantity	Unit Price	Original Contract Amount	Change Authorized Quantity	Change Authorized Amount	Total Authorized Quantity	Total Authorized Amount	This Estimate Quantity	This Estimate Amount	Previous Quantity	Total Estimate To Date Quantity	Total Estimate To Date Amount	% Auth.
		Ditch Road Resurfacing - C9-0053	1	9,200.00	9,200.00			1.00	9,200.00			1.00	1.00	9,200.00	
		Sierra Del Sol Resurfacing - C9-0054		9,200.00											
15	SOFT	MINOR CONCRETE (DRIVEWAY)	1,755	17.00	29,835.00			1,755.00	29,835.00			1,910.50	1,910.50	32,478.50	108%
		Ditch Road Resurfacing - C9-0053	575	17.00	9,775.00			575.00	9,775.00			488.00	488.00	8,296.00	
		Sierra Del Sol Resurfacing - C9-0054	1,180	17.00	20,060.00			1,180.00	20,060.00			1,422.50	1,422.50	24,182.50	
16	EA	PAVEMENT MARKER (RETROREFLECTIVE)	55	5.00	275.00			55.00	275.00			52.00	52.00	260.00	95%
		Ditch Road Resurfacing - C9-0053	55	5.00	275.00			55.00	275.00			7.00	7.00	35.00	
		Sierra Del Sol Resurfacing - C9-0054	59	5.00	295.00			59.00	295.00			45.00	45.00	225.00	
17	EA	BALVAPE ROADSIDE SIGN	19	73.00	1,387.00			19.00	1,387.00	19.00	1,387.00	52.00	19.00	1,387.00	100%
		Ditch Road Resurfacing - C9-0053	14	73.00	1,022.00			14.00	1,022.00	14.00	1,022.00	14.00	14.00	1,022.00	
		Sierra Del Sol Resurfacing - C9-0054	5	73.00	365.00			5.00	365.00	5.00	365.00	38.00	5.00	365.00	
18	EA	ROADSIDE SIGN - ONE POST	18	156.00	2,808.00			18.00	2,808.00	18.00	2,808.00	52.00	18.00	2,808.00	100%
		Ditch Road Resurfacing - C9-0053	14	156.00	2,184.00			14.00	2,184.00	14.00	2,184.00	14.00	14.00	2,184.00	
		Sierra Del Sol Resurfacing - C9-0054	4	156.00	624.00			4.00	624.00	4.00	624.00	38.00	4.00	624.00	
19	SOFT	THERMOPLASTIC PAVEMENT MARKING	830	5.20	4,316.00			830.00	4,316.00			887.00	887.00	4,612.40	95%
		Ditch Road Resurfacing - C9-0053	555	5.20	2,886.00			555.00	2,886.00			284.50	284.50	1,479.40	
		Sierra Del Sol Resurfacing - C9-0054	375	5.20	1,950.00			375.00	1,950.00			602.50	602.50	3,133.00	
20	LF	PAINT TRAFFIC STRIPE (2-COAT)	580	2.00	1,160.00			580.00	1,160.00			566.00	566.00	1,132.00	98%
		Ditch Road Resurfacing - C9-0053	2.00	2.00	4.00			2.00	4.00			2.00	2.00	4.00	
		Sierra Del Sol Resurfacing - C9-0054	578.00	2.00	1,156.00			578.00	1,156.00			564.00	564.00	1,128.00	
21	FA	MISCELLANEOUS WORK (AS DIRECTED)	1	70,000.00	70,000.00			1.00	70,000.00						
		Ditch Road Resurfacing - C9-0053	0.5	70,000.00	35,000.00			0.50	35,000.00						
		Sierra Del Sol Resurfacing - C9-0054	0.5	70,000.00	35,000.00			0.50	35,000.00						
		DITCH ROAD RESURFACING PROJECT - C9-0053			395,608.45				395,608.45		2,510.33			340,493.82	
		SIERRA DEL SOL RESURFACING PROJECT - C9-0054			254,391.55				254,391.55		3,489.33			231,985.77	

PROJECT: Dell Road Resurfacing Project and Sierra Del Sol Resurfacing Project
 County Project No.: C9-0043 and C9-0084
 Contract No.: 20-04-001

Contractor: Hardy & Harper, Inc.
 Address: 32 Rancho Circle
 City, State, Zip: Lake Forest, CA 92630

Estimate No. **2 Final**
 From: **July 7, 2019**
 To: **August 15, 2019**

Item No.	Item Description	Units	Quantity	Unit Price	Original Contract Amount	Change Authorized Quantity	Amount	Total Authorized Quantity	Amount	This Estimate Quantity	Amount	Previous Quantity	Amount	Total Estimate To Date Quantity	Amount	% Adm.
PROJECT TOTAL																
					650,000.00		650,000.00		650,000.00		6,009.96			572,489.59		

Made by: Steven Wann
 Checked by: TN
 OK Const. Supv. HD

Start Date: **6-5-20**
 End Date: **7-2-20**
 % \$ Complete: **88%**
 Original Contract: **\$650,000.00**
 Amended Contract: **\$650,000.00**

TOTAL VALUE OF WORK TO DATE: **\$572,489.59**
 LESS RETENTION: **5%**
 TOTAL DUE TO DATE: **\$543,865.13**
 LESS PREVIOUSLY INVOICED: **538,155.95**
 TOTAL DUE THIS PAYMENT: **\$6,709.18**

This Estimate Approved: [Signature] Date: **9/11/2020** For: _____

Patricia Romo, Director of Transportation

Received by Accounts Payable: _____

By: _____

[Signature] Date: 9/11/2020
 Hardy & Harper, Inc.

Quantities on This Estimate Approved _____

Payment Approval

FUND: **20000**

DEPT. ID.: **31305**

ACCOUNT: **527980**

ZC9-0054E

PROJECT: **ZC9-0053E**

ACTIVITY ID.: **Z3500**

RESOURCE **CNT**

SIGNATURE: [Signature]

DATE: **09/10/2020**

Transfiscal Approved
 By: Lori Conrad 5*3461
 Sept 14, 2020

[Signature]
 09/11/20
