

SUBMITTAL TO THE BOARD OF SUPERVISORS
COUNTY OF RIVERSIDE, STATE OF CALIFORNIA



ITEM: 3.38
(ID # 13739)

MEETING DATE:
Tuesday, December 15, 2020


FROM : TLMA-TRANSPORTATION:

SUBJECT: TRANSPORTATION AND LAND MANAGEMENT AGENCY/TRANSPORTATION:
Notice of Completion – Emergency Road and Storm Drain Repair Work,
Lakepointe Drive at Blue Bird Place, Community of Lake Hills, District 1. [\$0]

RECOMMENDED MOTION: That the Board of Supervisors:

1. Accept as complete the Construction of Emergency Road and Storm Drain Repair Work, Lakepointe Drive at Blue Bird Place, Community of Lake Hills, District 1;
2. Authorize the Chairman of the Board to execute the Notice of Completion on behalf of the County; and
3. Direct the Clerk of the Board to record the Notice of Completion.

ACTION:Policy




Mark Lancaster, Director of Transportation

11/30/2020

MINUTES OF THE BOARD OF SUPERVISORS

On motion of Supervisor Spiegel, seconded by Supervisor Jeffries and duly carried by unanimous vote, IT WAS ORDERED that the above matter is approved as recommended.

Ayes: Jeffries, Spiegel, Washington, Perez and Hewitt
Nays: None
Absent: None
Date: December 15, 2020
xc: Transp. , Record

Kecia R. Harper
Clerk of the Board
By: 
Deputy

**SUBMITTAL TO THE BOARD OF SUPERVISORS COUNTY OF RIVERSIDE,
STATE OF CALIFORNIA**

FINANCIAL DATA	Current Fiscal Year:	Next Fiscal Year:	Total Cost:	Ongoing Cost
COST	\$ 0	\$ 0	\$ 0	\$ 0
NET COUNTY COST	\$ 0	\$ 0	\$ 0	\$ 0
SOURCE OF FUNDS: N/A			Budget Adjustment:	No
			For Fiscal Year:	20/21

C.E.O. RECOMMENDATION: Approve

BACKGROUND:

Summary

On July 14, 2020, the Director of Transportation entered into an emergency contract with SRD Engineering Inc. of Anaheim, California, for Emergency Road and Storm Drain Repair Work, on Lakepointe Drive at Blue Bird Place in the community of Lake Hills. On August 4, 2020, Agenda Item 3.65, the Board of Supervisors received and filed this emergency contract.

The California Highway Patrol reported a sinkhole on July 4, 2020. The Transportation Department and Western Municipal Water District performed an inspection of the facilities in the area and believed that the sinkhole was due to leakage from an existing storm drain line with a faulty joint seal. SRD Engineering performed emergency repairs by sealing the storm drain joints, placing slurry backfill around the storm drain, filling the sinkhole and paving the roadway.

The original authorized amount of the contract was \$350,000. The total price of the contract was \$105,746 which is 69.8% less than the originally authorized amount. Due to the nature of the damage, the actual extent of the damage could not be fully determined at the time of contract execution and the quantity of repairs was less than originally anticipated.

The work was completed in conformance with the plans and specifications and the contractor was granted relief of maintenance on July 28, 2020.

Project Number ZM1607A6

Impact on Residents and Businesses

The emergency work has restored the safe access along Lakepointe Drive.

Additional Fiscal Information

**SUBMITTAL TO THE BOARD OF SUPERVISORS COUNTY OF RIVERSIDE,
STATE OF CALIFORNIA**

Budget

Original Contract Amount		\$350,000
Total Change Orders Authorized	0.0%	\$0
Estimated Pending Change Orders	0.0%	\$0
Authorized Contract Amount		\$350,000
* Quantity Adjustments	-69.8%	(\$244,254)
+ CCO FA Adjustments	0.0%	\$0
Total Amended Contract Amount	30.2%	\$105,746

Expenditures

Total Progress Payments		\$105,746
Estimated Pending Payments		\$0
Total Expenditures		\$105,746

(Over)/Under Contract Amount \$0

+ Change Orders using the Force Account method of payment issued prior to the work being completed generally do not use the total authorized amount.

* Caltrans Standard Specifications 9-1.06 (Changed Quantity Payment Adjustments). Increases or decreases in the quantity of a contract item of work will be determined by comparing the total pay quantity of such item of work with the Engineer's Estimate. If the total pay quantity of any item of work required under the contract varies from the Engineer's Estimate by 25 percent or less, payment will be made for the quantity of work of said item performed at the contract unit price, unless eligible for adjustment pursuant to Section 9-1.15, "Work-Character Changes."



This project was funded with \$105,746 of Gas Tax funds.

Contract History and Price Reasonableness

The contract was executed in accordance with authority that the Board has delegated to the Director of Transportation by Resolution No. 2019-035 (January 29, 2019; Agenda Item 3.24) and has been approved as to legal form by County Counsel.

ATTACHMENTS:

- Vicinity Map
- Progress Estimate Report
- Notice of Completion

 Jason Farin, Principal Management Analyst 12/9/2020	 Gregory V. Priarios, Director County Counsel 12/3/2020
---	---

PLEASE COMPLETE THIS INFORMATION
RECORDING REQUESTED BY:

KECIA R. HARPER, CLERK OF THE BOARD
RIVERSIDE CO. CLERK OF THE BOARD
4080 LEMON STREET, 1ST FLOOR CAC
P O BOX 1147 – RIVERSIDE, CA 92502

MAIL STOP # 1010

AND WHEN RECORDED MAIL TO:

RETURN TO: **STOP #1010**
RIVERSIDE COUNTY CLERK OF THE BOARD
P. O. BOX 1147 – RIVERSIDE, CA 92502

2020-0651356

12/22/2020 11:12 AM Fee: \$ 0.00

Page 1 of 1

Recorded in Official Records
County of Riverside
Peter Aldana
Assessor-County Clerk-Recorder



6080

THIS SPACE FOR RECORDERS USE ONLY

NOTICE OF COMPLETION

To be recorded with County Recorder
within 10 days after completion.
No recording fee.

Notice is hereby given by the undersigned owner, a public entity of the State of California, that a public work of improvement has been completed, as follows:

Project title or description of work: Emergency Road and Storm Drain Repair Work, Lakepointe Drive at Blue Bird Place, Project No. ZM1607A6

Date of Completion: Date Hereof **DEC 15 2020**

Nature of owner: County of Riverside, public entity

Interest or estate of owner: Public Road Right-of-Way

Address of owner: Clerk of the Board of Supervisors, County Administrative Center
4080 Lemon Street, 8th Floor, Riverside, CA 92501

Name and Address of contractor: SRD Engineering, Inc., 3578 East Enterprise Drive, Anaheim CA 92807

Street or legal description of site: Lakepointe Drive at Blue Bird Place, Community of Lake Hills

Dated: **DEC 15 2020**

Owner: County of Riverside
(Name of Public Entity)

By: *[Signature]*
Chairman, Board of Supervisors

STATE OF CALIFORNIA)

ss

COUNTY OF RIVERSIDE)

I am the Chairman of the governing board of the County of Riverside, the public entity which executed the foregoing notice and on whose behalf I make this verification; I have read this notice, know its contents, and the same is true. I certify under penalty of perjury that the foregoing is true and correct.

Executed at Riverside, California on **DEC 15 2020** (Date)

[Signature], Chairman of the Board of Supervisors



FORM APPROVED COUNTY COUNSEL
BY *[Signature]* **12/31/2020**
KRISTINE BELL-VALDEZ DATE

ATTEST:
KECIA R. HARPER, Clerk
By *[Signature]*
DEPUTY

DEC 15 2020 338

**County of Riverside
Transportation Department**

**Emergency Road and Storm Drain Repair Work
Lakepointe Drive at Blue Bird Place
Community of Lake Hills
Project No. 45-21110101**

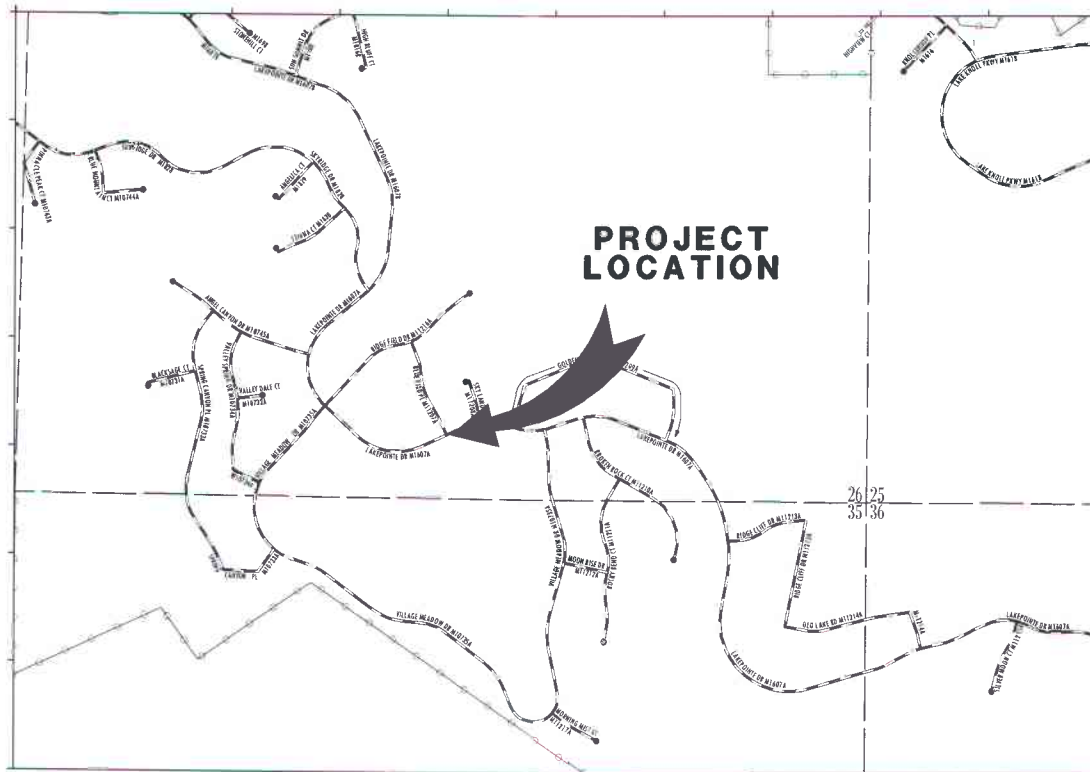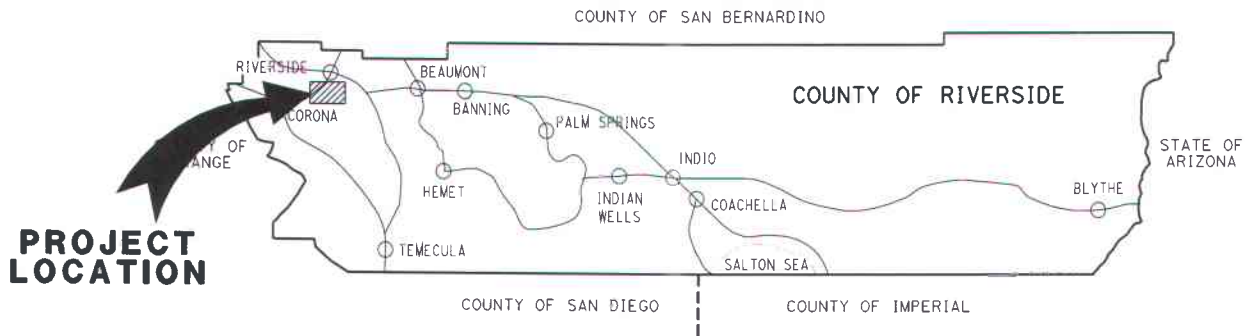

VICINITY MAP

PROJECT: Emergency Road and Storm Drain Repair Work, Lakepointe Drive at Blue Bird Place, Community of Lake Hills
 County Project No.: ZM1607A6
 Contract No. 20-07-002

Contractor: **SRD Engineering, Inc.**
 Address: **3578 East Enterprise Drive**
 City, State, Zip: **Anaheim, CA 92807**



Estimate No. **1 Final**
 From: **August 25, 2020**
 To: **August 25, 2020**

Item No.	Item Description	Units	Quantity	Unit Price	Original Contract Amount	Change Authorized		Total Authorized		The Estimate		Previous Quantity	Total Estimate To Date		% Auth.
						Quantity	Amount	Quantity	Amount	Quantity	Amount		Quantity	Amount	
1	Lakepointe Dr. Drain/Sinkhole	FA	1	350,000.00	350,000.00			1.00	350,000.00	0.3021317	105,746.10		0.3021317	105,746.10	30%
PROJECT TOTAL					350,000.00		0.00		350,000.00		105,746.10			105,746.10	

Made by Daniel Lima

Checked by TN

OK Const. Supv. _____

Working Days: N/A
 Days Added: N/A
 Subtotal: N/A
 Days Used: N/A
 % Time Elapsed: N/A

Start Date: _____
 End Date: TBD
 % \$ Complete: 30%
 Original Contract: \$350,000.00
 Amended Contract: \$350,000.00

TOTAL VALUE OF WORK TO DATE: \$105,746.10
 LESS RETENTION: 0% 0.00
 TOTAL DUE TO DATE: \$105,746.10
 LESS PREVIOUSLY INVOICED: 0.00
 LESS LABOR NON COMPLIANCE: 0.00
 TOTAL DUE THIS PAYMENT: \$105,746.10

This Estimate Approved Patricia Romo Date 9/24/2020 for \$105,746.10
 Patricia Romo, Director of Transportation

Quantities on This Estimate Approved U.A.N. Date 9/24/20
 SRD Engineering, Inc

Payment Approval

FUND: 20000
 DEPT. ID.: 31301
 ACCOUNT: 524660
 PROJECT: ZM1607A6
 ACTIVITY ID.: Z3055
 RESOURCE: CNT
 SIGNATURE: Linda B. Black
 DATE: 09/24/2020

Received by Accounts Payable: _____
 By ya

09/24/20

Transfiscal Approved
 By: Lori Conrad 5*3461
 Sept 28, 2020
