

SUBMITTAL TO THE BOARD OF SUPERVISORS
COUNTY OF RIVERSIDE, STATE OF CALIFORNIA



ITEM: 3.30
(ID # 14086)

MEETING DATE:
Tuesday, January 26, 2021

FROM : TLMA-TRANSPORTATION:

SUBJECT: TRANSPORTATION AND LAND MANAGEMENT AGENCY/TRANSPORTATION:
Notice of Completion – Chicago Avenue Reconstruction Project and Lloyd Street
and Thomas Street Resurfacing Projects, Community of Valle Vista. District 3.
[\$0]

RECOMMENDED MOTION: That the Board of Supervisors:

1. Accept as complete the Construction of Chicago Avenue Reconstruction Project and Lloyd Street and Thomas Street Resurfacing Projects, Community of Valle Vista, District 3;
2. Authorize the Chairman of the Board to execute the Notice of Completion on behalf of the County; and
3. Direct the Clerk of the Board to record the Notice of Completion.


ACTION:Policy


Mark Lancaster, Director of Transportation 12/30/2020

MINUTES OF THE BOARD OF SUPERVISORS

On motion of Supervisor Hewitt, seconded by Supervisor Spiegel and duly carried by unanimous vote, IT WAS ORDERED that the above matter is approved as recommended.

Ayes: Jeffries, Spiegel, Washington, Perez, and Hewitt
Nays: None
Absent: None
Date: January 26, 2021
xc: Transp., Recorder

Kecia R. Harper
Clerk of the Board
By: 
Deputy

**SUBMITTAL TO THE BOARD OF SUPERVISORS COUNTY OF RIVERSIDE,
STATE OF CALIFORNIA**

FINANCIAL DATA	Current Fiscal Year:	Next Fiscal Year:	Total Cost:	Ongoing Cost
COST	\$ 0	\$ 0	\$ 0	\$ 0
NET COUNTY COST	\$ 0	\$ 0	\$ 0	\$ 0
SOURCE OF FUNDS: NA			Budget Adjustment:	No
			For Fiscal Year:	20/21

C.E.O. RECOMMENDATION: Approve

BACKGROUND:

Summary

By Minute Order 3.18 of July 14, 2020, the Board of Supervisors entered into a contract with Onyx Paving Company, Inc. of Lake Forest, California for the construction of Chicago Avenue Reconstruction Project, Palm Avenue to Cedar Avenue, and Lloyd Street and Thomas Street Resurfacing Projects, Fairview Avenue to 0.10 Miles East of Fairview Avenue, Community of Valle Vista, District 3.

The original authorized amount of the contract was \$1,413,056. The total price of the contract came in at \$1,140,076 which is 19.3% less than the originally authorized amount. The decrease of the total cost was the result of using less quantities than anticipated to complete the work.

The work was completed in conformance with the plans and specifications and the contractor was granted relief of maintenance on September 28, 2020.

Project Nos. D0-0074 – Chicago Avenue Reconstruction Project
 B0-0661 – Lloyd Street Resurfacing Project
 B0-0672 – Thomas Street Resurfacing Project

Impact on Residents and Businesses

The improvements have provided the public with a smooth paved roadway, increasing safety and the flow of vehicular traffic.

Additional Fiscal Information

**SUBMITTAL TO THE BOARD OF SUPERVISORS COUNTY OF RIVERSIDE,
STATE OF CALIFORNIA**

Budget

Original Contract Amount		\$1,413,056
Total Change Orders Authorized	0.0%	\$0
Estimated Pending Change Orders	0.0%	\$0
Authorized Contract Amount		\$1,413,056
* Quantity Adjustments	-19.3%	(\$272,980)
+ CCO FA Adjustments	0.0%	\$0
Total Amended Contract Amount	80.7%	\$1,140,076

Expenditures

Total Progress Payments		\$1,140,076
Estimated Pending Payments		\$0
Total Expenditures		\$1,140,076

(Over)/Under Contract Amount \$0

+ Change Orders using the Force Account method of payment issued prior to the work being completed generally do not use the total authorized amount.

* Caltrans Standard Specifications 9-1.06 (Changed Quantity Payment Adjustments). Increases or decreases in the quantity of a contract item of work will be determined by comparing the total pay quantity of such item of work with the Engineer's Estimate. If the total pay quantity of any item of work required under the contract varies from the Engineer's Estimate by 25 percent or less, payment will be made for the quantity of work of said item performed at the contract unit price, unless eligible for adjustment pursuant to Section 9-1.15, "Work-Character Changes."

This project was funded with \$1,140,076 of Gas Tax/SB1 funds.

Contract History and Price Reasonableness

Seven bids were received ranging from \$1,413,056 to \$1,611,161. The basis for the selection of a contractor is the lowest responsive and responsible bid. The lowest responsible bid was submitted by Onyx Paving Company, Inc. in the amount of \$1,413,056, which is \$306,668 (17.8%) lower than the Engineer's Estimate.

ATTACHMENTS:

- Vicinity Map
- Progress Estimate Report
- Notice of Completion


Jason Farin, Principal Management Analyst

1/20/2021


Gregory L. Priamos, Director County Counsel

1/11/2021

PLEASE COMPLETE THIS INFORMATION
RECORDING REQUESTED BY:

**KECIA R. HARPER, CLERK OF THE BOARD
RIVERSIDE CO. CLERK OF THE BOARD
4080 LEMON STREET, 1ST FLOOR CAC
P O BOX 1147 – RIVERSIDE, CA 92502**

MAIL STOP # 1010

AND WHEN RECORDED MAIL TO:

**RETURN TO: STOP #1010
RIVERSIDE COUNTY CLERK OF THE BOARD
P. O. BOX 1147 – RIVERSIDE, CA 92502**

2021-0070361

02/03/2021 08:00 AM Fee: \$ 0.00

Page 1 of 2

Recorded in Official Records
County of Riverside
Peter Aldana
Assessor-County Clerk-Recorder



1628

THIS SPACE FOR RECORDERS USE ONLY

NOTICE OF COMPLETION

To be recorded with County Recorder
within 10 days after completion.
No recording fee.

Notice is hereby given by the undersigned owner, a public entity of the State of California, that a public work of improvement has been completed, as follows:

Project title or description of work: Chicago Avenue Reconstruction Project and Lloyd Street and Thomas Street Resurfacing Projects, Community of Valle Vista, Project Nos. D0-0074, B0-0661 and B0-0672

Date of Completion: Date Hereof **JAN 26 2021**

Nature of owner: County of Riverside, public entity

Interest or estate of owner: Public Road Right-of-Way

Address of owner: Clerk of the Board of Supervisors, County Administrative Center
4080 Lemon Street, 8th Floor, Riverside, CA 92501

Name and Address of contractor: Onyx Paving Company, 2890 East La Cresta Avenue, Anaheim, CA 92806

Street or legal description of site: Chicago Avenue, Palm Avenue to Cedar Avenue and Lloyd Street and Thomas Street, Fairview Avenue to 0.10 Miles East of Fairview Avenue

Dated: **JAN 26 2021**

Owner: County of Riverside
(Name of Public Entity)

By: Karen S. Spiegel
Chair, Board of Supervisors
KAREN SPIEGEL

STATE OF CALIFORNIA)

ss

COUNTY OF RIVERSIDE)

I am the Chair of the governing board of the County of Riverside, the public entity which executed the foregoing notice and on whose behalf I make this verification; I have read this notice, know its contents, and the same is true. I certify under penalty of perjury that the foregoing is true and correct.

Executed at Riverside, California on **JAN 26 2021** (Date)

Karen S. Spiegel, Chair of the Board of Supervisors

ATTEST:
KECIA R. HARPER, Clerk
By [Signature]
DEPUTY

FORM APPROVED COUNTY COUNSEL
BY [Signature]
KRISTINE BELL-VALDEZ DATE

JAN 26 2021 3.30

PETER ALDANA
COUNTY OF RIVERSIDE
ASSESSOR-COUNTY CLERK-RECORDER

Recorder
P.O. Box 751
Riverside, CA 92502-0751
(951) 486-7000

www.riversideacr.com

CERTIFICATION

Pursuant to the provisions of Government Code 27361.7, I certify under the penalty of perjury that the following is a true copy of illegible wording found in the attached document:

(Print or type the page number(s) and wording below):

CLARIFICATION FOR SEAL for the Riverside County Board of Supervisors
(EMBOSSSED ON DOCUMENT)



Date: JAN 26 2021

Signature: 



Print Name: Oksana Estrada Board Assistant

COUNTY OF RIVERSIDE
TRANSPORTATION DEPARTMENT

**CHICAGO AVENUE
RECONSTRUCTION PROJECT
PALM AVENUE TO CEDAR AVENUE**



COMMUNITY OF VALLE VISTA

PROJECT No. D0-0074

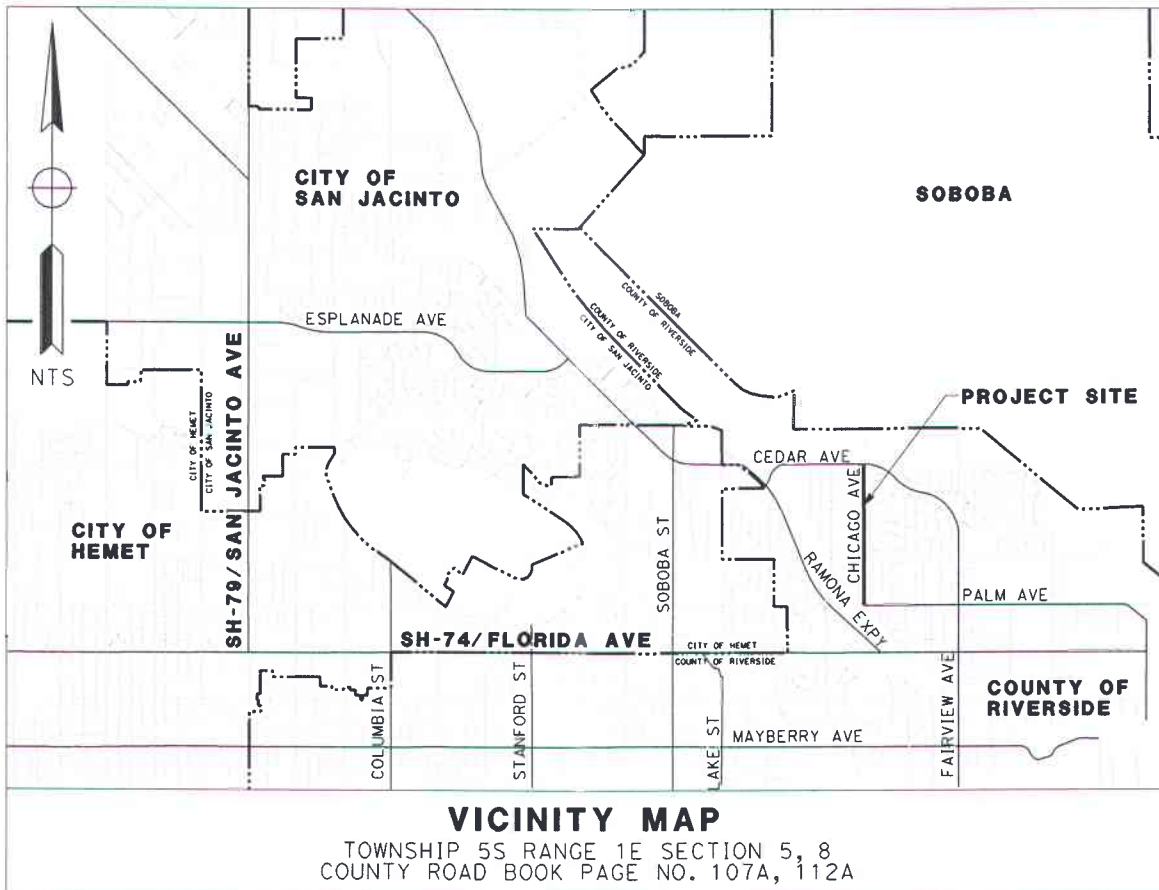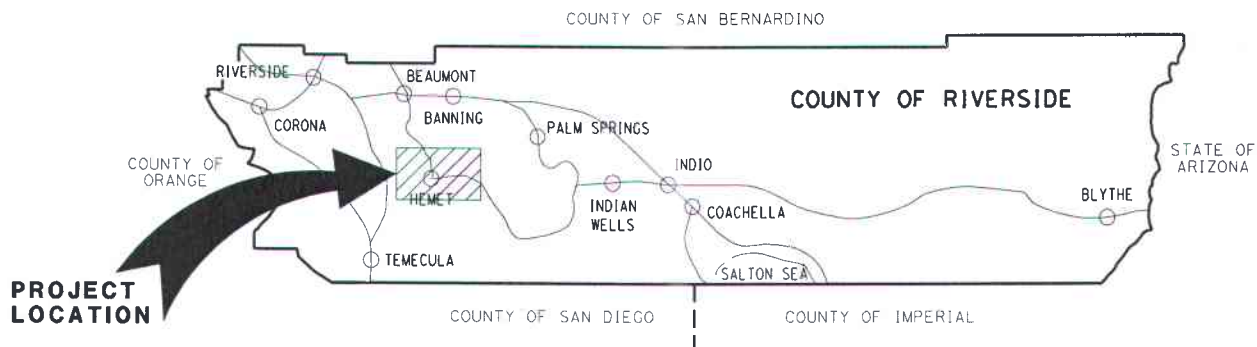

COUNTY OF RIVERSIDE
TRANSPORTATION DEPARTMENT

**LLOYD STREET AND THOMAS STREET
RESURFACING PROJECTS**
FAIRVIEW AVENUE TO 0.10 MILE EAST OF FAIRVIEW AVENUE
COMMUNITY OF VALLE VISTA
PROJECT No. B0-0661, B0-0672

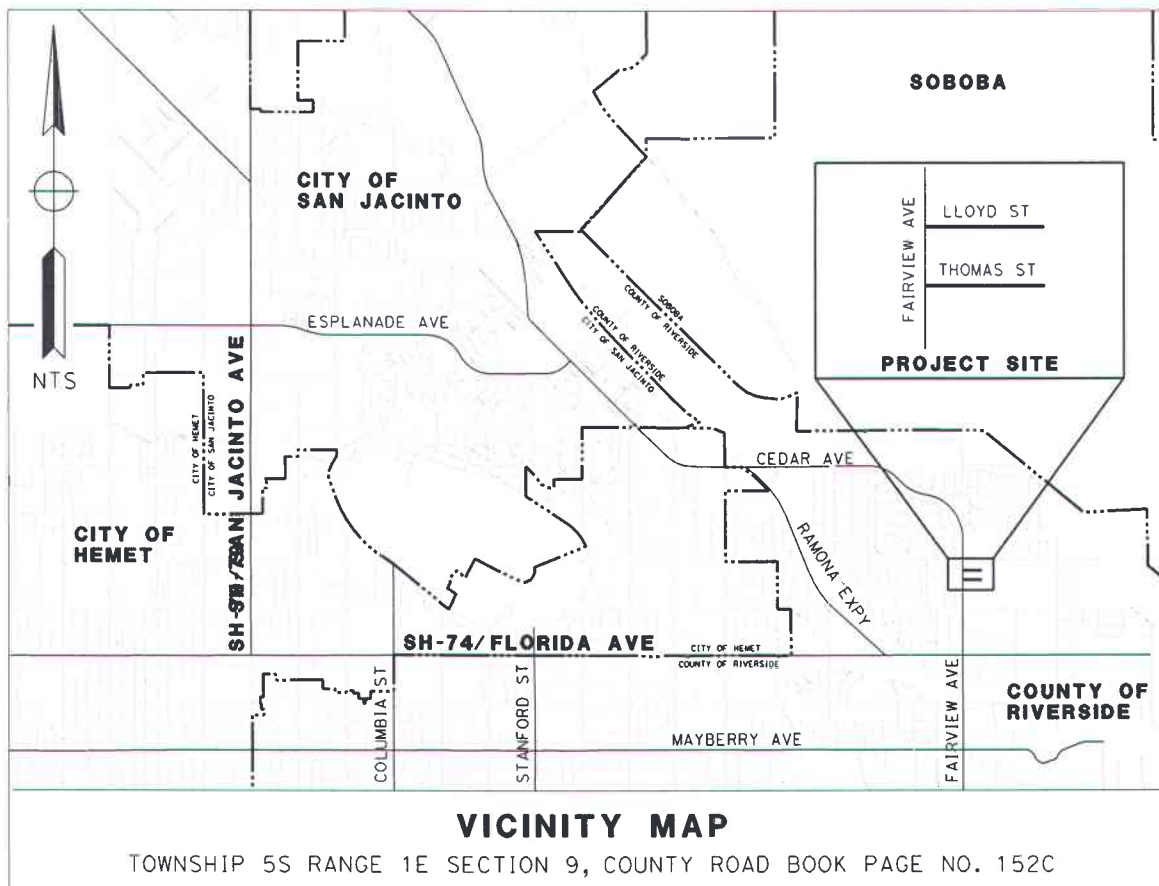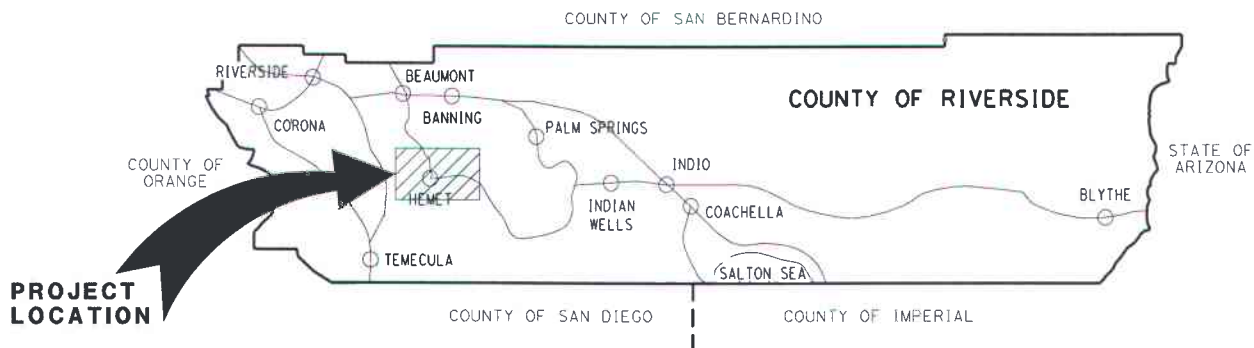

Item No.	Item Description	Units	Quantity	Unit Price	Original Contract Amount	Change Authorized		This Estimate		Total Estimate To Date		% Auth.
						Quantity	Amount	Quantity	Amount	Quantity	Amount	
1	CLEARING AND GRUBBING	LS	1	37,000.00	37,000.00					1.00	37,000.00	100%
2	DUST ABATEMENT	LS	1	2,000.00	2,000.00					1.00	2,000.00	100%
3	DEVELOP WATER SUPPLY	LS	1	2,000.00	2,000.00					1.00	2,000.00	100%
4	TRAFFIC CONTROL SYSTEM	LS	1	57,000.00	57,000.00					0.90	57,000.00	100%
5	PREPARE WATER POLLUTION CONTROL PROGRAM	LS	1	2,000.00	2,000.00					1.00	2,000.00	100%
6(F)	ROADWAY EXCAVATION	CY	2,930	30.00	87,900.00					2,930.00	87,900.00	100%
7	CEMENT (CEMENT STABILIZED SOIL)	TON	576	161.00	92,736.00					176.15	28,360.15	31%
8	CEMENT STABILIZED SOIL	SOYD	23,915	3.45	82,506.75					22,740.60	78,455.07	95%
9	ASPHALT CONCRETE OVERSIDE DRAIN (CRS 306)	EA	1	7,000.00	7,000.00					1.00	7,000.00	100%
10	ASPHALT CONCRETE DRIVEWAY	SQFT	646	8.00	5,168.00					694.00	5,552.00	107%
11	HOT MIX ASPHALT (TYPE A)	TON	3,697	69.69	257,643.93					3,089.35	215,296.80	84%
12	RUBBERIZED HOT MIX ASPHALT (GAP GRADED)	TON	2,753	96.96	266,930.88					2,568.72	249,063.09	93%
13	PLACE HOT MIX ASPHALT DIKE (TYPE E)	LF	355	13.00	4,615.00					402.00	5,226.00	113%
14	24 CORRUGATED STEEL PIPE (.064" THICK) *	LF	60	350.00	21,000.00					60.00	21,000.00	100%
15	24 STEEL FLARED END SECTION *	EA	1	2,000.00	2,000.00					1.00	2,000.00	100%
16	ADJUST MANHOLE	EA	12	1,200.00	14,400.00					6.00	15,600.00	109%
17	MINOR CONCRETE (CURB AND GUTTER) (CRS 201)	LF	40	100.00	4,000.00					51.00	5,100.00	128%
18	MINOR CONCRETE (CURB RAMP) (CRS 403 -CASE A)	EA	5	5,000.00	25,000.00					5.00	25,000.00	100%
19	MINOR CONCRETE (CROSS-GUTTER AND SPANDREL)	SQFT	5,700	17.00	96,900.00					5,700.00	96,900.00	100%
20	RELOCATE SIGN STRUCTURE	EA	1	1,168.81	1,168.81					1.00	1,168.81	100%
21	PAVEMENT MARKER (RETROREFLECTIVE)	EA	563	7.00	3,941.00					563.00	3,941.00	100%



Contractor: Onyx Paving Company
 Address: 2890 E La Cresta Ave.
 City, State, Zip: Anaheim Ave., CA 92806

PROJECT: Chicago Avenue Reconstruction and Lloyd Street and Thomas Street Resurfacing
 County Project No.: DD-0074, B0-0661 and B0-0672
 Contract No. 20-06-002

Estimate No. 3 Final
 From: September 20, 2020
 To: October 25, 2020



Contractor: Onyx Paving Company
 Address: 2890 E La Cresta Ave.
 City, State, Zip: Anaheim, CA 92806

PROJECT: Chicago Avenue Reconstruction and Lloyd Street and Thomas Street Resurfacing
 County Project No.: DD-0074, BD-0681 and BD-0672
 Contract No. 20-06-002

Estimate No. 3 Final
 From: November 20, 2019
 To: October 25, 2020

Item No.	Item Description	Units	Quantity	Unit Price	Original Contract Amount	Charge Authorized Quantity	Charge Authorized Amount	Total Authorized Quantity	Total Authorized Amount	This Estimate Quantity	This Estimate Amount	Previous Quantity	Total Estimate To Date Quantity	Total Estimate To Date Amount	% Auth.
22	SALVAGE ROADSIDE SIGN	EA	20	55.00	1,100.00			20.00	1,100.00			20.00	20.00	1,100.00	100%
23	ROADSIDE SIGN -ONE POST	EA	31	3.00	93.00			31.00	93.00			31.00	31.00	93.00	100%
24	THERMOPLASTIC CROSSWALK AND PAVEMENT MARKING	SQFT	1,015	5.00	5,075.00			1,015.00	5,075.00			990.50	990.50	4,952.50	98%
25	REMOVE PAINTED TRAFFIC STRIPE	LF	142	3.00	426.00			142.00	426.00			142.00	142.00	426.00	100%
26	REMOVE THERMOPLASTIC PAVEMENT MARKING	SQFT	406	3.00	1,218.00			406.00	1,218.00			406.00	406.00	1,218.00	100%
27	PAINT TRAFFIC STRIPE (2-COAT)	LF	15,327	0.69	10,575.63			15,327.00	10,575.63			15,327.00	15,327.00	10,575.63	100%
28	MISCELLANEOUS WORK (AS DIRECTED)	FA	1	100,000.00	100,000.00			1.00	100,000.00				1.00	0.00	0%
29	CLEARING AND GRUBBING	LS	1	6,000.00	6,000.00			1.00	6,000.00			1.00	1.00	6,000.00	100%
30	DUST ABATEMENT	LS	1	2,633.02	2,633.02			1.00	2,633.02			1.00	1.00	2,633.02	100%
31	DEVELOP WATER SUPPLY	LS	1	2,000.00	2,000.00			1.00	2,000.00			1.00	1.00	2,000.00	100%
32	TRAFFIC CONTROL SYSTEM	LS	1	5,000.00	5,000.00			1.00	5,000.00	0.10	500.00	0.90	1.00	5,000.00	100%
33	ROADWAY EXCAVATION	CY	382	30.00	11,460.00			382.00	11,460.00			382.00	382.00	11,460.00	100%
34	CLASS 2 AGGREGATE BASE	CY	135	77.00	10,395.00			135.00	10,395.00			75.40	75.40	5,805.80	56%
35	HOT MIX ASPHALT (TYPE A)	TON	542	69.69	37,771.98			542.00	37,771.98			469.96	469.96	32,751.51	87%
36	ADJUST MANHOLE	EA	2	1,200.00	2,400.00			2.00	2,400.00	1.00	1,200.00	1.00	2.00	2,400.00	100%
37	MINOR CONCRETE (CROSS-GUTTER AND SPANDREL)	SQFT	1,045	17.00	17,765.00			1,045.00	17,765.00			1,074.40	1,074.40	18,264.80	103%
38	SALVAGE ROADSIDE SIGN	EA	1	55.00	55.00			1.00	55.00			1.00	1.00	55.00	100%
39	ROADSIDE SIGN -ONE POST	EA	1	3.00	3.00			1.00	3.00			1.00	1.00	3.00	100%
40	THERMOPLASTIC CROSSWALK AND PAVEMENT MARKING	SQFT	35	5.00	175.00			35.00	175.00			35.00	35.00	175.00	100%
41	MISCELLANEOUS WORK (AS DIRECTED)	FA	1	15,000.00	15,000.00			1.00	15,000.00				1.00	0.00	0%

PROGRESS ESTIMATE RECORD - COUNTY OF RIVERSIDE

Item No.	Item Description	Units	Quantity	Unit Price	Original Contract Amount	Change Authorized Quantity	Change Authorized Amount	Total Authorized Quantity	Total Authorized Amount	This Estimate Quantity	This Estimate Amount	Previous Quantity	Estimate No. 3 Final		% Auth.
													Total Estimate To Date Quantity	Total Estimate To Date Amount	
<p>PROJECT: Chicago Avenue Reconstruction and Lloyd Street and Thomas Street Resurfacing</p> <p>Contractor: Onyx Paving Company</p> <p>Address: 2880 E La Cresta Ave.</p> <p>City, State, Zip: Anaheim Ave., CA 92806</p> <p>County Project No.: D0-0074, B0-0661 and B0-0672</p> <p>Contract No. 20-06-002</p>															
42	CLEARING AND GRUBBING	LS	1	6,000.00	6,000.00			1.00	6,000.00			1.00	1.00	6,000.00	100%
43	DUST ABATEMENT	LS	1	2,975.02	2,975.02			1.00	2,975.02			1.00	1.00	2,975.02	100%
44	DEVELOP WATER SUPPLY	LS	1	2,000.00	2,000.00			1.00	2,000.00			1.00	1.00	2,000.00	100%
45	TRAFFIC CONTROL SYSTEM	LS	1	5,000.00	5,000.00			1.00	5,000.00	0.10	500.00	0.90	1.00	5,000.00	100%
46	ROADWAY EXCAVATION (LIKE 1)	CY	382	30.00	11,460.00			382.00	11,460.00			382.00	382.00	11,460.00	100%
47	CLASS 2 AGGREGATE BASE	CY	135	77.00	10,395.00			135.00	10,395.00			75.40	75.40	5,805.80	56%
48	HOT MIX ASPHALT (TYPE A)	TON	542	69.69	37,771.98			542.00	37,771.98			478.05	478.05	33,315.30	88%
49	ADJUST MANHOLE	EA	2	1,200.00	2,400.00			2.00	2,400.00	1.00	1,200.00	1.00	2.00	2,400.00	100%
50	MINOR CONCRETE (CROSS-GUTTER AND SPANDREL)	SQFT	1,045	17.00	17,765.00			1,045.00	17,765.00			1,083.00	1,083.00	18,411.00	104%
51	SALVAGE ROADSIDE SIGN	EA	1	55.00	55.00			1.00	55.00			1.00	1.00	55.00	100%
52	ROADSIDE SIGN -ONE POST	EA	1	3.00	3.00			1.00	3.00			1.00	1.00	3.00	100%
53	THERMOPLASTIC CROSSWALK AND PAVEMENT MARKING	SQFT	35	5.00	175.00			35.00	175.00			35.00	35.00	175.00	100%
54	MISCELLANEOUS WORK (AS DIRECTED)	FA	1	15,000.00	15,000.00			1.00	15,000.00					0.00	0%



Item No.	Item Description	Units	Quantity	Unit Price	Original Contract Amount	Change Authorized Quantity	Change Authorized Amount	Total Authorized Quantity	Total Authorized Amount	This Estimate Quantity	This Estimate Amount	Previous Quantity	Total Estimate To Date Quantity	Total Estimate To Date Amount	% Auth.
	PROJECT TOTAL				1,413,056.00	0.00	0.00	1,413,056.00	1,413,056.00	17,500.00	17,500.00		1,140,076.30	1,140,076.30	

Contractor: Onyx Paving Company
 Address: 2890 E La Cresta Ave.
 City, State, Zip: Anaheim Ave., CA 92806

Estimate No. 3 Final
 From: _____
 To: _____

Working Days: 40 Start Date: 8-3-20
 Days Added: 0 End Date: 9-28-20
 Subtotal: 40 % \$ Complete: 81%
 Days Used: 40 Original Contract: \$1,413,056.00
 % Time Elapsed: 100% Amended Contract: \$1,413,056.00

TOTAL VALUE OF WORK TO DATE: \$1,140,076.30
 LESS RETENTION: 5% 57,003.81
 TOTAL DUE TO DATE: \$1,083,072.49
 LESS PREVIOUSLY INVOICED: 1,066,447.49
 LESS LABOR NON COMPLIANCE: 0.00
 TOTAL DUE THIS PAYMENT: \$16,625.00

Made by: Mehresh Sanati
 Checked by: TN
 OK Const. Supv: HD

This Estimate Approved [Signature] 11/9/2020 for: \$16,625.00
 Patricia Regno, Director of Transportation

Quantities on This Estimate Approved [Signature] Date: 11/4/2020

Received by Account Payable:
Payment Approval
 FUND: 20000
 DEPT. ID.: 31305
 ACCOUNT: 527980
 ZD0-0074E
 ZB0-0661E
 PROJECT: ZB0-0672E
 ACTIVITY ID.: Z3500
 RESOURCE CNT
 SIGNATURE: [Signature]
 DATE: 11/06/2020

Transfiscal Approved
 By: Lori Conrad 5*3461
 Nov 9, 2020

<p>PROJECT: Chicago Avenue Reconstruction and Lloyd Street and Thomas Street Resurfacing Projects County Project No.: D0-0074, B0-0661 and B0-0672 Contract No. 20-06-002</p>		<p>Contractor: Onyx Paving Company Address: 2890 E La Cresta Ave. City, State, Zip: Anaheim Av., CA 92806</p>	<p>Estimate No. 3 Final From: September 26, 2020 To: October 25, 2020</p>
---	---	---	--

Work Orders Breakdown:

BASE BID SCHEDULE "1" - Chicago Ave. Reconstruction Project - D0-0074

ESTIMATE TO DATE:		\$965,928.05
LESS RETENTION:	5%	48,296.39
LESS PREVIOUSLY INVOICED:		904,236.66
LESS LABOR NON COMPLIANCE:		0.00
TOTAL DUE THIS PAYMENT:		\$13,395.00

BASE BID SCHEDULE "2" - Lloyd Resurfacing Project - B0-0661

ESTIMATE TO DATE:		\$86,548.13
LESS RETENTION:	5%	4,327.41
LESS PREVIOUSLY INVOICED:		80,605.72
LESS LABOR NON COMPLIANCE:		0.00
TOTAL DUE THIS PAYMENT:		\$1,615.00

BASE BID SCHEDULE "3" - Thomas Street Resurfacing Project - B0-0672

ESTIMATE TO DATE:		\$87,600.12
LESS RETENTION:	5%	4,380.01
LESS PREVIOUSLY INVOICED:		81,605.11
LESS LABOR NON COMPLIANCE:		0.00
TOTAL DUE THIS PAYMENT:		\$1,615.00

TOTAL: \$16,625.00
