

**SUBMITTAL TO THE BOARD OF SUPERVISORS
COUNTY OF RIVERSIDE, STATE OF CALIFORNIA**



**ITEM: 3.23
(ID # 14347)**

MEETING DATE:
Tuesday, March 02, 2021

FROM: TLMA-TRANSPORTATION:

SUBJECT: TRANSPORTATION AND LAND MANAGEMENT AGENCY/TRANSPORTATION:
Notice of Completion and Contract Change Order No. 14 –Temescal Canyon Road Widening
Projects and Drainage Improvements Project at Coldwater Creek located within the Community
of Temescal Valley, District 1. [\$309,971 Change Order Cost - State Funds 50%, Local Funds
50%]

RECOMMENDED MOTION: That the Board of Supervisors:

1. Approve and Execute Contract Change Order No. 14 with Beador Construction Company on the Temescal Canyon Road Widening and Drainage Improvement Projects at Coldwater Creek;
2. Accept as Complete the construction of Temescal Canyon Road Widening and Drainage Improvement Projects at Coldwater Creek;
3. Authorize the Chairwoman of the Board to execute the Notice of Completion on behalf of the County; and
4. Direct the Clerk of the Board to record the Notice of Completion.


ACTION: Policy


Mark Lancaster, Director of Transportation 2/3/2021

MINUTES OF THE BOARD OF SUPERVISORS

On motion of Supervisor Jeffries, seconded by Supervisor Hewitt and duly carried by unanimous vote, IT WAS ORDERED that the above matter is approved as recommended.

Ayes: Jeffries, Spiegel, Washington, Perez, and Hewitt
Nays: None
Absent: None
Date: March 2, 2021
xc: Transp., Record

Kecia R. Harper
Clerk of the Board
By: 
Deputy

**SUBMITTAL TO THE BOARD OF SUPERVISORS COUNTY OF RIVERSIDE,
STATE OF CALIFORNIA**

FINANCIAL DATA	Current Fiscal Year:	Next Fiscal Year:	Total Cost:	Ongoing Cost
COST	\$ 309,971	\$ 0	\$ 309,971	\$ 0
NET COUNTY COST	\$ 0	\$ 0	\$ 0	\$ 0
SOURCE OF FUNDS: RCTC Measure A-Regional Arterial (50%), State SB1-Local Partnership Program (50%) There are no General Funds used in this project.			Budget Adjustment:	N/A
			For Fiscal Year:	20/21

C.E.O. RECOMMENDATION: Approve

BACKGROUND:

Summary

By Minute order 3.40, November 6, 2018 the Board of Supervisors entered into an agreement with Beador Construction Company for the construction of the Temescal Canyon Road Widening and Drainage Improvement Projects at Coldwater Creek within the Community of Temescal Valley in Supervisorial District 2.

Contract Change Order No. 14 was necessary to resolve a potential claim regarding cost impacts due to contract time extension delays caused by multiple delay impacts with utilities. The original contract completion time allotted was 207 working days but was increased to 315 working days. The extended contract time also resulted in increased overhead and escalation costs, including bid items and labor. The total amount of this Contract Change Order is, \$309,971 (2.28% of the original contract amount), which exceeds the maximum change order amount that can be authorized by the Director of Transportation and requires Board of Supervisors approval in accordance with Resolution No. 2019-035.

After a thorough review and analysis of the issues and costs of a more formal mediation process, staff is recommending the Board approve Contract Change Order No. 14. By approving this change order amount, the County of Riverside will avoid additional staff administration costs, professional legal fees, and interest paid to the contractor for the potential settlement claim amount and the Contractor expressly waves any other claims related to this project.

Not including this contract change order, the County of Riverside has issued 12 contract change orders totaling \$1,915,679 (14.10% of the original contract amount), which was the result of three (3) major factors:

- Unforeseen utility conflicts and impacts that could not be identified prior to the construction of the project. Utility relocations and various items of additional work was needed to resolve these utility conflicts at the request of the City of Corona, Temescal Valley Water District and Santa Ana Watershed Project Authority (\$787,000).

**SUBMITTAL TO THE BOARD OF SUPERVISORS COUNTY OF RIVERSIDE,
STATE OF CALIFORNIA**

- Modifications and additions to the traffic signal at Dawson Canyon Drive and storm drain facilities due to conflicts with existing utilities and compensation the contractor to provide temporary power to a local business impacted by the construction of the retaining wall improvements (\$243,679).
- Construction of headwall and retaining wall improvements at Cold Water Creek to facilitate the construction of Riverside County Flood Control District's detention basin project. These improvements minimized future disruptions to the public (\$170,000).

The original authorized amount of the contract was \$13,581,730. The total amended contract is \$15,692,642 which is 15.5% more than the originally authorized amount and was the result of 13 contract change orders and bid quantity adjustments as discussed in detail in the attached Contract Change Order Report.

The roadway was open to full public use in June 2020 and the contractor completed all punch list items on July 8, 2020.

Project Nos. C5-0072 and B9-0988

Impact on Residents and Businesses

The proposed improvements will increase safety, reduce vehicle emissions, improve access for emergency service responders, and improve the quality of life for residents and commuters along the Temescal Valley corridor.

Additional Fiscal Information

Budget

Original Contract Amount		\$13,581,730
Total Change Orders Authorized	16.4%	\$2,225,650
Estimated Pending Change Orders	0.0%	\$0
Authorized Contract Amount		\$15,807,380
* Quantity Adjustments	-0.8%	(\$114,738)
+ CCO FA Adjustments	0.0%	\$0
Total Amended Contract Amount	115.5%	\$15,692,642

Expenditures

Total Progress Payments	\$15,692,642
Estimated Pending Payments	\$0
Total Expenditures	\$15,692,642

(Over)/Under Contract Amount \$0

**SUBMITTAL TO THE BOARD OF SUPERVISORS COUNTY OF RIVERSIDE,
STATE OF CALIFORNIA**

+ Change Orders using the Force Account method of payment issued prior to the work being completed generally do not use the total authorized amount.

* Caltrans Standard Specifications 9-1.06 (Changed Quantity Payment Adjustments). Increases or decreases in the quantity of a contract item of work will be determined by comparing the total pay quantity of such item of work with the Engineer's Estimate. If the total pay quantity of any item of work required under the contract varies from the Engineer's Estimate by 25 percent or less, payment will be made for the quantity of work of said item performed at the contract unit price, unless eligible for adjustment pursuant to Section 9-1.15, "Work-Character Changes."

This project was funded with \$6,350,000 of RCTC Measure A-Regional Arterial, \$6,350,000 of State SB-1 Local Partnership Program, \$502,953 of TUMF-NW Zone, \$496,684 of DIF AP6 Major Improvement Temescal Canyon Area, \$220,000 of Temescal Valley Community, \$73,583 of Gas Tax/HUTA, \$52,000 Ash Fees, \$867,865 of City of Corona, \$451,710 of Temecula Valley Water, \$287,100 of Elsinore Valley Municipal Water District and \$40,747 of Santa Ana Water Project Authority funds.

Contract History and Price Reasonableness

N/A

ATTACHMENTS:

Change Order Report
Vicinity Map
Change Order Letter of Transmittal
Progress Estimate Report
Notice of Completion



Jason Farin, Principal Management Analyst 2/23/2021



Gregory L. Priamos, Director County Counsel 2/9/2021

LETTER OF TRANSMITTAL

**Local Agency: County of Riverside
Transportation Department**

DATE: December 10, 2020

**File: Temescal Canyon Road Widening
Projects**

W.O. No.: C5-0072

C.C.O.: 14

TO: Patricia Romo

From: Cindi Wachi

\$309,970.60 (2.28% of the original contract amount of \$13,988,730)

The Contractor has filed a Notice of Potential Claim for several issues in the construction of the Temescal Canyon Road Widening project in the Temescal Valley area of the County. After numerous meetings and discussions, this Contract Change Order is the result of negotiations between the parties for closing out the project which includes settlement of all outstanding claims, requests for time extensions, extended field overhead or home office overhead costs, escalation costs and all cumulative impact on work under the contract.

The amount of \$545,474.00 comprises the total settlement due the Contractor (and all subcontractors and suppliers) for all the claims. Contractor expressly waives any other claims related to this project.

This Contract Change Order includes \$235,503.40 of deletion and reduction of contract bid items not needed for the project. The amount of this Contract Change Order is \$309,970.60. The accumulation of all Contract Change Orders thus far, including this one, is \$2,225,649.92.

Previous Contract Change Order Amounts Approved:

See C.C.O. History
(attached)

\$1,915,679.32

File: Temescal Canyon Road Widening Projects

W.O. No.: C5-0072

C.C.O. No. 14

Page 2

This Contract Change Order was discussed with County Staff and they gave their concurrence to this change.

Adjustment of Time: 0 working days

ESTIMATE OF COST

Items	(\$235,503.40)
Force Account	
Agreed Lump Sum	\$545,474.00
Adjustment	
TOTAL	\$309,970.60

Cindi A. Wachi

Cindi Wachi

Engineering Division Manager

CCO	Amount	Funding Source
14	\$309,970.60	RCTC Measure A-Regional Arterial (50%), State SB1-Local Partnership Program (50%)

CCO Category		
AFA	Anticipated Force Account	
CFC	Changed Field Condition	√
CME	Contract Management Error	
DO	Design Omission	
OAM	Outside Agency Mandate	
RWO	Right-of-Way Obligation	
SE	Survey Error	
UB	Upgrade/Betterment	
UI	Utility Interference	



COUNTY OF RIVERSIDE
TRANSPORTATION DEPARTMENT

SHEET 2 OF 2 SHEETS

Contract Change Order No. 14

CONTRACT: Temescal Canyon Road Widening Projects

WORK ORDER NO. C5-0072
CALTRANS EA NO. _____
LOCAL-FED AID NO. _____
STATE-FED AID NO. LPPSB1L-5956(267)

TO: **Beador Construction** CONTRACTOR: YOU ARE HEREBY DIRECTED TO MAKE THE HEREIN DESCRIBED CHANGES FROM THE PLANS AND SPECIFICATIONS OR DO THE FOLLOWING DESCRIBED WORK NOT INCLUDED IN THE PLANS AND SPECIFICATIONS ON THIS CONTRACT.

Description of work to be done, estimate of quantities and prices to be paid. Segregated between additional work at contract price, agreed price and force account. Unless otherwise stated, rates for rental of equipment cover only such time as equipment is actually used and no allowance will be made for idle time.

Agreed Compensation for Settlement of Claims:

In accordance with Section 9-1.17D, "Final Payment and Claims," of the Standard Specifications, compensate the contractor for extended costs due to contract time extension, delays and impacts. A final determination of all costs for overhead, lump sum bid items, liquidated damages, deductions, and potential claims of damages, corrections and extra work has been reached as a resolution with an agreed lump sum payment adjustment. For the above listed claims, the contractor agrees to accept a lump sum payment of \$545,474.00 including all markups for this change. This change order provides full and final compensation for and resolves all aspects of the contractor's Claim and further agrees to be barred from arbitration.

Estimate of Agreed Lump Sum: \$545,474.00

Estimated Cost for this Contract Change Order: \$309,970.60

Estimated Cost: Decrease \$ _____ Increase \$309,970.60

Participating: Yes: No: N/A:

WE, the undersigned contractor, have given careful consideration to the change proposed and hereby agree that we will provide all equipment, furnish all materials, except as may otherwise be noted above, and perform all services necessary for the work above specified, and will accept as full payment therefor the prices shown above. By reason of this proposed change 0 days adjustment of time will be allowed.

Accepted DAVID A. BEADOR 12/2/20
Beador Construction Date

NOTE: This change order is not effective until approved by County. If the Contractor does not sign acceptance of this order, his attention is directed to the requirements of the specifications as to proceeding with the ordered work and filing a written protest with the time therein specified.

Cindi Wachi 11/24/2020
Approval Recommended Date
Cindi Wachi, Engineering Division Manager

Patricia Romo 12/10/2020
Approved Date
Patricia Romo, Director of Transportation

Karen S. Spiegel 03-02-2021
Approved Date
Chair, Riverside County Board of Supervisors
KAREN SPIEGEL

WITNESSES:
KECIA R. HARPER, Clerk
BY DUSTY GAY DEPUTY

Temescal Canyon Road Widening
 Contract CCO History

Contract No. 18-10-002
 Work Order No. C5-0072, C6-0066, B9-0988
 Contract Amount \$13,581,730.00

Single Maximum CCO \$210,000.00
 Maximum CCO's \$1,358,173.00

CCO Category Legend	
AFA	Anticipated Force Account
CFC	Changed Field Conditon
CME	Contract Management Error
DO	Design Omission
OAM	Outside Agency Mandate
RWO	Right-of-Way Obligation
SE	Survey Error
UB	Upgrade/Betterment
UI	Utility Interference

CCO No.	Amount This CCO	Authority	Cumulative CCO's	% Original Authorized	Cumulative CCO %	CCO Category	Classification
1	\$170,000.00	Director	\$170,000.00	1.25%	1.25%	CFC	Unavoidable
2	\$190,000.00	Director	\$360,000.00	1.40%	2.65%	CFC	Unavoidable
3	\$200,000.00	Director	\$560,000.00	1.47%	4.12%	CFC	Unavoidable
4	\$197,000.00	Director	\$757,000.00	1.45%	5.57%	OAM	Extra/Others
5	\$200,000.00	Director	\$957,000.00	1.47%	7.05%	CFC	Unavoidable
7	\$206,000.00	Director	\$1,163,000.00	1.52%	8.56%	CFC	Unavoidable
10	\$150,000.00	Director	\$1,313,000.00	1.10%	9.67%	CFC	Unavoidable
8	\$5,000.00	Director	\$1,318,000.00	0.04%	9.70%	CFC	Unavoidable
9R	\$4,147.74	Director	\$1,322,147.74	0.03%	9.73%	DO	Avoidable
13	\$28,531.58	Director	\$1,350,679.32	0.21%	9.94%	CFC	Unavoidable
9S1	\$150,000.00	Board	\$1,500,679.32	1.10%	11.05%	DO	Avoidable
12	\$415,000.00	Board	\$1,915,679.32	3.06%	14.10%	CFC	Unavoidable
14	\$309,970.60	Board	\$2,225,649.92	2.28%	16.39%	CFC	Unavoidable
			\$2,225,649.92	16.39%			

New Authorized Contract Total	\$15,807,379.92
Total CCO Dollars To Date	\$2,225,649.92
Total % Increased by CCO's	16.39%

COUNTY OF RIVERSIDE
TRANSPORTATION DEPARTMENT



Temescal Canyon Road Widening Projects

**Dawson Canyon Road to 0.7 Mile North,
Dos Lagos Drive to Leroy Road, and**

**Temescal Canyon Road Slurry Seal Project
0.7 Mile North of Dawson Canyon Road to Leroy Road**

In the Community of Temescal Valley

**Project No. C5-0072, C6-0066
State Project No. LPPSB1L-5956(267)**

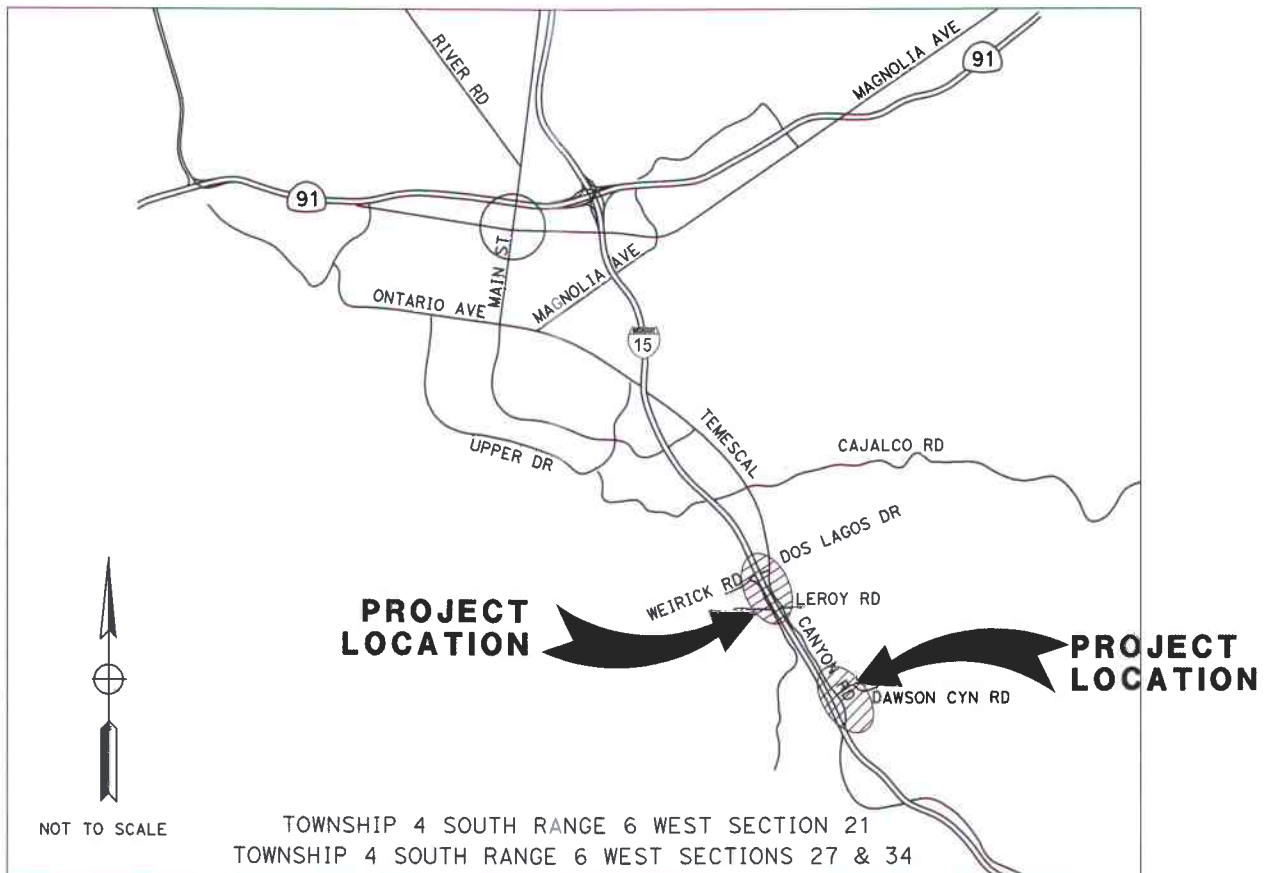
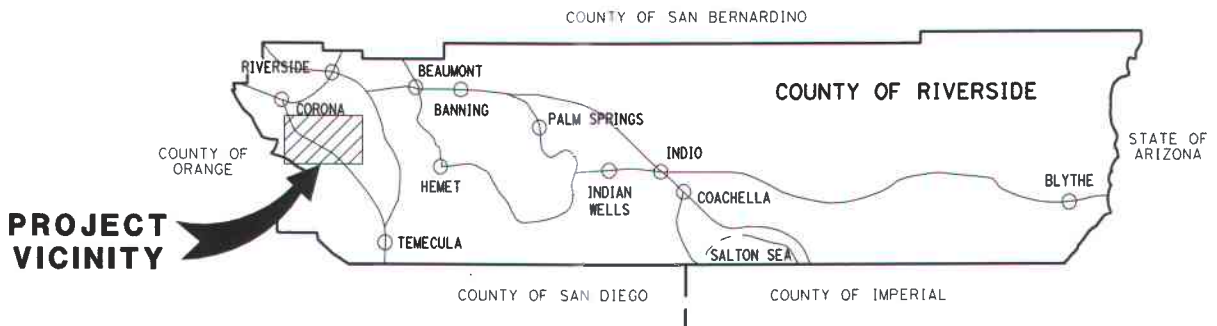


VICINITY MAP

COUNTY OF RIVERSIDE
TRANSPORTATION DEPARTMENT

**Temescal Canyon Road
Drainage Improvement Project
At Coldwater Creek**

**In the Community of Temescal Valley
Project No. B9-0988**

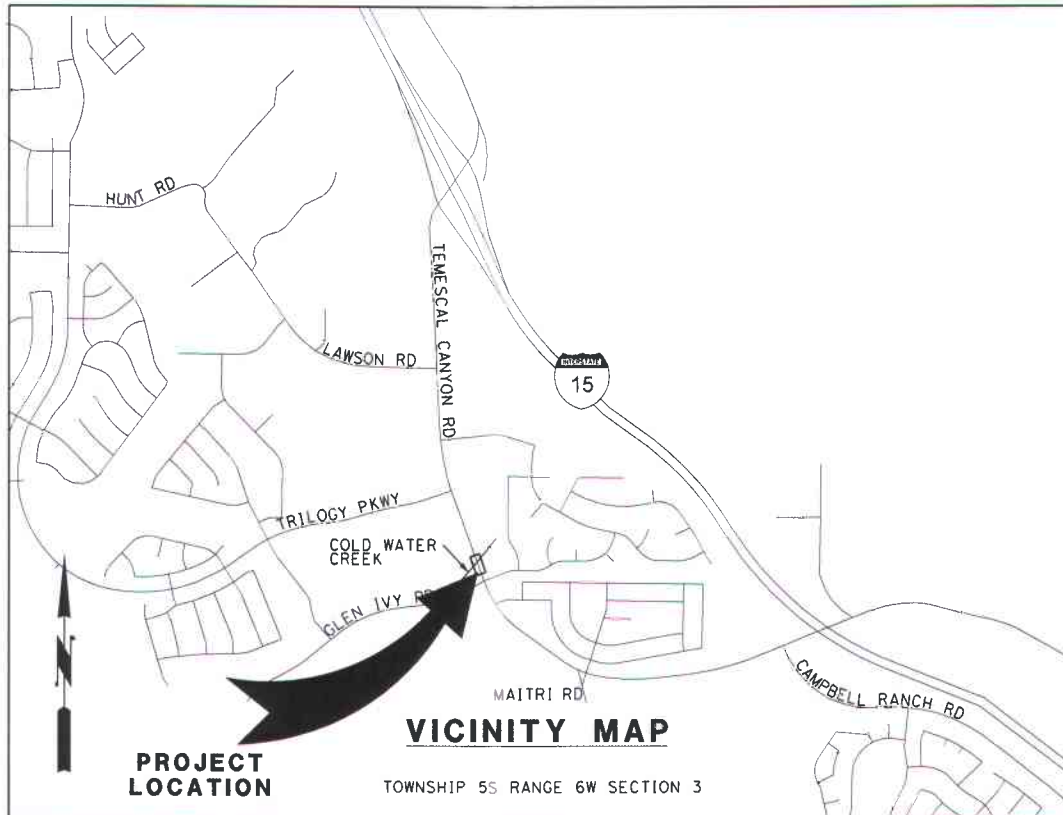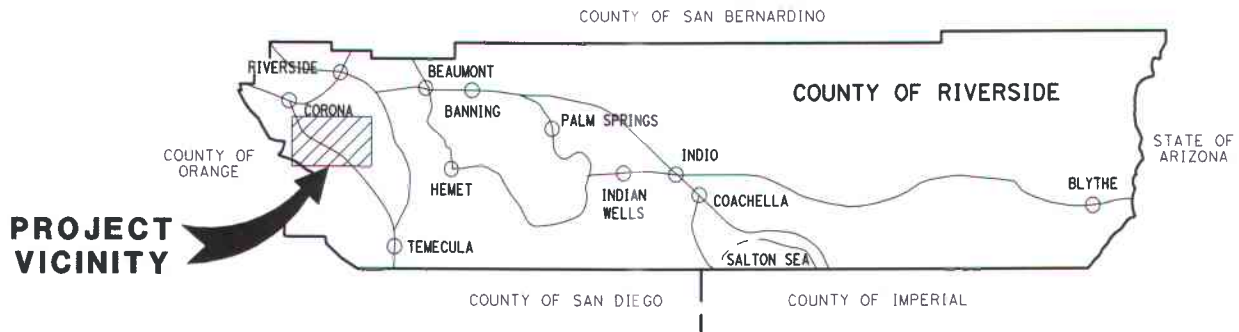

VICINITY MAP

CHANGE ORDER REPORT
(Temescal Canyon Road Widening and Drainage Project)

CCO #	Amount	Percent	Description
	Original Contract Amount \$13,581,730		
1	\$170,000	1.25%	Additional concrete headwall/retaining wall, including footing, was needed to accommodate the County of Riverside Flood Control District (RCFC) detention basin project. This additional work eliminated the need for RCFC to impact the culvert Improvements and the traveling public during the construction of their project.
2	\$190,000	1.40%	Santa Ana Water Project Authority (SAWPA) required all of their facilities to be protect in place within the project limits. Due to the existing field conditions and discussions with SAWPA, the protection plan for the SAWPA lines was revised. This work will be reimbursed by SAWPA.
3	\$200,000	1.47%	The City of Corona requested the relocation of water services and appurtenances that are in conflict with the construction of the widening of project. Exploratory potholing was necessary to properly identify utility depths and locations. This work will be reimbursed by the City of Corona.
4	\$197,000	1.45%	During the material submittal process the City of Corona determined that Ductile Iron Pipe (DIP) was prone to leaking over an extended period of time and requested a change in material from DIP to Cement Mortar Lined and Coated pipe. Due to the change in material, scope of work and unforeseen work associated with this relocation, it was deemed necessary by the City to proceed on Force Account. This work will be reimbursed by the City of Corona.
5	\$200,000	1.47%	Existing Temescal Valley Water District (TVWD) lines, blind flanges, blow-off valves and other facilities were not identified or shown on the project plans. Therefore, the contractor performed additional work including potholing and relocating facilities and appurtenances of the existing TVWD lines to accommodate the installation of the new storm drain lines per the approved project plans. This work will be reimbursed by TVWD.
7	\$206,000	1.52%	Utility conflicts within the project limits were not identified prior to construction. The contractor was directed to remove and/or relocate these utility conflicts in order to continue and not the delay the construction of the storm drain systems and other proposed improvements.
8	\$5,000	0.04%	The contractor was compensated for half of the invoiced costs for Alternate Dispute Resolution (DRA). DRA services were required. The project encountered a number of utility conflicts, significant delays were noted, and work was delayed, resulting in unforeseen cost.
9	\$4,148	0.03%	Installation of permanent erosion control measures to comply with the California Water Board Construction General Permit.

CHANGE ORDER REPORT
(Temescal Canyon Road Widening and Drainage Project)

10	\$150,000	1.10%	Modifications and additions to the traffic signal at Dawson Canyon Road due to conflicts with existing utilities. Contractor was also compensated to provide temporary power to local business due to construction of the retaining wall improvements.
13	\$28,532	0.21%	Miscellaneous work, including replace unsuitable material with geogrid fabric and class II aggregate base, Rockefeller paving and EVMWD Trench Repair.
9S1	\$150,000	1.10%	Installation of hydroseed for permanent erosion control measures to comply with the California Water Board Construction General Permit.
12	\$415,000	3.06%	Relocation of the existing City of Corona 18" waterline that is in direct conflict with the storm drain facility. The City of Corona requested the contractor to perform the work at force account. This work will be reimbursed by the City of Corona.
14	\$309,971	2.28%	Negotiations between the County and the Contractor resulted in a settlement of all outstanding claims, requests for time extensions, overhead and escalation costs and all impacts on work.
Quantity Adjustments	(\$114,738)	(0.8%)	
Change Order Total and New Contract Total	\$15,692,642		

PROJECT: Temescal Canyon Road Widening Projects, Temescal Canyon Slurry Seal Project and Temescal Canyon Road Drainage Improvement Project at Colobster Creek
 County Project No.: CS-4972, State Project No. LPPS81L-0886(2871) and 89-0886
 Contract No. 18-10-802

Contractor: Beador Construction Co.
 Address: 26320 Leister Circle
 City, State, Zip: Corona, CA 92883



Estimate No. 26 Final
 From: November 26, 2020
 To: December 23, 2020

Item No	Item Description	Units	Quantity	Unit Price	Original Contract Amount	Change Authorized Quantity	Change Authorized Amount	Total Authorized Quantity	Total Authorized Amount	This Estimate Quantity	This Estimate Amount	Previous Quantity	Previous Amount	Total Estimate To Date Quantity	Total Estimate To Date Amount	% Auth
	BASE BID SCHEDULE "1 & 2" - TEMESCAL CANYON ROAD WIDENING PROJECTS AND SLURRY SEAL - CS-4972 (Dresson Canyon and Dos Lagos Segments)				13,247,845 00		2,056,124 92		15,303,969 92		559,896 56		559,896 56		15,195,957 19	
	BASE BID SCHEDULE "3" - TEMESCAL CANYON ROAD DRAINAGE IMPROVEMENT PROJECT AT COLUMBIA CREEK - 89-0886				353,865 00		169,525 00		503,410 00		0 00		0 00		498,664 47	
PROJECT TOTAL					13,591,730 00		2,225,649 92		15,807,379 92		559,896 56		559,896 56		15,892,641 99	

Made by: David Hytkama
 Checked by: TN
 OK Const. Supv: HD

Working Days: 207
 Days Added: 108
 Subtotal: 315
 Days Used: 315
 % Time Elapsed: 100%

Start Date: 12-10-18
 End Date: 10-9-19
 % Complete: 99%
 Original Contract: \$13,581,730 00
 Amended Contract: \$15,807,379 92

TOTAL VALUE OF WORK TO DATE: \$15,692,641 66
 LESS RETENTION: 1% 156,926 38
 TOTAL DUE TO DATE: \$15,535,715 28
 LESS PREVIOUSLY INVOICED: 14,830,090 25
 LESS LABOR NON COMPLIANCE: 0 00
 TOTAL DUE THIS PAYMENT: \$705,625 03

This Estimate Approved _____ Date: _____ for: _____

Mark Lancaster, Director of Transportation

\$705,625 03

Received by Accounts Payable: _____

By: _____

Quantities on This Estimate Approved _____ Date: 12/31/20

Beador Construction Company

Payment Approval

FUND: 20000
 DEPT. ID: 31305
 ACCOUNT: 527980
 PROJECT: ZCS-0988E
 ACTIVITY ID: Z3500
 RESOURCE CNT

SIGNATURE: *Travis A. Wach*
 DATE: 01/08/2021



Contractor: Trenchal Construction Co.
Address: 35330 Lester Circle
City, State, Zip: Corona, CA 92883

PROJECT: Trenchal Canyon Road Widening Projects, Trenchal Canyon Slurry Seal Project and Trenchal Canyon Road Drainage Improvement Project at Coldwater Creek
County Project No. CS-0072, State Project No. LPPS81L-006(287) and BS-0000
Contract No. 16-18-002

Estimate No. 28 Final
From: November 28, 2020
To: December 23, 2020

Item No.	Item Description	Units	Quantity	Unit Price	Original Contract Amount	Charge Authorized Quantity	Charge Authorized Amount	Total Authorized Quantity	Total Authorized Amount	This Estimate Quantity	Amount	Previous Quantity	Amount	Total Estimate To Date Quantity	Total Estimate To Date Amount	% Auth.
1	BASE BID SCHEDULE "A" & "P" - TERRAZZO CANYON ROAD WIDENING PROJECTS AND SLURRY SEAL - CS-0072 (Downstream Canyon and Dos Lagos Segments)	SOYD	9,870	4.00	39,480.00			9,870.00	39,480.00			10,481.00		10,481.00	41,924.00	100%
2	CATCH BASIN (CURB INLET) WITH FULL TRASH CAPTURE DEVICE (CRS 300) [L=21', D=13"]	EA	1	20,500.00	20,500.00			1.00	20,500.00			1.00		1.00	20,500.00	100%
3	CATCH BASIN (CURB INLET) WITH FULL TRASH CAPTURE DEVICE (CRS 300) [L=21', D=9"]	EA	2	17,300.00	34,600.00			2.00	34,600.00			2.00		2.00	34,600.00	100%
4	CATCH BASIN (CURB INLET) WITH FULL TRASH CAPTURE DEVICE (CRS 300) [L=17', D=9"]	EA	4	9,000.00	36,000.00			4.00	36,000.00			4.00		4.00	36,000.00	100%
5	CATCH BASIN (CURB INLET) WITH FULL TRASH CAPTURE DEVICE (CRS 300) [L=14', D=9"]	EA	5	14,500.00	72,500.00			5.00	72,500.00			5.00		5.00	72,500.00	100%
6	TOE OF SLOPE DITCH INLET	EA	1	27,500.00	27,500.00			1.00	27,500.00			1.00		1.00	27,500.00	100%
7	CONCRETE DROP INLET WITH FULL TRASH CAPTURE DEVICE (RCFC & WCDS CB110) (D=6")	EA	1	6,500.00	6,500.00			1.00	6,500.00			1.00		1.00	6,500.00	100%
8	CIP DRAINAGE INLET (TYPE G1) WITH FULL TRASH CAPTURE DEVICE (CSP RSP DT20)	EA	1	9,100.00	9,100.00			1.00	9,100.00			1.00		1.00	9,100.00	100%
9	PRECAST DRAINAGE INLET (TYPE G1) (CSP DT38) & CGO 14	EA	1	3,200.00	3,200.00	-1.00	-3,200.00									N/A
10	PRECAST 24"X24" INLET, FRAME, AND GRATE	EA	6	2,150.00	12,900.00			6.00	12,900.00			7.00		7.00	15,050.00	117%
11	CONCRETE COLLAR	EA	7	1,900.00	13,300.00			7.00	13,300.00			8.00		8.00	15,200.00	114%
12	MANHOLE NO. 2 (RCFC & WCDS MH252) [CONNECTS RCP RANGE LF TO 38"]	EA	2	7,250.00	14,500.00			2.00	14,500.00			2.00		2.00	14,500.00	100%
13	MANHOLE NO. 4 (RCFC & WCDS MH254) [CONNECTS RCP RANGE 42" TO 48"]	EA	4	9,100.00	36,400.00			4.00	36,400.00			4.00		4.00	36,400.00	100%
14	MANHOLE NO. 4 (RCFC & WCDS MH254) [CONNECTS TO 80" X 38" RCP]	EA	4	11,800.00	47,200.00			4.00	47,200.00			4.00		4.00	47,200.00	100%
15	MANHOLE NO. 4 (RCFC & WCDS MH254) [CONNECTS RCP RANGE 24" TO 38"]	EA	2	6,500.00	13,000.00			2.00	13,000.00			2.00		2.00	13,000.00	100%
16	TRANSITION STRUCTURE NO.3 (RCFC & WCDS TS303) [CONNECTS RCP RANGE 24" TO 38"]	EA	5	8,500.00	42,500.00			5.00	42,500.00			5.00		5.00	42,500.00	100%
17	MINOR CONCRETE (CURB AND GUTTER) (CRS 200) & CGO 9	LF	13,280	24.00	318,720.00	-670.00	-16,080.00	12,610.00	302,640.00			12,426.00		12,426.00	298,272.00	95%
18	MINOR CONCRETE (PARKING LOT V-GUTTER)	LF	105	60.00	6,300.00			105.00	6,300.00			105.00		105.00	6,300.00	100%
19	MINOR CONCRETE (TYPE "D" CURB) (CRS 204)	LF	330	35.00	11,550.00			330.00	11,550.00			412.50		412.50	14,437.50	125%

PROGRESS ESTIMATE RECORD - COUNTY OF RIVERSIDE

PROJECT: Temescal Canyon Road Widening Project, Temescal Canyon Slurry Seal Project and Temescal Canyon Road Drainage Improvement Project - Check or Check
 County Project No.: CS-0072, State Project No.: LPPB81L-68662577 and ES-8986
 Contract No. 18-16-062

Contractor: Beadler Construction Co.
 Address: 26330 Leister Circle
 City, State, Zip: Corona, CA 92883



Estimate No. 26 Final
 From: November 26, 2020
 To: December 23, 2020

Item No.	Item Description	Units	Quantity	Unit Price	Original Contract Amount	Change Authorized Quantity	Change Authorized Amount	Total Authorized Quantity	Total Authorized Amount	This Estimate		Previous		% Auth.
										Quantity	Amount	Quantity	Amount	
39	ITEM DELETED PER ADDENDUM No 5	---	0	0.00	0.00									N/A
40	HYDROSEED EROSION CONTROL & CCO 14	SQYD	289,190	0.30	80,748.00	-251,304.00	-75,415.20	17,776.00	5,332.80	17,776.00	17,776.00	17,776.00	5,332.80	100%
41	CLASS 2 AGGREGATE BASE	CY	18,710	34.00	588,140.00			18,710.00	588,140.00	18,710.00	18,234.00	18,234.00	620,838.00	100%
42	HOT MIX ASPHALT (TYPE A)	TON	24,880	66.00	1,642,080.00	-1,000.00	-66,000.00	23,880.00	1,576,080.00	23,880.00	24,128.11	24,128.11	1,592,455.26	101%
42A	TEMPORARY HOT MIX ASPHALT PAVEMENT (TYPE A) & CCO 8	FA	1	48,000.00	48,000.00	(0.2450535)	-11,782.57	0.7549465	36,217.43	0.7549465	0.7549464	0.7549464	36,237.43	100%
43	RUBBERIZED HOT MIX ASPHALT (TYPE G)	TON	2,650	84.00	223,400.00			2,650.00	223,400.00	2,650.00	2,628.28	2,628.28	220,775.52	92%
44	PAVEMENT REINFORCING GRID & CCO 9	SQYD	4,360	9.00	39,240.00	-2,400.00	-21,600.00	1,960.00	17,640.00	1,960.00	1,960.00	1,960.00	17,640.00	100%
45	REMOVE CONCRETE PAVEMENT (BELOW EXIST AC PAVEMENT)	SQYD	11,000	6.50	71,500.00			11,000.00	71,500.00	11,000.00	13,750.00	13,750.00	89,375.00	125%
46	RETAINING WALL (CALTRANS TYPE 7, MOD) (MAX HT 12')	SQFT	4,000	150.00	600,000.00			4,000.00	600,000.00	4,000.00	4,000.00	4,000.00	600,000.00	100%
47	MASONRY RETAINING WALL (SPPWC 018-3) (MAX HT 6')	SQFT	1,410	37.00	52,170.00			1,410.00	52,170.00	1,410.00	1,410.00	1,410.00	52,170.00	100%
48	MINOR CONCRETE (HEADWALLS AND WINGWALLS)	CY	285	785.00	208,025.00			285.00	208,025.00	285.00	285.00	285.00	208,025.00	100%
49	MINOR CONCRETE (REINFORCED CONCRETE CAP)	CY	609	270.00	164,430.00			609.00	164,430.00	609.00	609.00	609.00	164,430.00	100%
50	ITEM DELETED PER ADDENDUM No 5	---	0	0.00	0.00									N/A
51	8" PLASTIC PIPE (ASTM D3034 SDR 23.5)	LF	447	60.00	26,820.00			447.00	26,820.00	447.00	420.00	420.00	25,200.00	94%
52	12" PLASTIC PIPE (ASTM D3034 SDR 23.5)	LF	104	80.00	8,320.00			104.00	8,320.00	104.00	117.00	117.00	9,380.00	113%
53	16" REINFORCED CONCRETE PIPE (CLASS II)	LF	168	50.00	8,400.00			168.00	8,400.00	168.00	159.00	159.00	7,950.00	95%
54	24" REINFORCED CONCRETE PIPE (CLASS V)	LF	975	110.00	107,250.00			975.00	107,250.00	975.00	963.00	963.00	105,930.00	99%
55	24" REINFORCED CONCRETE PIPE W/ WATER TIGHT JOINTS (CLASS V)	LF	180	110.00	19,800.00			180.00	19,800.00	180.00	175.00	175.00	19,250.00	97%
56	30" REINFORCED CONCRETE PIPE (CLASS II)	LF	1,745	120.00	209,400.00			1,745.00	209,400.00	1,745.00	1,732.00	1,732.00	207,840.00	99%
57	30" REINFORCED CONCRETE PIPE W/ WATER TIGHT JOINTS (CLASS II)	LF	360	120.00	43,200.00			360.00	43,200.00	360.00	358.00	358.00	42,960.00	99%
58	48" REINFORCED CONCRETE PIPE (CLASS II) & CCO 9	LF	30	450.00	13,500.00	-15.00	-6,750.00	15.00	6,750.00	15.00	15.00	15.00	6,750.00	100%
59	42" REINFORCED CONCRETE PIPE (CLASS II)	LF	108	215.00	22,780.00			108.00	22,780.00	108.00	104.00	104.00	22,360.00	98%
60	66" REINFORCED CONCRETE PIPE (CLASS II)	LF	610	600.00	366,000.00			610.00	366,000.00	610.00	610.00	610.00	366,000.00	100%
61	60" X 3/8" ELLIPTICAL RCP W/ WATER TIGHT JOINTS (CLASS III)	LF	915	380.00	329,400.00			915.00	329,400.00	915.00	915.00	915.00	329,400.00	100%
62	66" X 1/2" CORRUGATED STEEL PIPE ARCH W/ WATER TIGHT JOINTS (108" THICK)	LF	75	360.00	27,000.00			75.00	27,000.00	75.00	71.00	71.00	25,560.00	95%

PROGRESS ESTIMATE RECORD - COUNTY OF RIVERSIDE

SHEET 6 of 10

Processed Construction Inspection 1/8/2021

PROJECT: Temescal Canyon Road Widening Project, Temescal Canyon Slurry Seal Project and Temescal Canyon Road Drainage Improvement Project at Colorado Creek
 County Project No. CS-8072, State Project No. LPPS87L-6986(2587) and B4-0988
 Contract No. 18-1P-002

Contractor: Beador Construction Co.
 Address: 26320 Lestar Circle
 City, State, Zip: Corona, CA 92683



Estimate No. 28 Final
 From: November 26, 2020
 To: December 26, 2020

Item No	Item Description	Units	Quantity	Unit Price	Original Contract Amount	Change Authorized Quantity	Change Authorized Amount	Total Authorized Quantity	Total Authorized Amount	This Estimate Quantity	This Estimate Amount	Previous Quantity	Previous Amount	Total Estimate To Date Quantity	Total Estimate To Date Amount	% Auth
110	REMOVE THERMOPLASTIC PAVEMENT MARKING & CCO 13	SOFT	300	0.90	270.00	-300.00	-270.00	0.00	0.00	0.00	0.00	198,128.89	198,128.89	198,128.89	198,128.89	95%
CCO 7	POT HOLLING, EXCAVATING, FORMING, PLACING & RELOCATING UTILITIES		0	1.00	0.00	206,000.00	206,000.00	206,000.00	206,000.00	206,000.00	206,000.00	77,895.80	77,895.80	77,895.80	77,895.80	100%
CCO 10	ELECTRICAL CHANGES & CCO 14		0	1.00	0.00	77,895.80	77,895.80	77,895.80	77,895.80	77,895.80	77,895.80					N/A
CCO 8	ALTERNATE DISPUTE RESOLUTION & CCO 14		0	1.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00					N/A
CCO 9	PERMANENT SLOPE BMP'S	FA	0	1.00	0.00	123,605.31	123,605.31	123,605.31	123,605.31	123,605.31	123,605.31					100%
CCO 9S1	PERMANENT SLOPE BMP'S	FA	0	1.00	0.00	150,000.00	150,000.00	150,000.00	150,000.00	150,000.00	150,000.00					97%
CCO 13	UTILITY CONFLICTS, ADDITIONAL PARKING LOT, DRIVEWAY GRADING, ETC	FA	0	1.00	0.00	203,377.58	203,377.58	203,377.58	203,377.58	203,377.58	203,377.58					100%
CCO 14	FINAL PAYMENT AND CLAIMS	LS	0	1.00	0.00	545,474.00	545,474.00	545,474.00	545,474.00	545,474.00	545,474.00					100%
111	ALTERNATE BID SCHEDULE "A" - CITY OF CORONA - UTILITY RELOCATIONS - Dawson Canyon Segment	LS	1	112,000.00	112,000.00	-1.00	-112,000.00	112,000.00	112,000.00	112,000.00	112,000.00					N/A
112	RELOCATE 18" CHMLC PIPE CROSSING DAWSON LINE B AND LINE C - LOCATION 1) & CCO 4	LS	1	87,000.00	87,000.00	-1.00	-87,000.00	87,000.00	87,000.00	87,000.00	87,000.00					N/A
113	RELOCATE 18" CHMLC PIPE CROSSING DAWSON LINE D - LOCATION 2) & CCO 4	EA	1	8,100.00	8,100.00	-1.00	-8,100.00	8,100.00	8,100.00	8,100.00	8,100.00					N/A
114	RELOCATE AIR RELEASE VACUUM VALVE & CCO 4	EA	2	8,000.00	16,000.00	-2.00	-16,000.00	16,000.00	16,000.00	16,000.00	16,000.00					N/A
115	RELOCATE WATER PRESSURE RELEASE VALVE & CCO 4	EA	1	14,000.00	14,000.00	-1.00	-14,000.00	14,000.00	14,000.00	14,000.00	14,000.00					N/A
116	CONNECT TO EXISTING 8" FIRE SERVICE SALVAGE AND REINSTALL DBL DETECTOR CHECK ASBY & CCO 4	EA	1	20,000.00	20,000.00	-1.00	-20,000.00	20,000.00	20,000.00	20,000.00	20,000.00					N/A
117	SUPPORT EXISTING UTILITIES & CCO 4	EA	1	12,900.00	12,900.00	-1.00	-12,900.00	12,900.00	12,900.00	12,900.00	12,900.00					N/A
CCO 3	CITY OF CORONA	FA	0	1.00	0.00	200,000.00	200,000.00	200,000.00	200,000.00	200,000.00	200,000.00					98%
CCO 4	CITY OF CORONA	FA	0	1.00	0.00	470,000.00	470,000.00	470,000.00	470,000.00	470,000.00	470,000.00					99%
CCO 12	CITY OF CORONA	FA	0	1.00	0.00	415,000.00	415,000.00	415,000.00	415,000.00	415,000.00	415,000.00					98%
	ALTERNATE BID SCHEDULE "B" - NOT AWARDED - ITEMS 114-118															
	ALTERNATE BID SCHEDULE "C" - V.V.M. UTILITY RELOCATIONS (Dawson Canyon Segment)															
129	RELOCATE 20" PIPE CROSSING DAWSON SEGMENT LINE B AND LINE C1	LS	1	100,000.00	100,000.00	1.00	100,000.00	100,000.00	100,000.00	100,000.00	100,000.00					100%
130	RELOCATE 14" CHMLC PIPE CROSSING DAWSON SEGMENT LINE B AND LINE C1	LS	1	83,000.00	83,000.00	1.00	83,000.00	83,000.00	83,000.00	83,000.00	83,000.00					100%

PROGRESS ESTIMATE RECORD - COUNTY OF RIVERSIDE



Contractor: Baador Construction Co.
Address: 38326 Lester Circle
City, State, Zip: Corona, CA 92883

Estimate No. 28 Final
From: November 28, 2020
To: December 25, 2020

PROJECT: Temescal Canyon Road Widening Project, Temescal Canyon Shurry Seal Project and Temescal Canyon Road Drainage Improvement Project at Colowater Creek
County Project No. CS-0072, State Project No. LPP881L-886(257) and 88-0988
Contract No. 18-18-052

Item No.	Item Description	Units	Quantity	Unit Price	Original Contract Amount	Change Authorized Quantity	Change Authorized Amount	Total Authorized Quantity	Total Authorized Amount	This Estimate Quantity	This Estimate Amount	Previous Quantity	Previous Amount	Total Estimate To Date Quantity	Total Estimate To Date Amount	% Auth.
131	ADJUST MANHOLE TO GRADE	EA	7	770.00	5,390.00			7.00	5,390.00			7.00		7.00	5,390.00	100%
132	RECONSTRUCT TOP OF MANHOLE	EA	2	2,700.00	5,400.00			2.00	5,400.00			2.00		2.00	5,400.00	100%
133	RELOCATE AIR RELEASE VACUUM VALVE	EA	3	5,900.00	17,700.00			3.00	17,700.00			3.00		3.00	17,700.00	100%
134	RELOCATE WATER METER & COO 14	EA	3	7,250.00	21,750.00	-2.00	-14,500.00	1.00	7,250.00			1.00		1.00	7,250.00	100%
135	RELOCATE WATER METER AND PROVIDE WATER METER ENCLOSURE	EA	1	11,200.00	11,200.00			1.00	11,200.00			1.00		1.00	11,200.00	100%
136	RELOCATE WATER PRESSURE RELEASE VALVE	EA	1	9,600.00	9,600.00			1.00	9,600.00			1.00		1.00	9,600.00	100%
136A	SUPPORT EXISTING UTILITIES	LS	1	15,960.00	15,960.00			1.00	15,960.00			1.00		1.00	15,960.00	100%
CCO 5	EXISTING TIVID LINES	FA	0	1.00	0.00	200,000.00	200,000.00	200,000.00	200,000.00			196,209.69	196,209.69	196,209.69	98%	
	ALTERNATE BID SCHEDULE "D" - EYEMID - UTILITY RELOCATIONS (Dawson Canyon and Dos Lagos Segments)															
137	RELOCATE 42" PIPE CROSSING DAWSON SEGMENT LINE B AND LINE C	LS	1	205,000.00	205,000.00			1.00	205,000.00			1.00		1.00	205,000.00	100%
138	42" BUTTERFLY VALVE, FLANGED ENDS BURIED SERVICE (CLASS 350)	LS	1	56,000.00	56,000.00			1.00	56,000.00			1.00		1.00	56,000.00	100%
139	OVEREXCAVATION AND REPLACE UNSUITABLE MATERIAL & COO 14	CY	40	160.00	6,400.00	-40.00	-6,400.00									N/A
140	RELOCATE AIR RELEASE VACUUM VALVE & COO 14	EA	2	8,100.00	16,200.00	-1.00	-8,100.00	1.00	8,100.00			1.00		1.00	8,100.00	100%
141	RELOCATE HYDRANT & COO 14	EA	3	9,000.00	27,000.00	-1.00	-9,000.00	2.00	18,000.00			2.00		2.00	18,000.00	100%
	ALTERNATE BID SCHEDULE "E" - SAWPA - UTILITY RELOCATIONS (Dawson Canyon and Dos Lagos Segments)															
142	PROTECT 24" FORCE MAIN CROSSING DAWSON SEGMENT LINE B AND LINE C	LS	1	30,000.00	30,000.00			1.00	30,000.00			1.00		1.00	30,000.00	100%
143	ADJUST MANHOLE TO GRADE & COO 14	LS	9	775.00	6,975.00	-6.00	-4,650.00	3.00	2,325.00			3.00		3.00	2,325.00	100%
CCO 2	SAWPA	FA	0	1.00	0.00	190,000.00	190,000.00	190,000.00	190,000.00			180,500.00	180,500.00	180,500.00	95%	
	ALTERNATE BID SCHEDULE "F" - TREE REMOVAL - (Dawson Canyon and Dos Lagos Segment)															
143A	TREE REMOVAL	LS	1	25,000.00	25,000.00			1.00	25,000.00			1.00		1.00	25,000.00	100%
	BASE BID SCHEDULE "G" - TEMESCAL CANYON ROAD DRAINAGE IMPROVEMENT PROJECT AT COLDWATER CREEK - 88-8888															
144	DUST ABATEMENT	LS	1	7,500.00	7,500.00			1.00	7,500.00			1.00		1.00	7,500.00	100%
145	WATER POLLUTION CONTROL	LS	1	5,000.00	5,000.00			1.00	5,000.00			1.00		1.00	5,000.00	100%
146	TRAFFIC CONTROL SYSTEM	LS	1	100,000.00	100,000.00			1.00	100,000.00			1.00		1.00	100,000.00	100%



Contractor: Besdor Construction Co.
 Address: 28320 Lester Circle
 City, State, Zip: Corona, CA 92683

PROJECT: Temescal Canyon Road Widening Project, Temescal Canyon Slurry Seal Project and Temescal Canyon Road Drainage Improvement Project at Coldwater Creek
 County Project No.: CS-0072, State Project No. LPP887L-6866(207) and B8-6988
 Contract No. 14-19-002

Estimate No. 26 Final
 From: November 26, 2020
 To: December 29, 2020

Item No.	Item Description	Units	Quantity	Unit Price	Original Contract Amount	Change Authorized Quantity	Change Authorized Amount	Total Authorized Quantity	Total Authorized Amount	This Estimate Quantity	This Estimate Amount	Previous Quantity	Previous Amount	Total Estimate To Date Quantity	Total Estimate To Date Amount	% Auth
147	DEVELOP WATER SUPPLY [MPCPI]	LS	1	5,000.00	5,000.00			1.00	5,000.00	1.00	5,000.00			1.00	5,000.00	100%
148	FINISHING ROADWAY	LS	1	8,000.00	6,000.00			1.00	8,000.00	1.00	8,000.00			1.00	8,000.00	100%
149	CLEARING AND GRUBBING	LS	1	10,000.00	10,000.00			1.00	10,000.00	1.00	10,000.00			1.00	10,000.00	100%
150	TEMPORARY HIGH-VISIBILITY FENCE [TYPE ESA]	LF	800	7.50	6,000.00			800.00	6,000.00	750.00	5,925.00			750.00	5,925.00	94%
151	ROADWAY EXCAVATION	CY	100	80.00	8,000.00			100.00	8,000.00	120.00	9,600.00			120.00	9,600.00	120%
152	STRUCTURE EXCAVATION (CULVERT)	CY	180	56.00	8,800.00			180.00	8,800.00	200.00	11,200.00			200.00	11,200.00	125%
153	CLASS 2 AGGREGATE BASE	CY	70	125.00	8,750.00			70.00	8,750.00	87.50	10,937.50			87.50	10,937.50	125%
154	HOT MIX ASPHALT (TYPE A)	TON	100	200.00	20,000.00			100.00	20,000.00	125.00	25,000.00			125.00	25,000.00	125%
155	REINFORCED CONCRETE BOX CULVERT	LF	80	330.00	26,400.00			80.00	26,400.00	80.00	26,400.00			80.00	26,400.00	100%
156	MINOR CONCRETE (HEADWALL)	CY	40	985.00	39,400.00			40.00	39,400.00	30.00	29,550.00			30.00	29,550.00	75%
157	STRUCTURE BACKFILL (SLURRY CEMENT)	CY	50	200.00	10,000.00			50.00	10,000.00	62.61	12,522.00			62.61	12,522.00	125%
158	ROCK ENERGY DISSIPATOR	CY	50	160.00	8,000.00			50.00	8,000.00	48.00	7,360.00			48.00	7,360.00	92%
159	METAL BEAM GUARD RAILING (STEEL POST)	LF	70	220.00	15,400.00			70.00	15,400.00	70.00	15,400.00			70.00	15,400.00	100%
160	ALTERNATIVE FLARED TERMINAL SYSTEM [TYPE SRT]	EA	4	4,250.00	17,000.00			4.00	17,000.00	3.00	12,750.00			3.00	12,750.00	75%
161	THERMOPLASTIC PAVEMENT MARKING & CCO 14	SOFT	15	7.00	105.00	-15.00	-105.00									N/A
162	PAINT TRAFFIC STRIPE (2-COAT) & CCO 14	LF	400	0.50	200.00	-400.00	-200.00									N/A
163	PAVEMENT MARKER (RETROREFLECTIVE) & CCO 14	EA	40	4.25	170.00	-40.00	-170.00									N/A
164	MISCELLANEOUS WORK (AS DIRECTED)	FA	1	30,000.00	30,000.00			1.00	30,000.00	1.167899	35,039.97			1.167899	35,039.97	117%
CCO 1	COLD WATER CREEK	F	0	1.00	0.00	170,000.00	170,000.00	170,000.00	170,000.00	159,800.00	159,800.00			159,800.00	159,800.00	94%

PROJECT: Temescal Canyon Road Widening Projects, Temescal Canyon Slurry Seal Project
 County Project No.: CS-0072, State Project No. LPP881L-866(247) and BS-0988
 Contract No. 18-10-002

Contractor: Beador Construction, Co.
 Address: 28320 Lester Circle
 City, State, Zip: Corona, CA 92883



Estimate No. 25 Final
 From: November 26, 2020
 To: December 26, 2020

Work Orders Breakdown:

BASE BID SCHEDULE "1 & 2" - TEMESCAL CANYON ROAD
 WIDENING PROJECTS AND SLURRY SEAL - CS-0072
 (Dawson Canyon and Dos Lagos Segments)

ESTIMATE TO DATE: \$15,195,957.19
 LESS RETENTION: 1% 151,959.58
 LESS PREVIOUSLY INVOICED: 14,343,339.43
 LESS LABOR NON COMPLIANCE: 0.00
 TOTAL DUE THIS PAYMENT: \$700,658.18

BASE BID SCHEDULE "3" - TEMESCAL CANYON ROAD
 DRAINAGE IMPROVEMENT PROJECT AT COLDWATER
 CREEK - BS-0988

ESTIMATE TO DATE: \$496,684.47
 LESS RETENTION: 1% 4,966.84
 LESS PREVIOUSLY INVOICED: 486,750.78
 LESS LABOR NON COMPLIANCE: 0.00
 TOTAL DUE THIS PAYMENT: \$4,966.85

TOTAL: \$705,625.03

Temescal Canyon Road Est. 25 Final
Retention Reduction/Release

Total Estimate to Date as of (Est. 24)		\$15,132,745.11
*1% Retention Released		\$151,327.44
This Estimate Total (Est. 25)		\$559,896.55
Less 1% Retention (Est. 25)		\$5,598.97
Total Due This Payment		\$705,625.03
Total Estimate to Date as of (Est. 24) C5-0072	\$14,636,060.64	\$146,360.61
Total Estimate to Date as of (Est. 24) B9-0988	\$496,684.47	\$4,966.84
Less 1% Retention (Est. 24)		\$151,327.45

*Retention is being reduced to 1% (1% is being released)

**PETER ALDANA
COUNTY OF RIVERSIDE
ASSESSOR-COUNTY CLERK-RECORDER**

Recorder
P.O. Box 751
Riverside, CA 92502-0751
(951) 486-7000

www.riversideacr.com

CERTIFICATION

Pursuant to the provisions of Government Code 27361.7, I certify under the penalty of perjury that the following is a true copy of illegible wording found in the attached document:

(Print or type the page number(s) and wording below):

CLARIFICATION FOR SEAL for the Riverside County Board of Supervisors
(EMBOSSSED ON DOCUMENT)



Date:

March 2, 2021

Signature:

Priscilla Rasso

Print Name: Priscilla Rasso, Board Assistant

