

**SUBMITTAL TO THE BOARD OF SUPERVISORS  
COUNTY OF RIVERSIDE, STATE OF CALIFORNIA**



ITEM: 3.21  
(ID # 17210)

**MEETING DATE:**

Tuesday, November 02, 2021

**FROM :** TLMA-TRANSPORTATION:

**SUBJECT:** TRANSPORTATION AND LAND MANAGEMENT AGENCY/TRANSPORTATION:  
Notice of Completion – Cajalco Road Guardrail Reconstruction Project, Communities of El Cerrito and Lake Mathews. District 1. [\$0]

**RECOMMENDED MOTION:** That the Board of Supervisors:

1. Accept as complete the Construction of Cajalco Road Guardrail Reconstruction Project, District 1;
2. Authorize the Chair of the Board to execute the Notice of Completion on behalf of the County; and
3. Direct the Clerk of the Board to record the Notice of Completion.

**ACTION:Policy**


  
Mark Lancaster, Director of Transportation 9/14/2021

---

**MINUTES OF THE BOARD OF SUPERVISORS**

On motion of Supervisor Jeffries, seconded by Supervisor Hewitt and duly carried by unanimous vote, IT WAS ORDERED that the above matter is approved as recommended.

Ayes: Jeffries, Spiegel, Washington, Perez and Hewitt  
Nays: None  
Absent: None  
Date: November 2, 2021  
xc: Transp., Recorder

Kecia R. Harper  
Clerk of the Board  
By   
Deputy

**SUBMITTAL TO THE BOARD OF SUPERVISORS COUNTY OF RIVERSIDE,  
STATE OF CALIFORNIA**

<b>FINANCIAL DATA</b>	<b>Current Fiscal Year:</b>	<b>Next Fiscal Year:</b>	<b>Total Cost:</b>	<b>Ongoing Cost</b>
<b>COST</b>	\$ 0	\$ 0	\$ 0	\$ 0
<b>NET COUNTY COST</b>	\$ 0	\$ 0	\$ 0	\$ 0
<b>SOURCE OF FUNDS:</b> N/A			<b>Budget Adjustment:</b>	No
			<b>For Fiscal Year:</b>	21/22

**C.E.O. RECOMMENDATION:** Approve

**BACKGROUND:**

**Summary**

By Minute Order 3.27 of April 20, 2021, the Board of Supervisors entered into a contract with Danny C. Hubbs Construction, Inc., of California for the construction of the Cajalco Road Guardrail Reconstruction Project, in the communities of El Cerrito and Lake Mathews.

The original authorized amount of the contract was \$412,317. The total price of the contract came in at \$433,256 which is 5.1% more than the originally authorized amount. The increase of the total cost was the result of one (1) contract change order for the installation of additional asphalt concrete dike and for using more quantities than anticipated to complete the work. The contract change order is discussed in detail in the Contract Change Order Report.

The work was completed in conformance with the plans and specifications and the contractor was granted relief of maintenance on June 9, 2021.

Project Number D0-0011  
Federal Aid No. HSIPL-5956(272)

**Impact on Residents and Businesses**

The improvements have enhanced roadway safety within the project limits by providing a safety barrier intended to shield motorists who leave the roadway.

**Additional Fiscal Information**

**SUBMITTAL TO THE BOARD OF SUPERVISORS COUNTY OF RIVERSIDE,  
STATE OF CALIFORNIA**

**Budget**

Original Contract Amount		\$412,317
Total Change Orders Authorized	0.4%	\$1,577
Estimated Pending Change Orders	0.0%	\$0
Authorized Contract Amount		\$413,894
* Quantity Adjustments	4.7%	\$19,362
+ CCO FA Adjustments	0.0%	\$0
Total Amended Contract Amount	105.1%	\$433,256

**Expenditures**

Total Progress Payments	\$433,256
Estimated Pending Payments	\$0
Total Expenditures	\$433,256

**(Over)/Under Contract Amount** \$0

+ Change Orders using the Force Account method of payment issued prior to the work being completed generally do not use the total authorized amount.

\* Caltrans Standard Specifications 9-1.06 (Changed Quantity Payment Adjustments). Increases or decreases in the quantity of a contract item of work will be determined by comparing the total pay quantity of such item of work with the Engineer's Estimate. If the total pay quantity of any item of work required under the contract varies from the Engineer's Estimate by 25 percent or less, payment will be made for the quantity of work of said item performed at the contract unit price, unless eligible for adjustment pursuant to Section 9-1.15, "Work-Character Changes."


This project was funded with Highway Safety Improvement Program funds.

**Contract History and Price Reasonableness**

Five bids were received in February 2021 ranging from \$412,317 to \$623,247. The basis for the selection of a contractor is the lowest responsive and responsible bid. The lowest responsive and responsible bid was submitted by Danny C. Hubbs Construction, Inc. in the amount of \$412,317 which was \$240,568 (37%) lower than the Engineer's Estimate.

**ATTACHMENTS:**

Change Order Report  
Vicinity Map  
Progress Estimate Report  
Notice of Completion

  
Jason Farin, Principal Management Analyst 10/27/2021



  
Gregory L. Priamos, Director County Counsel 10/21/2021

COUNTY OF RIVERSIDE  
TRANSPORTATION DEPARTMENT

**CAJALCO ROAD  
GUARDRAIL RECONSTRUCTION  
TEMESCAL CANYON ROAD TO LA SIERRA AVENUE  
COMMUNITY OF EL CERRITO AND LAKE MATHEWS**

**PROJECT No. D0-0011  
FEDERAL AID No. HSIPL-5956 (272)**

**PROJECT  
LOCATION**

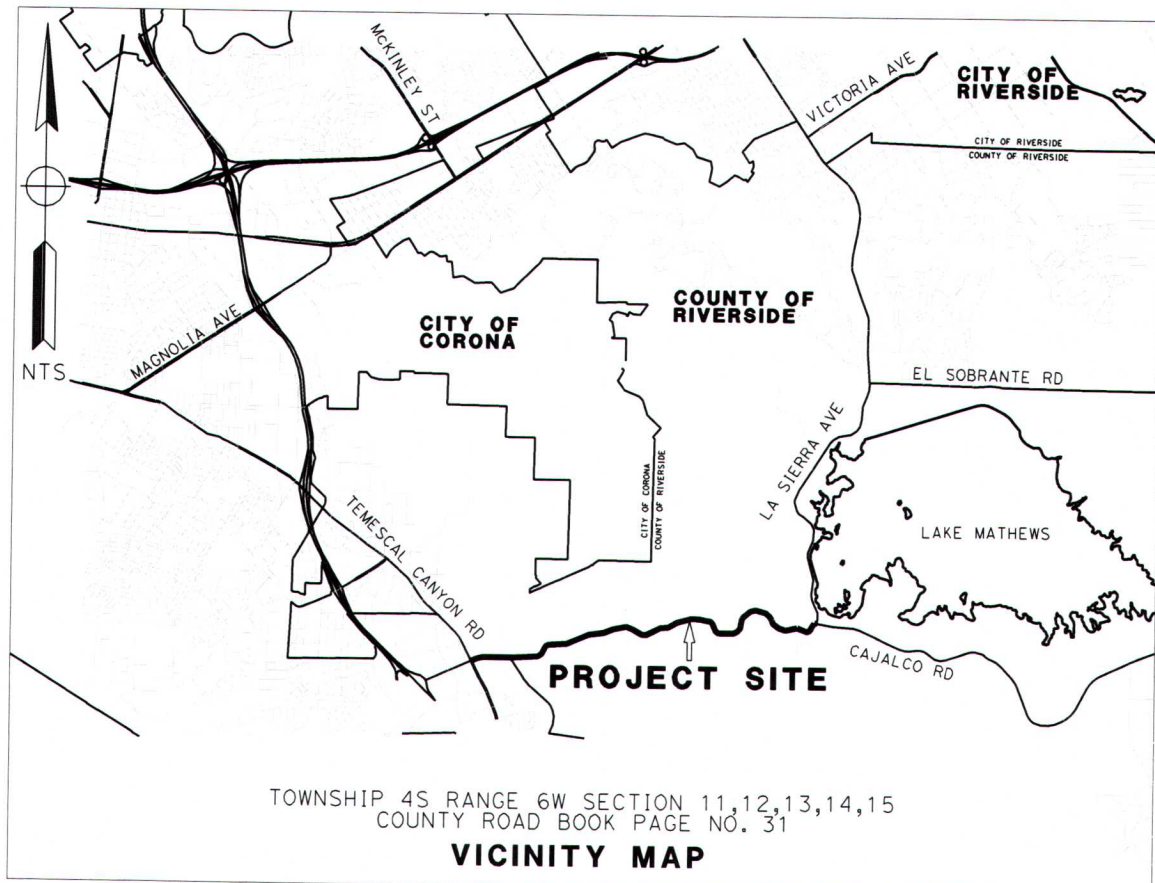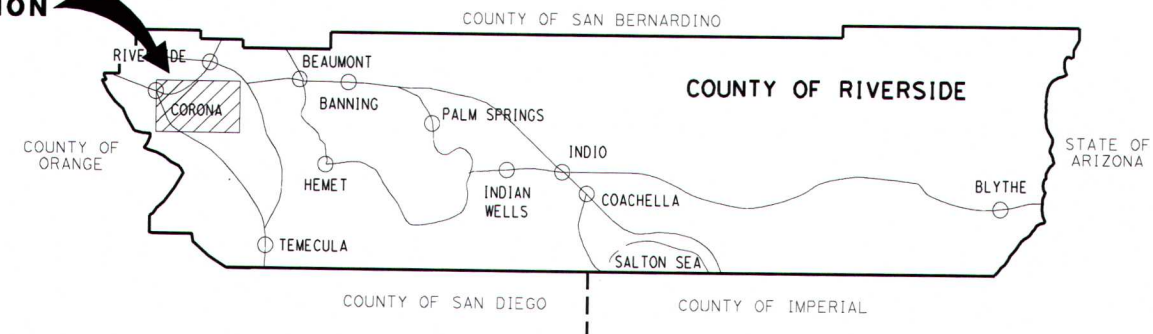

PROGRESS ESTIMATE RECORD - COUNTY OF RIVERSIDE

SHEET 2 of 2

Processed Construction Inspection 7/8/2021

PROJECT: Cajalco Road Guardrail Reconstruction, Temescal Canyon Rd. to La Sierra Ave., Community of  
El Cerrito and Lake Mathews  
County Project No.: D0-0011, Federal Aid No. HSIPL-5956(272)  
Contract No. 21-02-004

Contractor: D C Hubbs Construction  
Address: 37306 Vista View Dr.  
City, State, Zip: Yucaipa, CA 92399



Estimate No. 3 Final  
From: June 18, 2021  
To: July 7, 2021

Item No.	Item Description	Units	Quantity	Unit Price	Original Contract Amount	Change Orders Quantity	Change Orders Amount	Amended Contract Quantity	Amended Contract Amount	This Estimate Quantity	This Estimate Amount	Previous Quantity	Total Estimate To Date Quantity	Total Estimate To Date Amount	% Auth.
<b>PROJECT TOTAL</b>					412,317.00		1,577.00		413,894.00		14,177.00			433,255.50	

Made by Paul Castillo/David Hylkema

Checked by TN

OK Const. Supv. HD

Working Days: 20  
Days Added: 0  
Subtotal: 20  
Days Used: 19  
% Time Elapsed: 95%

Start Date: 5-10-21  
End Date: 6-9-21  
% \$ Complete: 105%  
Original Contract: \$412,317.00  
Amended Contract: \$413,894.00

TOTAL VALUE OF WORK TO DATE: \$433,255.50  
LESS RETENTION: 0% 0.00  
TOTAL DUE TO DATE: \$433,255.50  
LESS PREVIOUSLY INVOICED: 419,078.50  
LESS LABOR NON COMPLIANCE: 0.00  
TOTAL DUE THIS PAYMENT: \$14,177.00

This Estimate Approved Mojahed Salama 8/17/2021  
Mark Lancaster, Director of Transportation

Quantities on This Estimate Approved [Signature] Date: 7-8-21  
D C Hubbs Construction

\$14,177.00

Received by Accounts Payable

By:

Payment Approval

FUND: 20000

DEPT. ID.: 31305

ACCOUNT: 527980

PROJECT: ZD0-0011E

ACTIVITY ID.: Z3500

RESOURCE CNT

SIGNATURE: Cindi A. Wachter

DATE: 08/17/2021

ya

08/17/21

Transfiscal Approved  
By: Lori Conrad 5\*3461  
Aug 17, 2021

PROGRESS ESTIMATE RECORD - COUNTY OF RIVERSIDE

SHEET 1 of 2

Processed Construction Inspection 7/8/2021

PROJECT: Cajalco Road Guardrail Reconstruction, Temescal Canyon Rd. to La Sierra Ave., Community of El Cerrito and Lake Mathews  
County Project No.: D0-0011, Federal Aid No. HSIPL-5956(272)  
Contract No. 21-02-004

Contractor: D C Hubbs Construction  
Address: 37306 Vista View Dr.  
City, State, Zip: Yucaipa, CA 92399



Estimate No. 3 Final  
From: June 18, 2021  
To: July 7, 2021

Item No.	Item Description	Units	Quantity	Unit Price	Original Contract Amount	Change Orders		Amended Contract		This Estimate		Previous Quantity	Total Estimate To Date		% Auth.
						Quantity	Amount	Quantity	Amount	Quantity	Amount		Quantity	Amount	
1	DUST ABATEMENT	LS	1	11,675.00	11,675.00			1.00	11,675.00			1.00	1.00	11,675.00	100%
2	DEVELOP WATER SUPPLY	LS	1	8,100.00	8,100.00			1.00	8,100.00	0.38271605	3,100.00	0.61728395	1.00	8,100.00	100%
3	TRAFFIC CONTROL SYSTEM	LS	1	64,300.00	64,300.00			1.00	64,300.00			1.00	1.00	64,300.00	100%
4	PREPARE WATER POLLUTION CONTROL PROGRAM	LS	1	2,800.00	2,800.00			1.00	2,800.00			1.00	1.00	2,800.00	100%
5	CLEARING AND GRUBBING	LS	1	14,500.00	14,500.00			1.00	14,500.00	0.310345	4,500.00	0.689655	1.00	14,500.00	100%
6	PLACE HOT MIX ASPHALT DIKE (TYPE F) & CCO 1	LF	3,155	7.00	22,085.00	65.00	455.00	3,220.00	22,540.00	65.00	455.00	3,943.00	4,008.00	28,056.00	124%
7	GUARD RAILING DELINEATOR & CCO 1	EA	131	33.00	4,323.00	34.00	1,122.00	165.00	5,445.00	34.00	1,122.00	164.00	198.00	6,534.00	120%
8	MIDWEST GUARDRAIL SYSEM (STEEL POST)	LF	4,090	37.00	151,330.00			4,090.00	151,330.00			4,481.50	4,481.50	165,815.50	110%
9	END ANCHOR ASSEMBLY (TYPE SFT)	EA	2	1,740.00	3,480.00			2.00	3,480.00			2.00	2.00	3,480.00	100%
10	ALERNATIVE IN-LINE TERMINAL SYSTEM	EA	16	3,430.00	54,880.00			16.00	54,880.00			16.00	16.00	54,880.00	100%
11	REMOVE GUARDRAIL	LF	4,988	13.00	64,844.00			4,988.00	64,844.00			4,855.00	4,855.00	63,115.00	97%
12	MOBILIZATION (INCLUDES DEMOBILIZATION AND FINAL CLEAN UP)	LS	1	10,000.00	10,000.00			1.00	10,000.00	0.50	5,000.00	0.50	1.00	10,000.00	100%

PLEASE COMPLETE THIS INFORMATION  
RECORDING REQUESTED BY:

KECIA R. HARPER, CLERK OF THE BOARD  
RIVERSIDE CO. CLERK OF THE BOARD  
4080 LEMON STREET, 1<sup>ST</sup> FLOOR CAC  
P O BOX 1147 - RIVERSIDE, CA 92502

MAIL STOP # 1010

AND WHEN RECORDED MAIL TO:

**RETURN TO: STOP #1010**  
RIVERSIDE COUNTY CLERK OF THE BOARD  
P. O. BOX 1147 - RIVERSIDE, CA 92502

**2021-0712019**

12/02/2021 09:53 AM Fee: \$ 0.00

Page 1 of 2

Recorded in Official Records  
County of Riverside  
Peter Aldana  
Assessor-County Clerk-Recorder



THIS SPACE FOR RECORDERS USE ONLY

6080

### NOTICE OF COMPLETION

To be recorded with County Recorder  
within 10 days after completion.  
No recording fee.

Notice is hereby given by the undersigned owner, a public entity of the State of California, that a public work of improvement has been completed, as follows:

**Project title or description of work:** Cajalco Road Guardrail Reconstruction Project, Project No. D0-0011, Federal Aid No. HSIPL-5956(272)

**Date of Completion:** Date Hereof **NOV 02 2021**

**Nature of owner:** County of Riverside, public entity

**Interest or estate of owner:** Public Road Right-of-Way

**Address of owner:** Clerk of the Board of Supervisors, County Administrative Center  
4080 Lemon Street, 8th Floor, Riverside, CA 92501

**Name and Address of contractor:** Danny C. Hubbs Construction, Inc., 37306 Vista View Dr., Yucaipa, CA 92399

**Street or legal description of site:** Cajalco Road from Temescal Canyon Road to La Sierra Avenue, Community of El Cerrito and Lake Mathews

Dated: **NOV 02 2021**

Owner: County of Riverside  
(Name of Public Entity)

By: Karen S. Spiegel  
Chair, Board of Supervisors  
**KAREN SPIEGEL**

STATE OF CALIFORNIA )

COUNTY OF RIVERSIDE )

ss

I am the Chair of the governing board of the County of Riverside, the public entity which executed the foregoing notice and on whose behalf I make this verification; I have read this notice, know its contents, and the same is true. I certify under penalty of perjury that the foregoing is true and correct.

Executed at Riverside, California on **NOV 02 2021** (Date)

Karen S. Spiegel  
**KAREN SPIEGEL**, Chair of the Board of Supervisors

FORM APPROVED COUNTY COUNSEL  
BY: Danielle D. Maland  
**DANIELLE D. MALAND**

NOV 02 2021 **3.21**

ATTEST:

KECIA R. HARPER, Clerk

By: [Signature]  
DEPUTY

PETER ALDANA  
COUNTY OF RIVERSIDE  
ASSESSOR-COUNTY CLERK-RECORDER

Recorder  
P.O. Box 751  
Riverside, CA 92502-0751  
(951) 486-7000

www.riversideacr.com

**CERTIFICATION**

Pursuant to the provisions of Government Code 27361.7, I certify under the penalty of perjury that the following is a true copy of illegible wording found in the attached document:

(Print or type the page number(s) and wording below):

CLARIFICATION FOR SEAL for the Riverside County Board of Supervisors  
(EMBOSSSED ON DOCUMENT)



Date:

11-02-2021

Signature:

*Priscilla Rasso*

Print Name: Priscilla Rasso, Board Assistant
