

**SUBMITTAL TO THE BOARD OF SUPERVISORS
COUNTY OF RIVERSIDE, STATE OF CALIFORNIA**



**ITEM: 3.38
(ID # 17746)**

MEETING DATE:
Tuesday, January 11, 2022

FROM : TLMA-TRANSPORTATION:

SUBJECT: TRANSPORTATION AND LAND MANAGEMENT AGENCY/TRANSPORTATION:
Notice of Completion – Briggs Road and Evening Glow Drive Traffic Signal and Safety Lighting Project, Community of French Valley. District 3. [\$0]

RECOMMENDED MOTION: That the Board of Supervisors:

1. Accept as complete the Briggs Road and Evening Glow Drive Traffic Signal and Safety Lighting Project, District 3;
2. Authorize the Chair of the Board to execute the Notice of Completion on behalf of the County; and
3. Direct the Clerk of the Board to record the Notice of Completion.


ACTION:Policy


Mark Lancaster, Director of Transportation 12/1/2021

MINUTES OF THE BOARD OF SUPERVISORS

On motion of Supervisor Jeffries, seconded by Supervisor Spiegel and duly carried by unanimous vote, IT WAS ORDERED that the above matter is approved as recommended.

Ayes: Jeffries, Spiegel, Washington, Perez and Hewitt
Nays: None
Absent: None
Date: January 11, 2022
xc: TLMA-Trans, Recorder

Kecia R. Harper
Clerk of the Board
By: 
Deputy

**SUBMITTAL TO THE BOARD OF SUPERVISORS COUNTY OF RIVERSIDE,
STATE OF CALIFORNIA**

FINANCIAL DATA	Current Fiscal Year:	Next Fiscal Year:	Total Cost:	Ongoing Cost
COST	\$ 0	\$ 0	\$ 0	\$ 0
NET COUNTY COST	\$ 0	\$ 0	\$ 0	\$ 0
SOURCE OF FUNDS: N/A			Budget Adjustment:	No
			For Fiscal Year:	21/22

C.E.O. RECOMMENDATION: Approve

BACKGROUND:

Summary

By Minute Order 3.35 of December 8, 2020, the Board of Supervisors entered into a contract with Elecnor Belco Electric, Inc. of Chino, California for the Traffic Signal Construction at the Intersection of Briggs Road and Evening Glow Drive, Community of French Valley, District 3.

The original authorized amount of the contract was \$356,105. The total price of the contract came in at \$327,932 which is 7.9% lower than the originally authorized amount. The reduction of the total cost was the result of using less quantities than anticipated to complete the work.

The work was completed in conformance with the plans and specifications and the contractor was granted relief of maintenance on November 3, 2021.

Project Number D0-0088

Impact on Residents and Businesses

The traffic signal improves traffic safety by providing controlled traffic movements.

Additional Fiscal Information

Budget

Original Contract Amount		\$356,105
Total Change Orders Authorized	0.0%	\$0
Estimated Pending Change Orders	0.0%	\$0
Authorized Contract Amount		\$356,105
* Quantity Adjustments	-7.9%	(\$28,173)
+ CCO FA Adjustments	0.0%	\$0
Total Amended Contract Amount	92.1%	\$327,932

Expenditures

Total Progress Payments	\$327,932
Estimated Pending Payments	\$0
Total Expenditures	\$327,932

(Over)/Under Contract Amount \$0

**SUBMITTAL TO THE BOARD OF SUPERVISORS COUNTY OF RIVERSIDE,
STATE OF CALIFORNIA**

+ Change Orders using the Force Account method of payment issued prior to the work being completed generally do not use the total authorized amount.

* Caltrans Standard Specifications 9-1.06 (Changed Quantity Payment Adjustments). Increases or decreases in the quantity of a contract item of work will be determined by comparing the total pay quantity of such item of work with the Engineer's Estimate. If the total pay quantity of any item of work required under the contract varies from the Engineer's Estimate by 25 percent or less, payment will be made for the quantity of work of said item performed at the contract unit price, unless eligible for adjustment pursuant to Section 9-1.15, "Work-Character Changes."

This project was funded with \$327,932 of Western County DIF Signal Mitigation Funds.

Contract History and Price Reasonableness

Eight bids were received on Wednesday, September 16, 2020, ranging from \$356,105 to \$433,412. The basis for the selection of a contractor is the lowest responsive and responsible bid. The lowest responsive and responsible bid was submitted by Elecnor Belco Electric, Inc. in the amount of \$356,105, which was (5%) lower than the Engineer's Estimate.

ATTACHMENTS:

Vicinity Map
Progress Estimate Report
Notice of Completion



Jason Farin, Principal Management Analyst 1/4/2022



Gregory L. Priarios, Director County Counsel 12/20/2021



COUNTY OF RIVERSIDE
TRANSPORTATION DEPARTMENT

BRIGGS RD AND EVENING GLOW DR

TRAFFIC SIGNAL

COMMUNITY OF FRENCH VALLEY

PROJECT No. D0-0088

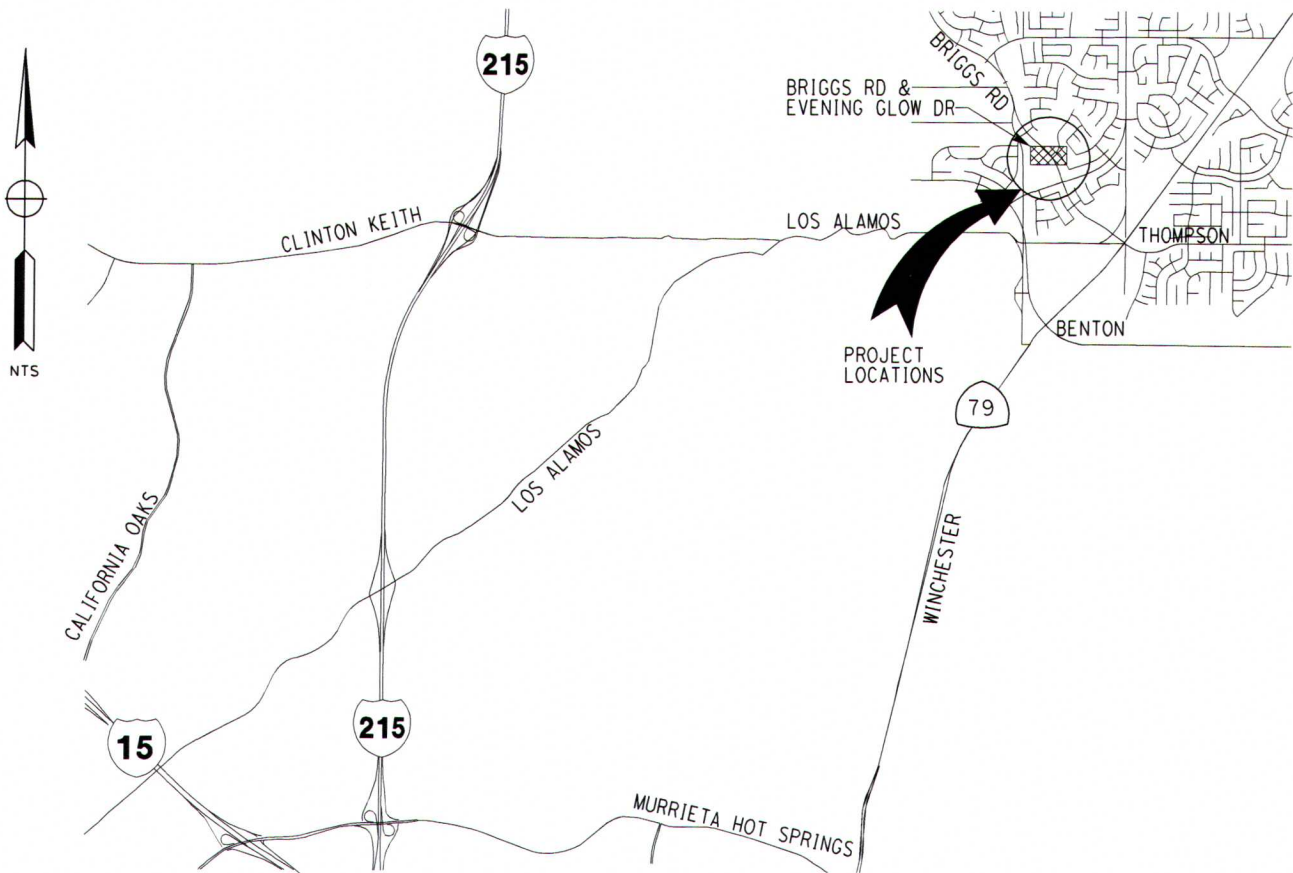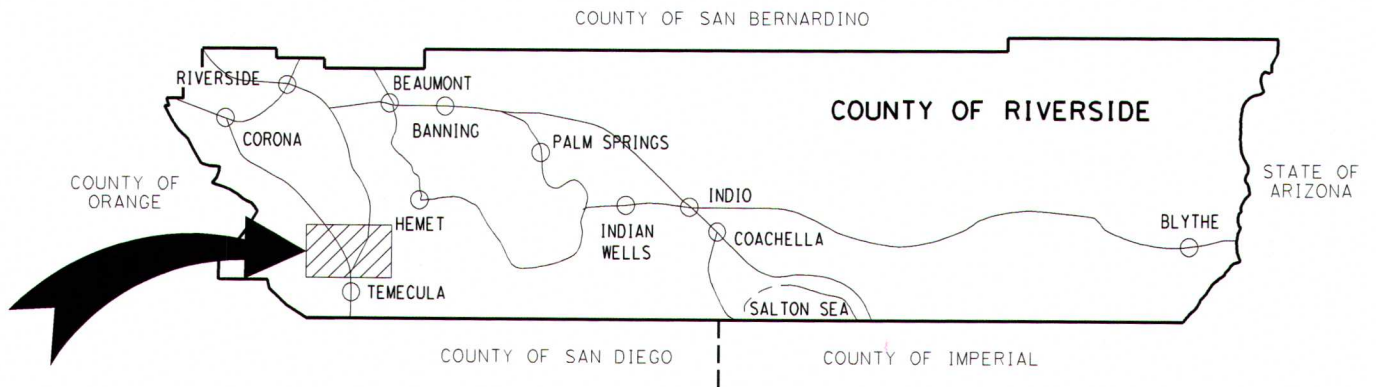

VICINITY MAP

TOWNSHIP 6S RANGE 2W SECTION 31
COUNTY ROAD BOOK PAGE No. 121B

PROJECT: Briggs Road and Evening Glow Drive, Traffic Signal and Safety Lighting Project
 Community of French Valley
 County Project No.: D0-0088
 Contract No. 20-10-003

Contractor: Eecnor Belco Electric, Inc.
 Address: 14320 Albers Way
 City, State, Zip: Chino, CA 91710



Estimate No. 4 Final
 From: July 26, 2021
 To: November 3, 2021

Item No.	Item Description	Units	Quantity	Unit Price	Original Contract Amount	Change Orders		Amended Contract		This Estimate		Previous Quantity	Total Estimate To Date		% Auth.
						Quantity	Amount	Quantity	Amount	Quantity	Amount		Quantity	Amount	
1	CLEARING AND GRUBBING	LS	1	1,500.00	1,500.00			1.00	1,500.00			1.00	1.00	1,500.00	100%
2	DEVELOP WATER SUPPLY	LS	1	1,500.00	1,500.00			1.00	1,500.00			1.00	1.00	1,500.00	100%
3	DUST CONTROL	LS	1	1,500.00	1,500.00			1.00	1,500.00			1.00	1.00	1,500.00	100%
4	FUNDING AWARENESS SIGN	EA	2	800.00	1,600.00			2.00	1,600.00			2.00	2.00	1,600.00	100%
5	MINOR CONCRETE (CURB RAMP) (CRS 403 - CASE A)	EA	4	7,900.00	31,600.00			4.00	31,600.00			4.00	4.00	31,600.00	100%
6	MISCELLANEOUS WORK (AS DIRECTED)	FA	1	30,000.00	30,000.00			1.00	30,000.00	0.060916	1,827.48		0.060916	1,827.48	6%
7	MOBILIZATION, DEMOBILIZATION, AND FINAL CLEANUP	LS	1	10,000.00	10,000.00			1.00	10,000.00	0.10	1,000.00	0.90	1.00	10,000.00	100%
8	PAINT CURB (2-COAT)	LF	260	2.00	520.00			260.00	520.00	260.00	520.00		260.00	520.00	100%
9	PAINT TRAFFIC STRIPE (2-COAT)	LF	4,325	0.68	2,941.00			4,325.00	2,941.00	4,325.00	2,941.00		4,325.00	2,941.00	100%
10	PAVEMENT MARKER (RETROREFLECTIVE)	EA	165	5.00	825.00			165.00	825.00	165.00	825.00		165.00	825.00	100%
11	PREPARE WATER POLLUTION CONTROL PROGRAM	LS	1	1,100.00	1,100.00			1.00	1,100.00			1.00	1.00	1,100.00	100%
12	REMOVE ROADSIDE SIGN	EA	11	52.00	572.00			11.00	572.00	11.00	572.00		11.00	572.00	100%
13	REMOVE TRAFFIC STRIPE AND PAVEMENT MARKING	SQFT	3,970	1.10	4,367.00			3,970.00	4,367.00	3,970.00	4,367.00		3,970.00	4,367.00	100%
14	ROADSIDE SIGN - ONE POST	EA	5	296.00	1,480.00			5.00	1,480.00	5.00	1,480.00		5.00	1,480.00	100%
15	ROADSIDE SIGN - TWO POST	EA	2	791.00	1,582.00			2.00	1,582.00	2.00	1,582.00		2.00	1,582.00	100%
16	SIGNAL AND LIGHTING SYSTEM	LS	1	250,000.00	250,000.00			1.00	250,000.00	0.1870	46,750.00	0.8130	1.0000	250,000.00	100%
17	THERMOPLASTIC PAVEMENT MARKING	SQFT	965	5.20	5,018.00			965.00	5,018.00	965.00	5,018.00		965.00	5,018.00	100%
18	TRAFFIC CONTROL SYSTEM	LS	1	10,000.00	10,000.00			1.00	10,000.00	0.10	1,000.00	0.90	1.00	10,000.00	100%

PROJECT: Briggs Road and Evening Glow Drive, Traffic Signal and Safety Lighting Project Community of French Valley County Project No.: D0-0088 Contract No. 20-10-003	Contractor: Eecnor Belco Electric, Inc. Address: 14320 Albers Way City, State, Zip: Chino, CA 91710		Estimate No. 4 Final From: July 26, 2021 To: November 3, 2021
--	---	---	---

Item No.	Item Description	Units	Quantity	Unit Price	Original Contract Amount	Change Orders		Amended Contract		This Estimate		Previous Quantity	Total Estimate To Date		% Auth.
						Quantity	Amount	Quantity	Amount	Quantity	Amount		Quantity	Amount	
PROJECT TOTAL					356,105.00		0.00		356,105.00		67,882.48			327,932.48	

Made by <u>Scott Gibson</u> Checked by <u>TN</u> OK Const. Supv. <u>HD</u>	Working Days: 40 Days Added: 20 Subtotal: 60 Days Used: 60 % Time Elapsed: 100%	Start Date: 5-10-21 End Date: 11-3-21 % \$ Complete: 92% Original Contract: \$356,105.00 Amended Contract: \$356,105.00	TOTAL VALUE OF WORK TO DATE: \$327,932.48 LESS RETENTION: 5% 16,396.62 TOTAL DUE TO DATE: \$311,535.86 LESS PREVIOUSLY INVOICED: 247,047.50 LESS LABOR NON COMPLIANCE: 0.00 TOTAL DUE THIS PAYMENT: \$64,488.36	<div style="border: 1px solid black; padding: 5px;"> <p>Payment Approval</p> <p>FUND: <u>20000</u></p> <p>DEPT. ID.: <u>31305</u></p> <p>ACCOUNT: <u>527980</u></p> <p>PROJECT: <u>ZD0-0088E</u></p> <p>ACTIVITY ID.: <u>Z3500</u></p> <p>RESOURCE CNT: _____</p> <p>SIGNATURE: <u>Cindi A. Wachs</u></p> <p>DATE: <u>11/05/2021</u></p> </div>
--	---	---	--	--

This Estimate Approved Mark Lancaster Date: 11/8/2021 for: \$64,488.36
 Mark Lancaster, Director of Transportation

Quantities on This Estimate Approved Sean Parks Date: 11/5/21
 Eecnor Belco Electric, Inc.

Received by Accounts Payable: _____
 By: _____
Yes
 11/08/21

Transfiscal Approved
 By: Lori Conrad 5*3461
 Nov 10, 2021

PLEASE COMPLETE THIS INFORMATION
RECORDING REQUESTED BY:

**KECIA R. HARPER, CLERK OF THE BOARD
RIVERSIDE CO. CLERK OF THE BOARD
4080 LEMON STREET, 1ST FLOOR CAC
P O BOX 1147 – RIVERSIDE, CA 92502
MAIL STOP # 1010**

AND WHEN RECORDED MAIL TO:
**RETURN TO: STOP #1010
RIVERSIDE COUNTY CLERK OF THE BOARD
P. O. BOX 1147 – RIVERSIDE, CA 92502**

2022-0049497

01/31/2022 10:32 AM Fee: \$ 0.00

Page 1 of 2

Recorded in Official Records
County of Riverside
Peter Aldana
Assessor-County Clerk-Recorder



6080

THIS SPACE FOR RECORDERS USE ONLY

NOTICE OF COMPLETION

To be recorded with County Recorder
within 10 days after completion.
No recording fee.

Notice is hereby given by the undersigned owner, a public entity of the State of California, that a public work of improvement has been completed, as follows:

Project title or description of work: Briggs Road and Evening Glow Drive Traffic Signal and Safety Lighting Project, Project No. D0-0088

Date of Completion: Date Hereof **JAN 11 2022**

Nature of owner: County of Riverside, public entity

Interest or estate of owner: Public Road Right-of-Way

Address of owner: Clerk of the Board of Supervisors, County Administrative Center
4080 Lemon Street, 8th Floor, Riverside, CA 92501

Name and Address of contractor: Elecnor Belco Electric, Inc., 14320 Albers Way, Chino, CA 91710

Street or legal description of site: Briggs Road and Evening Glow Drive, Community of French Valley

Dated: JAN 11 2022

Owner: County of Riverside
(Name of Public Entity)

By: *Jeff Hewitt*
Chair, Board of Supervisors
JEFF HEWITT

STATE OF CALIFORNIA)
 ss
COUNTY OF RIVERSIDE)

I am the Chair of the governing board of the County of Riverside, the public entity which executed the foregoing notice and on whose behalf I make this verification; I have read this notice, know its contents, and the same is true. I certify under penalty of perjury that the foregoing is true and correct.

Executed at Riverside, California on JAN 11 2022 (Date)
Jeff Hewitt, Chair of the Board of Supervisors
JEFF HEWITT

ATTEST: *Kecia R. Harper*
By: *[Signature]*
Deputy

FORM APPROVED COUNTY COUNSEL
BY: *[Signature]*
DANIELLE D. MALAND

JAN 11 2022 3.38



PETER ALDANA
COUNTY OF RIVERSIDE
ASSESSOR-COUNTY CLERK-RECORDER

Recorder
P.O. Box 751
Riverside, CA 92502-0751
(951) 486-7000

www.riversideacr.com

CERTIFICATION

Pursuant to the provisions of Government Code 27361.7, I certify under the penalty of perjury that the following is a true copy of illegible wording found in the attached document:

(Print or type the page number(s) and wording below):

CLARIFICATION FOR SEAL for the Riverside County Board of Supervisors
(EMBOSSSED ON DOCUMENT)



Date:

January 11, 2022

Signature:

[Handwritten Signature]

Print Name:

Priscilla Proso, Board Assistant
