SUBMITTAL TO THE BOARD OF SUPERVISORS COUNTY OF RIVERSIDE, STATE OF CALIFORNIA



ITEM: 3.34 (ID # 18238)

MEETING DATE:

Tuesday, March 22, 2022

FROM:

TLMA-TRANSPORTATION:

SUBJECT: TRANSPORTATION AND LAND MANAGEMENT AGENCY/TRANSPORTATION: Notice of Completion – Grand Avenue Resurfacing Project, Plumas Street to Patrick Court, Community of West Elsinore. District 1. [\$0]

RECOMMENDED MOTION: That the Board of Supervisors:

- 1. Accept as complete the Grand Avenue Resurfacing Project, Plumas Street to Patrick Court, District 1;
- 2. Authorize the Chair of the Board to execute the Notice of Completion on behalf of the County; and
- 3. Direct the Clerk of the Board to record the Notice of Completion.

ACTION:Policy

ransportation

MINUTES OF THE BOARD OF SUPERVISORS

On motion of Supervisor Spiegel, seconded by Supervisor Perez and duly carried by unanimous vote, IT WAS ORDERED that the above matter is approved as recommended.

1/27/2022

Ayes:

Jeffries, Spiegel, Washington, Perez and Hewitt

Nays:

None

Absent:

None

Date:

March 22, 2022

XC:

Trans., Recorder

Deputy

Kecia R. Harper

Clerk of the Boar

SUBMITTAL TO THE BOARD OF SUPERVISORS COUNTY OF RIVERSIDE, STATE OF CALIFORNIA

FINANCIAL DATA	Current Fiscal Y	ear:	Next Fiscal Yea	ır:	Total Cost:		Ongoi	ng Cost	
COST	\$	0	\$	0	\$	0		\$	0
NET COUNTY COST	\$	0	\$	0	\$	0		\$	0
SOURCE OF FUNDS	5: N/A				Budget	Adj	ustment:	No	
					For Fise	cal Y	ear:	21/22	

C.E.O. RECOMMENDATION: Approve

BACKGROUND:

Summary

By Minute Order 3.34 of May 11, 2021, the Board of Supervisors entered into a contract with Onyx Paving Company, Inc. of Anaheim, California for the Grand Avenue Resurfacing Project, Plumas Street to Patrick Court, in the Community of West Elsinore, District 1.

The original authorized amount of the contract was \$1,431,000. The total price of the contract came in at \$1,946,119 which is 36% more than the originally authorized amount. The increase of the total cost was the result of (2) contract change orders. The contract change orders are discussed in detail in the Contract Change Order Report. The factors that resulted in contract change orders for this project are:

- Additional street improvements (\$487,533)
- Sidewalk improvements (\$207,645)

The work was completed in conformance with the plans and specifications and the contractor was granted relief of maintenance on November 12, 2021.

Project Number C6-0073

Impact on Residents and Businesses

The improvements benefit the project area by significantly improving the safety and efficiency of vehicular traffic.

Additional Fiscal Information

SUBMITTAL TO THE BOARD OF SUPERVISORS COUNTY OF RIVERSIDE, STATE OF CALIFORNIA

Budget		
Original Contract Amount		\$1,431,000
Total Change Orders Authorized	48.6%	\$695,178
Estimated Pending Change Orders	0.0%	\$0
Authorized Contract Amount		\$2,126,178
* Quantity Adjustments	-12.6%	(\$180,059)
+ CCO FA Adjustments	0.0%	\$0
Total Amended Contract Amount	136.0%	\$1,946,119
Expenditures		
Total Progress Payments		\$1,946,119
Estimated Pending Payments		\$0
Total Expenditures		\$1,946,119
(Over)/Under Contract Amount		\$0

- + Change Orders using the Force Account method of payment issued prior to the work being completed generally do not use the total authorized amount.
- * Caltrans Standard Specifications 9-1.06 (Changed Quantity Payment Adjustments). Increases or decreases in the quantity of a contract item of work will be determined by comparing the total pay quantity of such item of work with the Engineer's Estimate. If the total pay quantity of any item of work required under the contract varies from the Engineer's Estimate by 25 percent or less, payment will be made for the quantity of work of said item performed at the contract unit price, unless eligible for adjustment pursuant to Section 9-1.15, "Work-Character Changes."

This project was funded with \$1,946,119 of Gas Tax/SB1 funds.

Contract History and Price Reasonableness

Eleven bids were received on March 3, 2021, ranging from \$1,434,000 to \$1,930,821. The basis for the selection of a contractor is the lowest responsive and responsible bid. The lowest responsive and responsible bid was submitted by Onyx Paving in the amount of \$1,434,000, which was \$257,995 (16%) lower than the Engineer's Estimate. The contract amount of 1,431,000 varies from bid amount \$1,434,000 because Alternate Bid Schedule 1 in the amount of \$3,000 was not selected for award.

ATTACHMENTS:

Vicinity Map
Notice of Completion
Progress Estimate Report
Change Order Report

SUBMITTAL TO THE BOARD OF SUPERVISORS COUNTY OF RIVERSIDE, STATE OF CALIFORNIA

Jason Farin Principal Management Analyst 3/15/2022 Gregory Priantos, Director County Counsel 2/22/2022

PLEASE COMPLETE THIS INFORMATION RECORDING REQUESTED BY:

KECIA R. HARPER, CLERK OF THE BOARD RIVERSIDE CO. CLERK OF THE BOARD 4080 LEMON STREET, 18T FLOOR CAC P O BOX 1147 - RIVERSIDE, CA 92502

MAIL STOP # 1010

AND WHEN RECORDED MAIL TO:

RETURN TO:

STOP #1010

RIVERSIDE COUNTY CLERK OF THE BOARD P. O. BOX 1147 - RIVERSIDE, CA 92502

sent to recorder

THIS SPACE FOR RECORDERS USE ONLY

NOTICE OF COMPLETION

To be recorded with County Recorder within 10 days after completion. No recording fee.

Notice is hereby given by the undersigned owner, a public entity of the State of California, that a public work of improvement has been completed, as follows:

Project title or description of work: Grand Avenue Resurfacing Project, Project No. C6-0073

Date of Completion:

Date Hereof

MAR 2 2 2022

Nature of owner:

County of Riverside, public entity

Interest or estate of owner:

Public Road Right-of-Way

Address of owner:

Clerk of the Board of Supervisors, County Administrative Center

4080 Lemon Street, 8th Floor, Riverside, CA 92501

Name and Address of contractor:

Onyx Paving Company, Inc., 2890 F. La Cresta Ave. Anaheim, CA 92806

Street or legal description of site:

Grand Avenue, Plumas Street to Patrick Court, Community of West Elsinore

Dated: MAR 2 2 2022

County of Riverside Name of Public Entits

STATE OF CALIFORNIA)

COUNTY OF RIVERSIDE)

I am the Chair of the governing board of the County of Riverside, the public entity which executed the foregoing notice and on whose behalf I make this verification; I have read this notice, know its contents, and the same is true. I certify under penalty of perjury that the foregoing is true and correct.

Executed at

___ California on MAR 2 2 2022 (Date)

, Chair of the Board of Supervisors

MAR 2 2 2022 3.31


GRAND AVENUE

RESURFACING

PLUMAS ST. TO PATRICK CT.

COMMUNITY OF WEST ELSINORE

PROJECT No. C6-0073

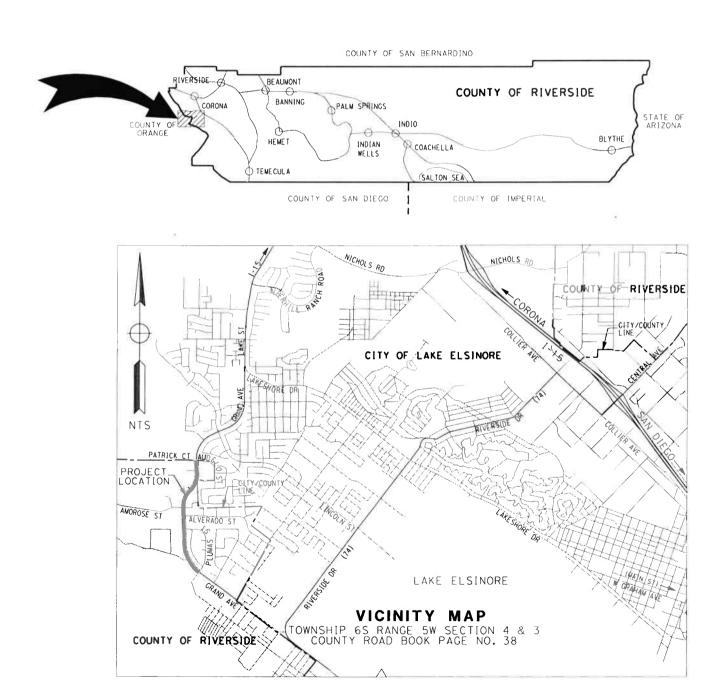

PROGRESS ESTIMATE RECORD - COUNTY OF RAVENCE

43,000,00,100% 44,000.00 100% 112,314,00 112% 3,000.00 100% 9,969,00 100% 454,542,73 93% 175,514,75 85% Processed Construction Impaction 1/4/2022 December 25, 2821 October 26, 2021 17,911,346,1 \$1,848,813,17 1,754,672.59 \$94,140,58 \$1,946,119.11 97,305.94 Tot at Estimate To Date
Oumtify Amount 6 frank: fo: 2% 00 . 1.00 1.00 175,514.75 175,514.75 33,230.00 454,542.73 454,542.73 1,123140 Previous Quantity 0.40314 33.230.00 0.90 06.0 F WORK TO DATE AL DUE TO DATE NON COMPLIANCE E THIS PAYMENT. LESS PREFIOUSLY INVOICED. LESS RETENTION: counts Payable SHET 2 of 2 4,400.00 72,000 00 4,300.00 3,000.00 99,095.35 TOTAL VALUE TOTAL D Received by A LESS LABOR The Estimate 0.10 1.00 0.72000 00.000,00 43,000.00 44,000.00 3,000.00 487,533 40 207,645.00 9,969.00 2,129,178.40 \$2,129,178 40 PROJECT: ZC6-0073E Aniended Contract Quantity Orginal Contract: \$1,431,000,00 Amended Contract: \$2,129,178.4 487,533 40 207,645.00 00 Payment Approval 11.22.21 33.230.00 8 8 00.1 7-26-21 ACCOUNT: 527980 FUND: 20000 ** DEP 1: 1D.: 31305 0.00 467.533.40 487,533.40 0.00 207.645.00 207,645.00 695,178.40 Start Date: Original Centract Oranga Orders Amount Ouanting | Aviount Contract or Onys Paving Company, Inc. Addition: 2890 E. La Cantra Ave. Czy, Stete, Zgr. Anabaim, CA 12886 00.696.6 44,000,00 43,000.00 100,000,001 3,000.00 \$1,431,000.00 Days Used: Working Days: Days Added. Subtotal. % Time Bapsed. 0 30 43,000.00 100,000,001 00. 1.00 44,000.00 3,000.00 - Our 1/13/22 Unit Price Quentity. 33,230 Mojahed Salama 1113/2022 S S Αp Ą 4 æ Ø Onyx Paving Company, Inc. ROJECT, Grand Avenue Remertacing Project, Plansa Street to Patrick Court, Community of West Editop MODIFYING BASTING BLECTRICAL SYSTEM (PATRICK CT INTERSECTION) VIDEO CAMERA DETECTION SYSTEM [PATRICK CT INTERSECTION] Mark Lancester, Director of Transportation CHANGES TO PROJECT PLANS (CITY OF LAKE ELSINOPE) Rem Description MISCELLANEOUS WORK (AS DIRECTED) Quantities on This Estamate Approved PAINT TRAFFIC STRIPE (2-COAT) CCO 2 - CHANCES TO PROJECT PLANS Made by Payl Castifto Checked by TN OK Const. Supv. ___HD__ This Estimate Approved ADJUST MANHOLE PROJECT TOTAL perty Project No.: OL 4673 perind No. 21-03-803 8 56 30 £ 9 27 26 58

SIGNATURE: CLACK O. Wach

01/13/22

ACTIVITY ID.: Z3500

RESOURCE CNT

DATE: 1/13/2022

Transifscal Approved By: Lori Conrad 5*3461 Jan 13, 2022

Comparison Com	A A	PROCRESS ESTIMATE RECORD - COUNTY OF AVERSIDE														
Control Cont	PROJEC	T: Grand Avenue Resurfacing Project, Plumas Street to Patrick Court, Community of West Estinore				Contractor: Onyx Pavi	ng Company, Inc.	10						Stimate No.	A Rhai	
1, 1, 1, 1, 1, 1, 1, 1, 1, 1, 1, 1, 1,	County	Project No.: Cs. 4073 1 No. 21-03-003				Address; 2890 ELa C City, State, Zip: Anahe	resta Ave. im, CA 92806							From: To:	October 26, 20 December 25, 2	021
NUMBER OF CHANNEL OF C	E 9		\$ 5	Quantity	Pig.	Original Contract Amount	Change Orde Quantity	1 1	Amended Con Quantity	1 1 1	This Estim Quantity		Previous Quantity	Total Estimate T Quantity	o Date Amount	% 54 4 4
Vacio Chambe Deficiency STEPLING STEP	56	PAINT TRAFFIC STRPE (2-COAT)	5	33,230	0.30	00 696 6		. Approxygang to a great to the second	33,230,00	00.696.6	Jr. 5 ress.		33,230,00	33,230,00	9 969.00	100%
Modern M	27	VIDEO CAMERA DETECTION SYSTEM [PATROK CT INTERSECTION]	s.	-	43,000,00	43,000.00		M	1.00	43,000.00	0.10	4,300.00	06'0	1.00	43,000.00	100%
Manage M	28	MODIFYING EXISTING ELECTRICAL SYSTEM [PATRICK CT INTERSECTION]	rs	-	44,000.00	44,000.00			1 00	44 000.00	0 10	4.400.00	06.0	1.00	44,000.00	100%
ADDITION NOT LAND COLVER ENVOIGN AND 1 1200 CO 100 COLVER ENVOIGN AND 1 1200 COLVER ENVOIGN AND	29		Ą	-	100 000 001	100 000 001			1 00		0.72000	72,000.00	0.40314	1 123140	112,314,00	112%
Control Cont	30	ADJUST MANHOLE	\$	-	3.000.00	3,000.00			1 00	3,000.00	1.00	3,000.00	Marijovino	1.00	3,000.00	100%
1,12,12,12,12,12,12,12,12,12,12,12,12,12	99		A	0	1.00	00.0	487 533 40	487,533,40	487 533 40	487,533,40			454,542,73	454 542 73	454,542.73	. 93%
Marking Days	8		AP	O	00.	00 0	207,645.00	207,645,00	207,645,50	207,645.00		•	175 514 75.	175,514,75	175 514 75	85%
1431,000.00 695,178.40 99,095.35																-,
Menking Days		PROJECT TOTAL				1,431,000,00		695,178,40		2,129,178.40		99,095.35	g(1.0ph/00070)		1,946,119,11	
Date 11-12-21 TOTAL VALUE OF WORKTO DATE Solution Soluti		Made byPaul Castillo		s	Vorking Days	30		Start Date	7-26-21							
Saktivalia 65		Z			Days Added	3.5		End Date	11-12-21		,TOT	AL VALUE OF WO	RK TO DATE		\$1,946,119,11	
Days Used 65 Original Contract; 52,129,178 40 LESS PREVIOUSLY IN VOICED	_				Subtotal	65	•	% \$ Complete:	91%			LESS	RETENTION		97,305.94	
W Time Based: 100% Amended Cantract: \$2,129,178.40 LESS LABON NON COMPLANCE Director of Transportation Less Labor NON COMPLANCE TOTAL Due THIS PAYMENT: Date. Da					Days Used	6.5	ð	ginal Contract	\$1,431,0	00.00		TOTAL D	UE TO DATE:		\$1.848.813.17	
Date: Date	_			%	Time Elapsed:	100%	Amer	nded Contract:	\$2,129,1	78 40		LESS PREVIOUS	LY INVOICED:		1,754,672,59	
Director of Transportation Director of Transportation Director of Transportation Date:	_										_	ESS LABOR NON (COMPLIANCE		00.0	
Orector of Transportation Date:												TOTAL DUE TH	IIS PAYMENT		\$94,140.58	
Director of Transportation Date:	-			for:			\$94,14	86.04			ě	seived by Account	ts Payable			
Onyx Paving Company, Inc.		Mark Lancaster, Director of Transportation										w.	.Ye			
Onyx Paving Company, Inc.		Dantites on This Estimate Approved	O ate.													
Onyx Paving Company, Inc.																
		Олух Paving Company, Inc.														

PROGRESS ESTIMATE RECORD - COUNTY OF RIVERSIDE

200	PROCPESS ESTIMATE RECORD & COUNTY OF RIVERSIDE									HH-S	SHET ' of 2	Processed Construc	Processed Construction Inspection 114/2022	2022
PROJECT	PROJECT Grand Avenue Resurtacing Project , Plumas Street to Patrick Court, Community of West Bsinone			ď	Contractor: Onyx Paving Company, Inc	Company, Inc.						Estimate No.	4 Final	
County i	County Project No; 05:073 Confined No; 21:03:003			₹ 5	Address: 2880 E La Cresta Ave. City, State, Zip: Anaheim, CA 92806	Ka Ave. 1. CA 92806						From: To:	October 26, 2021 December 25, 2021	- 2
Rea No.	them Description	Units	Quantity	Uhit Price	Original Contract Amount	Change Orders Amount Quantity	Amended Contract	Amount	This Estimate Quantity	Amount	Previous Quantity	Total Estimate To Date Quantity Am	o Date Amount	8, 24 F, F
-	DEVELOP WATER SUPPLY	LS	-	2,000.00	2,000 00	-1-1	1 00	2,000 00	0.05	100.00	0.95	1.00	2,000.00	100%
8	TRAFFIC CONTROL SYSTEM	rs	+	00.000.99	66,000.00		1 00	66,000.00	90.0	3,300,00	0 95	1.00	66,000.00	100%
n	PREPARE WATER POLLUTION CONTROL PROGRAM	rs		2 000 00	2,000.00		1.00	2.000.00	0 05	100.00	0	1.00	2,000,00	100%
4	CLEARNG AND GRUBBING (LS)	rs r	-	11,000,00	11,000.00		1.00	11,000.00	1. 0		1 00	1.00	11,000.00	100%
S.	DUST ABATMENT	rs.	<u> </u>	13,406,95	13,406.95		1.00	13,406.95	0 05	670 35	56.0	1 00	13,406.95 100%	100%
9	WEDGE PLANE ASPHALT CONCRETE	E.	7,060	88.0	6.212.80	2	7,060.00	6.212.80	THE TOLINA		7,162.00	7,162,00	6,302,56	101%
7	SHOULDER BACKING	5	520	7.00	3,640.00		520.00	3,640,00			520.00	520 00	3,640,00 100%	100%
8(F)	ROADWAY EXCAVATION	5	1,380	22 00	30,360.00		1,380.00	30,360.00			1,380 00	1,380,00	30,360.00	100%
6	ASPHALT RUBBER HOT MIX	10N	4.830	84.84	409,777.20		4,830,00	409,777.20			4,155,46	4 155.46	352,549,23	86%
10	PLACE ASPHALT CONCRETE DIKE (CRS 212) (6*)	H.	205	20,00	4 100.00	ent land	205 00	4,100.00			205.00	205.00	4,100.00	100%
Ξ	HOT MIX ASPHALT (TYPE A)	TON	5,670	74.47	422,244,90	φ.	5 670 00	422,244.90	-		4,907.46	4,907.46	365,458.55	87%
12	COLD PLANE ASPHALT CONCRETE PAVEMENT	SQYD 2	23,730	1.88	44 612 40	23	23,730.00	44,612.40			21,067.00	21,067.00	39,605,96	89%
13	MINOR CONCRETE (CLRB AND GUTTER) (CRS 200)	J.	120	00 99	7,920.00	. ,	120.00	7,920.00			120.00	120.00	7,920 00	100%
<u>+</u>	MINOR CONCRETE (CURB AND GUTTER) (CRS 201)	5	55	99	3,630.00		55.00	3,630,00			55.00	55 00	3,630.00	100%
15	MINOR CONCRETE (COMMERCIAL DRIVEWAY) (CRS 207A)	8	096	15.00	14,400.00		00.096	14,400.00			946 75	946.75	14,201.25	%66
16	MINOR CONCRETE (CROSS GUTTER AND SPANDREL)	3067	7,505	18 25	136,966.25	2	7,505.00	136,966 25			7,108.50	7,108,50	129,730,13	%56
17	MINOR CONCRETE (SIDEWALK)	SOFT	650	10 50	6,825.00		650 00	6,825.00	11 3000 300		425.00	425,00	4,462,50	%59
÷.	MINOR CONCRETE (CURB RAMP) [MODIFIED PER PLAN]	\$	4	6,100.00	24,400 00		4 00	24,400.00			0 0	00.4	24,400.00 100%	100%
6	REMOVE YELLOW PAINTED TRAFFIC STRPE (HAZARDOUS WASTE)	5	170	25.00	4,250.00		170.00,	4,250.00	1-1		75.00	75 00	1,875.00	44%
20	PAVEMENT MARKER (RETRORFLECTIVE)	\$	855	3.50	2,992,50	270	855.00	2,992.50			855.00	855.00	2,992,50 100%	100%
2.1	OBJECT MARKER	\$	9	20.00	300.00		00 9	300.00	6.00	300.00	ddd d dda y 1	9	300.00 100%	100%
22	SALVAGE ROADSIDE SIGN	Æ	18	25 00	450 00		18.00	450 00	18 00	450 00	se 111111164.11	18.00	450.00 100%	100%
23	ROADSIDE SIGN - ONE POST	A.	28	325.00	9,100.00		28.00	9 100 00	28.00	9,100.00	h-7-11 h-8-8-8	28.00	00.001,6	100%
24	THEPMOPLASTIC PAVEMENT MARKING	Sort	1,640	3.70	6,068,00		1,640,00	6,068 00			1,870.00	1,870.00	6,919.00	114%
25	REMOVE THERMOPLASTIC PAVEMENT MARKING	8	250	5.50	1,375.00		250.00	1,375.00	250,00	1 375 00		250.00	1,375.00 100%	100%

CHANGE ORDER REPORT

(Grand Avenue Resurfacing Project)

CCO#	Amount	Percent	Description
	Original Contract Amount		
	\$1,431,000		
1	\$487,533	34.07%	The County of Riverside entered into an agreement with the City of Lake Elsinore to perform additional street improvements on Grand Avenue, from Machado Street to Riverside Drive and Bonnie Lea Drive to Ortega Highway.
2	\$207,645	48.58%	Sidewalk improvements were added to the project to enhance public safety by improving pedestrian routes and access to schools in the area.
Quantity Adjustments	(\$180,059)	(12.6%)	
Change Order Total and New Contract Total	1,946,119		

PLEASE COMPLETE THIS INFORMATION RECORDING REQUESTED BY:

KECIA R. HARPER, CLERK OF THE BOARD RIVERSIDE CO. CLERK OF THE BOARD 4080 LEMON STREET, 18T FLOOR CAC P O BOX 1147 - RIVERSIDE, CA 92502

MAIL STOP # 1010

AND WHEN RECORDED MAIL TO:

RETURN TO:

STOP #1010

RIVERSIDE COUNTY CLERK OF THE BOARD P. O. BOX 1147 - RIVERSIDE, CA 92502

2022-0152169

03/30/2022 11:50 AM Fee: \$ 0.00

Page 1 of 2

Recorded in Official Records County of Riverside Peter Aldana

Assessor-County Clerk-Recorder



779

THIS SPACE FOR RECORDERS USE ONLY

NOTICE OF COMPLETION

To be recorded with County Recorder within 10 days after completion. No recording fee.

Notice is hereby given by the undersigned owner, a public entity of the State of California, that a public work of improvement has been completed, as follows:

Project title or description of work: Grand Avenue Resurfacing Project, Project No. C6-0073

Date of Completion:

Date Hereof

MAR 2 2 2022

Nature of owner:

County of Riverside, public entity

Interest or estate of owner:

Public Road Right-of-Way

Address of owner:

Clerk of the Board of Supervisors, County Administrative Center

4080 Lemon Street, 8th Floor, Riverside, CA 92501

Name and Address of contractor:

Onyx Paving Company, Inc., 2890 E La Cresta Ave. Anaheim, CA 92806

Street or legal description of site:

Grand Avenue, Plumas Street to Patrick Court, Community of West Elsinore

Dated:

MAR 2 2 2022

County of Riverside Owner:

(Name of Public Entity)

STATE OF CALIFORNIA)

COUNTY OF RIVERSIDE)

I am the Chair of the governing board of the County of Riverside, the public entity which executed the foregoing notice and on whose behalf I make this verification; I have read this notice, know its contents, and the same is true. I certify under penalty of perjury that the foregoing is true and correct.

California on Executed at

, Chair of the Board of Supervisors

MAR 2 2 2022 3,5

PETER ALDANA COUNTY OF RIVERSIDE ASSESSOR-COUNTY CLERK-RECORDER

Recorder P.O. Box 751 Riverside, CA 92502-0751 (951) 486-7000

www.riversideacr.com

CERTIFICATION

Pursuant to the provisions of Government Code 27361.7, I certify under the penalty of perjury that the following is a true copy of illegible wording found in the attached document:

(Print or type the page number(s) and wording below):

CLARIFICATION FOR SEAL for the Riverside County Board of Supervisors (EMBOSSED ON DOCUMENT)



Date:

March 22, 2022 priscular Cost

Signature:

Print Name: Priscilla Rasso, Board Assistant

ACR 601P-AS4RE0 (Rev. 09/2005)
