SUBMITTAL TO THE BOARD OF SUPERVISORS COUNTY OF RIVERSIDE, STATE OF CALIFORNIA



ITEM: 3.50 (ID # 24630) MEETING DATE: Tuesday, May 21, 2024

FROM: TLMA-TRANSPORTATION:

SUBJECT: TRANSPORTATION AND LAND MANAGEMENT AGENCY/TRANSPORTATION: Notice of Completion – Stetson Avenue Resurfacing Project, in the Community of East Hemet. District 3. [\$0]

RECOMMENDED MOTION: That the Board of Supervisors:

- 1. Accept as complete the Construction of Stetson Avenue Resurfacing Project, in the Community of East Hemet, District 3;
- 2. Authorize the Chair of the Board to execute the Notice of Completion on behalf of the County; and
- 3. Direct the Clerk of the Board to record the Notice of Completion.

ACTION:Policy

Dennis Acuna, Director of Transportation

4/11/2024

MINUTES OF THE BOARD OF SUPERVISORS

On motion of Supervisor Gutierrez, seconded by Supervisor Jeffries and duly carried by unanimous vote, IT WAS ORDERED that the above matter is approved as recommended.

Ayes:

Jeffries, Spiegel, Washington, Perez and Gutierrez

Nays:

None

Kimberly A. Rector

Absent: Date:

None

Clerk of the Board By: Mamu, 1

xc:

May 21, 2024 Trans., Recorder

Deputy

SUBMITTAL TO THE BOARD OF SUPERVISORS COUNTY OF RIVERSIDE, STATE OF CALIFORNIA

FINANCIAL DATA	Current Fiscal Y	ear:	Next Fiscal Yea	Total Cost:		Ongoing Cost			
COST	\$	0	\$	0	\$	0		\$	0
NET COUNTY COST	\$	0	\$	0	\$	0		\$	0
SOURCE OF FUNDS	5: N/A				Budget	ustment:	N/A	٩	
					For Fise	cal Y	'ear:	23/24	

C.E.O. RECOMMENDATION: Approve

BACKGROUND:

Summary

By Minute Order 3.17 of November 1, 2022, the Board of Supervisors entered into a contract with Onyx Paving Company, Inc. (Onyx Paving) of Anaheim, California for the construction of the Stetson Avenue Resurfacing Project from Santa Fe Street to 150-Feet East of Hemet Street in the Community of East Hemet of Riverside County.

The original authorized amount of the contract was \$3,172,000. The total amended contract is \$3,206,935 which is 1.1% more than the originally authorized amount and was the result of (1) contract change order which provided compensation to the Contractor for traffic signal modifications as discussed in the attached Change Order Report.

The total value of work came in at \$3,090,213 which was 3.7% lower than the total amended contract amount. The reduction of the total cost was the result of using less quantities than anticipated to complete the work.

The work was completed in conformance with the plans and specifications and the Contractor was granted relief of maintenance on March 20, 2024.

Project Number:

D0-0016

Impact on Residents and Businesses

The improvements benefit the project area by providing the public with a smooth paved roadway that will improve the safety and efficiency of vehicular traffic.

SUBMITTAL TO THE BOARD OF SUPERVISORS COUNTY OF RIVERSIDE, STATE OF CALIFORNIA

Additional	Fiscal	Information
Additional	I IOCUI	minomination

Budget		
Original Contract Amount		\$3,172,000
Total Change Orders Authorized	1.1%	\$34,935
Estimated Pending Change Orders	0.0%	\$0
Authorized Contract Amount		\$3,206,935
* Quantity Adjustments	-3.7%	(\$116,722)
+ CCO FA Adjustments	0.0%	\$0
Total Value of Work	97.4%	\$3,090,213
Expenditures		
Total Progress Payments		\$3,090,213
Estimated Pending Payments		\$0
Total Expenditures		\$3,090,213
(Over)/Under Contract Amount		\$0

- + Change Orders using the Force Account method of payment issued prior to the work being completed generally do not use the total authorized amount.
- * <u>Caltrans Standard Specifications 9-1.06 (Changed Quantity Payment Adjustments)</u>. Increases or decreases in the quantity of a contract item of work will be determined by comparing the total pay quantity of such item of work with the Engineer's Estimate. If the total pay quantity of any item of work required under the contract varies from the Engineer's Estimate by 25 percent or less, payment will be made for the quantity of work of said item performed at the contract unit price, unless eligible for adjustment pursuant to Section 9-1.15, "Work-Character Changes."

Contract History and Price Reasonableness

A total of four bids were received on Wednesday, August 24, 2022 ranging from \$3,172,000 to \$4,480,521. The basis for the selection of a contractor is the lowest responsive and responsible bid. The lowest responsive and responsible bid was submitted by Onyx Paving Company, Inc. (Onyx Paving) in the amount of \$3,172,000 which was \$248,586 (8.5%) above the engineer's cost estimate.

ATTACHMENTS:

Vicinity Map
Change Order Report
Progress Estimate Report
Notice of Completion

Jason Farin Principal Management Analyst 5/15/2024

Saron Settis
Aaron Gettis, Chief of Deput County Counsel 5/9/2024

PLEASE COMPLETE THIS INFORMATION RECORDING REQUESTED BY:

KIMBERLY RECTOR. CLERK OF THE BOARD RIVERSIDE CO. CLERK OF THE BOARD 4080 LEMON STREET, 1ST FLOOR CAC P O BOX 1147 - RIVERSIDE, CA 92502 **MAIL STOP # 1010**

AND WHEN RECORDED MAIL TO:

RETURN TO:

STOP #1010

RIVERSIDE COUNTY CLERK OF THE BOARD P. O. BOX 1147 - RIVERSIDE, CA 92502

2024-0148905

05/22/2024 04:02 PM Fee: \$ 0.00

Page 1 of 2

Recorded in Official Records County of Riverside Peter Aldana

Assessor-County Clerk-Recorder



THIS SPACE FOR RECORDERS USE ONLY

8427

W COUNSE!

NOTICE OF COMPLETION

To be recorded with County Recorder within 10 days after completion. No recording fee.

Notice is hereby given by the undersigned owner, a public entity of the State of California, that a public work of improvement has been completed, as follows:

Project title or description of work:

Stetson Avenue Resurfacing

Project No. D0-0016

Date of Completion:

Date Hereof

Nature of owner:

County of Riverside, public entity

Interest or estate of owner:

Public Road Right-of-Way

Address of owner:

Clerk of the Board of Supervisors, County Administrative Center

4080 Lemon Street, 8th Floor, Riverside, CA 92501

Name and Address of contractor:

Onyx Paving Company, Inc., 2890 E La Cresta Ave, Anaheim, CA 92806

Street or legal description of site:

Santa Fe Street to 150-Feet East of Hemet Street

Community of East Hemet

Dated: May 21, 2024

County of Riverside Owner:

(Name of Public Entity)

Chair, Board of Supervisors Chuck Washington

STATE OF CALIFORNIA)

COUNTY OF RIVERSIDE)

I am the Chair of the governing board of the County of Riverside, the public entity which executed the foregoing notice and on whose behalf I make this verification; I have read this notice, know its contents, and the same is true. I certify under penalty of perjury that the foregoing is true and correct.

, California on May 21, 2024

(Date)

ATTEST: Kimberly Rector, Clerk

Chair of the Board of Supervisors Chuck Washington

PETER ALDANA COUNTY OF RIVERSIDE ASSESSOR-COUNTY CLERK-RECORDER

Recorder P.O. Box 751 Riverside, CA 92502-0751 (951) 486-7000

www.riversideacr.com

CERTIFICATION

Pursuant to the provisions of Government Code 27361.7, I certify under the penalty of perjury that the following is a true copy of illegible wording found in the attached document:

(Print or type the page number(s) and wording below):

CLARIFICATION FOR SEAL for the Riverside County Board of Supervisors (EMBOSSED ON DOCUMENT)



Date:

05/21/2024

Signature:


Print Name: Naomy Sicra, Clerk of the Board Assistant


ACR 601P-AS4RE0 (Rev. 09/2005)

COUNTY OF RIVERSIDE TRANSPORTATION DEPARTMENT

STETSON AVENUE RESURFACING PROJECT

SANTA FE STREET TO 150-FEET EAST OF HEMET STREET **COMMUNITY OF EAST HEMET** PROJECT No. D0-0016



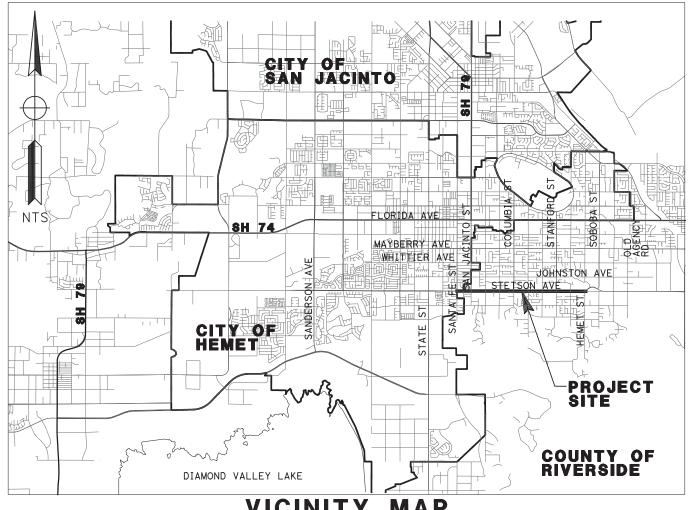

CHANGE ORDER REPORT

(Stetson Avenue Resurfacing Project)

CCO#	Amount	Percent	Description
	Original Contract Amount		
	\$3,172,000		
1	\$34,934.78	1.10%	Traffic signal modifications including grounding of video controller, replacing existing signal heads and adding reflective backing plates and battery backups (BBS) to existing traffic controllers.
Total Change Orders	\$34,934.78	1.10%	
Revised Contract Amount	\$3,206,934.78		

PROGRESS ESTIMATE RECORD - COUNTY OF RIVERSIDE SHEET 1 of 4 Processed Construction Inspection 3/21/2024

County	T: Stetson Avenue Resurfacing Project, Community of East Hemet Project No.: D0-0016 t No. 22-08-002				Contractor: Onyx Pavin Address: 2890 E La C City, State, Zip: Anahe	esta Ave.					A DAY OF RIVE		Estimate No. From: To:	6 FINAL June 26, 202 February 25, 20	
It em No.	Item Description	Units	Quantity	Unit Price	Original Contract Amount	Change Orde Quantity	rs Amount	Amended Co Quantity	ont ract Amount	This Estimate Quantity	Amount	Previous Quantity	Total Estimate To Quantity	Date Amount	% Auth.
	BASE BID SCHEDULE - Stetson Street Resurfacing														
1	DEVELOP WATER SUPPLY	LS	1	11,000.00	11,000.00			1.00	11,000.00			1.00	1.00	11,000.00) 100%
2	TRAFFIC CONTROL SYSTEM	LS	1	227,000.00	227,000.00			1.00	227,000.00			1.00	1.00	227,000.00) 100%
3	FUNDING AWARENESS SIGN	EA	2	2,000.00	4,000.00			2.00	4,000.00			2.00	2.00	4,000.00) 100%
4	PREPARE WATER POLLUTION CONTROL PROGRAM	LS	1	7,000.00	7,000.00			1.00	7,000.00			1.00	1.00	7,000.00) 100%
5	CLEARING AND GRUBBING	LS	1	172,769.92	172,769.92			1.00	172,769.92			1.00	1.00	172,769.92	100%
6	DUST ABATEMENT	LS	1	11,000.00	11,000.00			1.00	11,000.00			1.00	1.00	11,000.00) 100%
7(F)	ROADWAY EXCAVATION	CY	1,050	55.00	57,750.00			1,050.00	57,750.00			1,050.00	1,050.00	57,750.00) 100%
8	PLACE ASPHALT CONCRETE DIKE (CRS 212) (6")	LF	7,454	2.00	14,908.00			7,454.00	14,908.00			6,271.00	6,271.00	12,542.00	84%
9	PLACE ASPHALT CONCRETE DIKE (CRS 212) (8")	LF	2,906	2.00	5,812.00			2,906.00	5,812.00			2,336.00	2,336.00	4,672.00	80%
10	PLACE HOT MIX ASPHALT DIKE (TYPE E)	LF	248	2.00	496.00			248.00	496.00			40.00	40.00	80.08	16%
11	PLACE HOT MIX ASPHALT (MISCELLANEOUS AREA) [DRAINAGE INLET PAVING]	EA	6	3,500.00	21,000.00			6.00	21,000.00			6.00	6.00	21,000.00) 100%
12	ASPHALT CONCRETE (DRIVEWAY APPROACH WITH ASPHALT CONCRETE DIKE) (CRS 206)	SQFT	23,100	2.00	46,200.00			23,100.00	46,200.00			25,618.00	25,618.00	51,236.00) 1119
13	ASPHALT CONCRETE (DRIVEWAY APPROACH WITH ASPHALT CONCRETE DIKE) (CRS 206) [MODIFIED PER PLAN]	SQFT	7,000	2.00	14,000.00			7,000.00	14,000.00			3,054.00	3,054.00	6,108.00) 44%
14	HOT MIX ASPHALT (TYPE A)	TON	1,400	111.00	155,400.00			1,400.00	155,400.00			1,750.00	1,750.00	194,250.00	125%
15	RUBBERIZED HOT MIX ASPHALT (GAP GRADED)	TON	7,950	123.00	977,850.00			7,950.00	977,850.00			7,267.70	7,267.70	893,927.10) 91%
16	COLD PLANE ASPHALT CONCRETE PAVEMENT	SQYD	62,000	2.22	137,640.00			62,000.00	137,640.00			57,080.00	57,080.00	126,717.60	92%
17	ADJUST MANHOLE [LHMWD, RCFC]	EA	46	1,000.00	46,000.00			46.00	46,000.00			24.00	24.00	24,000.00) 52%
18	MINOR CONCRETE (CURB AND GUTTER) (CRS 200)	LF	70	95.00	6,650.00			70.00	6,650.00			82.00	82.00	7,790.00) 1179
19	MINOR CONCRETE (CURB AND GUTTER) (CRS 201)	LF	9	95.00	855.00			9.00	855.00						0%
20	MINOR CONCRETE (CURB RAMP) (CRS 403 - CASE A)	EA	2	7,000.00	14,000.00			2.00	14,000.00			2.00	2.00	14,000.00) 100%
21	MINOR CONCRETE (CURB RAMP) (CRS 403 - CASE B)	EA	4	7,000.00	28,000.00			4.00	28,000.00			4.00	4.00	28,000.00) 100%
22	MINOR CONCRETE (CURB RAMP) (CRS 403 - CASE B) [MODIFIED]	EA	7	7,000.00	49,000.00			7.00	49,000.00			6.00	6.00	42,000.00	86%

PROGRESS ESTIMATE RECORD - COUNTY OF RIVERSIDE SHEET 2 of 4 Processed Construction Inspection 3/21/2024

County F	: Stetson Avenue Resurfacing Project, Community of East Hemet Project No.: D0-0016 No. 22-08-002				Contractor: Onyx Pavin Address: 2890 E La C City, State, Zip: Anahe	resta Ave.					THE PATION OF RIVERS		Estimate No. From: To:	6 FINAL June 26, 202 February 25, 20	
It em No.	Item Description	Units	Quantity	Unit Price	Original Contract Amount	Change Orde Quantity	rs Amount	Amended C Quantity	ontract Amount	This Estimate Quantity	Amount	Previous Quant it y	Total Estimate Quantity	To Date Amount	% Auth.
23	MINOR CONCRETE (CURB RAMP) [MODIFIED CALTRANS STD. A88A CASE A]	EΑ	2	7,000.00	14,000.00			2.00	14,000.00			2.00	2.00	14,000.00	100%
24	MINOR CONCRETE (CROSS-GUTTER AND SPANDREL) (AND SPANDREL ONLY)	SQFT	9,400	20.00	188,000.00			9,400.00	188,000.00			8,820.38	8,820.38	176,407.60	94%
25	MINOR CONCRETE (DRIVEWAY) [CRS 206]	SQFT	2,100	16.00	33,600.00			2,100.00	33,600.00			1,752.00	1,752.00	28,032.00	83%
26	MINOR CONCRETE (COMMERCIAL DRIVEWAY) (CRS 207A) [MODIFIED]	SQFT	50	27.00	1,350.00			50.00	1,350.00			43.00	43.00	1,161.00	86%
27	MINOR CONCRETE (COMMERCIAL DRIVEWAY) (CRS 207A)	SQFT	660	27.00	17,820.00			660.00	17,820.00			820.00	820.00	22,140.00	124%
28	MINOR CONCRETE (CURB) [CALTRANS STD A87A TYPE D-4]	LF	632	48.00	30,336.00			632.00	30,336.00			712.00	712.00	34,176.00	113%
29	MINOR CONCRETE (SIDEWALK)	SQFT	550	11.00	6,050.00			550.00	6,050.00			685.00	685.00	7,535.00	125%
30	PAVEMENT MARKER (RETROREFLECTIVE)	EA	1,054	3.50	3,689.00			1,054.00	3,689.00			1,054.00	1,054.00	3,689.00	100%
31	REMOVE ROADSIDE SIGN [AND SALVAGE]	EA	13	77.00	1,001.00			13.00	1,001.00			13.00	13.00	1,001.00	100%
32	ROADSIDE SIGN - ONE POST	EA	75	222.00	16,650.00			75.00	16,650.00			75.00	75.00	16,650.00	100%
33	PAINT TRAFFIC STRIPE (2-COAT)	LF	27,932	0.69	19,273.08			27,932.00	19,273.08			27,932.00	27,932.00	19,273.08	100%
34	THERMOPLASTIC CROSSWALK AND PAVEMENT MARKING	SQFT	1,400	11.00	15,400.00			1,400.00	15,400.00			1,750.00	1,750.00	19,250.00	125%
35	DELINEATOR (CLASS 2)	EA	5	100.00	500.00			5.00	500.00			5.00	5.00	500.00	100%
36	SIGNAL AND LIGHTING SYSTEM [GIRARD STREET]	LS	1	111,000.00	111,000.00			1.00	111,000.00	0.10	11,100.00	0.90	1.00	111,000.00	100%
37	SIGNAL AND LIGHTING SYSTEM [COLUMBIA STREET]	LS	1	110,000.00	110,000.00			1.00	110,000.00	0.10	11,000.00	0.90	1.00	110,000.00	100%
38	SIGNAL AND LIGHTING SYSTEM [DARTMOUTH STREET]	LS	1	72,000.00	72,000.00			1.00	72,000.00	0.10	7,200.00	0.90	1.00	72,000.00	100%
39	SIGNAL AND LIGHTING SYSTEM [BULLDOG WAY (HEMET HIGH SCHOOL)]	LS	1	72,000.00	72,000.00			1.00	72,000.00	0.10	7,200.00	0.90	1.00	72,000.00	100%
40	SIGNAL AND LIGHTING SYSTEM [STANFORD STREET]	LS	1	84,000.00	84,000.00			1.00	84,000.00	0.10	8,400.00	0.90	1.00	84,000.00	100%
41	3" SCHEDULE 80 PVC CONDUIT & CCO 1	LF	80	300.00	24,000.00	-80.00	-24,000.00								N/ A
42	PULL BOX (NO. 6 PER CALTRANS STD. ES-8B) & CCO 1	EA	4	2,500.00	10,000.00	-4.00	-10,000.00								N/ A
43	MISCELLANEOUS WORK (AS DIRECTED)	FA	1	150,000.00	150,000.00			1.00	150,000.00			0.9295233	0.9295233	139,428.50	93%
CCO 1	Traffic Signal Modifications	FA	0	68,934.78	0.00	1.00	68,934.78	1.00	68,934.78	1.00000	68,934.78		1.0000000	68,934.78	100%
	ALTERNATIVE BID SCHEDULE 1 - City of Hemet Portion (Santa Fe Street to City Limit)														
44	DEVELOP WATER SUPPLY	LS	1	3,000.00	3,000.00			1.00	3,000.00			1.00	1.00	3,000.00	100%

PROGRESS ESTIMATE RECORD - COUNTY OF RIVERSIDE SHEET 3 of 4 Processed Construction Inspection 3/21/2024

	Γ: Stetson Avenue Resurfacing Project, Community of East Hemet Project No.: D0-0016		Contractor: Onyx Paving Company, Inc. Address: 2890 E La Cresta Ave.						SHIN OF RIVERS		Estimate No. From:	6 FINAL June 26, 202	23		
1	t No. 22-08-002				City, State, Zip: Anahei	m, CA 92806				To:	February 25, 20				
lt em			С		Original Contract	Change Orders		Amended Co		This Estimate		Previous	Total Estimate To		%
No.	Item Description	Units	Quantity	Unit Price	Amount	Quantity /	Amount	Quantity	Amount	Quantity	Amount	Quantity	Quantity	Amount	Auth.
45	TRAFFIC CONTROL SYSTEM	LS	1	27,846.00	27,846.00			1.00	27,846.00			1.0000000	1.0000000	27,846.00	100%
46	CLEARING AND GRUBBING (LS)	LS	1	13,000.00	13,000.00			1.00	13,000.00			1.0000000	1.0000000	13,000.00	100%
47	DUST ABATEMENT	LS	1	3,000.00	3,000.00			1.00	3,000.00			1.00	1.00	3,000.00	100%
48(F)	ROADWAY EXCAVATION	CY	390	55.00	21,450.00			390.00	21,450.00			390.00	390.00	21,450.00	100%
49	PLACE ASPHALT CONCRETE DIKE (CRS 212) (8")	LF	107	2.00	214.00			107.00	214.00			70.00	70.00	140.00	65%
50	ASPHALT CONCRETE (DRIVEWAY APPROACH WITH ASPHALT CONCRETE DIKE) (CRS 206)	SQFT	500	2.00	1,000.00			500.00	1,000.00			330.00	330.00	660.00	66%
51	HOT MIX ASPHALT (TYPE A)	TON	550	111.00	61,050.00			550.00	61,050.00			550.00	550.00	61,050.00	100%
52	RUBBERIZED HOT MIX ASPHALT (GAP GRADED)	TON	280	123.00	34,440.00			280.00	34,440.00			293.06	293.06	36,046.38	105%
53	ADJUST MANHOLE [RCFC]	EA	1	1,000.00	1,000.00			1.00	1,000.00			1.00	1.00	1,000.00	100%
	ALTERNATIVE BID SCHEDULE 2 - EMWD MANHOLE ADJUSTMENTS													,	
54	ADJUST MANHOLE [EMWD]	EA	15	1,000.00	15,000.00			15.00	15,000.00			3.00	3.00	3,000.00	20%
	ALTERNATIVE BID SCHEDULE 3 - FRONTIER MANHOLE ADJUSTMENTS													!	
55	ADJUST MANHOLE [FRONTIER]	EA	1	2,000.00	2,000.00			1.00	2,000.00			1.00	1.00	2,000.00	100%

DROCDESS ESTIMATE RECORD COLINITY OF RIVERSIDE SHEET 4 of 4 Processed Construction Inspection 3/21/2024

ounty P	Stetson Avenue Resurfacing Project, Community of East Hemet roject No.: D0-0016 No. 22-08-002				Contractor: Onyx Pavin Address: 2890 E La Cro City, State, Zip: Anahei	esta Ave.				DULLY OF RIVERBO		Estimate No. From: To:	6 FINAL June 26, 2023 February 25, 2024
Item No.	It em Description	Units	Quantity	Unit Price	Original Contract Amount	Change Orders Quantity Amount	Amended (Quantity	Contract Amount	This Estimate Quantity	Amount	Previous Quant it y	Total Estimate Quantity	Fo Dat e Amount A
=	PROJECT TOTAL				3,172,000.00	34,934.78		3,206,934.78		113,834.78			3,090,212.96
	Made by _Rick Morton Checked byTN OK Const. SupvMS			Working Days: Days Added: Subtotal: Days Used: Time Elapsed: Suspended from	0 60 61 102%	Start Date End Date % \$ Complete Original Contrac Amended Contrac	2-21-24 2 96% 3 \$3,172	,000.00 ,934.78	Т	TOTAL LESS PREVIOU LESS LABOR NON TOTAL DUE	ESS RETENTION: DUE TO DATE: USLY INVOICED: N COMPLIANCE: THIS PAYMENT:	5%	\$3,090,212.96 154,510.65 \$2,935,702.31 2,827,559.28 0.00 \$108,143.04
Thi	s Estimate ApprovedPatricia Romo, Interim Director of Transpo		ate: <u>3/24/2</u> 0	024 _{for:}		\$108,143.04				Received by Acc			
Qu	antities on This Estimate ApprovedOnyx Paving Compan	y, Inc.		Dat e: <u>3/22/2024</u>		DEP ACCO PRO ACTIVIT RESO SIGNA	Payment Appround	D. Davil	3/26/24 JC				
