

**SUBMITTAL TO THE BOARD OF SUPERVISORS
COUNTY OF RIVERSIDE, STATE OF CALIFORNIA**



**ITEM: 3.24
(ID # 25795)**

MEETING DATE:
Tuesday, October 29, 2024

FROM : TLMA-TRANSPORTATION

SUBJECT: TRANSPORTATION AND LAND MANAGEMENT AGENCY/TRANSPORTATION:
Notice of Completion – Johnston Avenue Resurfacing Project, in the Community of East Hemet;
District 3. [\$0]

RECOMMENDED MOTION: That the Board of Supervisors:

1. Accept as complete the Construction of Johnston Avenue Resurfacing Project, in the Community of East Hemet; District 3;
2. Authorize the Chair of the Board to execute the Notice of Completion on behalf of the County; and
3. Direct the Clerk of the Board to record the Notice of Completion.


ACTION:Policy


Dennis Acuna, Director of Transportation 10/17/2024

MINUTES OF THE BOARD OF SUPERVISORS

On motion of Supervisor Spiegel, seconded by Supervisor Gutierrez and duly carried by unanimous vote, IT WAS ORDERED that the above matter is approved as recommended.

Ayes: Jeffries, Spiegel, Washington, Perez and Gutierrez
Nays: None
Absent: None
Date: October 29, 2024
xc: Trans., Recorder

Kimberly A. Rector
Clerk of the Board
By: 
Deputy

**SUBMITTAL TO THE BOARD OF SUPERVISORS COUNTY OF RIVERSIDE,
STATE OF CALIFORNIA**

FINANCIAL DATA	Current Fiscal Year:	Next Fiscal Year:	Total Cost:	Ongoing Cost
COST	\$ 0	\$ 0	\$ 0	\$ 0
NET COUNTY COST	\$ 0	\$ 0	\$ 0	\$ 0
SOURCE OF FUNDS: N/A			Budget Adjustment:	N/A
			For Fiscal Year:	24/25

C.E.O. RECOMMENDATION: Approve

BACKGROUND:

Summary

By Minute Order 3.37 of September 12, 2023, the Board of Supervisors entered into a contract with Onyx Paving Company, Inc. of Anaheim, California for the Construction of the Johnston Avenue Resurfacing Project. The limits of the project along Johnston Avenue are from San Jacinto Street to 630-Foot East of Stanford Street in the community of East Hemet.

The original authorized amount of the contract was \$2,938,000.00. The total value of work came in at \$2,536,064 which was 13.7% lower than the originally authorized amount. The reduction of the total cost was the result of using less quantities than anticipated to complete the work.

The work was completed in conformance with the plans and specifications and the Contractor was granted relief of maintenance on June 6, 2024.

Project Number: B0-0612

Impact on Residents and Businesses

The improvements benefit the project area by providing the public with a smooth paved roadway that will improve the overall safety and efficiency of vehicular traffic.

Additional Fiscal Information

Budget			
Original Contract Amount			\$2,938,000
Total Change Orders Authorized	0.0%		\$0
Estimated Pending Change Orders	0.0%		\$0
Authorized Contract Amount			\$2,938,000
* Quantity Adjustments	-13.7%		(\$401,936)
+ CCO FA Adjustments	0.0%		\$0
Total Value of Work	86.3%		\$2,536,064
Expenditures			
Total Progress Payments			\$2,536,064
Estimated Pending Payments			\$0
Total Expenditures			\$2,536,064
(Over)/Under Contract Amount			\$0

* Caltrans Standard Specifications 9-1.06 (Changed Quantity Payment Adjustments). Increases or decreases in the quantity of a contract item of work will be determined by comparing the total pay quantity of such item of work with the Engineer's Estimate. If the total pay quantity of any

**SUBMITTAL TO THE BOARD OF SUPERVISORS COUNTY OF RIVERSIDE,
STATE OF CALIFORNIA**

item of work required under the contract varies from the Engineer's Estimate by 25 percent or less, payment will be made for the quantity of work of said item performed at the contract unit price, unless eligible for adjustment pursuant to Section 9-1.15, "Work-Character Changes."

Contract History and Price Reasonableness

A total of four bids were received on Wednesday, July 5, 2023 ranging from \$2,938,000 to \$3,730,258. The basis for the selection of a contractor is the lowest responsive and responsible bid. The lowest responsive and responsible bid was submitted by Onyx Paving Company, Inc., in the amount of \$2,938,000 which was \$6,850 (0.2%) above the engineer's cost estimate.

ATTACHMENTS:

Vicinity Map
Progress Estimate Report
Notice of Completion



Jason Farin, Principal Management Analyst 10/22/2024



Aaron Gettis, Chief of Deputy County Counsel 10/18/2024

PLEASE COMPLETE THIS INFORMATION
RECORDING REQUESTED BY:

**KIMBERLY RECTOR, CLERK OF THE BOARD
RIVERSIDE CO. CLERK OF THE BOARD
4080 LEMON STREET, 1ST FLOOR CAC
P O BOX 1147 – RIVERSIDE, CA 92502
MAIL STOP # 1010**

2024-0338521

11/07/2024 10:42 AM Fee: \$ 0.00

Page 1 of 2

Recorded in Official Records
County of Riverside
Peter Aldana
Assessor-County Clerk-Recorder



AND WHEN RECORDED MAIL TO:

**RETURN TO: STOP #1010
RIVERSIDE COUNTY CLERK OF THE BOARD
P. O. BOX 1147 – RIVERSIDE, CA 92502**

2148

THIS SPACE FOR RECORDERS USE ONLY

NOTICE OF COMPLETION

To be recorded with County Recorder
within 10 days after completion.
No recording fee.

Notice is hereby given by the undersigned owner, a public entity of the State of California, that a public work of improvement has been completed, as follows:

Project title or description of work: Johnston Avenue Resurfacing
Project No. B0-0612

Date of Completion: Date Hereof

Nature of owner: County of Riverside, public entity

Interest or estate of owner: Public Road Right-of-Way

Address of owner: Clerk of the Board of Supervisors, County Administrative Center
4080 Lemon Street, 8th Floor, Riverside, CA 92501

Name and Address of contractor: Onyx Paving Company, Inc., 2890 E. La Cresta Avenue, Anaheim, CA 92806

Street or legal description of site: San Jacinto Street to 630-Feet East of Stanford Street, Community of East Hemet

Dated: October 29, 2024

Owner: County of Riverside
(Name of Public Entity)

By: *Chuck Washington*
Chair, Board of Supervisors
Chuck Washington

STATE OF CALIFORNIA)

ss


COUNTY OF RIVERSIDE)

I am the Chair of the governing board of the County of Riverside, the public entity which executed the foregoing notice and on whose behalf I make this verification; I have read this notice, know its contents, and the same is true. I certify under penalty of perjury that the foregoing is true and correct.

Executed at Riverside, California on October 29, 2024 (Date)

Chuck Washington, Chair of the Board of Supervisors
Chuck Washington

ATTEST: Kimberly Rector, Clerk
By: *Kimberly Rector*
Deputy



FORM APPROVED COUNTY COUNSEL

BY: *Danielle*
DANIELLE J. [unclear]

**PETER ALDANA
COUNTY OF RIVERSIDE
ASSESSOR-COUNTY CLERK-RECORDER**

Recorder
P.O. Box 751
Riverside, CA 92502-0751
(951) 486-7000

www.riversideacr.com

CERTIFICATION

Pursuant to the provisions of Government Code 27361.7, I certify under the penalty of perjury that the following is a true copy of illegible wording found in the attached document:

(Print or type the page number(s) and wording below):

CLARIFICATION FOR SEAL for the Riverside County Board of Supervisors
(EMBOSSSED ON DOCUMENT)



Date: 10/29/2024

Signature: _____

Print Name: Naomy Sicra, Clerk of the Board Assistant



COUNTY OF RIVERSIDE
TRANSPORTATION DEPARTMENT

JOHNSTON AVENUE RESURFACING

SAN JACINTO STREET TO 630-FEET EAST OF STANFORD STREET

COMMUNITY OF EAST HEMET

PROJECT No. B0-0612

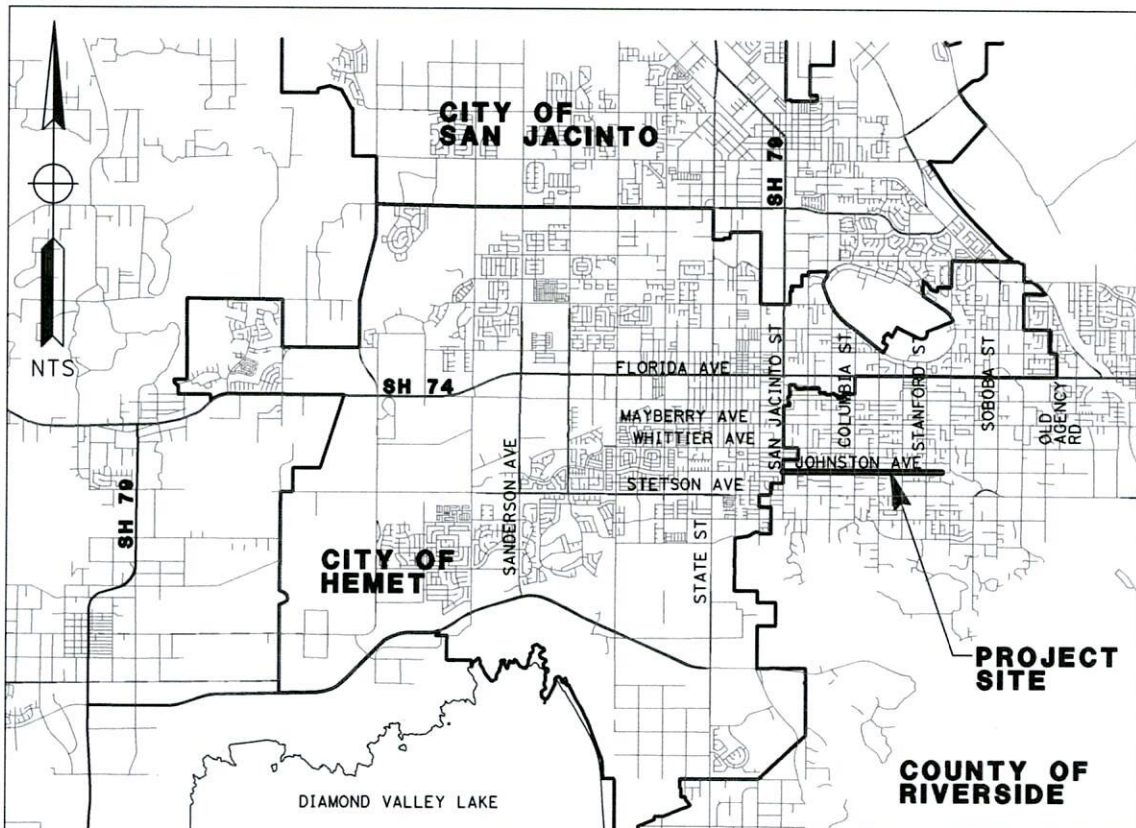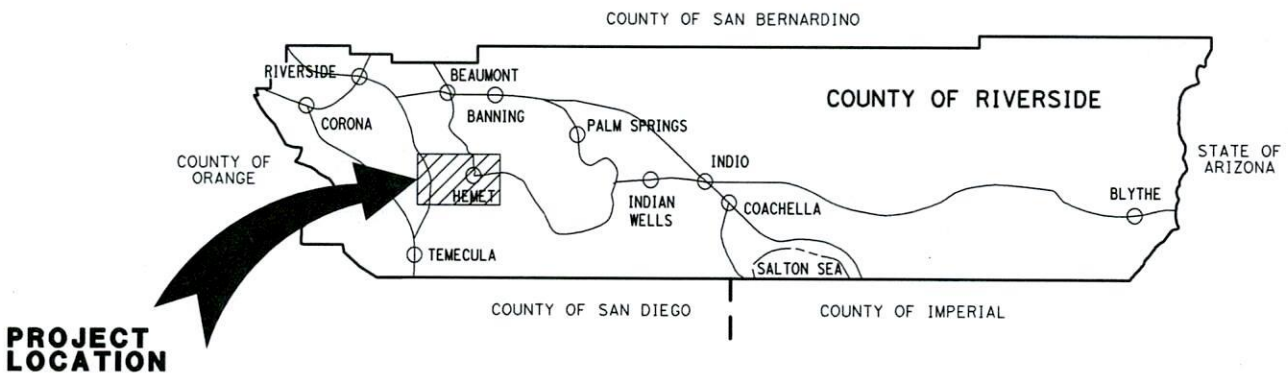

PROJECT: Johnston Avenue Resurfacing Project
 County Project No. 18-0612
 Contract No. 23-07-004

Contractor: Onyx Paving Company, Inc.
 Address: 2880 E. La Cresta Ave.
 City, State, Zip: Anaheim, CA 92816

Estimate No. 7 Final
 From: May 26, 2024
 To: July 25, 2024



Item No.	Item Description	Units	Quantity	Unit Price	Original Contract		Change Orders		Amended Contract		This Estimate		Previous Quantity	Total Estimate To Date	%	
					Amount	Quantity	Amount	Quantity	Amount	Quantity	Amount	Quantity				
1	DEVELOP WATER SUPPLY	LS	1	11,602.00	11,602.00	1.00							1.00	11,602.00	100%	
2	TRAFFIC CONTROL SYSTEM	LS	1	222,000.00	222,000.00	1.00							1.00	222,000.00	100%	
3	PREPARE WATER POLLUTION CONTROL PROGRAM	LS	1	11,000.00	11,000.00	1.00							1.00	11,000.00	100%	
4	CLEARING AND GRUBBING	LS	1	333,000.00	333,000.00	1.00							1.00	333,000.00	100%	
5	DUST ABATEMENT	LS	1	11,000.00	11,000.00	1.00							1.00	11,000.00	100%	
6	ROADWAY EXCAVATION	CY	5,300	55.00	291,500.00	5,300.00			5,300.00	291,500.00			5,300.00	5,300.00	100%	
7	PLACE ASPHALT CONCRETE DIKE (OPS 212) (6")	LF	95	11.00	1,045.00	95.00			95.00	1,045.00			95.00	913.00	87%	
8	PLACE ASPHALT CONCRETE DIKE (OPS 212) (8")	LF	95	11.00	1,045.00	95.00			95.00	1,045.00			78.00	856.00	82%	
9	PLACE HOT MIX ASPHALT DIKE (TYPE D)	LF	1,900	11.00	20,900.00	1,900.00			1,900.00	20,900.00			1,924.00	21,164.00	101%	
10	PLACE HOT MIX ASPHALT DIKE (TYPE D) [PER CALTRANS STD A878, MODIFIED TO 8" HEIGHT]	LF	550	11.00	6,050.00	550.00			550.00	6,050.00			540.00	5,940.00	98%	
11	PLACE HOT MIX ASPHALT DIKE (TYPE B) (PER CALTRANS ST A878)	LF	30	11.00	330.00	30.00			30.00	330.00					0%	
12	HOT MIX ASPHALT (TYPE A)	TON	11,500	11.00	1,276,500.00	11,500.00			11,500.00	1,276,500.00			9,880.93	9,880.93	1,056,783.23	86%
13	ASPHALT CONCRETE (DRIVEWAY APPROACH WITH ASPHALT CONCRETE DIKE) (OPS 206)	SOFT	180	10.00	1,800.00	180.00			180.00	1,800.00			134.00	1,340.00	74%	
14	ASPHALT CONCRETE (DRIVEWAY APPROACH WITH ASPHALT CONCRETE DIKE) (OPS 206) [MODIFIED FOR ASPHALT CONCRETE DRIVEWAY] (3.5-INCH ON NATIVE)	SOFT	6,600	6.00	39,600.00	6,600.00			6,600.00	39,600.00			8,250.00	8,250.00	125%	
15	ASPHALT CONCRETE DRIVEWAY (3.5-INCH ON NATIVE)	SOFT	18,000	5.00	90,000.00	18,000.00			18,000.00	90,000.00			17,772.00	17,772.00	99%	
16	ADJUST UTILITY COVER TO GRADE (WATER METER LHMWD)	EA	15	2,000.00	30,000.00	15.00			15.00	30,000.00			8.00	16,000.00	53%	
17	ADJUST MANHOLE (LHMWD)	EA	24	1,500.00	36,000.00	24.00			24.00	36,000.00			24.00	36,000.00	100%	
18	ADJUST SEWER CLEANOUT TO GRADE (LHMWD)	EA	2	1,500.00	3,000.00	2.00			2.00	3,000.00			1.00	1,500.00	50%	
19	MINOR CONCRETE (DRIVEWAY) (OPS 213)	SOFT	160	20.00	3,200.00	160.00			160.00	3,200.00			124.00	2,480.00	78%	
20	MINOR CONCRETE (DRIVEWAY) [MODIFIED FOR MOUNTABLE DIKE]	SOFT	1,400	20.00	28,000.00	1,400.00			1,400.00	28,000.00			1,393.60	1,393.60	100%	
21	MINOR CONCRETE (DRIVEWAY) [6-INCH ON NATIVE]	SOFT	950	20.00	19,000.00	950.00			950.00	19,000.00			1,061.90	21,238.00	112%	

PROJECT: Johnson Avenue Rebuilding Project
 County Project No.: 06-0612
 Contract No. 23-07-024



Contractor: Onyx Paving Company, Inc.
 Address: 2890 E. La Cresta Ave.
 City, State, Zip: Anaheim, CA 92806

Estimate No. 7 Final
 From: May 26, 2024
 To: July 25, 2024

Item No.	Item Description	Units	Quantity	Unit Price	Original Contract Amount	Change Orders Quantity	Change Orders Amount	Amended Contract Quantity	Amended Contract Amount	The Estimate Quantity	Estimate Amount	Previous Quantity	Total Estimate To Date	% Aurb
22	MINOR CONCRETE (DRIVEWAY APPROACH WITH ASPHALT CONCRETE DIB) (CRS 206) [MODIFIED FOR CURB AND GUTTER]	SOFT	550	20.00	11,000.00			550.00	11,000.00		11,000.00	564.00	11,260.00	103%
23	MINOR CONCRETE (CURB AND GUTTER) (CRS 209)	LF	420	69.00	28,980.00			420.00	28,980.00		28,980.00	511.00	35,259.00	122%
24	MINOR CONCRETE (CURB RAMP) (CRS 403 - CASE A)	EA	4	8,400.00	33,600.00			4.00	33,600.00		33,600.00	4.00	33,600.00	100%
25	MINOR CONCRETE (CURB RAMP) (CRS 403 - CASE B) [MODIFIED PER PLAN] MINOR CONCRETE	EA	2	8,400.00	16,800.00			2.00	16,800.00		16,800.00	2.00	16,800.00	100%
26	MINOR CONCRETE (CROSS-GUTTER AND SPANDREL) (CRS 209)	SOFT	4,100	27.00	110,700.00			4,100.00	110,700.00		110,700.00	3,122.09	84,296.43	76%
27	MINOR CONCRETE (MINOR STRUCTURE) (CRS 308, MODIFIED FOR REVERSE FLOW INLET, WIDTH=4')	EA	1	27,000.00	27,000.00			1.00	27,000.00		27,000.00	1.00	27,000.00	100%
28	UNDER SIDEWALK DRAIN CAST IN PLACE (CRS 309)	EA	1	16,880.00	16,880.00			1.00	16,880.00		16,880.00	1.00	16,880.00	100%
29	MINOR CONCRETE (GUTTER DEPRESSION)	EA	1	9,000.00	9,000.00			1.00	9,000.00		9,000.00	1.00	9,000.00	100%
30	MINOR CONCRETE (SIDEWALK) [AND 4' WALKWAYS]	SOFT	670	13.00	8,710.00			670.00	8,710.00		8,710.00	653.60	8,486.80	98%
31	RESET MAILBOX (OR RELOCATE MAILBOX)	EA	15	400.00	6,000.00			15.00	6,000.00		6,000.00	13.00	5,200.00	87%
32(F)	PAVEMENT MARKER (RETROREFLECTIVE)	EA	310	11.00	3,410.00			310.00	3,410.00		3,410.00	310.00	3,410.00	100%
33	REMOVE ROADSIDE SIGN [AND SALVAGE]	EA	22	111.00	2,442.00			22.00	2,442.00		2,442.00	14.00	1,554.00	64%
34	ROADSIDE SIGN - ONE POST	EA	22	373.00	8,206.00			22.00	8,206.00		8,206.00	14.00	5,222.00	64%
35(F)	PAINT TRAFFIC STRIPE - ONE POST	LFT	14,500	0.55	7,975.00			14,500.00	7,975.00		7,975.00	14,500.00	14,500.00	100%
36	THERMOPLASTIC CROSSWALK AND PAVEMENT MARKING	SOFT	675	7.00	4,725.00			675.00	4,725.00		4,725.00	843.75	5,906.25	125%
37	MISCELLANEOUS WORK (AS DIRECTED)	FA	1	200,000.00	200,000.00			1.00	200,000.00		200,000.00	0.04417375	8,834.75	4%
38	ADJUST MANHOLE (BAND)	EA	5	1,200.00	6,000.00			5.00	6,000.00		6,000.00	4.00	4,800.00	80%
PROJECT TOTAL					2,938,000.00	0.00	2,938,000.00	0.00	2,938,000.00		2,938,000.00	0.00	2,535,054.46	

Made by: Douglas Christensen M&E, Inc. Working Days: 60 Start Date: 12-11-23

PROJECT: Johnston Avenue Restriping Project
 County Project No.: 80-0612
 Contract No. 23-07-004



Contractor: Onyx Paving Company, Inc.
 Address: 2890 E. La Cresta Ave.
 Chy. State, Zip: Anaheim, CA 92805

Estimate No. 7 Final
 From: May 28, 2024
 To: July 15, 2024

Item No.	Item Description	Units	Quantity	Unit Price	Original Contract Amount	Amended Contract Quantity	Amended Contract Amount	Change Orders Quantity	Change Orders Amount	Total Estimate Quantity	Total Estimate Amount	% Auth.
Checked by: TN												
OK Const. Supv. JMS												
	Days Added:		0		End Date:	4-8-24				TOTAL VALUE OF WORK TO DATE	\$2,536,064.46	
	Subtotal:		60		% S Complete:	86%				LESS RETENTION:	126,803.22	5%
	Days Used:		60		Original Contract:	\$2,938,000.00				TOTAL DUE TO DATE	\$2,409,261.24	
	% Time Elapsed:		100%		Amended Contract:	\$2,938,000.00				LESS PREVIOUSLY INVOICED:	2,409,261.24	
										LESS LABOR NON COMPLIANCE	0.00	
										TOTAL DUE THIS PAYMENT:	\$0.00	

This Estimate Approved for 7/29/2024 Date: 7/29/2024 for \$0.00

Dennis Acuna, Director of Transportation

Quantities on This Estimate Approved Date: 7/29/2024

Onyx Paving Company, Inc.

Payment Approval
 FUND: 20000
 DEPT. ID.: 31305
 ACCOUNT: 527980
 PROJECT: 280-0612E
 ACTIVITY ID.: 25500
 RESOURCE CNT
 SIGNATURE: DATE: 7/29/24

Received by Accounts Payable _____
 By: _____
