

**SUBMITTAL TO THE FLOOD CONTROL AND
WATER CONSERVATION DISTRICT BOARD OF SUPERVISORS
COUNTY OF RIVERSIDE, STATE OF CALIFORNIA**

602B



FROM: General Manager-Chief Engineer

SUBMITTAL DATE:
November 3, 2015

SUBJECT: Approve Contract Change Order No. 1, Little Lake MDP Line B, Stage 1,
Project No. 4-0-00265-01, District 3, [\$162,916] 100% District Funds

RECOMMENDED MOTION: That the Board of Supervisors:
Ratify the attached Contract Change Order No. 1 between the District and Gwinco Construction & Engineering, Inc., providing compensation for Extra Work required for the completion of the Little Lake MDP Line B, Stage 1 project.

BACKGROUND:

Summary

The Board approved a contract with Gwinco Construction & Engineering, Inc., in the amount of \$6,398,777 as Agenda Item No. 11-3 on September 30, 2014.

AD:mcv
P8\172566

WARREN D. WILLIAMS
General Manager-Chief Engineer

FINANCIAL DATA	Current Fiscal Year:	Next Fiscal Year:	Total Cost:	Ongoing Cost:	POLICY/CONSENT (per Exec. Office)
COST	\$ 162,916	\$ 0	\$ 162,916	\$ 0	Consent <input type="checkbox"/> Policy <input type="checkbox"/>
NET DISTRICT COST	\$ 162,916	\$ 0	\$ 162,916	\$ 0	
SOURCE OF FUNDS: 25140 947460 527980 Zone 4 Const/Maint/Misc-Contracts				Budget Adjustment: No	
				For Fiscal Year: 15/16	

C.E.O. RECOMMENDATION:

APPROVE
BY:
Steven C. Horn

County Executive Office Signature

MINUTES OF THE BOARD OF SUPERVISORS

FORM APPROVED COUNTY COUNSEL
BY: GREGORY P. PRIAMOS
DATE: 11/20/15

FISCAL PROCEDURES APPROVED
JEANINE J. REY, FINANCE DIRECTOR
BY: REGINA L. NEAL
Departmental Concurrence
DATE: 11/21/15

- A-30
- 4/5 Vote
- Positions Added
- Change Order

**SUBMITTAL TO THE FLOOD CONTROL AND WATER CONSERVATION DISTRICT
BOARD OF SUPERVISORS, COUNTY OF RIVERSIDE, STATE OF CALIFORNIA**

FORM 11: Approve Contract Change Order No. 1, Little Lake MDP Line B, Stage 1,
Project No. 4-0-00265-01, District 3, [\$162,916] 100% District Funds

DATE: November 3, 2015

PAGE: Page 2 of 2

BACKGROUND:

Summary (continued)

Per Section II, Article 2.07A Board authorization of Contract Change Order No. 1 is necessary to ratify payment for Extra Work associated with the extra roadway paving that is necessary to ensure safe driving conditions (see Change Order Report below for Technical Summary).

This Contract Change Order is set at a not to exceed cost of \$162,916. The adjusted authorized contract amount is \$6,561,693, which is (2.5%) above the original authorized contract amount (reflected in Financial Data on Page 1 of this Form 11).

ATTACHMENTS:

A. Change Order Report

NUMBER	AMOUNT	PERCENT	DESCRIPTION
Change Order No. 1	\$162,916	2.5%	Additional Street Paving

Change Order No. 1 Technical Summary - The original project paving and earthwork plan indicates that hot mix asphalt (HMA) and aggregate base (AB) are to be replaced over the storm drain trench limits along Park Avenue and Meridian Street. The plan also shows that the remainder of the existing streets is to receive a 1.5" HMA grind and overlay.

After the storm drain construction through the intersection of Park Avenue and Meridian Street near Lincoln Avenue, the existing street was in such poor condition that it was deemed undrivable. The entire street width near the intersection required full AB and HMA replacement.

The street paving described above requires the placement of an additional 586.6 cubic yards of AB and 468.9 tons of HMA.

B. Additional Paving Limits Map

P8\172566

RIVERSIDE COUNTY FLOOD CONTROL & WATER CONSERVATION DISTRICT

Project: Little Lake MDP Line B, Stage 1
Project No. 4-0-00265-01

Sheet 1 of 1 sheets

CONTRACT CHANGE ORDER NO. 1

To Gwinco Construction and Engineering, Inc., Contractor
You are hereby directed to make the herein described changes from the plans and specifications or to do the following described work not included in the plans and specifications.

NOTE: THIS CHANGE ORDER IS NOT EFFECTIVE UNTIL APPROVED BY THE GENERAL MANAGER-CHIEF ENGINEER OR THE BOARD OF SUPERVISORS OF THE DISTRICT.

Description of work to be done, estimate of quantities, and prices to be paid. Unless otherwise stated, rates for rental of equipment cover only such time as equipment is actually used and no allowance will be made for idle time. Change requested by District

This change order covers the additional hot mix asphalt (HMA) and Class II Aggregate Base needed to restore Park Avenue to an acceptable driving condition. The District and the City of Hemet worked together to determine the restoration limits and the required pavement section. The approved Plans and Specifications did not identify this work.

The Extra Work defined in this change order is based on a lump sum basis in accordance with Section II, Article 2.07 and Section VII, Article 7.03 of the General Provisions.

The lump sum cost associated with this is \$162,916.26.

Estimated Cost: Decrease \$ _____ or Increase \$162,916.26

By reason of this order the time of completion will be adjusted as follows: 0

Submitted by: [Signature] Date: 9/3/15
KENT ALLEN, Construction Engineer

Approved: [Signature] Date: 10/20/15
WARREN D. WILLIAMS, General Manager-Chief Engineer


Chairman, Board of Supervisors

We, the undersigned Contractor, have given careful consideration to the change proposed and hereby agree, if this proposal is approved, that we will provide all equipment, furnish all materials, except as may be otherwise noted above, and perform all services necessary for the work above specified, and will accept as full payment therefor the prices shown above.


Accepted: Date 9-8-15 Contractor GWINCO CONSTRUCTION & ENGINEERING INC
By: [Signature] Title PRESIDENT

If the Contractor does not sign acceptance of this order, his attention is directed to the requirements of the specifications as to the proceeding with the ordered work and filing a written protest within the time therein specified.

FORM APPROVED COUNTY COURSE
BY: [Signature]
NEAL R. KIRINIS
DATE: 10/15

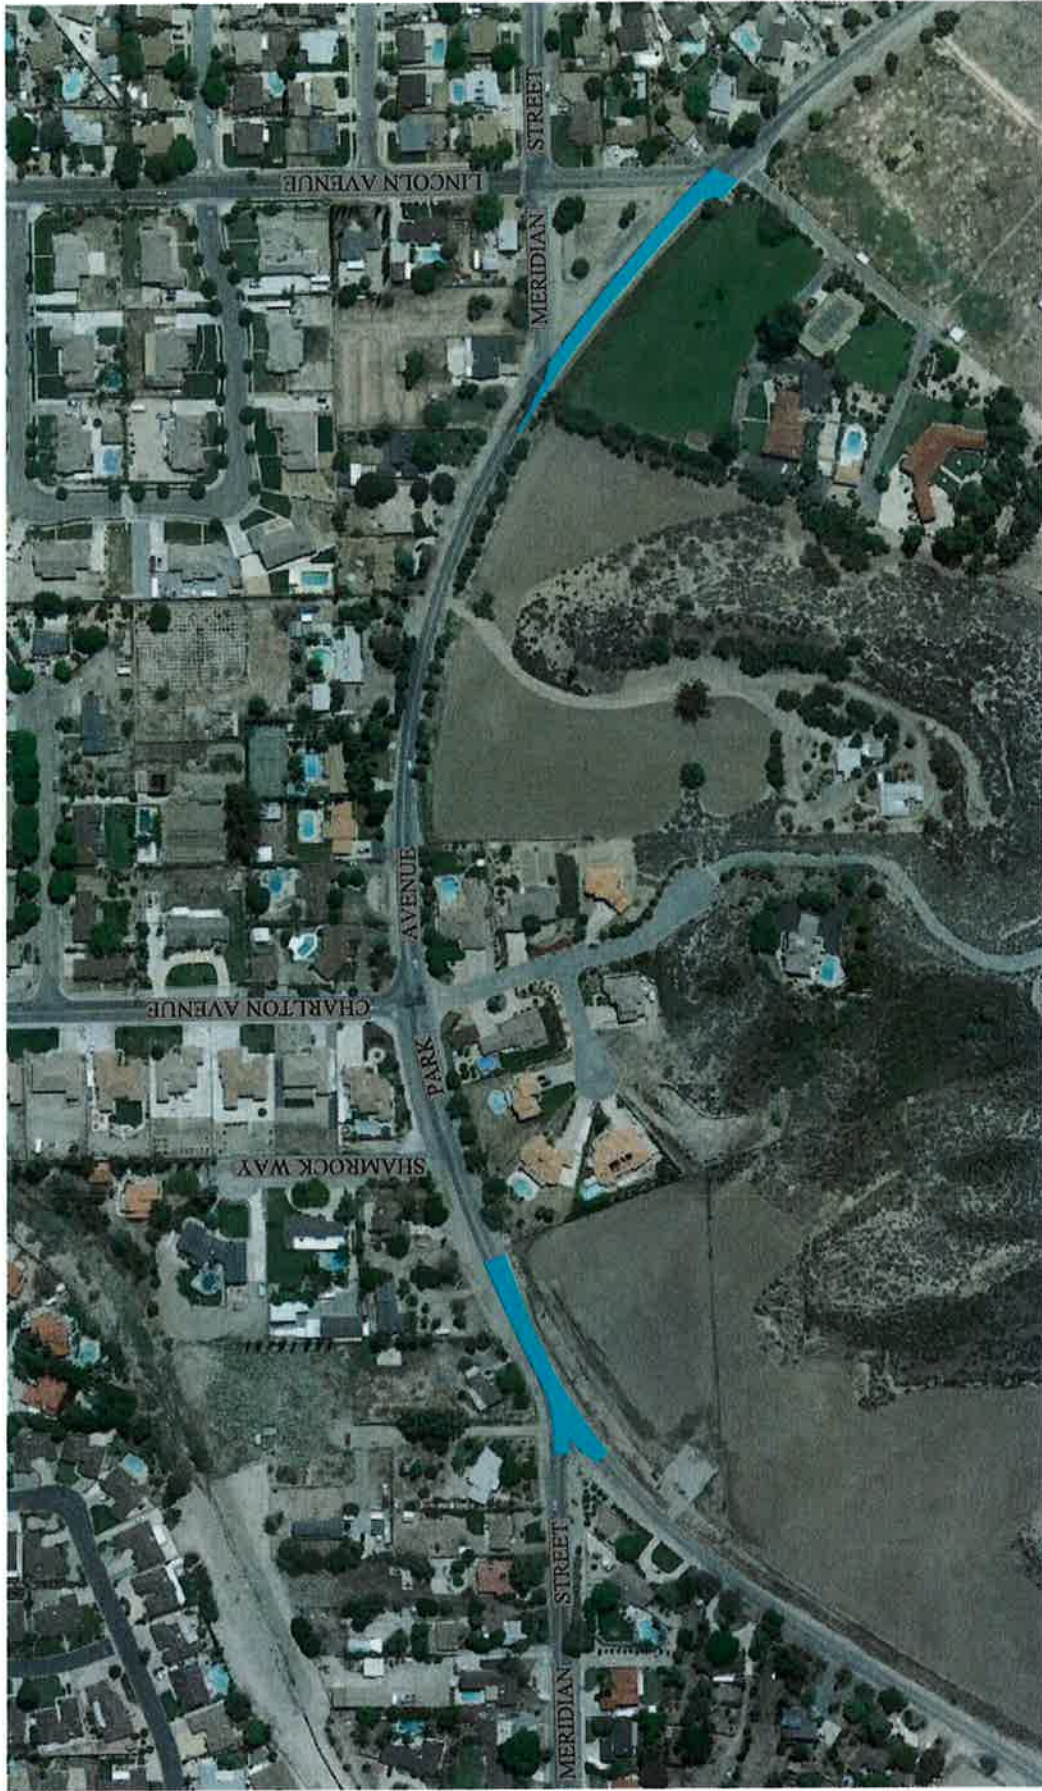

ADDITIONAL PAVING LIMITS



REV.	DATE	DESCRIPTION	DESIGNED BY:	RECOMMENDED FOR APPROVAL BY:	APPROVED BY:
			A. DONOHOO		
			DATE: MARCH, OCTOBER, 2015	DATE:	DATE:

RIVERBEND COUNTY FLOOD CONTROL
 WATER CONSERVATION DISTRICT
LITTLE LAKE MDP
LINE B
STAGE 1
 ADDITIONAL PAVING LIMITS

PROJECT NO.
4-0-0265
 DRAWING NO.
 SHEET NO.
1 OF **1**
