

**SUBMITTAL TO THE BOARD OF SUPERVISORS
COUNTY OF RIVERSIDE, STATE OF CALIFORNIA**



**ITEM: 3.32
(ID # 27295)**

MEETING DATE:
Tuesday, April 15, 2025

FROM : TLMA-TRANSPORTATION

SUBJECT: TRANSPORTATION AND LAND MANAGEMENT AGENCY/TRANSPORTATION:
Approve Contract Change Order No. 11 – Between the County of Riverside and Skanska USA Civil West California District, Inc. for the Construction of the Gilman Springs Road Phase 6 Safety Project, District 5. [\$75,000 Total Cost – State Funds 100%]

RECOMMENDED MOTION: That the Board of Supervisors:

1. Approve Contract Change Order No. 11 with Skanska USA Civil West California District, Inc. on the Gilman Springs Road Phase 6 Safety Project, and authorize the Chair of the Board to execute the same; and
2. Authorize the Transportation Department to issue Contract Change Order No. 11 with Skanska USA Civil West California District, Inc. on the Gilman Springs Road Phase 6 Safety Project.


ACTION:Policy


Dennis Acuna, Director of Transportation 3/17/2025

MINUTES OF THE BOARD OF SUPERVISORS

On motion of Supervisor Spiegel, seconded by Supervisor Gutierrez and duly carried by unanimous vote, IT WAS ORDERED that the above matter is approved as recommended.

Ayes: Medina, Spiegel, Washington, Perez and Gutierrez
Nays: None
Absent: None
Date: April 15, 2025
xc: Transp.

Kimberly A. Rector
Clerk of the Board
By: 
Deputy

**SUBMITTAL TO THE BOARD OF SUPERVISORS COUNTY OF RIVERSIDE,
STATE OF CALIFORNIA**

FINANCIAL DATA	Current Fiscal Year:	Next Fiscal Year:	Total Cost:	Ongoing Cost
COST	\$ 75,000	\$ 0	\$ 75,000	\$ 0
NET COUNTY COST	\$ 0	\$ 0	\$ 0	\$ 0
SOURCE OF FUNDS: HSIP (82%), Gas Tax/HUTA (18%). There are no General Funds used in this project.			Budget Adjustment:	No
			For Fiscal Year:	24/25

C.E.O. RECOMMENDATION: Approve

BACKGROUND:

Summary

By Minute Order 3.33 of July 9, 2024, the Board of Supervisors entered into a contract with Skanska USA Civil West California District to construct the Gilman Springs Road Phase 6 Safety Project in the Eastern Moreno Valley and Gilman Hot Springs areas of the County of Riverside.

The original authorized amount of the contract was \$20,203,423. The total amount of Contract Change Order No. 11 exceeds the cumulative change order amounts that can be authorized by the Director of Transportation. Therefore, this change order requires approval from the Board of Supervisors in accordance with Resolution No. 2019-035:

Details of the Contract Change Order is as follows:

- Contract Change Order No. 11 is \$75,000.00 (0.37% of the original contract amount)

Contract Change Order No. 11 provides compensation to the contractor for the installation of 12 concrete end blocks (Caltrans Type 60). This change order was necessary to protect proposed drainage system headwalls and to properly transition the proposed Midwest Guardrail Systems.

In addition to this Contract Change Order, the Transportation Department has issued 10 Contract Change Orders to date totaling \$1,987,412.87 (9.84% of the original contract amount). For more details, please refer to the change order report listing previously approved contract change orders.

Project No. C2-0161
Federal Aid No. HSIPL-5956(263)

Impact on Residents and Businesses

The project will provide the public with a smooth paved roadway surface, refuge area for vehicles that need to pull off the roadway and passing lane improvements that will enhance the overall safety and efficiency of vehicular traffic.

SUBMITTAL TO THE BOARD OF SUPERVISORS COUNTY OF RIVERSIDE,
STATE OF CALIFORNIA

Additional Fiscal Information


Contract Change Order No. 11 brings the total current authorized contract change order amount to \$2,062,412.87, which is 10.21% over the originally authorized contract amount of \$20,203,423.00.

ATTACHMENTS:

Vicinity Map

CCO No. 11

Change Order Report



Jason Farin, Principal Policy Analyst 4/10/2025



Aaron Gettis, Chief of Deputy County Counsel 4/1/2025

LETTER OF TRANSMITTAL

**Local Agency: County of Riverside
Transportation Department**

DATE: March 27, 2025

**File: Gilman Springs Road Phase 6
Safety Project**

W.O. No.: C2-0161

Local-Federal Aid No.: HSIPL-5956 (263)

C.C.O.: 11

TO: Dennis Acuna

From: John Ashlock

\$75,000.00 (0.37% of the original contract amount of \$20,203,423.00)

This Contract Change Order provides for:

This contract change order provides compensation to the contractor for the installation of 12 concrete end blocks (Caltrans Type 60).

Reason for Change:

This change order was necessary to protect proposed drainage system headwalls and to properly transition the proposed Midwest Guardrail Systems.

Payment:

This work will be paid on a force account basis as outlined in Section 9-1.04, "Force Account," of the contract Standard Specifications since the scope of work can't be exactly quantified.

The amount of this Contract Change Order is \$75,000.00. The cumulation of all Contract Change Orders thus far, including this one, is \$2,062,412.87.

Previous Contract Change Order Amounts Approved: \$1,987,412.87

See C.C.O. History (attached)

File: Gilman Springs Road Phase 6 Safety Project

W.O. No.: C2-0161

Local-Federal No.: HSIPL-5956 (263)

C.C.O. No.: 11

Page 2

This Contract Change Order was discussed with County Staff and they gave their concurrence to this change.

Adjustment of Time: 0 working days

ESTIMATE OF COST

Items	\$0.00
Force Account	\$75,000.00
Agreed Price	\$0.00
Adjustment	\$0.00

TOTAL \$75,000.00



John Ashlock

Engineering Division Manager

CCO Category		
AFA	Anticipated Force Account	
CFC	Changed Field Condition	
CME	Contract Management Error	
DO	Design Omission	√
OAM	Outside Agency Mandate	
RWO	Right-of-Way Obligation	
SE	Survey Error	
UB	Upgrade/Betterment	
UI	Utility Interference	



COUNTY OF RIVERSIDE
TRANSPORTATION DEPARTMENT

SHEET 1 OF 1 SHEETS

Contract Change Order No. 11

CONTRACT: Gilman Springs Road Phase 6 Safety Project

WORK ORDER NO. C2-0161
CALTRANS EA NO. N/A
LOCAL-FED AID NO. HSIPL-5956 (263)
STATE-FED AID NO. N/A

TO: SKANSKA USA CIVIL WEST CALIFORNIA DISTRICT INC. CONTRACTOR: YOU ARE HEREBY DIRECTED TO MAKE THE HEREIN DESCRIBED CHANGES FROM THE PLANS AND SPECIFICATIONS OR DO THE FOLLOWING DESCRIBED WORK NOT INCLUDED IN THE PLANS AND SPECIFICATIONS ON THIS CONTRACT.

Description of work to be done, estimate of quantities and prices to be paid. Segregated between additional work at contract price, agreed price and force account. Unless otherwise stated, rates for rental of equipment cover only such time as equipment is actually used and no allowance will be made for idle time.

Estimate of Extra Work at Force Account:

As directed by the Engineer and in accordance with Section 9-1.04, "Force Account," of the Standard Specifications, compensate the contractor for the additional costs to be incurred for the construction of 12 (each) concrete End Blocks (Type 60) per Caltrans Standards.

Total Estimate of Extra Work at Force Account \$75,000.00

As determined by the Engineer, provide all additional labor, materials, equipment, tools and incidentals to complete the Construction of End Blocks. All work shall be performed in accordance with the Standard Specifications and contract documents.

Estimated Cost: Decrease \$0.00 Increase \$75,000.00

Participating: Yes: No: N/A:

WE, the undersigned contractor, have given careful consideration to the change proposed and hereby agree that we will provide all equipment, furnish all materials, except as may otherwise be noted above, and perform all services necessary for the work above specified, and will accept as full payment therefor the prices shown above. By reason of this proposed change 0 days adjustment of time will be allowed.

Approval Recommended John Ashlock, Engineering Division Manager 2/27/25 Date

Approved Dennis Acuna, Director of Transportation 2/27/2025 Date

Accepted [Signature] 2/19/2025 Contractor Date

ATTEST: KIMBERLY A. RECTOR, Clerk

By [Signature] DEPUTY

Approved V. MANUEL PEREZ APR 15 2025 Date
Chairman, Riverside County Board of Supervisors

FORM 77 COUNTY COUNSEL

CANIELLE D. WALAND

Gilman Springs Road Phase 6 Safety Project
 Contract CCO History

Contract No. 24-05-004
 Work Order No. C2-0161
 Contract Amount \$20,203,423.00

Single Maximum CCO \$210,000.00
 Maximum CCO's \$2,020,342.30


CCO Category Legend	
AFA	Anticipated Force Account
CFC	Changed Field Condition
CME	Contract Management Error
DO	Design Omission
OAM	Outside Agency Mandate
RWO	Right-of-Way Obligation
SE	Survey Error
UB	Upgrade/Betterment
UI	Utility Interference

CCO No.	Amount This CCO	Authority	Cumulative CCO's	% Original Authorized	Cumulative CCO %	CCO Category	Classification
1	\$0.00	Director		0.00%	0.00%	UB	Unavoidable
3	\$30,000.00	Director	\$30,000.00	0.15%	0.15%	AFA	Unavoidable
4	\$25,000.00	Director	\$55,000.00	0.12%	0.27%	AFA	Unavoidable
2	-\$163,822.30	Director	-\$108,822.30	-0.81%	-0.54%	UB	Unavoidable
5	-\$84,379.98	Director	-\$193,202.28	-0.42%	-0.96%	UB	Unavoidable
6	\$1,865,834.00	Board	\$1,672,631.72	9.24%	8.28%	UB	Unavoidable
8	\$163,138.80	Director	\$1,835,770.52	0.81%	9.09%	DO	Unavoidable
7	\$90,922.35	Director	\$1,926,692.87	0.45%	9.54%	UB	Unavoidable
10	\$60,720.00	Director	\$1,987,412.87	0.30%	9.84%	CFC	Unavoidable
11	\$75,000.00	Board	\$2,062,412.87	0.37%	10.21%	DO	Unavoidable
					10.21%		

New Authorized Contract Total	\$22,265,835.87
Total CCO Dollars To Date	\$2,062,412.87
Total % Increased by CCO's	10.21%

**COUNTY OF RIVERSIDE
TRANSPORTATION DEPARTMENT**

**GILMAN SPRINGS ROAD PHASE 6 SAFETY PROJECT
FROM 8,920 FEET S/O ALESSANDRO BOULEVARD TO 5,340 FEET S/O BRIDGE STREET
EASTERN MORENO VALLEY AND GILMAN HOT SPRINGS AREAS
PROJECT No. C2-0161
FEDERAL AID No. HSIPL-5956 (263)**

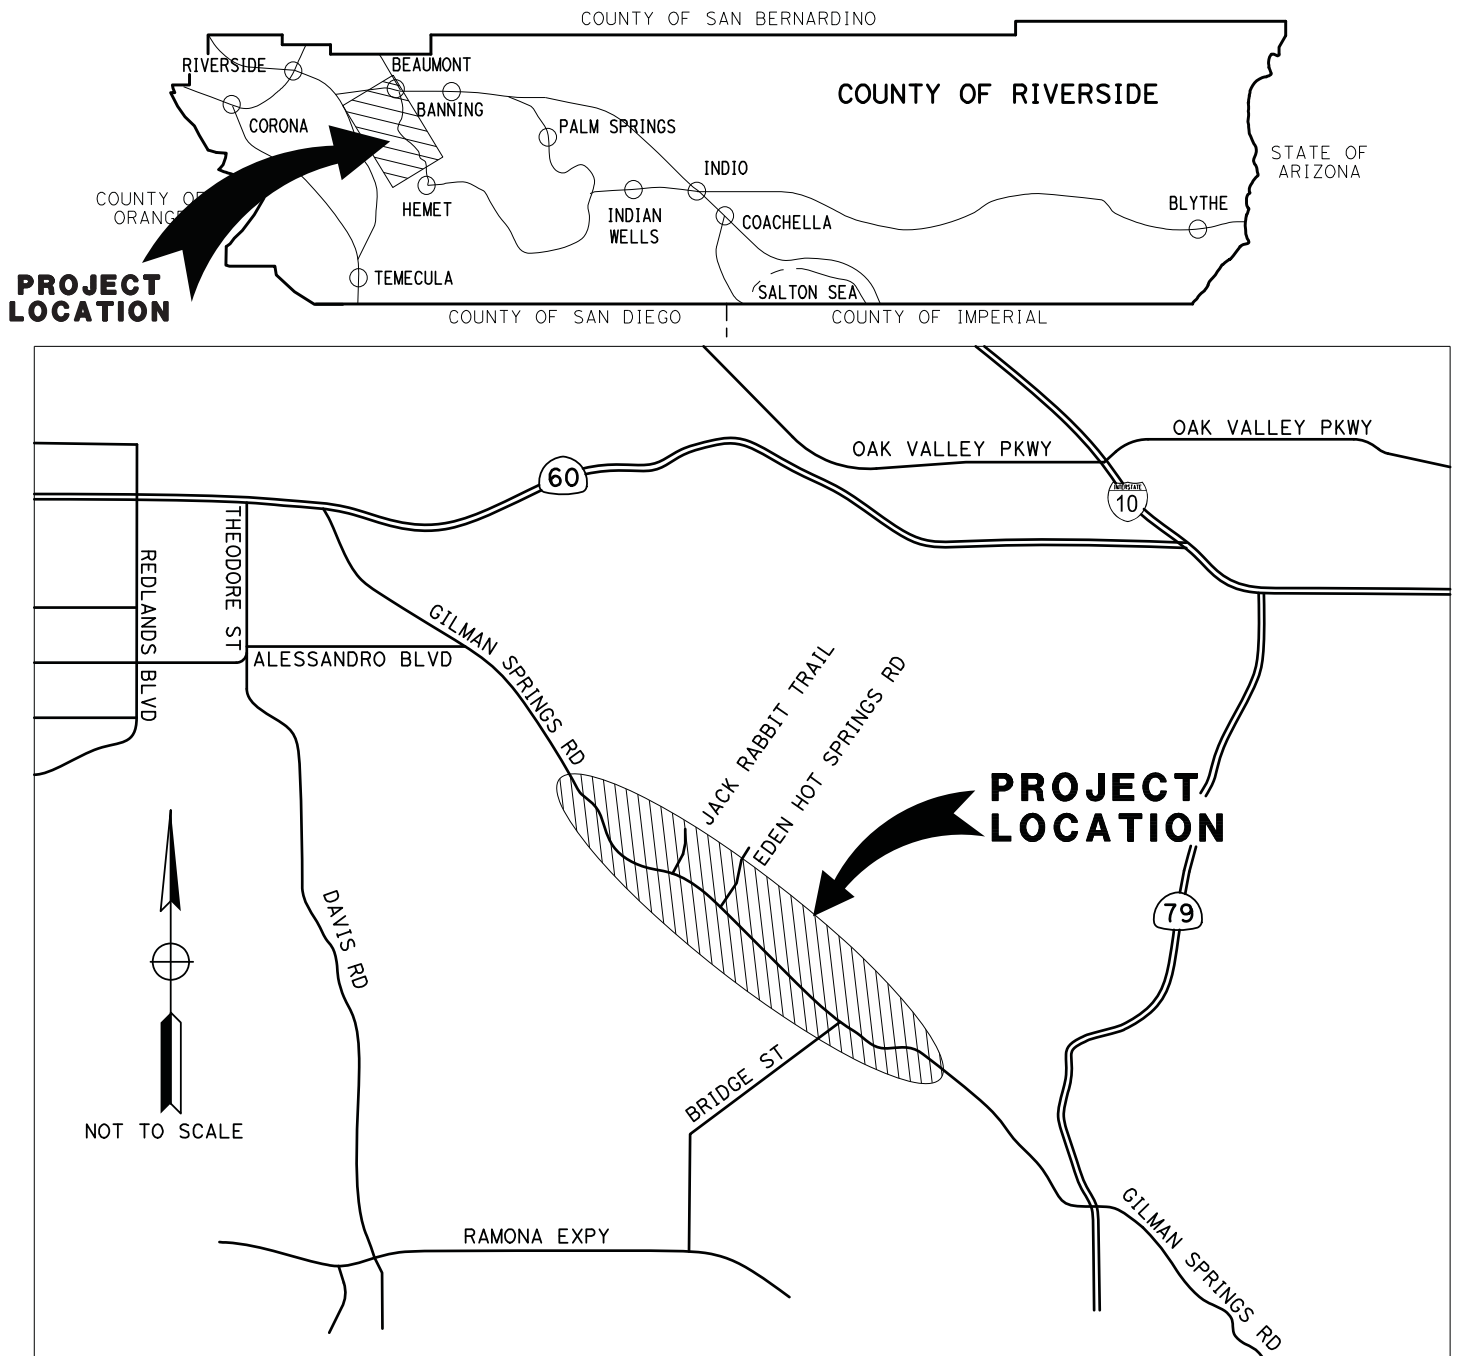

VICINITY MAP

CHANGE ORDER REPORT
(Gilman Springs Road Phase 6 Safety Project)

CCO #	Amount	Percent	Description
	Original Contract Amount \$20,203,423		
1	\$0.00	0%	Legal Holiday modification
3	\$30,000.00	0.15%	Traffic control services
4	\$25,000.00	0.12%	Clean existing storm drain systems
2	-\$163,822.30	-0.81%	Using geotextile as an overall structural section resulting in cost savings.
5	-\$84,379.98	-0.42%	Extending the roadway closure to enhance roadway safety per Valued Engineering Cost Proposal.
6	\$1,865,834.00	9.24%	Planned future safety improvements
8	\$163,138.80	0.81%	Installing hydroseed within the project limits
7	\$90,922.35	0.45%	Modify the existing left turn pocket on Ramona Expwy towards Bridge Street
10	\$60,720.00	0.30%	Installation of 23 additional overside drains
11	\$75,000.00	0.37%	Installation of 12 concrete end blocks (Caltrans Type 60)
Total Change Orders	\$2,062,412.87	10.21%	
Revised Contract Amount	\$22,265,835.87		
