

**SUBMITTAL TO THE BOARD OF SUPERVISORS
COUNTY OF RIVERSIDE, STATE OF CALIFORNIA**

722A



SUBMITTAL DATE:
January 7, 2008

FROM: TLMA - Transportation Dept.

SUBJECT: Construction of Scott Road, 500 Feet East of Antelope Road to 900 Feet East of El Centro Lane, Menifee area

RECOMMENDED MOTION: That the Board accept the low bid of All American Asphalt of Corona, CA in the amount of \$4,925,850. Award the contract to that firm and authorize the Chairman of the Board to execute the contract documents. Amend the Transportation Improvement Program's project budget as proposed on Attachment "A".

BACKGROUND: By Minute Order dated October 2, 2007 (agenda item 3.71) the Board authorized the Clerk of the Board to advertise for the construction of roadway widening, reconstruction and traffic signals on Scott Road, from 500 feet east of Antelope Road to 900 feet east of El Centro Lane in the Menifee area of Riverside County. Bids for the project were opened in the office of the Director of Transportation at 2:00 PM, Wednesday, October 31, 2007. Nine bids were received. The lowest and best bid was submitted by All American Asphalt in the amount of \$4,925,850. The bid is \$1,693,638 (25.6%) less than the Engineer's Estimate.

*Just C. Perez
Deputy Director*

George A. Johnson
Director of Transportation

GAJ:sd
(Continued On Attached Page)

| | | | | |
|-----------------------|--------------------------------------|--------------|--------------------------------|-----------|
| FINANCIAL DATA | Current F.Y. Total Cost: | \$ 4,925,850 | In Current Year Budget: | Yes |
| | Current F.Y. Net County Cost: | \$ 0 | Budget Adjustment: | No |
| | Annual Net County Cost: | \$ 0 | For Fiscal Year: | 2007/2008 |

| | | |
|--|---|--------------------------|
| SOURCE OF FUNDS: Scott Road R&BBD (34.4%), CFD 05-8 (62.6%), EMWD (.2%), Developer Contribution (1.7%), Western Traffic Signal DIF (\$96,000, 1.0%) | Positions To Be Deleted Per A-30 | <input type="checkbox"/> |
| | Requires 4/5 Vote | <input type="checkbox"/> |

C.E.O. RECOMMENDATION:

APPROVE

BY: *Tina Grande*
Tina Grande

County Executive Office Signature

FORM APPROVED COUNTY COUNSEL
BY: *MSY/KLW*
MARSHAL L. VICTOR
DATE: *01/08/08*
Departmental Concurrence

Dept't Recomm.: Consent Policy Policy
Per Exec. Ofc.: Consent Policy

Prev. Agn. Ref. 10/2/07 (3.71) | District: 3 | Agenda Number:

3.57

The Honorable Board of Supervisors

RE: Construction of Scott Road, 500 Feet East of Antelope Road to 900 Feet East of El Centro Lane, Menifee area

December 27, 2007

Page 2 of 2

The project provides for the construction of roadway widening to provide for four lanes of traffic on Scott Road within the project limits. A separate project is planned for Scott Road which will provide for 6 lanes of traffic from Antelope Road to State Route 79.

The scope of this interim project includes the widening of Scott Road, installation of four through lanes of traffic, road profile improvements to provide improved sight distance, and the following traffic signal improvements:

1. Scott Road and Lindenberger Road (Modification)
2. Scott Road and Brighton Wood Street / Revival Driveway (New)
3. Scott Road and Briggs Road (New)
4. Scott Road and Menifee Road (New)

The three new traffic signal locations meet warrants for the construction of a traffic signal, which will provide protected traffic movements and improve traffic safety.

Annual traffic signal operation and maintenance costs are estimated at \$4,500 for each location, to be funded from gas tax.

The adjustment to grade and relocation of utilities owned by Eastern Municipal Water District (EMWD) was included in the bid package as an alternate bid schedule. EMWD has approved the award of the alternate bid schedule as bid by the apparent low bidder, and the costs for the work will be funded by the EMWD.

The Contractor has executed the contract and has provided bonds and insurance certificate documents which meet the requirements of the contract. The contractor is qualified.

Project Nos. A5-0256 and B7-0706.

Attachment "A"

Riverside County Transportation Department

Project: **Scott Road and Scott Road/Brighton Wood Signal Improvements**

Project No.(s): **A50256 and B70706**

Expenses as of: 11/26/07

Project Costs and Budget

| Activity | Incurred Costs | Projected Costs | Total Costs | Existing Budget | Proposed Budget |
|---------------------------------------|------------------|------------------|------------------|-------------------|------------------|
| Preliminary Survey | 262,598 | 0 | 262,598 | 324,000 | 263,000 |
| Environmental | 347,839 | 20,000 | 367,839 | 343,000 | 368,000 |
| Design | 1,739,985 | 150,000 | 1,889,985 | 1,648,000 | 1,890,000 |
| Right-of-way | 9,715 | 2,000 | 11,715 | 9,000 | 12,000 |
| Utilities | 163,475 | 10,000 | 173,475 | 176,000 | 264,000 |
| Construction | 1,228 | 4,925,850 | 4,927,078 | 7,530,000 | 5,657,000 |
| Construction Contingency 10% - 15% | | 729,953 | 729,953 | | |
| Construction Engineering & Inspection | 23,743 | 648,000 | 671,743 | 628,000 | 672,000 |
| Construction Survey | 12,808 | 442,000 | 454,808 | 463,000 | 455,000 |
| Totals: | 2,561,391 | 6,927,803 | 9,489,193 | 11,121,000 | 9,581,000 |

Project Funding

| Code | Name | Existing Budget | Proposed Budget |
|---------------|---|-------------------|------------------|
| 215 | Proposition 1B (State Bond Funds) | 1,000,000 | |
| 343 | TUMF - Identified/Unfunded | 3,500,000 | |
| 433 | Scott Road & Bridge Benefit District | 3,665,000 | 2,528,000 |
| 469 | CFD 05-8 Scott Road | 8,000 | 6,000,000 |
| 839 | EMWD | | 19,000 |
| 602 | Developer Cash-in-Lieu | | 131,000 |
| 369 | West Traffic Signal DIF | 166,000 | 131,000 |
| 433 | Scott Road & Bridge Benefit District (center 2 lanes) | | 772,000 |
| 999 | Unfunded | 2,777,000 | |
| Totals | | 11,116,000 | 9,581,000 |

Comments

Attachment "A"

Riverside County Transportation Department

Project: **Scott Rd Widening Project**

Project No.(s): **A50256**

Expenses as of: 11/26/07

Project Costs and Budget

| Activity | Inurred Costs | Projected Costs | Total Costs | Existing Budget | Proposed Budget |
|---------------------------------------|------------------|------------------|------------------|-------------------|------------------|
| Preliminary Survey | 262,598 | 0 | 262,598 | 324,000 | 263,000 |
| Environmental | 347,839 | 20,000 | 367,839 | 343,000 | 368,000 |
| Design | 1,734,844 | 150,000 | 1,884,844 | 1,623,000 | 1,885,000 |
| Right-of-way | 9,715 | 2,000 | 11,715 | 9,000 | 12,000 |
| Utilities | 161,256 | 100,000 | 261,256 | 171,000 | 261,000 |
| Construction | | 4,747,350 | 4,747,350 | 7,280,000 | 5,459,000 |
| Construction Contingency 15.0% | | 712,103 | 712,103 | | |
| Construction Engineering & Inspection | 23,743 | 610,000 | 633,743 | 590,000 | 634,000 |
| Construction Survey | 7,814 | 429,000 | 436,814 | 445,000 | 437,000 |
| Totals: | 2,547,809 | 6,770,453 | 9,318,262 | 10,785,000 | 9,319,000 |

Project Funding

| Code | Name | Existing Budget | Proposed Budget |
|---------------|---|-------------------|------------------|
| 215 | Proposition 1B (State Bond Funds) | 1,000,000 | |
| 343 | TUMF - Identified/Unfunded | 3,500,000 | |
| 433 | Scott Road & Bridge Benefit District | 3,665,000 | 2,528,000 |
| 469 | CFD 05-8 Scott Road | 8,000 | 6,000,000 |
| 839 | EMWD | | 19,000 |
| 602 | Developer Cash-in-Lieu | | |
| 369 | West Traffic Signal DIF | | |
| 433 | Scott Road & Bridge Benefit District (center 2 lanes) | | 772,000 |
| 999 | Unfunded | 2,612,000 | |
| Totals | | 10,785,000 | 9,319,000 |

Comments

Attachment "A"

Riverside County Transportation Department

Project: **Scott Road/Brighton Wood Signal Improvements**

Project No.(s): **B70706**

Expenses as of: 11/26/07

Project Costs and Budget

| Activity | Incurring Costs | Projected Costs | Total Costs | Existing Budget | Proposed Budget |
|---------------------------------------|-----------------|-----------------|----------------|-----------------|-----------------|
| Preliminary Survey | | 0 | 0 | | 0 |
| Environmental | 0 | 0 | 0 | 1,000 | 0 |
| Design | 5,141 | | 5,141 | 25,000 | 5,000 |
| Right-of-way | 0 | 0 | 0 | | 0 |
| Utilities | 2,218 | 1,000 | 3,218 | 5,000 | 3,000 |
| Construction | 1,228 | 178,500 | 179,728 | | |
| Construction Contingency 10.0% | | 17,850 | 17,850 | 250,000 | 198,000 |
| Construction Engineering & Inspection | 0 | 38,000 | 38,000 | 38,000 | 38,000 |
| Construction Survey | 4,994 | 13,000 | 17,994 | 12,000 | 18,000 |
| Totals: | 13,582 | 248,350 | 261,932 | 331,000 | 262,000 |

Project Funding



| Code | Name | Existing Budget | Proposed Budget |
|---------------|---|-----------------|-----------------|
| 215 | Proposition 1B (State Bond Funds) | | |
| 343 | TUMF - Identified/Unfunded | | |
| 433 | Scott Road & Bridge Benefit District | | |
| 469 | CFD 05-8 Scott Road | | |
| 839 | EMWD | | |
| 602 | Developer Cash-in-Lieu | | 131,000 |
| 369 | West Traffic Signal DIF | 166,000 | 131,000 |
| 433 | Scott Road & Bridge Benefit District (center 2 lanes) | | |
| 999 | Unfunded | 165,000 | |
| Totals | | 331,000 | 262,000 |

Comments

COUNTY OF RIVERSIDE

SCOTT ROAD

FROM ANTELOPE ROAD TO
EL CENTRO LANE

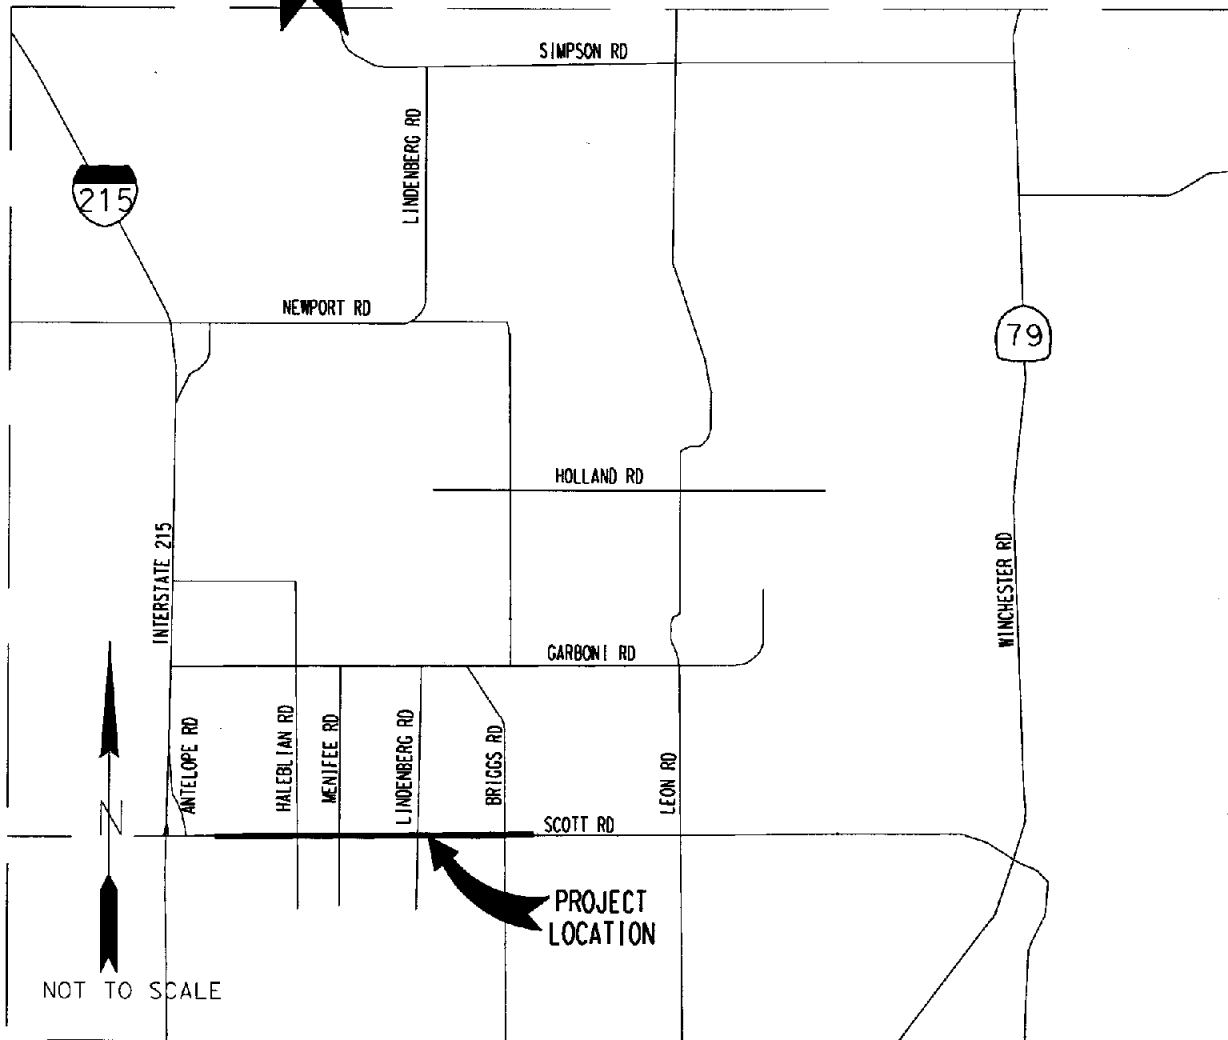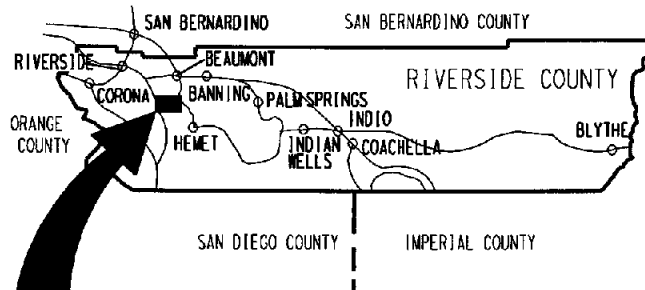

PROJECT LENGTH = 2.15 MILES
TOWNSHIP 6S RANGE 2W SECTION 14/23, 17
VICINITY MAP

**Riverside County Transportation Department
Summary of Bids**

PROJECT: Scott Road - Antelope Road to El Centro Lane

**Advertised: October 2, 2007 (Agenda Item 3.71)
Bids Open: 2:00 pm Date: October 31, 2007**

PROJECT NO. A5-0256

| Base Bid | | COUNTRY'S ESTIMATE | | | | ALL AMERICAN ASPHALT Corona, CA 92878 | | |
|----------|-----------|--|-------|----------|------------|--|------------|--------------|
| ITEM NO. | ITEM CODE | CONTRACT ITEM | UNITS | QUANTITY | UNIT PRICE | ENG ESTIMATE | BID | AMOUNT |
| 1 | 800701 | WOOD FENCE | LF | 40 | 25.00 | 1,000.00 | 69.00 | 2,760.00 |
| 2 | 011506 | WEDGE PLANE ASPHALT CONCRETE | LF | 7,000 | 2.75 | 19,250.00 | 2.65 | 18,550.00 |
| 3 | 013904 | PLACE ASPHALT CONCRETE DIKE (CRS 212) (8") | LF | 870 | 7.00 | 6,090.00 | 9.25 | 8,047.50 |
| 4 | 017302 | MINOR CONCRETE (CROSS-GUTTER) (CRS 209) | SQFT | 3,900 | 20.00 | 78,000.00 | 8.65 | 33,735.00 |
| 5 | 017305 | MINOR CONCRETE (CURB AND GUTTER) (CRS 201) | LF | 1,600 | 20.00 | 32,000.00 | 18.75 | 30,000.00 |
| 6 | 017315 | MINOR CONCRETE (CURB RAMP) (CRS 403-CASE A) | EA | 8 | 3,000.00 | 24,000.00 | 2,400.00 | 19,200.00 |
| 7 | 017316 | MINOR CONCRETE (CURB RAMP) (CRS 403-CASE B) | EA | 4 | 3,000.00 | 12,000.00 | 2,400.00 | 9,600.00 |
| 8 | 066102 | DUST ABATEMENT | LS | 1 | 3,000.00 | 3,000.00 | 4,400.00 | 4,400.00 |
| 9 | 074020 | WATER POLLUTION CONTROL | LS | 1 | 20,000.00 | 20,000.00 | 30,000.00 | 30,000.00 |
| 10 | 120100 | TRAFFIC CONTROL SYSTEM | LS | 1 | 300,000.00 | 300,000.00 | 80,000.00 | 80,000.00 |
| 11 | 160101 | CLEARING AND GRUBBING | LS | 1 | 20,000.00 | 20,000.00 | 20,000.00 | 20,000.00 |
| 12 | 170101 | DEVELOP WATER SUPPLY | LS | 1 | 10,000.00 | 10,000.00 | 3,800.00 | 3,800.00 |
| 13 | 190101 | ROADWAY EXCAVATION | CY | 78,400 | 20.00 | 1,568,000.00 | 9.60 | 752,640.00 |
| 14 | 220101 | FINISHING ROADWAY | LS | 1 | 15,000.00 | 15,000.00 | 7,900.00 | 7,900.00 |
| 15 | 260201 | CLASS 2 AGGREGATE BASE | CY | 26,900 | 25.00 | 672,500.00 | 21.25 | 571,625.00 |
| 16 | 360155 | ASPHALT CONCRETE (TYPE A) | TON | 17,900 | 75.00 | 1,342,500.00 | 66.00 | 1,181,400.00 |
| 17 | 013901 | ASPHALT RUBBER HOT MIX | TON | 10,000 | 90.00 | 900,000.00 | 81.25 | 812,500.00 |
| 18 | 510501 | MINOR CONCRETE (OVERSIDE DRAIN) | CY | 1 | 1,000.00 | 1,000.00 | 1,200.00 | 1,200.00 |
| 19 | 566011 | ROADSIDE SIGN - ONE POST | EA | 32 | 250.00 | 8,000.00 | 301.00 | 9,632.00 |
| 20 | 650014 | 18" REINFORCED CONCRETE PIPE | LF | 50 | 200.00 | 10,000.00 | 124.00 | 6,200.00 |
| 21 | 650420 | 30" REINFORCED CONCRETE PIPE (CLASS IV) | LF | 12 | 400.00 | 4,800.00 | 540.00 | 6,480.00 |
| 22 | 665017 | 18" CORRUGATED STEEL PIPE (0.079" THICK) | LF | 21 | 140.00 | 2,940.00 | 284.00 | 5,964.00 |
| 23 | 731521 | MINOR CONCRETE (SIDEWALK) | SQFT | 2,510 | 6.00 | 15,060.00 | 4.15 | 10,416.50 |
| 24 | 800360 | CHAIN LINK FENCE (TYPE CL-6) | LF | 170 | 25.00 | 4,250.00 | 42.00 | 7,140.00 |
| 25 | 840656 | PAINT TRAFFIC STRIPE (2-COAT) | LF | 83,500 | 0.50 | 41,750.00 | 0.19 | 15,865.00 |
| 26 | 840506 | 8" THERMOPLASTIC TRAFFIC STRIPE | LF | 5,600 | 2.00 | 11,200.00 | 0.50 | 2,800.00 |
| 27 | 850102 | PAVEMENT MARKER (REFLECTIVE) | EA | 1,800 | 5.00 | 9,000.00 | 2.65 | 4,770.00 |
| 28 | 840519 | THERMOPLASTIC CROSSWALK AND PAVEMENT MARKING | SQFT | 6,700 | 6.00 | 40,200.00 | 2.29 | 15,343.00 |
| 29 | 860301 | SIGNAL AND LIGHTING (MENIFEE ROAD AND SCOTT ROAD) | LS | 1 | 200,000.00 | 200,000.00 | 173,394.00 | 173,394.00 |
| 30 | 860301 | SIGNAL AND LIGHTING (BRIGGS ROAD AND SCOTT ROAD) | LS | 1 | 200,000.00 | 200,000.00 | 153,400.00 | 153,400.00 |
| 31 | 861502 | MODIFY SIGNAL (LINDENBERGER ROAD AND SCOTT ROAD) | LS | 1 | 150,000.00 | 150,000.00 | 87,000.00 | 87,000.00 |
| 32 | 860301 | SIGNAL AND LIGHTING (BRIGHTON WOOD STREET/REVIVAL DRIVEWAY AND SCOTT ROAD) | LS | 1 | 200,000.00 | 200,000.00 | 178,500.00 | 178,500.00 |
| 33 | 510060 | STRUCTURAL CONCRETE, RETAINING WALL | CY | 400 | 1,075.00 | 430,000.00 | 1,165.00 | 466,000.00 |
| 34 | 510545 | MINOR CONCRETE (HEADWALL) | CY | 3 | 2,300.00 | 6,900.00 | 2,800.00 | 8,400.00 |
| 35 | 066003 | INSTALL ENVIRONMENTALLY SENSITIVE AREA (ESA) FENCING | LF | 1,220 | 9.50 | 11,590.00 | 3.10 | 3,782.00 |
| 36 | 820130 | OBJECT MARKER (TYPE L-1) | EA | 4 | 50.00 | 200.00 | 36.50 | 146.00 |

**Riverside County Transportation Department
Summary of Bids**

PROJECT: Scott Road - Antelope Road to El Centro Lane

**Advertised: October 2, 2007 (Agenda Item 3.71)
Bids Open: 2:00 pm Date: October 31, 2007**

PROJECT NO. A5-0256

| Base Bid | | COUNTY'S ESTIMATE | | | | ALL AMERICAN ASPHALT Corona, CA 92878 | |
|----------------------------|-----------|---|-------|----------|------------|--|---------------------|
| ITEM NO. | ITEM CODE | CONTRACT ITEM | UNITS | QUANTITY | UNIT PRICE | ENG ESTIMATE | AMOUNT |
| 37 | 394002 | PLACE ASPHALT CONCRETE (MISCELLANEOUS AREA) | SQFT | 129 | 2.00 | 258.00 | 35.00 |
| 38 | 066105 | RESIDENT ENGINEERS OFFICE | LS | 1 | 25,000.00 | 25,000.00 | 26,000.00 |
| 39 | 152440 | ADJUST MANHOLE TO GRADE [STORM DRAIN] | EA | 9 | 500.00 | 4,500.00 | 4,500.00 |
| 40 | 989890 | MOBILIZATION | LS | 1 | 200,000.00 | 200,000.00 | 126,985.00 |
| 41 | 510501 | MINOR CONCRETE (PROTECTIVE SLAB) | LF | 80 | 150.00 | 12,000.00 | 52.00 |
| SUBTOTAL (BASE BID) | | | | | | 6,611,988.00 | 4,908,750.00 |
| ITEMS 1-41 | | | | | | | |

| Alternate 1 | | COUNTY'S ESTIMATE | | | | ALL AMERICAN ASPHALT Corona, CA 92878 | |
|-------------------------------|-----------|---------------------------------|-------|----------|------------|--|------------------|
| ITEM NO. | ITEM CODE | CONTRACT ITEM | UNITS | QUANTITY | UNIT PRICE | ENG ESTIMATE | AMOUNT |
| 42 | 152440 | ADJUST MANHOLE TO GRADE [SEWER] | EA | 7 | 500.00 | 3,500.00 | 3,500.00 |
| 43 | 152351 | RELOCATE HYDRANT | EA | 2 | 2,000.00 | 4,000.00 | 6,800.00 |
| SUBTOTAL (ALTERNATE 1) | | | | | | 7,500.00 | 17,100.00 |
| ITEMS 42-43 | | | | | | | |

| PROJECT TOTAL | | | | | | ALL AMERICAN ASPHALT Corona, CA 92878 | |
|----------------------|------|----------|------------|--------------|--------|--|---------------------|
| ITEMS | 1-43 | QUANTITY | UNIT PRICE | ENG ESTIMATE | AMOUNT | AMOUNT | |
| PROJECT TOTAL | | | | | | 6,619,488.00 | 4,925,850.00 |
| ITEMS 1-43 | | | | | | | |

**Riverside County Transportation Department
Summary of Bids**

PROJECT: Scott Road - Antelope Road to El Centro Lane

Advertised: October 2, 2007 (Agenda Item 3.71)

Bids Open: 2:00 pm Date: October 31, 2007

PROJECT NO. A5-0256

| Base Bid | | SUKUT CONSTRUCTION, INC. Riverside, CA 92505 | | | | R.J. NOBLE COMPANY Orange, CA 92856 | | | |
|----------|-----------|--|-------|----------|------------|--|------------|--------------|--------|
| ITEM NO. | ITEM CODE | CONTRACT ITEM | UNITS | QUANTITY | BID | AMOUNT | BID | AMOUNT | AMOUNT |
| 1 | 800701 | WOOD FENCE | LF | 40 | 26.75 | 1,070.00 | 81.30 | 3,252.00 | |
| 2 | 011506 | WEDGE PLANE ASPHALT CONCRETE | LF | 7,000 | 1.50 | 10,500.00 | 1.30 | 9,100.00 | |
| 3 | 013904 | PLACE ASPHALT CONCRETE DIKE (CRS 212) (8") | LF | 870 | 5.35 | 4,654.50 | 7.40 | 6,438.00 | |
| 4 | 017302 | MINOR CONCRETE (CROSS-GUTTER) (CRS 209) | SQFT | 3,900 | 8.50 | 33,150.00 | 11.25 | 43,875.00 | |
| 5 | 017305 | MINOR CONCRETE (CURB AND GUTTER) (CRS 201) | LF | 1,600 | 19.25 | 30,800.00 | 24.65 | 39,440.00 | |
| 6 | 017315 | MINOR CONCRETE (CURB RAMP) (CRS 403-CASE A) | EA | 8 | 2,875.00 | 23,000.00 | 4,630.00 | 37,040.00 | |
| 7 | 017316 | MINOR CONCRETE (CURB RAMP) (CRS 403-CASE B) | EA | 4 | 3,050.00 | 12,200.00 | 4,855.00 | 19,420.00 | |
| 8 | 066102 | DUST ABATEMENT | LS | 1 | 26,085.00 | 26,085.00 | 19,500.00 | 19,500.00 | |
| 9 | 074020 | WATER POLLUTION CONTROL | LS | 1 | 31,950.00 | 31,950.00 | 12,000.00 | 12,000.00 | |
| 10 | 120100 | TRAFFIC CONTROL SYSTEM | LS | 1 | 122,300.00 | 122,300.00 | 175,000.00 | 175,000.00 | |
| 11 | 160101 | CLEARING AND GRUBBING | LS | 1 | 9,300.00 | 9,300.00 | 20,000.00 | 20,000.00 | |
| 12 | 170101 | DEVELOP WATER SUPPLY | LS | 1 | 19,745.00 | 19,745.00 | 3,300.00 | 3,300.00 | |
| 13 | 190101 | ROADWAY EXCAVATION | CY | 78,400 | 7.85 | 615,440.00 | 9.00 | 705,600.00 | |
| 14 | 220101 | FINISHING ROADWAY | LS | 1 | 33,575.00 | 33,575.00 | 57,650.00 | 57,650.00 | |
| 15 | 260201 | CLASS 2 AGGREGATE BASE | CY | 26,900 | 29.50 | 793,550.00 | 35.35 | 950,915.00 | |
| 16 | 390155 | ASPHALT CONCRETE (TYPE A) | TON | 17,900 | 76.00 | 1,360,400.00 | 59.70 | 1,068,630.00 | |
| 17 | 013901 | ASPHALT RUBBER HOT MIX | TON | 10,000 | 97.00 | 970,000.00 | 76.00 | 760,000.00 | |
| 18 | 510501 | MINOR CONCRETE (OVERSIDE DRAIN) | CY | 1 | 2,140.00 | 2,140.00 | 915.00 | 915.00 | |
| 19 | 566011 | ROADSIDE SIGN - ONE POST | EA | 32 | 310.00 | 9,920.00 | 310.00 | 9,920.00 | |
| 20 | 650014 | 18" REINFORCED CONCRETE PIPE | LF | 50 | 96.00 | 4,800.00 | 152.00 | 7,600.00 | |
| 21 | 650420 | 30" REINFORCED CONCRETE PIPE (CLASS IV) | LF | 12 | 181.00 | 2,172.00 | 252.00 | 3,024.00 | |
| 22 | 665017 | 18" CORRUGATED STEEL PIPE (0.079" THICK) | LF | 21 | 106.00 | 2,226.00 | 186.00 | 3,486.00 | |
| 23 | 731521 | MINOR CONCRETE (SIDEWALK) | SQFT | 2,510 | 6.40 | 16,064.00 | 5.10 | 12,801.00 | |
| 24 | 800360 | CHAIN LINK FENCE (TYPE CL-6) | LF | 170 | 23.50 | 3,995.00 | 27.05 | 4,598.50 | |
| 25 | 840656 | PAINT TRAFFIC STRIPE (2-COAT) | LF | 83,500 | 0.11 | 9,185.00 | 0.06 | 5,010.00 | |
| 26 | 840506 | 8" THERMOPLASTIC TRAFFIC STRIPE | LF | 5,600 | 1.07 | 5,992.00 | 1.07 | 5,992.00 | |
| 27 | 850102 | PAVEMENT MARKER (REFLECTIVE) | EA | 1,800 | 3.00 | 5,400.00 | 3.48 | 6,264.00 | |
| 28 | 840519 | THERMOPLASTIC CROSSWALK AND PAVEMENT MARKING | SQFT | 6,700 | 2.50 | 16,750.00 | 2.14 | 14,338.00 | |
| 29 | 860301 | SIGNAL AND LIGHTING [MENIFEE ROAD AND SCOTT ROAD] | LS | 1 | 160,000.00 | 160,000.00 | 168,200.00 | 168,200.00 | |
| 30 | 860301 | SIGNAL AND LIGHTING [BRIGGS ROAD AND SCOTT ROAD] | LS | 1 | 150,000.00 | 150,000.00 | 157,600.00 | 157,600.00 | |
| 31 | 861502 | MODIFY SIGNAL [LINDENBERGER ROAD AND SCOTT ROAD] | LS | 1 | 90,000.00 | 90,000.00 | 92,350.00 | 92,350.00 | |
| 32 | 860301 | SIGNAL AND LIGHTING [BRIGHTON WOOD STREET/REVIVAL DRIVEWAY AND SCOTT ROAD] | LS | 1 | 145,000.00 | 145,000.00 | 153,600.00 | 153,600.00 | |
| 33 | 510060 | STRUCTURAL CONCRETE, RETAINING WALL | CY | 400 | 718.00 | 287,200.00 | 970.00 | 388,000.00 | |
| 34 | 510545 | MINOR CONCRETE (HEADWALL) | CY | 3 | 6,300.00 | 18,900.00 | 3,265.00 | 9,795.00 | |
| 35 | 066003 | INSTALL ENVIRONMENTALLY SENSITIVE AREA (ESA) FENCING | LF | 1,220 | 6.75 | 8,235.00 | 7.50 | 9,150.00 | |
| 36 | 820130 | OBJECT MARKER [TYPE L-1] | EA | 4 | 37.50 | 150.00 | 38.00 | 152.00 | |

**Riverside County Transportation Department
Summary of Bids**

PROJECT: Scott Road - Antelope Road to El Centro Lane

**Advertised: October 2, 2007 (Agenda Item 3.71)
Bids Open: 2:00 pm Date: October 31, 2007**

PROJECT NO. A5-0256

| Base Bid | | SUKUT CONSTRUCTION, INC. Riverside, CA 92505 | | R.J. NOBLE COMPANY Orange, CA 92856 | | | | |
|----------------------------|-----------|---|-------|--|-----------|---------------------|------------|---------------------|
| ITEM NO. | ITEM CODE | CONTRACT ITEM | UNITS | QUANTITY | BID | AMOUNT | BID | AMOUNT |
| 37 | 394002 | PLACE ASPHALT CONCRETE (MISCELLANEOUS AREA) | SQFT | 129 | 10.00 | 1,290.00 | 15.50 | 1,999.50 |
| 38 | 066105 | RESIDENT ENGINEERS OFFICE | LS | 1 | 19,300.00 | 19,300.00 | 21,000.00 | 21,000.00 |
| 39 | 152440 | ADJUST MANHOLE TO GRADE (STORM DRAIN) | EA | 9 | 535.00 | 4,815.00 | 645.00 | 5,805.00 |
| 40 | 999990 | MOBILIZATION | LS | 1 | 66,500.00 | 66,500.00 | 200,000.00 | 200,000.00 |
| 41 | 510501 | MINOR CONCRETE (PROTECTIVE SLAB) | LF | 80 | 109.00 | 8,720.00 | 109.00 | 8,720.00 |
| SUBTOTAL (BASE BID) | | | | | | 5,136,473.50 | | 5,221,480.00 |
| ITEMS 1-41 | | | | | | | | |

| Alternate 1 | | SUKUT CONSTRUCTION, INC. Riverside, CA 92505 | | R.J. NOBLE COMPANY Orange, CA 92856 | | | | |
|-------------------------------|-----------|---|-------|--|----------|------------------|----------|------------------|
| ITEM NO. | ITEM CODE | CONTRACT ITEM | UNITS | QUANTITY | BID | AMOUNT | BID | AMOUNT |
| 42 | 152440 | ADJUST MANHOLE TO GRADE (SEWER) | EA | 7 | 550.00 | 3,850.00 | 645.00 | 4,515.00 |
| 43 | 152351 | RELOCATE HYDRANT | EA | 2 | 3,750.00 | 7,500.00 | 5,240.00 | 10,480.00 |
| SUBTOTAL (ALTERNATE 1) | | | | | | 11,350.00 | | 14,995.00 |
| ITEMS 42-43 | | | | | | | | |

| PROJECT TOTAL | | ITEMS 1-43 | |
|---------------|--|---------------------|---------------------|
| | | 5,147,823.50 | 5,236,475.00 |

**Riverside County Transportation Department
Summary of Bids**

PROJECT: Scott Road - Antelope Road to El Centro Lane

**Advertised: October 2, 2007 (Agenda Item 3.71)
Bids Open: 2:00 pm Date: October 31, 2007**

PROJECT NO. A5-0256

| Base Bid | | GRIFFITH COMPANY Santa Ana, CA 92704 | | BEADOR CONSTRUCTION COMPANY, INC. Corona, CA 92883 | | | | |
|----------|-----------|--|-------|--|------------|--------------|------------|--------------|
| ITEM NO. | ITEM CODE | CONTRACT ITEM | UNITS | QUANTITY | BID | AMOUNT | BID | AMOUNT |
| 1 | 800701 | WOOD FENCE | LF | 40 | 71.00 | 2,840.00 | 55.00 | 2,200.00 |
| 2 | 011508 | WEDGE PLANE ASPHALT CONCRETE | LF | 7,000 | 1.32 | 9,240.00 | 1.40 | 9,800.00 |
| 3 | 013904 | PLACE ASPHALT CONCRETE DIKE (CRS 212)(8") | LF | 870 | 1.65 | 1,435.50 | 6.30 | 5,481.00 |
| 4 | 017302 | MINOR CONCRETE (CROSS-GUTTER) (CRS 209) | SQFT | 3,900 | 10.00 | 39,000.00 | 8.50 | 33,150.00 |
| 5 | 017305 | MINOR CONCRETE (CURB AND GUTTER) (CRS 201) | LF | 1,600 | 24.00 | 38,400.00 | 21.00 | 33,600.00 |
| 6 | 017315 | MINOR CONCRETE (CURB RAMP) (CRS 403-CASE A) | EA | 8 | 5,000.00 | 40,000.00 | 5,500.00 | 44,000.00 |
| 7 | 017316 | MINOR CONCRETE (CURB RAMP) (CRS 403-CASE B) | EA | 4 | 5,200.00 | 20,800.00 | 5,500.00 | 22,000.00 |
| 8 | 066102 | DUST ABATEMENT | LS | 1 | 20,000.00 | 20,000.00 | 50,000.00 | 50,000.00 |
| 9 | 074020 | WATER POLLUTION CONTROL | LS | 1 | 35,000.00 | 35,000.00 | 50,000.00 | 50,000.00 |
| 10 | 120100 | TRAFFIC CONTROL SYSTEM | LS | 1 | 118,000.00 | 118,000.00 | 279,860.00 | 279,860.00 |
| 11 | 160101 | CLEARING AND GRUBBING | LS | 1 | 20,000.00 | 20,000.00 | 20,000.00 | 20,000.00 |
| 12 | 170101 | DEVELOP WATER SUPPLY | LS | 1 | 20,000.00 | 20,000.00 | 50,000.00 | 50,000.00 |
| 13 | 190101 | ROADWAY EXCAVATION | CY | 78,400 | 10.00 | 784,000.00 | 7.75 | 607,600.00 |
| 14 | 220101 | FINISHING ROADWAY | LS | 1 | 2.25 | 2.25 | 55,000.00 | 55,000.00 |
| 15 | 260201 | CLASS 2 AGGREGATE BASE | CY | 26,900 | 25.00 | 672,500.00 | 29.00 | 780,100.00 |
| 16 | 390155 | ASPHALT CONCRETE (TYPE A) | TON | 17,900 | 66.00 | 1,181,400.00 | 68.00 | 1,217,200.00 |
| 17 | 013901 | ASPHALT RUBBER HOT MIX | TON | 10,000 | 86.00 | 860,000.00 | 86.00 | 860,000.00 |
| 18 | 510501 | MINOR CONCRETE (OVERSIDE DRAIN) | CY | 1 | 2,000.00 | 2,000.00 | 2,750.00 | 2,750.00 |
| 19 | 566011 | ROADSIDE SIGN - ONE POST | EA | 32 | 300.00 | 9,600.00 | 250.00 | 8,000.00 |
| 20 | 650014 | 18" REINFORCED CONCRETE PIPE | LF | 50 | 200.00 | 10,000.00 | 110.00 | 5,500.00 |
| 21 | 650420 | 30" REINFORCED CONCRETE PIPE (CLASS IV) | LF | 12 | 330.00 | 3,960.00 | 185.00 | 2,220.00 |
| 22 | 665017 | 18" CORRUGATED STEEL PIPE (0.078" THICK) | LF | 21 | 195.00 | 4,095.00 | 185.00 | 3,885.00 |
| 23 | 731521 | MINOR CONCRETE (SIDEWALK) | SQFT | 2,510 | 5.50 | 13,805.00 | 4.40 | 11,044.00 |
| 24 | 800360 | CHAIN LINK FENCE (TYPE CL-6) | LF | 170 | 43.00 | 7,310.00 | 29.00 | 4,930.00 |
| 25 | 840656 | PAINT TRAFFIC STRIPE (2-COAT) | LF | 83,500 | 0.22 | 18,370.00 | 0.20 | 16,700.00 |
| 26 | 840506 | 8" THERMOPLASTIC TRAFFIC STRIPE | LF | 5,600 | 1.30 | 7,280.00 | 0.55 | 3,080.00 |
| 27 | 850102 | PAVEMENT MARKER (REFLECTIVE) | EA | 1,800 | 5.25 | 9,450.00 | 2.20 | 3,960.00 |
| 28 | 840519 | THERMOPLASTIC CROSSWALK AND PAVEMENT MARKING | SQFT | 6,700 | 2.90 | 19,430.00 | 3.30 | 22,110.00 |
| 29 | 860301 | SIGNAL AND LIGHTING [MENIFEE ROAD AND SCOTT ROAD] | LS | 1 | 167,000.00 | 167,000.00 | 169,500.00 | 169,500.00 |
| 30 | 860301 | SIGNAL AND LIGHTING [BRIGGS ROAD AND SCOTT ROAD] | LS | 1 | 165,000.00 | 165,000.00 | 159,500.00 | 159,500.00 |
| 31 | 861502 | MODIFY SIGNAL [LINDENBERGER ROAD AND SCOTT ROAD] | LS | 1 | 110,000.00 | 110,000.00 | 94,900.00 | 94,900.00 |
| 32 | 860301 | SIGNAL AND LIGHTING [BRIGHTON WOOD STREET/REVIVAL DRIVEWAY AND SCOTT ROAD] | LS | 1 | 167,000.00 | 167,000.00 | 153,500.00 | 153,500.00 |
| 33 | 510060 | STRUCTURAL CONCRETE, RETAINING WALL | CY | 400 | 1,280.00 | 512,000.00 | 1,000.00 | 400,000.00 |
| 34 | 510545 | MINOR CONCRETE (HEADWALL) | CY | 3 | 2,800.00 | 8,400.00 | 9.20 | 27.60 |
| 35 | 066003 | INSTALL ENVIRONMENTALLY SENSITIVE AREA (ESA) FENCING | LF | 1,220 | 3.25 | 3,965.00 | 3.75 | 4,575.00 |
| 36 | 820130 | OBJECT MARKER [TYPE L-1] | EA | 4 | 70.00 | 280.00 | 28.00 | 112.00 |

**Riverside County Transportation Department
Summary of Bids**

PROJECT: Scott Road - Antelope Road to El Centro Lane

**Advertised: October 2, 2007 (Agenda Item 3.71)
Bids Open: 2:00 pm Date: October 31, 2007**

PROJECT NO. A5-0256

| Base Bid | | GRIFFITH COMPANY Santa Ana, CA 92704 | | | BEADOR CONSTRUCTION COMPANY, INC. Corona, CA 92883 | | |
|----------------------------|-----------|---|-------|----------|--|---------------------|---------------------|
| ITEM NO. | ITEM CODE | CONTRACT ITEM | UNITS | QUANTITY | BID | AMOUNT | AMOUNT |
| 37 | 394002 | PLACE ASPHALT CONCRETE (MISCELLANEOUS AREA) | SCFT | 129 | 14.00 | 1,806.00 | 17.00 |
| 38 | 066105 | RESIDENT ENGINEERS OFFICE | LS | 1 | 20,000.00 | 20,000.00 | 46,600.00 |
| 39 | 152440 | ADJUST MANHOLE TO GRADE [STORM DRAIN] | EA | 9 | 850.00 | 7,650.00 | 610.00 |
| 40 | 999990 | MOBILIZATION | LS | 1 | 200,000.00 | 200,000.00 | 200,000.00 |
| 41 | 510501 | MINOR CONCRETE [PROTECTIVE SLAB] | LF | 80 | 53.00 | 4,240.00 | 100.00 |
| SUBTOTAL (BASE BID) | | | | | | 5,335,258.75 | |
| ITEMS 1-41 | | | | | | | 5,448,567.60 |

| Alternate 1 | | GRIFFITH COMPANY Santa Ana, CA 92704 | | | BEADOR CONSTRUCTION COMPANY, INC. Corona, CA 92883 | | |
|-------------------------------|-----------|---|-------|----------|--|------------------|------------------|
| ITEM NO. | ITEM CODE | CONTRACT ITEM | UNITS | QUANTITY | BID | AMOUNT | AMOUNT |
| 42 | 152440 | ADJUST MANHOLE TO GRADE [SEWER] | EA | 7 | 850.00 | 5,950.00 | 1,500.00 |
| 43 | 152351 | RELOCATE HYDRANT | EA | 2 | 11,000.00 | 22,000.00 | 7,500.00 |
| SUBTOTAL (ALTERNATE 1) | | | | | | 27,950.00 | |
| ITEMS 42-43 | | | | | | | 25,500.00 |

| PROJECT TOTAL | | ITEMS 1-43 | | | ITEMS 1-43 | | |
|---------------|--|------------|--|--|------------|---------------------|---------------------|
| | | | | | | 5,363,208.75 | 5,474,067.60 |

**Riverside County Transportation Department
Summary of Bids**

PROJECT: Scott Road - Antelope Road to El Centro Lane

Advertised: October 2, 2007 (Agenda Item 3.71)

Bids Open: 2:00 pm Date: October 31, 2007

PROJECT NO. A5-0256

| Base Bid | | ELITE BOBCAT SERVICE, INC. Corona, CA 92879 | | | SEQUEL CONTRACTORS, INC. Santa Fe Springs, CA 90670 | | | |
|----------|-----------|---|-------|----------|--|--------------|------------|--------------|
| ITEM NO. | ITEM CODE | CONTRACT ITEM | UNITS | QUANTITY | BID | AMOUNT | BID | AMOUNT |
| 1 | 800701 | WOOD FENCE | LF | 40 | 69.00 | 2,760.00 | 50.00 | 2,000.00 |
| 2 | 011506 | WEDGE PLANE ASPHALT CONCRETE | LF | 7,000 | 1.25 | 8,750.00 | 1.25 | 8,750.00 |
| 3 | 013904 | PLACE ASPHALT CONCRETE DIKE (CRS 212) (8") | LF | 870 | 6.00 | 5,220.00 | 9.00 | 7,830.00 |
| 4 | 017302 | MINOR CONCRETE (CROSS-GUTTER) (CRS 209) | SQFT | 3,900 | 7.25 | 28,275.00 | 9.00 | 35,100.00 |
| 5 | 017305 | MINOR CONCRETE (CURB AND GUTTER) (CRS 201) | LF | 1,600 | 20.00 | 32,000.00 | 20.00 | 32,000.00 |
| 6 | 017315 | MINOR CONCRETE (CURB RAMP) (CRS 403-CASE A) | EA | 8 | 2,700.00 | 21,600.00 | 2,000.00 | 16,000.00 |
| 7 | 017316 | MINOR CONCRETE (CURB RAMP) (CRS 403-CASE B) | EA | 4 | 2,700.00 | 10,800.00 | 2,000.00 | 8,000.00 |
| 8 | 066102 | DUST ABATEMENT | LS | 1 | 20,000.00 | 20,000.00 | 40,000.00 | 40,000.00 |
| 9 | 074020 | WATER POLLUTION CONTROL | LS | 1 | 20,000.00 | 20,000.00 | 40,000.00 | 40,000.00 |
| 10 | 120100 | TRAFFIC CONTROL SYSTEM | LS | 1 | 152,000.00 | 152,000.00 | 290,000.00 | 290,000.00 |
| 11 | 160101 | CLEARING AND GRUBBING | LS | 1 | 32,000.00 | 32,000.00 | 20,000.00 | 20,000.00 |
| 12 | 170101 | DEVELOP WATER SUPPLY | LS | 1 | 20,000.00 | 20,000.00 | 8,000.00 | 8,000.00 |
| 13 | 190101 | ROADWAY EXCAVATION | CY | 78,400 | 15.50 | 1,215,200.00 | 15.75 | 1,234,800.00 |
| 14 | 220101 | FINISHING ROADWAY | LS | 1 | 57,000.00 | 57,000.00 | 125,000.00 | 125,000.00 |
| 15 | 260201 | CLASS 2 AGGREGATE BASE | CY | 26,900 | 23.00 | 618,700.00 | 30.00 | 807,000.00 |
| 16 | 390155 | ASPHALT CONCRETE (TYPE A) | TON | 17,900 | 63.00 | 1,127,700.00 | 69.00 | 1,235,100.00 |
| 17 | 013901 | ASPHALT RUBBER HOT MIX | TON | 10,000 | 85.00 | 850,000.00 | 80.00 | 800,000.00 |
| 18 | 510501 | MINOR CONCRETE (OVERSIDE DRAIN) | CY | 1 | 1,600.00 | 1,600.00 | 4,500.00 | 4,500.00 |
| 19 | 566011 | ROADSIDE SIGN - ONE POST | EA | 32 | 300.00 | 9,600.00 | 300.00 | 9,600.00 |
| 20 | 650014 | 16" REINFORCED CONCRETE PIPE | LF | 50 | 118.00 | 5,900.00 | 150.00 | 7,500.00 |
| 21 | 650420 | 30" REINFORCED CONCRETE PIPE (CLASS IV) | LF | 12 | 525.00 | 6,300.00 | 300.00 | 3,600.00 |
| 22 | 665017 | 18" CORRUGATED STEEL PIPE (0.079" THICK) | LF | 21 | 265.00 | 5,565.00 | 125.00 | 2,625.00 |
| 23 | 731521 | MINOR CONCRETE (SIDEWALK) | SQFT | 2,510 | 5.00 | 12,550.00 | 4.50 | 11,295.00 |
| 24 | 800360 | CHAIN LINK FENCE (TYPE CL-6) | LF | 170 | 41.00 | 6,970.00 | 26.00 | 4,420.00 |
| 25 | 840656 | PAINT TRAFFIC STRIPE (2-COAT) | LF | 83,500 | 0.07 | 5,845.00 | 0.20 | 16,700.00 |
| 26 | 840506 | 8" THERMOPLASTIC TRAFFIC STRIPE | EA | 5,800 | 1.05 | 5,880.00 | 1.00 | 5,600.00 |
| 27 | 850102 | PAVEMENT MARKER (REFLECTIVE) | EA | 1,800 | 3.50 | 6,300.00 | 4.00 | 7,200.00 |
| 28 | 840519 | THERMOPLASTIC CROSSWALK AND PAVEMENT MARKING | SQFT | 6,700 | 2.10 | 14,070.00 | 3.00 | 20,100.00 |
| 29 | 860301 | SIGNAL AND LIGHTING [MENIFEE ROAD AND SCOTT ROAD] | LS | 1 | 192,000.00 | 192,000.00 | 160,000.00 | 160,000.00 |
| 30 | 860301 | SIGNAL AND LIGHTING [BRIGGS ROAD AND SCOTT ROAD] | LS | 1 | 178,000.00 | 178,000.00 | 158,000.00 | 158,000.00 |
| 31 | 861502 | MODIFY SIGNAL [LINDENBERGER ROAD AND SCOTT ROAD] | LS | 1 | 125,000.00 | 125,000.00 | 100,000.00 | 100,000.00 |
| 32 | 860301 | SIGNAL AND LIGHTING [BREIGHTON WOOD STREET/REVIVAL DRIVEWAY AND SCOTT ROAD] | LS | 1 | 200,000.00 | 200,000.00 | 160,000.00 | 160,000.00 |
| 33 | 510060 | STRUCTURAL CONCRETE, RETAINING WALL | CY | 400 | 900.00 | 360,000.00 | 275.00 | 110,000.00 |
| 34 | 510545 | MINOR CONCRETE (HEADWALL) | CY | 3 | 2,600.00 | 7,800.00 | 1,000.00 | 3,000.00 |
| 35 | 066003 | INSTALL ENVIRONMENTALLY SENSITIVE AREA (ESA) FENCING | LF | 1,220 | 3.50 | 4,270.00 | 10.00 | 12,200.00 |
| 36 | 820130 | OBJECT MARKER [TYPE L-1] | EA | 4 | 40.00 | 160.00 | 200.00 | 800.00 |

**Riverside County Transportation Department
Summary of Bids**

PROJECT: Scott Road - Antelope Road to El Centro Lane

**Advertised: October 2, 2007 (Agenda Item 3.71)
Bids Open: 2:00 pm Date: October 31, 2007**

PROJECT NO. A5-0256

| Base Bid | | ELITE BOBCAT SERVICE, INC. Corona, CA 92879 | | | SEQUEL CONTRACTORS, INC. Santa Fe Springs, CA 90670 | | |
|----------------------------|-----------|--|-------|----------|--|---------------------|---------------------|
| ITEM NO. | ITEM CODE | CONTRACT ITEM | UNITS | QUANTITY | BID | AMOUNT | AMOUNT |
| 37 | 394002 | PLACE ASPHALT CONCRETE (MISCELLANEOUS AREA) | SQFT | 129 | 15.00 | 1,935.00 | 3,612.00 |
| 38 | 066105 | RESIDENT ENGINEERS OFFICE | LS | 1 | 55,000.00 | 55,000.00 | 25,000.00 |
| 39 | 152440 | ADJUST MANHOLE TO GRADE [STORM DRAIN] | EA | 9 | 400.00 | 3,600.00 | 3,150.00 |
| 40 | 999990 | MOBILIZATION | LS | 1 | 129,250.00 | 129,250.00 | 200,000.00 |
| 41 | 510501 | MINOR CONCRETE [PROTECTIVE SLAB] | LF | 80 | 60.00 | 4,800.00 | 6,000.00 |
| SUBTOTAL (BASE BID) | | | | | | 5,564,400.00 | 5,744,482.00 |
| ITEMS 1-41 | | | | | | | |

| Alternate 1 | | ELITE BOBCAT SERVICE, INC. Corona, CA 92879 | | | SEQUEL CONTRACTORS, INC. Santa Fe Springs, CA 90670 | | |
|-------------------------------|-----------|--|-------|----------|--|------------------|------------------|
| ITEM NO. | ITEM CODE | CONTRACT ITEM | UNITS | QUANTITY | BID | AMOUNT | AMOUNT |
| 42 | 152440 | ADJUST MANHOLE TO GRADE [SEWER] | EA | 7 | 400.00 | 2,800.00 | 2,450.00 |
| 43 | 152351 | RELOCATE HYDRANT | EA | 2 | 6,500.00 | 13,000.00 | 20,000.00 |
| SUBTOTAL (ALTERNATE 1) | | | | | | 15,800.00 | 22,450.00 |
| ITEMS 42-43 | | | | | | | |

| PROJECT TOTAL | | ELITE BOBCAT SERVICE, INC. Corona, CA 92879 | | | SEQUEL CONTRACTORS, INC. Santa Fe Springs, CA 90670 | | |
|---------------|---------------------|--|----------|-----|--|---------------------|--------|
| ITEMS | AMOUNT | UNITS | QUANTITY | BID | AMOUNT | AMOUNT | AMOUNT |
| ITEMS 1-43 | 5,580,200.00 | | | | | 5,766,932.00 | |

**Riverside County Transportation Department
Summary of Bids**

PROJECT: Scott Road - Antelope Road to El Centro Lane

**Advertised: October 2, 2007 (Agenda Item 3.71)
Bids Open: 2:00 pm Date: October 31, 2007**

PROJECT NO. A5-0256

| Base Bid | | SKANSKA USA CIVIL WEST Riverside, CA 92509 | | SOUTHLAND PAVING, INC. Escondido, CA 92029 | | | | |
|----------|-----------|---|-------|---|------------|--------------|------------|--------------|
| ITEM NO. | ITEM CODE | CONTRACT ITEM | UNITS | QUANTITY | BID | AMOUNT | BID | AMOUNT |
| 1 | 800701 | WOOD FENCE | LF | 40 | 45.00 | 1,800.00 | 50.00 | 2,000.00 |
| 2 | 011506 | WEDGE PLANE ASPHALT CONCRETE | LF | 7,000 | 1.50 | 10,500.00 | 1.64 | 11,480.00 |
| 3 | 013904 | PLACE ASPHALT CONCRETE DIKE (CRS 212) (8") | LF | 870 | 4.00 | 3,480.00 | 7.70 | 6,699.00 |
| 4 | 017302 | MINOR CONCRETE (CROSS-GUTTER) (CRS 209) | SQFT | 3,900 | 12.00 | 46,800.00 | 7.70 | 30,030.00 |
| 5 | 017305 | MINOR CONCRETE (CURB AND GUTTER) (CRS 201) | LF | 1,600 | 25.00 | 40,000.00 | 17.60 | 28,160.00 |
| 6 | 017315 | MINOR CONCRETE (CURB RAMP) (CRS 403-CASE A) | EA | 8 | 4,500.00 | 36,000.00 | 3,850.00 | 30,800.00 |
| 7 | 017316 | MINOR CONCRETE (CURB RAMP) (CRS 403-CASE B) | EA | 4 | 4,500.00 | 18,000.00 | 3,300.00 | 13,200.00 |
| 8 | 066102 | DUST ABATEMENT | LS | 1 | 60,000.00 | 60,000.00 | 77,000.00 | 77,000.00 |
| 9 | 074020 | WATER POLLUTION CONTROL | LS | 1 | 90,000.00 | 90,000.00 | 99,000.00 | 99,000.00 |
| 10 | 120100 | TRAFFIC CONTROL SYSTEM | LS | 1 | 132,000.00 | 132,000.00 | 176,000.00 | 176,000.00 |
| 11 | 160101 | CLEARING AND GRUBBING | LS | 1 | 20,000.00 | 20,000.00 | 20,000.00 | 20,000.00 |
| 12 | 170101 | DEVELOP WATER SUPPLY | LS | 1 | 30,000.00 | 30,000.00 | 22,000.00 | 22,000.00 |
| 13 | 190101 | ROADWAY EXCAVATION | CY | 78,400 | 10.00 | 784,000.00 | 19.60 | 1,536,640.00 |
| 14 | 220101 | FINISHING ROADWAY | LS | 1 | 20,000.00 | 20,000.00 | 64,000.00 | 64,000.00 |
| 15 | 260201 | CLASS 2 AGGREGATE BASE | CY | 26,900 | 28.00 | 753,200.00 | 25.50 | 685,950.00 |
| 16 | 390155 | ASPHALT CONCRETE (TYPE A) | TON | 17,900 | 80.00 | 1,432,000.00 | 69.80 | 1,249,420.00 |
| 17 | 013901 | ASPHALT RUBBER HOT MIX | TON | 10,000 | 100.00 | 1,000,000.00 | 97.00 | 970,000.00 |
| 18 | 510501 | MINOR CONCRETE (OVERSIDE DRAIN) | CY | 1 | 1,000.00 | 1,000.00 | 1,100.00 | 1,100.00 |
| 19 | 566011 | ROADSIDE SIGN - ONE POST | EA | 32 | 225.00 | 7,200.00 | 242.00 | 7,744.00 |
| 20 | 850014 | 18" REINFORCED CONCRETE PIPE | LF | 50 | 120.00 | 6,000.00 | 165.00 | 8,250.00 |
| 21 | 850420 | 30" REINFORCED CONCRETE PIPE (CLASS IV) | LF | 12 | 360.00 | 4,320.00 | 200.00 | 2,400.00 |
| 22 | 665017 | 18" CORRUGATED STEEL PIPE (0.079" THICK) | LF | 21 | 165.00 | 3,465.00 | 165.00 | 3,465.00 |
| 23 | 731521 | MINOR CONCRETE (SIDEWALK) | SQFT | 2,510 | 7.50 | 18,825.00 | 4.65 | 11,671.50 |
| 24 | 800360 | CHAIN LINK FENCE (TYPE CL-6) | LF | 170 | 25.00 | 4,250.00 | 28.00 | 4,760.00 |
| 25 | 840656 | PAINT TRAFFIC STRIPE (2-COAT) | LF | 83,500 | 0.20 | 16,700.00 | 0.24 | 20,040.00 |
| 26 | 840508 | 8" THERMOPLASTIC TRAFFIC STRIPE | LF | 5,600 | 1.00 | 5,600.00 | 0.53 | 2,968.00 |
| 27 | 850102 | PAVEMENT MARKER (REFLECTIVE) | EA | 1,800 | 4.00 | 7,200.00 | 2.81 | 5,058.00 |
| 28 | 840519 | PAVEMENT MARKER (REFLECTIVE) | SQFT | 6,700 | 2.00 | 13,400.00 | 3.70 | 24,790.00 |
| 29 | 860301 | THERMOPLASTIC CROSSWALK AND PAVEMENT MARKING | LS | 1 | 180,000.00 | 180,000.00 | 178,500.00 | 178,500.00 |
| 30 | 860301 | SIGNAL AND LIGHTING [MENIFEE ROAD AND SCOTT ROAD] | LS | 1 | 177,000.00 | 177,000.00 | 167,300.00 | 167,300.00 |
| 31 | 861502 | SIGNAL AND LIGHTING [BRIGGS ROAD AND SCOTT ROAD] | LS | 1 | 120,000.00 | 120,000.00 | 73,000.00 | 73,000.00 |
| 32 | 860301 | MODIFY SIGNAL [LINDENBERGER ROAD AND SCOTT ROAD] | LS | 1 | 180,000.00 | 180,000.00 | 163,100.00 | 163,100.00 |
| 33 | 510060 | SIGNAL AND LIGHTING [BRIGHTON WOOD STREET/REVIVAL DRIVEWAY AND SCOTT ROAD] | LS | 1 | 180,000.00 | 180,000.00 | 163,100.00 | 163,100.00 |
| 34 | 510545 | STRUCTURAL CONCRETE, RETAINING WALL | CY | 400 | 1,100.00 | 440,000.00 | 1,256.00 | 502,400.00 |
| 35 | 066003 | MINOR CONCRETE (HEADWALL) | CY | 3 | 2,500.00 | 7,500.00 | 1,000.00 | 3,000.00 |
| 36 | 820130 | INSTALL ENVIRONMENTALLY SENSITIVE AREA (ESA) FENCING OBJECT MARKER [TYPE L-1] | LF | 1,220 | 10.00 | 12,200.00 | 2.15 | 2,623.00 |
| | | | EA | 4 | 60.00 | 240.00 | 33.00 | 132.00 |

**Riverside County Transportation Department
Summary of Bids**

PROJECT: Scott Road - Antelope Road to El Centro Lane

**Advertised: October 2, 2007 (Agenda Item 3.71)
Bids Open: 2:00 pm Date: October 31, 2007**

PROJECT NO. A5-0256

| Base Bid | | SKANSKA USA CIVIL WEST Riverside, CA 92509 | | SOUTHLAND PAVING, INC. Escondido, CA 92029 | | | | |
|----------------------------|-----------|---|-------|---|------------|---------------------|------------|---------------------|
| ITEM NO. | ITEM CODE | CONTRACT ITEM | UNITS | QUANTITY | BID | AMOUNT | BID | AMOUNT |
| 37 | 394002 | PLACE ASPHALT CONCRETE (MISCELLANEOUS AREA) | SQFT | 129 | 16.00 | 2,064.00 | 20.00 | 2,580.00 |
| 38 | 066105 | RESIDENT ENGINEERS OFFICE | LS | 1 | 60,000.00 | 60,000.00 | 27,500.00 | 27,500.00 |
| 39 | 152440 | ADJUST MANHOLE TO GRADE (STORM DRAIN) | EA | 9 | 1,200.00 | 10,800.00 | 420.00 | 3,780.00 |
| 40 | 999990 | MOBILIZATION | LS | 1 | 200,000.00 | 200,000.00 | 200,000.00 | 200,000.00 |
| 41 | 510501 | MINOR CONCRETE (PROTECTIVE SLAB) | LF | 80 | 80.00 | 6,400.00 | 27.50 | 2,200.00 |
| SUBTOTAL (BASE BID) | | | | | | 5,961,944.00 | | 6,440,740.50 |
| ITEMS 1-41 | | | | | | | | |

| Alternate 1 | | SKANSKA USA CIVIL WEST Riverside, CA 92509 | | SOUTHLAND PAVING, INC. Escondido, CA 92029 | | | | |
|-------------------------------|-----------|---|-------|---|----------|------------------|----------|------------------|
| ITEM NO. | ITEM CODE | CONTRACT ITEM | UNITS | QUANTITY | BID | AMOUNT | BID | AMOUNT |
| 42 | 152440 | ADJUST MANHOLE TO GRADE (SEWER) | EA | 7 | 2,000.00 | 14,000.00 | 420.00 | 2,940.00 |
| 43 | 152351 | RELOCATE HYDRANT | EA | 2 | 5,000.00 | 10,000.00 | 3,850.00 | 7,700.00 |
| SUBTOTAL (ALTERNATE 1) | | | | | | 24,000.00 | | 10,640.00 |
| ITEMS 42-43 | | | | | | | | |

| PROJECT TOTAL | | ITEMS 1-43 | |
|---------------|--|------------|---------------------|
| | | | 5,985,944.00 |
| | | | 6,451,380.50 |

**ENCUMBRANCE INFORMATION
FOR BOARD OF SUPERVISORS APPROVED CONTRACTS
COUNTY OF RIVERSIDE**

B-PO NO.: **B**

VENDOR NAME AND ADDRESS:
 All American Asphalt
 P.O. Box 2229
 Corona, Ca. 92878-2229
 (951) 736-7600

DEPT: **Transportation**
 DATE: **November 20, 2007**
 BUDGET F.Y.: **2007 / 2008**

BOS APPROVAL DATE: _____
 AGENDA NUMBER: _____

VENDOR CODE: _____

TRANS CODE: **PO**

TRANS DEPT: **3130500000**

DOCUMENT TOTAL: **\$ 4,925,850.00**

| LINE NO. | FUND | DEPT. | ORG. | SUB ORG. | APPR CODE | OBJECT | ACTIVITY | JOB/PROJECT | LINE AMOUNT |
|----------|--------------|-------|------|----------|-----------|--------|----------|-------------|-------------|
| | 20000 | | | | | | | | |

NOTE:

Fund 20000 is exempt from encumbering construction contracts per agreement with A-C General Accounting Division. (Contact: Bob Barton Ext. 5-3843)

Regular contract or Blanket contract.
 If blanket: Encumber, Do not encumber.
 Current year contract, or
 Multi-year contract.

If multi-year contract, encumbrance amount for:
 First year \$ N/A
 Second year \$ _____
 Third year \$ _____

CONTRACT DESCRIPTION:
**Construction of Road Improvements
 Scott Road, Antelope Road to El Centro Lane
 Menifee area
 Project no. A5-0256**

PREPARED BY: **Stan A. Dery**

DATE: **November 20, 2007**

APPROVED BY: _____

DATE: _____

A-C ENCUMBRANCE:

ENCUMBERED BY: _____

PHONE: (951) 955-6785
